

POWERACT

CONSULTING



USER GUIDE

CortexSkills

What to do and what to type, task by task, for large companies and SMEs

Version 1.0.0 · 2026-09-29
Prepared by POWERACT Consulting

Table of Contents

1. About this guide.....	7
How to read a task table.....	7
2. Getting around the application.....	8
2.1 The header.....	8
2.2 The menu.....	8
2.3 Roles and accounts.....	9
3. Start from the tenancy: Group, Organization, Project.....	10
3.1 Create a Group and an Organization (administrator).....	10
3.2 Create a project.....	10
3.3 The complexity score (decision matrix).....	11
4. Working on a task.....	13
4.1 Complete a task.....	13
4.2 AI help.....	14
4.3 Gates and checklists.....	14
4.4 Reopen a task.....	14
5. Following progress.....	15
6. Large and big companies (any sector).....	17
6.1 Enablers (run across all phases).....	17
E2E-15 · Data-AI-Integration.....	17
E2E-17 · Change-to-Adoption.....	18
E2E-18 · Quality-Risk-Improvement.....	18
6.2 Scope & evidence — gate G1.....	19
E2E-32 · Scope-of-Work-to-Engineering-Plan.....	19
E2E-33 · Questionnaire-to-Response-Collection.....	20
E2E-19 · Consulting Engagement-to-Closure.....	21
E2E-24 · Competitive Intelligence-to-Strategy.....	21
6.3 Diagnosis — gate G2.....	22
E2E-20 · Multi-Axis Diagnostic-to-Maturity Report.....	22
E2E-25 · Job Architecture-to-Competency Map.....	23
E2E-26 · GPEC-to-Training Plan.....	24
E2E-27 · Demand Collection-to-Consolidation.....	25
E2E-28 · Performance Assessment-to-RAG Dashboard.....	26
E2E-29 · Functional SWOT-to-Improvement Axes.....	26
E2E-02 · Skills-to-Gap Diagnosis.....	27
E2E-21 · Previous Plan Impact-to-Strategy Update.....	28
6.4 Training Engineering Report & plan — gate G3.....	29
E2E-01 · Strategy-to-Learning Plan.....	29
E2E-03 · Needs-to-Training Engineering Report & Roadmap.....	30
E2E-30 · Prioritization-to-Resource Plan.....	31
E2E-22 · Multi-Site Plan-to-Deployment.....	31
E2E-23 · Regulatory Submission-to-Validation.....	32
E2E-16 · Vendor-to-Finance.....	33
AUTO-E2E-02 · Automotive Critical-Skills-to-Transformation Plan.....	33
6.5 Design & delivery — gate G4.....	34

E2E-04 · Roadmap-to-Curriculum Design.....	34
E2E-05 · Design-to-Delivery.....	35
E2E-06 · Learner-Journey-to-Engagement.....	36
E2E-13 · Content-Curate-to-Retire.....	36
E2E-14 · Extended-Enterprise-Training.....	37
6.6 Evaluation, compliance & impact — gate G5.....	38
E2E-07 · Assessment-to-Evaluation.....	38
E2E-08 · Learning-to-ROI.....	39
E2E-09 · Compliance-to-Certification.....	39
AUTO-E2E-01 · Automotive Compliance-to-Certification Readiness.....	40
6.7 Talent, knowledge & continuous improvement — gate G6.....	40
E2E-10 · Talent-to-Mobility.....	40
E2E-11 · Onboarding-to-Productivity.....	41
E2E-12 · Knowledge-Capture-to-Transfer.....	42
E2E-31 · Engagement-to-Roadmap.....	42
7. SMEs (any sector).....	44
7.1 Enablers (run across all phases).....	45
E2E-15 · Data-AI-Integration.....	45
E2E-17 · Change-to-Adoption.....	45
E2E-18 · Quality-Risk-Improvement.....	46
7.2 Scope & evidence — gate G1.....	46
E2E-32 · Scope-of-Work-to-Engineering-Plan.....	46
E2E-33 · Questionnaire-to-Response-Collection.....	47
E2E-19 · Consulting Engagement-to-Closure.....	48
E2E-24 · Competitive Intelligence-to-Strategy.....	49
SME-E2E-01 · SME Snapshot-to-Plan in 30 days.....	50
7.3 Diagnosis — gate G2.....	50
E2E-20 · Multi-Axis Diagnostic-to-Maturity Report.....	50
E2E-25 · Job Architecture-to-Competency Map.....	51
E2E-26 · GPEC-to-Training Plan.....	52
E2E-27 · Demand Collection-to-Consolidation.....	53
E2E-28 · Performance Assessment-to-RAG Dashboard.....	54
E2E-29 · Functional SWOT-to-Improvement Axes.....	54
E2E-02 · Skills-to-Gap Diagnosis.....	55
E2E-21 · Previous Plan Impact-to-Strategy Update.....	56
7.4 Training Engineering Report & plan — gate G3.....	57
E2E-01 · Strategy-to-Learning Plan.....	57
E2E-03 · Needs-to-Training Engineering Report & Roadmap.....	58
E2E-30 · Prioritization-to-Resource Plan.....	59
E2E-22 · Multi-Site Plan-to-Deployment.....	60
E2E-23 · Regulatory Submission-to-Validation.....	60
E2E-16 · Vendor-to-Finance.....	61
AUTO-E2E-02 · Automotive Critical-Skills-to-Transformation Plan.....	62
SME-E2E-02 · SME Funding-to-Refund.....	62
7.5 Design & delivery — gate G4.....	62
E2E-04 · Roadmap-to-Curriculum Design.....	62

E2E-05 · Design-to-Delivery.....	63
E2E-06 · Learner-Journey-to-Engagement.....	64
E2E-13 · Content-Curate-to-Retire.....	65
E2E-14 · Extended-Enterprise-Training.....	66
SME-E2E-03 · SME Upskill-to-Adoption.....	67
7.6 Evaluation, compliance & impact — gate G5.....	67
E2E-07 · Assessment-to-Evaluation.....	67
E2E-08 · Learning-to-ROI.....	68
E2E-09 · Compliance-to-Certification.....	68
AUTO-E2E-01 · Automotive Compliance-to-Certification Readiness.....	69
7.7 Talent, knowledge & continuous improvement — gate G6.....	70
E2E-10 · Talent-to-Mobility.....	70
E2E-11 · Onboarding-to-Productivity.....	70
E2E-12 · Knowledge-Capture-to-Transfer.....	71
E2E-31 · Engagement-to-Roadmap.....	72
8. SMEs in AEC (architecture, engineering, construction).....	73
8.1 Enablers (run across all phases).....	73
E2E-15 · Data-AI-Integration.....	73
E2E-17 · Change-to-Adoption.....	74
E2E-18 · Quality-Risk-Improvement.....	74
8.2 Scope & evidence — gate G1.....	75
E2E-32 · Scope-of-Work-to-Engineering-Plan.....	75
E2E-33 · Questionnaire-to-Response-Collection.....	76
E2E-19 · Consulting Engagement-to-Closure.....	77
E2E-24 · Competitive Intelligence-to-Strategy.....	78
SME-E2E-01 · SME Snapshot-to-Plan in 30 days.....	78
8.3 Diagnosis — gate G2.....	79
E2E-20 · Multi-Axis Diagnostic-to-Maturity Report.....	79
E2E-25 · Job Architecture-to-Competency Map.....	80
E2E-26 · GPEC-to-Training Plan.....	80
E2E-27 · Demand Collection-to-Consolidation.....	81
E2E-28 · Performance Assessment-to-RAG Dashboard.....	82
E2E-29 · Functional SWOT-to-Improvement Axes.....	83
E2E-02 · Skills-to-Gap Diagnosis.....	83
E2E-21 · Previous Plan Impact-to-Strategy Update.....	84
8.4 Training Engineering Report & plan — gate G3.....	85
E2E-01 · Strategy-to-Learning Plan.....	85
E2E-03 · Needs-to-Training Engineering Report & Roadmap.....	86
E2E-30 · Prioritization-to-Resource Plan.....	87
E2E-22 · Multi-Site Plan-to-Deployment.....	88
E2E-23 · Regulatory Submission-to-Validation.....	89
E2E-16 · Vendor-to-Finance.....	89
AEC-E2E-02 · AEC & Construction Critical-Skills-to-Transformation Plan.....	90
SME-E2E-02 · SME Funding-to-Refund.....	90
8.5 Design & delivery — gate G4.....	91
E2E-04 · Roadmap-to-Curriculum Design.....	91

E2E-05 · Design-to-Delivery.....	92
E2E-06 · Learner-Journey-to-Engagement.....	93
E2E-13 · Content-Curate-to-Retire.....	94
E2E-14 · Extended-Enterprise-Training.....	94
SME-E2E-03 · SME Upskill-to-Adoption.....	95
8.6 Evaluation, compliance & impact — gate G5.....	96
E2E-07 · Assessment-to-Evaluation.....	96
E2E-08 · Learning-to-ROI.....	96
E2E-09 · Compliance-to-Certification.....	97
AEC-E2E-01 · AEC & Construction Compliance-to-Certification Readiness.....	98
8.7 Talent, knowledge & continuous improvement — gate G6.....	98
E2E-10 · Talent-to-Mobility.....	98
E2E-11 · Onboarding-to-Productivity.....	99
E2E-12 · Knowledge-Capture-to-Transfer.....	99
E2E-31 · Engagement-to-Roadmap.....	100
9. SMEs in healthcare.....	102
9.1 Enablers (run across all phases).....	102
E2E-15 · Data-AI-Integration.....	102
E2E-17 · Change-to-Adoption.....	103
E2E-18 · Quality-Risk-Improvement.....	103
9.2 Scope & evidence — gate G1.....	104
E2E-32 · Scope-of-Work-to-Engineering-Plan.....	104
E2E-33 · Questionnaire-to-Response-Collection.....	105
E2E-19 · Consulting Engagement-to-Closure.....	106
E2E-24 · Competitive Intelligence-to-Strategy.....	107
SME-E2E-01 · SME Snapshot-to-Plan in 30 days.....	107
9.3 Diagnosis — gate G2.....	108
E2E-20 · Multi-Axis Diagnostic-to-Maturity Report.....	108
E2E-25 · Job Architecture-to-Competency Map.....	109
E2E-26 · GPEC-to-Training Plan.....	109
E2E-27 · Demand Collection-to-Consolidation.....	110
E2E-28 · Performance Assessment-to-RAG Dashboard.....	111
E2E-29 · Functional SWOT-to-Improvement Axes.....	112
E2E-02 · Skills-to-Gap Diagnosis.....	112
E2E-21 · Previous Plan Impact-to-Strategy Update.....	113
9.4 Training Engineering Report & plan — gate G3.....	114
E2E-01 · Strategy-to-Learning Plan.....	114
E2E-03 · Needs-to-Training Engineering Report & Roadmap.....	115
E2E-30 · Prioritization-to-Resource Plan.....	116
E2E-22 · Multi-Site Plan-to-Deployment.....	117
E2E-23 · Regulatory Submission-to-Validation.....	118
E2E-16 · Vendor-to-Finance.....	118
HCPR-E2E-02 · Healthcare Providers Critical-Skills-to-Transformation Plan.....	119
SME-E2E-02 · SME Funding-to-Refund.....	119
9.5 Design & delivery — gate G4.....	120
E2E-04 · Roadmap-to-Curriculum Design.....	120

E2E-05 · Design-to-Delivery.....	121
E2E-06 · Learner-Journey-to-Engagement.....	122
E2E-13 · Content-Curate-to-Retire.....	123
E2E-14 · Extended-Enterprise-Training.....	123
SME-E2E-03 · SME Upskill-to-Adoption.....	124
9.6 Evaluation, compliance & impact — gate G5.....	125
E2E-07 · Assessment-to-Evaluation.....	125
E2E-08 · Learning-to-ROI.....	125
E2E-09 · Compliance-to-Certification.....	126
HCPR-E2E-01 · Healthcare Providers Compliance-to-Certification Readiness.....	127
9.7 Talent, knowledge & continuous improvement — gate G6.....	127
E2E-10 · Talent-to-Mobility.....	127
E2E-11 · Onboarding-to-Productivity.....	128
E2E-12 · Knowledge-Capture-to-Transfer.....	128
E2E-31 · Engagement-to-Roadmap.....	129
10. Administration.....	131
Appendix — Status colours.....	132

1. About this guide

CortexSkills guides a training engineering engagement from its scope to the evaluation of its results: 33 end-to-end processes, grouped into seven phases, each made of user tasks and steps. This guide tells you where to click and, for every task, exactly what to type. The examples come from the demonstration data, so you can follow them on screen.

Parts 6 to 9 each follow one type of organization from start to finish:

Part	Audience	Example organization used	Sign in as
6	Large and big companies (any sector)	Atlas Motors Kénitra — Automotive, large company	headld@atlasmotorskenitra.ma
7	SMEs (any sector)	Tanger Auto Parts — Automotive, SME	headld@tangerautoparts.ma
8	SMEs in AEC (architecture, engineering, construction)	Souss BTP Solutions — AEC & Construction, SME	headld@soussbtpolutions.ma
9	SMEs in healthcare	Clinique Al Amal — Healthcare Providers, SME	headld@cliniquealamal.ma

Every organization has two full runs: a Digital skills run and an AI skills run. Both follow the same tasks; the task tables show what to type in the Digital run and, where the text differs, what to type in the AI run.

How to read a task table

Column	Meaning
Task	The task code (UFT-xx-yy), its name, and the role that does it (R = Responsible).
Steps	The steps you tick inside the task, with their codes. They come from the process design.
What to type	The text to enter in the task's result box. The same text is shown in the application in the "What to type" panel.

Password for every demonstration account

CortexSkills#2026 — except the platform administrator: admin@cortexskills.app / Admin#2026.

2. Getting around the application

After you sign in, the screen has three parts: the menu on the side, the header at the top and the work area in the middle.

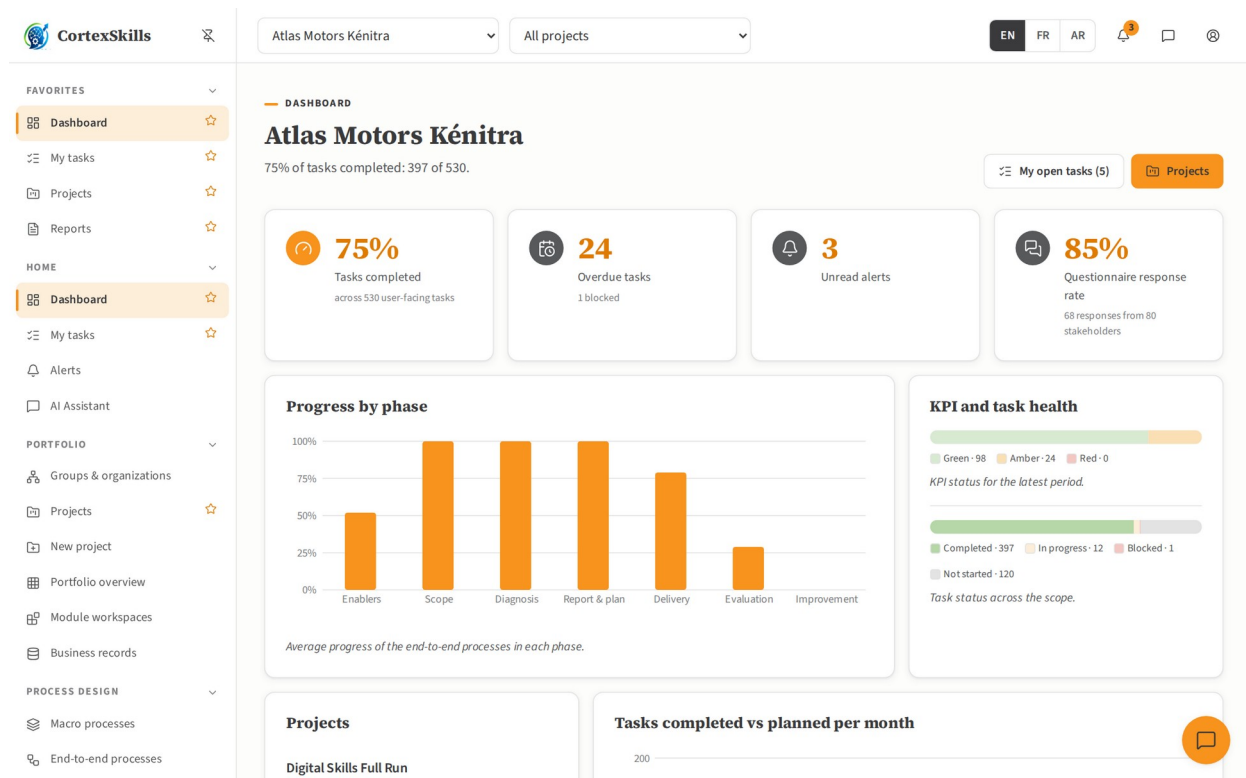


Figure 1 — Dashboard of a large company (Head of L&D)

2.1 The header

Element	What it does
Organization selector	Chooses the organization you work in. Only the platform administrator sees every organization; Group members can read sister organizations.
Project selector	Limits every screen to one project (run), or shows all projects.
EN · FR · AR	Changes the language at once. Arabic turns the whole application right-to-left. Your choice is remembered.
Bell	Opens your alerts. The number shows unread alerts.
Speech bubble	Opens the AI Assistant from any screen.
Person icon	Your settings and sign-out.

2.2 The menu

The menu is grouped by what you do: Home, Portfolio, Process design, Governance & risk, AI & knowledge, Reports, Administration and Settings. You only see what your role allows.

- Click the star next to a screen to add it to Favorites, at the top of the menu.
- Click the pin to keep the menu open, or unpin it: it then slides in when you point at the edge.
- In Settings you can dock the menu on the left, right, top or bottom.

2.3 Roles and accounts

Each organization has one demonstration account per role. The e-mail address is the name in the second column followed by @ and the organization's domain (for example hrd@atlasmotorskenitra.ma). SMEs have a smaller set of roles.

Role	E-mail name	Role	E-mail name
Platform Administrator	admin	HR Business Partner / Job Analyst	hrbp
HR Director / Steering Committee Chair	hrd	GPEC Specialist	gpec
Head of L&D	headld	Finance Manager	finance
L&D Analyst	analyst	Purchasing Officer	purchasing
L&D Strategist	strategist	Compliance Officer / DPO	compliance
L&D Business Partner	ldbp	Quality Manager	quality
L&D Planner	planner	IT Architect	itarch
Instructional Designer	designer	Consultant (PM / Partner)	consultant
Content Developer / Curator	content	Knowledge Manager	km
Training Administrator	trainadmin	Change Manager	change
Trainer / Coach	trainer	Extended Enterprise Manager	ee
Employee / Learner	employee	Site L&D Coordinator	site
Manager / Hiring Manager	manager	Subject Matter Expert	sme
Performance Analyst	perf	Auditor (Read-Only)	auditor
Strategy Analyst / Head of Strategy	strategy		

3. Start from the tenancy: Group, Organization, Project

Everything in CortexSkills belongs to an organization, and optionally to a Group of organizations. Always start here: choose or create the Group (Yes or No), then the Organization, then the project.

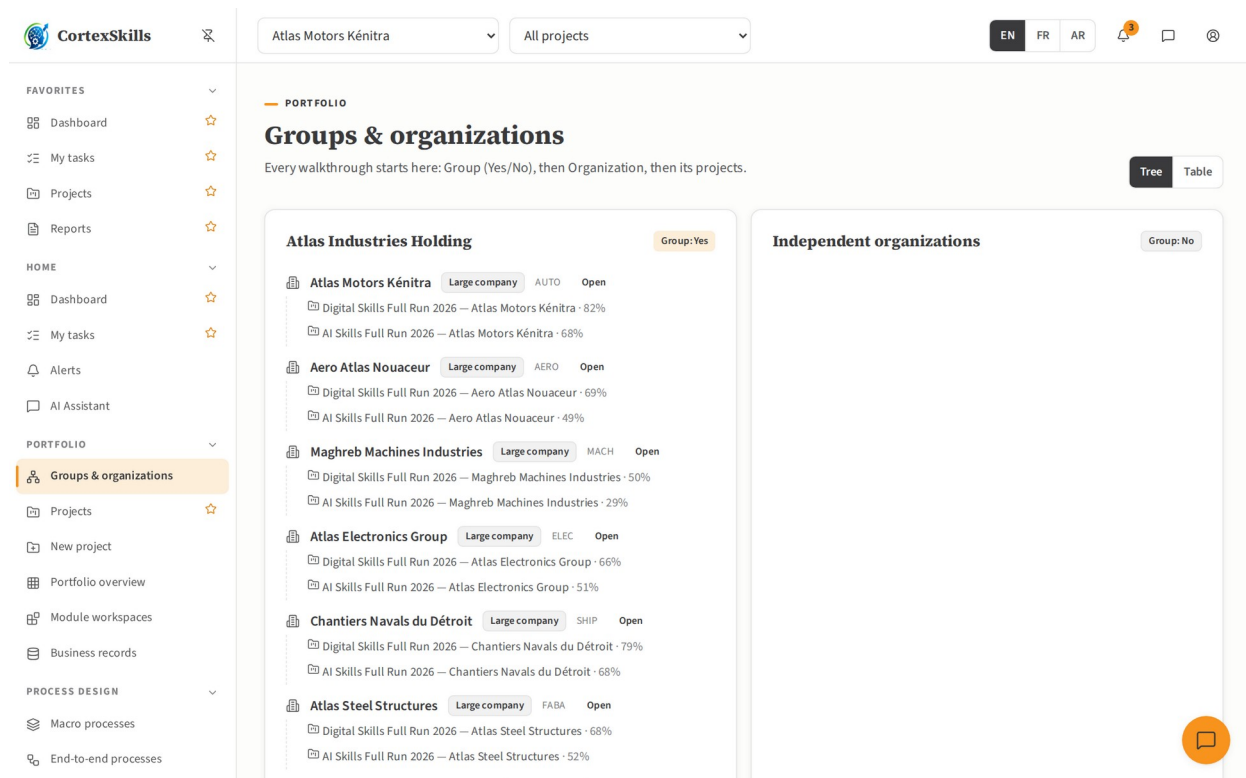


Figure 2 — Portfolio › Groups and organizations: the tenancy tree and table

3.1 Create a Group and an Organization (administrator)

1. Sign in as admin@cortexskills.app and open Portfolio › Groups and organizations.
2. Group: click New group, type the name (for example “Atlas Industrial Holding”) and save. If the organization is independent, skip this step: its Group is “No”.
3. Click New organization. Type the name, choose the sector, the segment (Large or SME), the number of employees, the country, the default language and the e-mail domain (for example atlasmotorskenitra.ma).
4. Choose the Group, or No group. Tick “Create a starting team” to receive one account per role under that domain.
5. Save. The organization receives its structure (OBS), governance catalog, AI use cases, checklists and templates.

3.2 Create a project

Open Portfolio › New project. There are three ways to create it, on the same screen:

Mode	When to use it	What you do
From the catalog	The usual case	Pick a published template that matches your sector, mode and track. Its phases, gates, checklists and roles are copied into the project.

Mode	When to use it	What you do
Manual	A very specific engagement	Type the project, choose sector, mode and track, and build the phases by attaching gates and checklists.
With AI	You have a short description	Type two or three sentences (for example “Digital skills plan for the maintenance team, two sites, quality audit next year”). The AI proposes the fields, scores, mode, track, template, phases, gates and checklists; accept, change or reject each item, then save.

Figure 3 — Portfolio > New project: the three creation modes and the complexity score

3.3 The complexity score (decision matrix)

In every mode you rate the project from 1 to 5 on seven weighted criteria. The score (0–100) recommends the mode: 70 and above → Full mode; below 70 → SME mode, with the SME track that matches the score. You can change the track only with a written justification, which is recorded.

Criterion	Weight	1 — Very low	2 — Low	3 — Moderate	4 — High	5 — Very high
Strategic impact	20%	Routine, well known, little at stake	Some new elements, limited stakes	Noticeable change, several functions involved	Major change, significant stakes or constraints	Transformational, strong constraints, high risk
Technical novelty	15%	Routine, well known, little at stake	Some new elements, limited stakes	Noticeable change, several functions involved	Major change, significant stakes or constraints	Transformational, strong constraints, high risk
Regulatory burden	15%	Routine, well known, little at stake	Some new elements, limited stakes	Noticeable change, several functions involved	Major change, significant stakes or constraints	Transformational, strong constraints, high risk
Investment size	15%	Routine, well known, little at stake	Some new elements, limited stakes	Noticeable change, several functions involved	Major change, significant stakes or constraints	Transformational, strong constraints, high risk

Criterion	Weight	1 — Very low	2 — Low	3 — Moderate	4 — High	5 — Very high
Cross-functional scope	15%	Routine, well known, little at stake	Some new elements, limited stakes	Noticeable change, several functions involved	Major change, significant stakes or constraints	Transformational, strong constraints, high risk
Market uncertainty	10%	Routine, well known, little at stake	Some new elements, limited stakes	Noticeable change, several functions involved	Major change, significant stakes or constraints	Transformational, strong constraints, high risk
Time-to-market pressure	10%	Routine, well known, little at stake	Some new elements, limited stakes	Noticeable change, several functions involved	Major change, significant stakes or constraints	Transformational, strong constraints, high risk

Score	Recommended mode and track
70 – 100	Full mode: all phases and gates G1 to G5
50 – 69	SME mode, track T3 (extended)
30 – 49	SME mode, track T2 (standard)
0 – 29	SME mode, track T1 (essential)

4. Working on a task

A project is made of end-to-end processes (E2E), each with user tasks. You find your tasks in Home › My tasks, or through the project: Portfolio › Projects › your project › the process › the task.

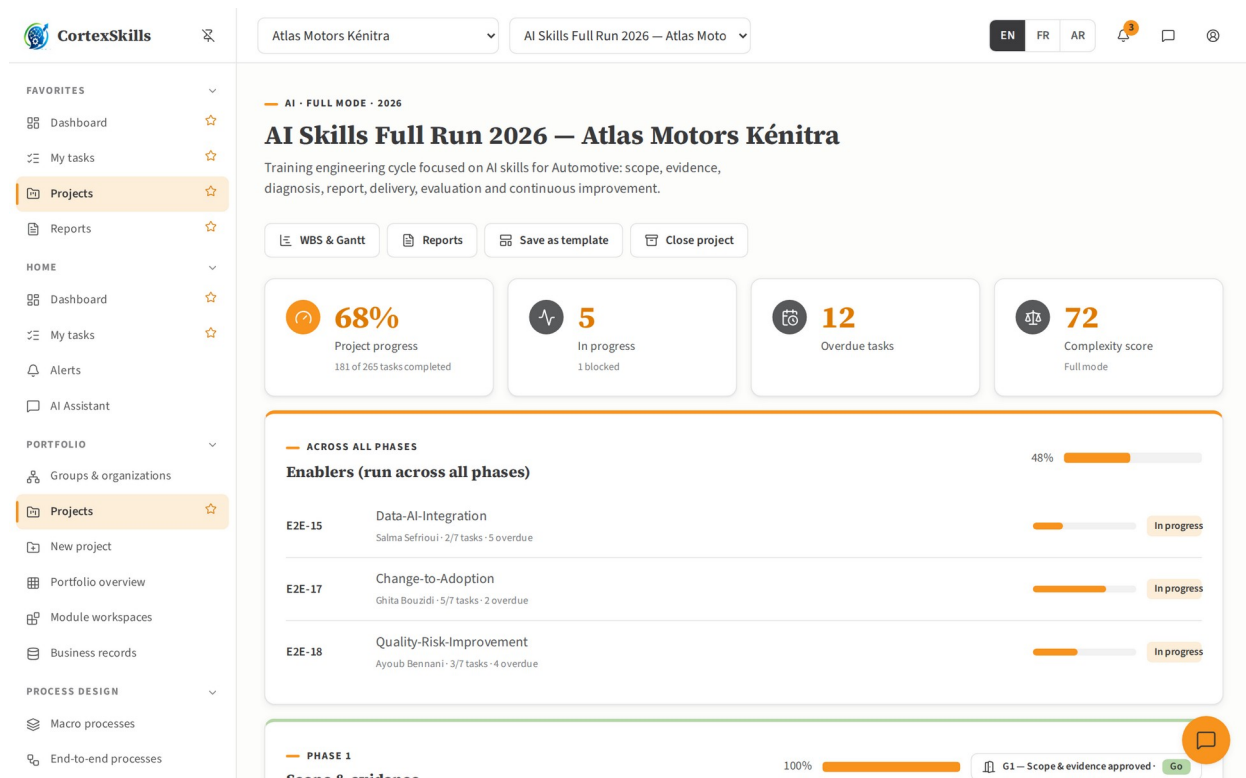


Figure 4 — A project workspace: phases, processes, progress and gates

4.1 Complete a task

1. Open the task. A panel opens on the side with four tabs: Work, RACSI, Files and History.
2. Read the “What to type” box: it shows the expected answer for this task. Parts 6 to 9 of this guide list it for every task.
3. If the task is Not started, click Start.
4. Tick each step as you do it.
5. Type your result in “Your result”. You can use the AI help (below).
6. Attach evidence in the Files tab if needed (documents, spreadsheets, images, drawings, archives...).
7. Click Complete. A task cannot be completed before the previous task of the same process, or while the gate of the previous phase has open mandatory items.
8. A window proposes to record a lesson learned (REX): click Fill now, or Skip.

Figure 5 — The task panel with “What to type”, steps, result, owner and evaluator

4.2 AI help

When an AI use case is linked to the task, an “AI help” box appears. Click the use case: the suggestion is labelled as AI-generated with its confidence and sources. Click Accept to copy it into your result, Edit then accept to change it first, or Reject. Every choice is logged. The owner and the evaluator of a task are always two different people.

4.3 Gates and checklists

Each phase ends with a gate. Its checklist items must be ticked (with evidence when required) before the next phase can start. The gate owner then records a decision: Go, No-Go, Hold or Recycle.

Gate	Purpose
G1 — Scope & evidence approved	Confirm the approved Scope of Work and a consolidated questionnaire dataset.
G2 — Diagnostic validated	Validate diagnostic findings, gaps, demands, RAG and SWOT.
G3 — Report & roadmap approved	Approve the Training Engineering Report, prioritized plan and budget.
G4 — Delivery readiness	Confirm designs, content, trainers and logistics before delivery.
G5 — Evaluation & impact validated	Validate effectiveness, ROI and compliance status.
G6 — Closure & continuous improvement	Close the cycle with REX and the post-engagement roadmap.

4.4 Reopen a task

A completed task can be reopened with a written justification, until the gate of its phase has been submitted. The reopening is recorded in the audit log.

5. Following progress

Screen	Where	What you see
Dashboard	Home › Dashboard	Completion, overdue tasks, alerts, response rate, progress by phase, KPI health.
My tasks	Home › My tasks	Your open tasks, with due dates, sorted by urgency.
Alerts	Home › Alerts (bell)	Overdue steps, red KPIs, licence and quota warnings. Mark as read or dismiss.
Portfolio view	Portfolio › Portfolio view	One row per project, one column per phase, with the status of each cell.
WBS and Gantt	Project › WBS and Gantt	Phases, processes and tasks on one timeline. Print or save as PDF.
Reports	Reports	Standard reports, exported to PDF, Excel or Word.
AI Assistant	Speech bubble / Home › AI Assistant	Ask questions such as “How many tasks are overdue?” or “How do I export a report?”.
Benchmark	Reports › Benchmark	Compare projects inside your organization, or organizations of your Group (aggregates only).

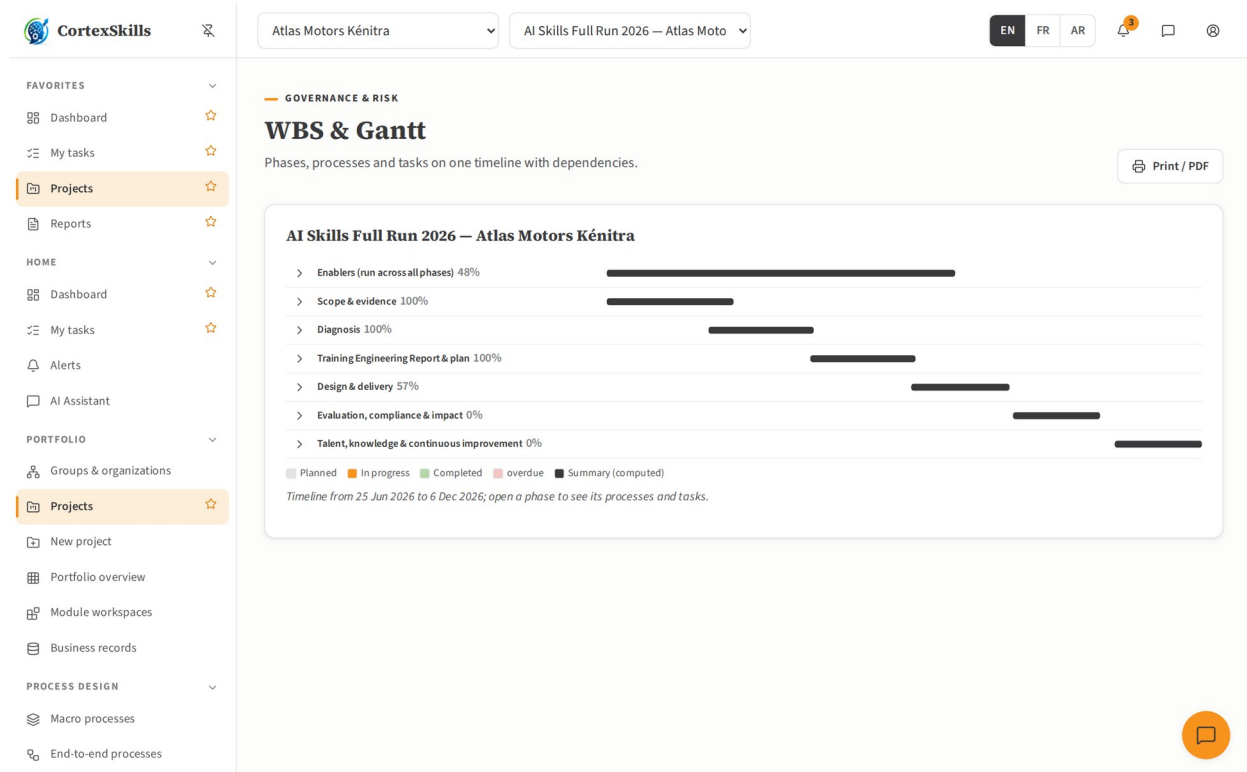


Figure 6 — WBS and Gantt of a full run

REPORTS

Reports

34 standard reports; preview, then download PDF, Excel or Word.

Report catalog

- RPT-001 Training Engineering Report
- RPT-002 Prioritized Training Plan
- RPT-003 Skills Gap Matrix
- RPT-004 Consolidated Demand Matrix
- RPT-005 MS/MQ/OP RAG Dashboard
- RPT-006 Functional SWOT & Improvement Axes
- RPT-007 Competitive Intelligence Report
- RPT-008 Job Architecture Health
- RPT-009 GPEC Integration Report
- RPT-010 Post-Engagement Roadmap
- RPT-011 Budget vs Actual
- RPT-012 ROI & Business Impact Report
- RPT-013 Compliance & Certification Status
- RPT-014 Delivery & Attendance Report
- RPT-015 Learner Engagement Cockpit
- RPT-016 Kirkpatrick Evaluation Report

Project

AI Skills Full Run 2026 — Atlas Motors Kénitra

PDF Excel Word

RPT-001 · ON DEMAND (PER PLAN CYCLE)

Training Engineering Report

Atlas Motors Kénitra · AI Skills Full Run 2026 — Atlas Motors Kénitra

Audience: Head of L&D; HR Director

Key performance indicators

ID	KPI	Value	Target	Period
KPI-004	Training Engineering Report cycle time	29.7	≤ 30 days	2026-09

Training Engineering Report

Label	Status	AI-drafted sections
Training Engineering Report — Atlas Motors Kénitra	Published	4

Training Need

Figure 7 — Reports: choose a report, a project and a format

AI Assistant

Ask about your data or about how to use the application.

Automatic Data query Application help

Type your question

Ask

How many overdue tasks? What is the questionnaire response rate? How do I approve a Scope of Work?

Top risks

What the Assistant can answer

Each data question needs one permission, checked before any data is read.

- Projects — projects.view
- Overdue tasks — projects.view
- My open tasks — tasks.execute
- Unread alerts — alerts.view
- Project progress — projects.view
- KPIs off target — reports.view
- Top risks — governance.view
- Questionnaire response rate — m54.view
- Budget spend — m18.view
- Priority themes — m49.view
- Stakeholders — m53.view
- AI usage — ai.view
- Licence status — config.view
- Users — users.manage

Figure 8 — The AI Assistant answers from your own data, within your permissions

6. Large and big companies (any sector)

This part follows Atlas Motors Kénitra, a large company in the Automotive sector (4200 employees, Kénitra, member of Atlas Industries Holding). Sign in as headld@atlasmotorskenitra.ma. The same steps apply to any organization of this type: replace the names, figures and themes with your own.

Item	Digital skills run	AI skills run
Project	Digital Skills Full Run 2026 — Atlas Motors Kénitra	AI Skills Full Run 2026 — Atlas Motors Kénitra
Mode and track	Full	Full
Processes and tasks	35 processes · 265 tasks	35 processes · 265 tasks

Phase	Gate	End-to-end processes
Enablers (run across all phases)	—	E2E-15, E2E-17, E2E-18
Scope & evidence	G1	E2E-32, E2E-33, E2E-19, E2E-24
Diagnosis	G2	E2E-20, E2E-25, E2E-26, E2E-27, E2E-28, E2E-29, E2E-02, E2E-21
Training Engineering Report & plan	G3	E2E-01, E2E-03, E2E-30, E2E-22, E2E-23, E2E-16, AUTO-E2E-02
Design & delivery	G4	E2E-04, E2E-05, E2E-06, E2E-13, E2E-14
Evaluation, compliance & impact	G5	E2E-07, E2E-08, E2E-09, AUTO-E2E-01
Talent, knowledge & continuous improvement	G6	E2E-10, E2E-11, E2E-12, E2E-31

6.1 Enablers (run across all phases)

E2E-15 · Data-AI-Integration

Goal: Govern data, AI, integrations. **Starts when:** New integration, data source or AI use case to govern. **Ends when:** Integrations, data and AI governed with health, retention and usage reviewed.

Task	Steps	What to type
UFT-15-01 Register external integration R: Platform Administrator	MP-16.1 Register external integration	Register integration 'HRIS — Workday' (INT-HR-01); credential reference stored encrypted.
UFT-15-02 Map fields and check health R: IT Architect	MP-16.2 Map integration fields MP-16.3 Check integration health	Map fields: employee_id → matricule; position → poste. Health check: success.
UFT-15-03 Run HRIS synchronisation R: IT Architect	MP-16.4 Run HRIS synchronisation MP-16.5 Review synchronisation rejections	Sync run: 1,204 records updated, 3 rejected (missing position) — corrected.
UFT-15-04 Set data retention rule R: Data Protection Officer	MP-16.6 Set data retention rule	Retention: questionnaire responses 3 years; training records 10 years.
UFT-15-05 Maintain AI use case register R: Platform Administrator	MP-16.7 Maintain AI use case register	Add custom use case 'Shift-report summarizer' (Assistive), version 1.

Task	Steps	What to type
UFT-15-06 Set AI activation per scope R: Platform Administrator	MP-16.8 Set AI activation per scope MP-24.1 Enable personalization per scope	Activate AIUC-35 and AIUC-36 for the organization; override Off for pilot project B.
UFT-15-07 Review AI usage log R: IT Architect	MP-16.9 Review AI usage log MP-28.2 Validate dataset quality	Usage review: 412 suggestions — 71% accepted, 20% edited, 9% rejected.

E2E-17 · Change-to-Adoption

Goal: Drive sustained adoption and culture change. **Starts when:** Approved plan or new platform capability requiring adoption. **Ends when:** Sustained adoption reached with low-adoption groups reinforced.

Task	Steps	What to type
UFT-17-01 Assess change impact R: Change Manager	MP-19.1 Assess change impact	Impact: Assembly & Production supervisors high, operators medium, support functions low.
UFT-17-02 Build adoption plan R: Change Manager	MP-19.2 Build adoption plan	Adoption plan: sponsor message, 6 champions, weekly 15-minute huddles for 8 weeks.
UFT-17-03 Launch communication campaign R: Change Manager	MP-19.3 Launch communication campaign	Campaign 'MES and digital shop-floor tracking — why it matters' on e-mail, intranet and screens. AI run: Campaign 'AI visual inspection of welds and paint — why it matters' on e-mail, intranet and screens.
UFT-17-04 Open community space R: Knowledge Manager	MP-12.3 Create community space MP-12.4 Moderate community posts MP-26.1 Create learning cohort group	Community space 'MES and digital shop-floor tracking Q&A' opened; moderation rules published. AI run: Community space 'AI visual inspection of welds and paint Q&A' opened; moderation rules published.
UFT-17-05 Track adoption usage R: L&D Analyst	MP-19.4 Track adoption usage MP-08.5 Monitor engagement indicators	Weekly active users: 64% of the target population.
UFT-17-06 Identify low-adoption groups R: Change Manager	MP-19.5 Identify low-adoption groups	Low adoption confirmed for night shift (31%); one group rejected as false positive.
UFT-17-07 Run reinforcement actions R: Change Manager	MP-19.6 Run reinforcement actions MP-08.6 Trigger re-engagement nudge	Reinforcement: night-shift coaching sessions; adoption reached 58% after 4 weeks.

E2E-18 · Quality-Risk-Improvement

Goal: Improve processes and mitigate risk. **Starts when:** Risk logged, periodic quality review due or control test scheduled. **Ends when:** Risks mitigated, actions evaluated by a different person, controls rated.

Task	Steps	What to type
UFT-18-01 Log risk or opportunity R: Quality Manager	MP-20.1 Log risk or opportunity	Risk 'Trainers unavailable in Q3': likelihood 3, impact 4, score 12.
UFT-18-02 Assign mitigation action R: Quality Manager	MP-20.2 Assign mitigation action	Action: contract a second vendor; owner Purchasing Officer; evaluator Quality Manager.

Task	Steps	What to type
UFT-18-03 Execute improvement action R: Action Owner	MP-20.3 Execute improvement action	Action done: framework contract signed with vendor B; evidence attached.
UFT-18-04 Evaluate action effectiveness R: Action Evaluator	MP-20.4 Evaluate action effectiveness	Verdict: effective. The evaluator is a different user from the owner.
UFT-18-05 Review access and security R: IT Architect	MP-17.4 Review access violation log MP-17.6 Enforce login rate limit MP-17.2 Assign roles to user MP-17.3 Edit permission matrix MP-17.5 Issue signed session token	Access review: 2 dormant accounts disabled; 0 cross-tenant attempts.
UFT-18-06 Run periodic quality review R: Quality Manager	MP-20.5 Run periodic quality review MP-09.7 Review evaluation results	Quality review minutes: 3 KPIs red, 2 actions opened, next review in 30 days.
UFT-18-07 Update control effectiveness R: Quality Manager	MP-20.6 Update control effectiveness rating	Control CTRL-002 effectiveness: Effective; CTRL-031: Partially effective.

6.2 Scope & evidence — gate G1

E2E-32 · Scope-of-Work-to-Engineering-Plan

Goal: Define and approve the structured scope of work and stakeholder register. **Starts when:** New training engineering engagement, annual plan cycle, or executive request. **Ends when:** Approved Scope of Work with criteria matrix and stakeholder register released to questionnaire design (E2E-33) and needs analysis (E2E-03).

Task	Steps	What to type
UFT-32-01 Define scope frame R: Head of L&D	MP-53.1 Define scope frame (Group Yes/No) MP-53.2 Select Organization	Group scope: No. Organization: Atlas Motors Kénitra.
UFT-32-02 Select sector R: L&D Analyst	MP-53.3 Select sector	Sector: Automotive.
UFT-32-03 Select decision levels R: L&D Analyst	MP-53.4 Select decision level (MS/MO/OP/Custom)	Decision levels: MS, MO, OP (no custom level).
UFT-32-04 Map functions × decision levels R: L&D Analyst	MP-53.5 Map functions × decision level	Matrix: Assembly & Production × MS/MO/OP; Quality × MO/OP; Finance × MS/MO; HR × MS/MO.
UFT-32-05 Select focus and add custom criteria R: Head of L&D	MP-53.6 Select focus (All/Digital/AI/Custom) MP-53.7 Add custom criteria	Focus: Digital. Custom criterion: 'Readiness for MES and digital shop-floor tracking' (weight 2.00). AI run: Focus: AI. Custom criterion: 'Readiness for AI visual inspection of welds and paint' (weight 2.00).
UFT-32-06 Identify stakeholders R: HR Business Partner	MP-53.8 Identify stakeholders	Register 40 stakeholders: name, role, function, level, site, preferred channel (Email, Face-to-Face or Hybrid).
UFT-32-07 Validate scope R: Head of L&D	MP-53.9 Validate and approve scope	Validation: every function in scope has at least 3 stakeholders; completeness 100%.

Task	Steps	What to type
UFT-32-08 Approve scope R: HR Director / Consultant PM	MP-53.9 Validate and approve scope MP-53.10 Publish scope and register stakeholders	Approval status: Approved (version 1). Justification: scope aligned with SO-1 and SO-2.
UFT-32-09 Publish scope and register stakeholders R: L&D Analyst	MP-53.10 Publish scope and register stakeholders	Generate the SOW document (RPT-033) and release scope and stakeholders to the questionnaire studio.

E2E-33 · Questionnaire-to-Response-Collection

Goal: Design, distribute and collect questionnaire responses across channels. **Starts when:** An approved Scope of Work becomes available (end of E2E-32). **Ends when:** Consolidated, validated questionnaire response dataset feeding needs analysis (E2E-03), diagnostic (E2E-20) and demand collection (E2E-27).

Task	Steps	What to type
UFT-33-01 Select questionnaire template R: L&D Analyst	MP-54.1 Select questionnaire template by focus	Template: 'Digital needs — Automotive' in the user's language, 5 sections. AI run: Template: 'AI needs — Automotive' in the user's language, 5 sections.
UFT-33-02 Elaborate questionnaire R: L&D Analyst	MP-54.2 Elaborate questionnaire (Load/AI/Manual)	Elaboration mode: AI. 24 questions generated from the approved Scope of Work.
UFT-33-03 Tailor and validate content R: L&D Analyst	MP-54.3 Tailor to sector and focus	Validate each question; reword 5 with Assembly & Production vocabulary; delete 2 duplicates.
UFT-33-04 Allocate RACSI R: Head of L&D	MP-54.4 Allocate RACSI per section	Section 'Digital practices': R L&D Analyst, A Head of L&D, C Consultant PM, S IT, I CHRO (one Accountable only).
UFT-33-05 Select distribution channels R: Survey Administrator	MP-54.5 Select distribution channels	Channels: MS and MO by Email; OP Face-to-Face with tablets; night shift Hybrid.
UFT-33-06 Distribute questionnaire R: Survey Administrator	MP-54.6 Distribute to stakeholders	Distribute to 40 stakeholders; 40 dispatches logged.
UFT-33-07 Send reminders R: Survey Administrator	MP-54.7 Send reminders on cadence	Reminder 1 on day 5 to 17 non-respondents; reminder 2 on day 10 to 8.
UFT-33-08 Collect responses R: Stakeholders	MP-54.8 Collect responses	Responses: 34 collected (22 online, 12 offline synchronised).
UFT-33-09 Validate completeness R: L&D Analyst	MP-54.9 Validate completeness and consent	Completeness: 31 complete, 3 incomplete flagged.
UFT-33-10 Consolidate responses R: L&D Analyst	MP-54.10 Consolidate responses	Consolidated dataset: 31 responses, 24 questions, by function and level.
UFT-33-11 Check consent and release dataset R: L&D Analyst	MP-54.11 Feed responses to needs analysis and diagnostic MP-54.12 Report on response rate and engagement	Consent given for 31 of 31 stored responses; release to needs analysis, diagnostic and demand collection.

Task	Steps	What to type
UFT-33-12 Report on response and engagement R: L&D Analyst	MP-54.12 Report on response rate and engagement	Response rate 85%; engagement rate 78%; completeness 91% (RPT-034).

E2E-19 · Consulting Engagement-to-Closure

Goal: Manage full consulting engagement lifecycle. **Starts when:** Client purchase order or engagement request received. **Ends when:** Engagement closed with client acceptance and REX recorded.

Task	Steps	What to type
UFT-19-01 Register engagement and purchase order R: Consultant PM	MP-36.1 Register engagement and purchase order	Engagement 'Training engineering 2026 — Atlas Motors Kénitra', PO-CL-221, 45 consulting days.
UFT-19-02 Hold kickoff meeting R: Consultant PM	MP-36.2 Hold kickoff meeting	Kickoff held on 10 February with HR Director, Head of L&D and 4 function heads.
UFT-19-03 Draft meeting minutes R: Consultant PM	MP-36.3 Draft meeting minutes	Review the AI minutes: 6 decisions, 9 actions, RACSI extracted; correct 1 owner name.
UFT-19-04 Align with client strategy R: Consultant PM	MP-01.1 Record corporate strategic objectives MP-01.2 Link objectives to functions and sites	Client objectives recorded: MES and digital shop-floor tracking and IATF 16949 compliance for Assembly & Production. AI run: Client objectives recorded: AI visual inspection of welds and paint and IATF 16949 compliance for Assembly & Production.
UFT-19-05 Plan engagement work breakdown R: Consultant PM	MP-36.4 Plan engagement work breakdown	WBS: 6 phases, 14 deliverables, Gantt from February to November.
UFT-19-06 Plan change support R: Change Manager	MP-19.1 Assess change impact MP-19.2 Build adoption plan	Change plan: 3 sponsor messages, champion network, 2 town-halls.
UFT-19-07 Track engagement deliverables R: Consultant PM	MP-36.5 Track engagement deliverables MP-20.5 Run periodic quality review	Deliverables: 9 of 14 delivered on time, 1 late (SWOT), 4 planned.
UFT-19-08 Deliver final report and obtain acceptance R: Consultant PM	MP-36.6 Deliver final report MP-36.7 Obtain client acceptance	Final report delivered; acceptance signed by the HR Director on 28 November.
UFT-19-09 Record engagement REX R: Consultant PM	MP-36.8 Record engagement REX MP-12.6 Record REX entry MP-12.5 Prompt REX at closure	REX: went well — stakeholder register; did not — late SWOT inputs; root cause — no function-head backup; rating 4/5.

E2E-24 · Competitive Intelligence-to-Strategy

Goal: Analyze external environment and feed L&D strategy. **Starts when:** Annual strategy cycle or executive request for market positioning analysis. **Ends when:** Validated competitive intelligence report feeding into L&D strategy and organizational diagnostic.

Task	Steps	What to type
UFT-24-01 Define intelligence scope R: Strategy Analyst	MP-43.1 Define intelligence scope	Scope: Automotive market in Morocco and export markets; horizon 3 years; focus on MES and digital shop-floor tracking and PLM and digital engineering change. AI run: Scope: Automotive market in Morocco and export markets; horizon 3 years; focus on AI visual inspection of welds and paint and Predictive maintenance of press lines.
UFT-24-02 Conduct Porter's Five Forces R: Strategy Analyst	MP-43.2 Conduct Porter's Five Forces analysis	Rivalry 4/5; new entrants 3/5; substitutes 2/5; supplier power 3/5; buyer power 4/5.
UFT-24-03 Map market segments R: Market Analyst	MP-43.3 Map market segments	Segments: key accounts (55% revenue), resellers (30%), direct small customers (15%).
UFT-24-04 Analyze competitor positioning R: Market Analyst	MP-43.4 Analyze competitor positioning	Competitor A leads on MES and digital shop-floor tracking; competitor B cheaper but weaker on IATF 16949. AI run: Competitor A leads on AI visual inspection of welds and paint; competitor B cheaper but weaker on IATF 16949.
UFT-24-05 Monitor regulatory and technology trends R: Regulatory Analyst	MP-43.5 Monitor regulatory changes MP-43.6 Track technology trends MP-43.7 Benchmark against industry	Trends: revision of IATF 16949 expected next year; fast growth of Supplier portal and EDI. AI run: Trends: revision of IATF 16949 expected next year; fast growth of Generative AI for 8D problem solving.
UFT-24-06 Identify L&D implications R: L&D Strategist	MP-43.8 Identify strategic implications for L&D	L&D implication: build MES and digital shop-floor tracking skills for key-account teams before competitor A scales. AI run: L&D implication: build AI visual inspection of welds and paint skills for key-account teams before competitor A scales.
UFT-24-07 Publish intelligence report R: Strategy Analyst	MP-43.9 Produce intelligence report MP-43.10 Feed intelligence into strategy and diagnostic MP-43.11 Update intelligence continuously MP-43.12 Report to executive leadership	Publish RPT-007 Competitive Intelligence Report to the executive committee.

6.3 Diagnosis — gate G2

E2E-20 · Multi-Axis Diagnostic-to-Maturity Report

Goal: Conduct 5-axis diagnostic + CMM maturity + leadership assessment. **Starts when:** Engagement kickoff or approved Scope of Work requesting a diagnostic. **Ends when:** 5-axis diagnostic, CMM maturity and leadership maturity report validated with the sponsor.

Task	Steps	What to type
UFT-20-01 Define diagnostic axes and sample R: Consultant PM	MP-37.1 Define diagnostic axes and sample	Axes: strategy, organization, processes, people, information systems. Sample: 40 people (MS 8, MO 16, OP 16).
UFT-20-02 Deploy diagnostic questionnaire R: Consultant PM	MP-37.2 Deploy diagnostic questionnaire MP-37.4 Collect questionnaire responses	Diagnostic questionnaire deployed to 40 people; 34 responses (85%).

Task	Steps	What to type
UFT-20-03 Conduct semi-structured interviews R: Consultant	MP-37.3 Conduct semi-structured interviews	Interview notes (OP, Assembly & Production): 'Procedures exist but are not updated since 2023.'
UFT-20-04 Score diagnostic axes R: Consultant	MP-37.5 Score diagnostic axes	Axis scores (1-5): strategy 3.4, organization 2.8, processes 2.6, people 3.1, IS 2.2.
UFT-20-05 Select maturity model R: Consultant	MP-38.1 Select maturity model levels MP-38.2 Define evidence criteria per level	Maturity model: CMM 5 levels; evidence for level 3 = documented and applied process.
UFT-20-06 Rate process maturity R: Consultant	MP-38.3 Rate maturity per process area MP-38.4 Compute maturity profile	Maturity: training management level 2; Assembly & Production processes level 3.
UFT-20-07 Assess leadership maturity R: HR Business Partner	MP-42.1 Launch leadership 360 assessment MP-42.2 Compute leadership maturity level	Leadership 360: average level 3 (Team Leadership) across 18 managers.
UFT-20-08 Cross-check skills and needs R: L&D Analyst	MP-02.7 Validate skills inventory MP-03.2 Review gap matrix by site and function	Cross-check: IS axis weakness confirmed by the MES and digital shop-floor tracking gap (-1.4). AI run: Cross-check: IS axis weakness confirmed by the AI visual inspection of welds and paint gap (-1.4).
UFT-20-09 Draft diagnostic findings R: Consultant	MP-37.6 Draft diagnostic findings MP-38.5 Produce maturity report	Edit AI findings: keep 5, merge 2, add one on IATF 16949 documentation.
UFT-20-10 Validate findings with sponsor R: Consultant PM	MP-37.7 Validate findings with sponsor MP-38.6 Agree target maturity	Findings validated with the sponsor; target maturity level 3 by 2026+1.

E2E-25 · Job Architecture-to-Competency Map

Goal: Manage organizational charts, position descriptions, gap analysis. **Starts when:** Organizational change, new role creation, or annual job architecture review. **Ends when:** Approved organizational charts, position descriptions, and competency maps with gap analysis.

Task	Steps	What to type
UFT-25-01 Map organizational structure R: HR Analyst	MP-44.1 Map organizational structure	Structure: 6 functions, 14 departments, 3 sites; 212 positions.
UFT-25-02 Design organizational charts R: Org Design Consultant	MP-44.2 Design organizational charts	Org chart 'Assembly & Production': director → 3 managers → 9 supervisors → operators.
UFT-25-03 Conduct job analysis R: Job Analyst	MP-44.3 Conduct job analysis	Job analysis 'Assembly & Production supervisor': 8 main activities, 2 of them now supported by MES and digital shop-floor tracking. AI run: Job analysis 'Assembly & Production supervisor': 8 main activities, 2 of them now supported by AI visual inspection of welds and paint.

Task	Steps	What to type
UFT-25-04 Draft position descriptions R: Job Analyst	MP-44.4 Draft position descriptions	Position description drafted: mission, activities, competencies (MES and digital shop-floor tracking level 3, IATF 16949 level 3), KPIs. AI run: Position description drafted: mission, activities, competencies (AI visual inspection of welds and paint level 3, IATF 16949 level 3), KPIs.
UFT-25-05 Validate with managers R: HR Business Partner	MP-44.5 Validate descriptions with managers	Validated by the Assembly & Production manager with 2 changes on activities.
UFT-25-06 Conduct gap analysis R: Job Analyst	MP-44.6 Conduct gap analysis existing versus real	Gap existing vs real: 11 descriptions outdated; 4 roles with new MES and digital shop-floor tracking tasks. AI run: Gap existing vs real: 11 descriptions outdated; 4 roles with new AI visual inspection of welds and paint tasks.
UFT-25-07 Identify roles to develop R: HR Business Partner	MP-44.7 Identify roles to develop MP-44.8 Update job architecture MP-44.9 Align with competency framework	Roles 'To develop': data-literate supervisor, maintenance technician 4.0.
UFT-25-08 Publish approved architecture R: HR Director	MP-44.10 Publish approved position descriptions MP-44.11 Track job architecture changes MP-44.12 Report on architecture health	Publish 212 approved descriptions and the architecture map to all employees.

E2E-26 · GPEC-to-Training Plan

Goal: Integrate Forward Planning of Jobs and Skills into L&D. **Starts when:** Annual HR strategic planning cycle or GPEC (Forward Planning of Jobs and Skills) review. **Ends when:** Training plan aligned with GPEC and HR strategic orientations.

Task	Steps	What to type
UFT-26-01 Define GPEC scope R: GPEC Specialist	MP-45.1 Define GPEC scope	GPEC scope: Assembly & Production and Information Systems jobs; horizon 3 years.
UFT-26-02 Map HR strategic orientations R: HR Director	MP-45.2 Map HR strategic orientations MP-45.3 Align training with GPEC	HR orientations: internal mobility first; 30% of promotions from internal talent.
UFT-26-03 Update development foundation R: HR Business Partner	MP-45.4 Update development foundation MP-45.5 Support human capital development	Development foundation updated: descriptions, annual objectives, evaluation grid.
UFT-26-04 Update Jobs and Skills Directory (REC) R: GPEC Specialist	MP-45.6 Update Jobs and Skills Directory (REC)	REC updated: 42 jobs, 3 new jobs linked to MES and digital shop-floor tracking. AI run: REC updated: 42 jobs, 3 new jobs linked to AI visual inspection of welds and paint.
UFT-26-05 Redynamize periodic evaluations R: HR Business Partner	MP-45.7 Redynamize periodic evaluations	Periodic evaluation redesigned: 2 reviews per year, competency section added.

Task	Steps	What to type
UFT-26-06 Design career paths R: HR Director	MP-45.8 Design career paths	Career path: operator → team leader → supervisor → Assembly & Production manager.
UFT-26-07 Document career management R: HR Director	MP-45.9 Document career management process MP-45.10 Implement collective compensation	Career management procedure documented (v1): eligibility, committee, calendar.
UFT-26-08 Align training with GPEC R: L&D Strategist	MP-45.11 Feed GPEC into training needs MP-45.12 Report on GPEC integration	Training aligned with GPEC: 4 themes cover the 3 new jobs; 2 themes removed.

E2E-27 · Demand Collection-to-Consolidation

Goal: Collect individual and collective training demands. **Starts when:** Annual training plan cycle or ad-hoc demand collection request. **Ends when:** Consolidated and prioritized demand repository integrated into the training needs analysis.

Task	Steps	What to type
UFT-27-01 Design demand collection forms R: L&D Analyst	MP-46.1 Design demand collection forms	Forms: individual form (5 questions) and collective form per team (3 questions).
UFT-27-02 Deploy individual demand collection R: L&D Analyst	MP-46.2 Deploy individual demand collection	Individual collection open 1-20 March; 146 demands received.
UFT-27-03 Deploy collective demand collection R: L&D Analyst	MP-46.3 Deploy collective demand collection	Collective collection: 18 team demands received.
UFT-27-04 Collect manager recommendations R: L&D Business Partner	MP-46.4 Collect manager recommendations	Manager recommendations: 24 received, 9 flagged as priority.
UFT-27-05 Consolidate demands by function R: L&D Analyst	MP-46.5 Consolidate demands by function	Consolidated: Assembly & Production 64 demands, Operations 41, Quality 22, others 37.
UFT-27-06 Map demands to competencies R: L&D Analyst	MP-46.6 Map demands to competencies MP-46.7 Prioritize demands	Accept AI mapping for 139 demands; map 7 manually to 'PLM and digital engineering change'. AI run: Accept AI mapping for 139 demands; map 7 manually to 'Predictive maintenance of press lines'.
UFT-27-07 Prioritize and validate demands R: L&D Business Partner	MP-46.8 Validate demands with managers MP-46.9 Integrate demands into needs analysis MP-46.10 Report on demand patterns MP-46.11 Track demand fulfillment MP-46.12 Improve demand collection	Validated: 112 demands (High 38, Medium 51, Low 23); 34 rejected with reason.

E2E-28 · Performance Assessment-to-RAG Dashboard

Goal: Assess MS/MO/OP performance with RAG ratings. **Starts when:** Annual performance cycle or management request for performance visualization. **Ends when:** Validated MS/MO/OP (Strategic Management / Operational Management / Operational Level) performance assessment with RAG (Green/Amber/Red) dashboards.

Task	Steps	What to type
UFT-28-01 Define MS/MO/OP framework R: Performance Analyst	MP-47.1 Define MS/MO/OP framework	MS = executive committee; MO = managers and supervisors; OP = operators and technicians.
UFT-28-02 Define RAG criteria R: Performance Analyst	MP-47.2 Define RAG criteria	Green ≥ 90% of target; Amber 70-89%; Red < 70%.
UFT-28-03 Collect performance data by function R: Performance Analyst	MP-47.3 Collect performance data by function	Data collected for 6 functions: 18 KPIs, last 12 months.
UFT-28-04 Assess MS performance R: Performance Analyst	MP-47.4 Assess MS performance	MS: strategy deployment Amber (78%); governance Green (92%).
UFT-28-05 Assess MO performance R: Performance Analyst	MP-47.5 Assess MO performance	MO: Assembly & Production team management Red (64%); planning Amber (81%).
UFT-28-06 Assess OP performance R: Performance Analyst	MP-47.6 Assess OP performance MP-47.7 Apply RAG ratings	OP: IATF 16949 compliance Amber (85%); productivity Green (93%).
UFT-28-07 Publish RAG dashboard R: Performance Analyst	MP-47.8 Visualize performance dashboards MP-47.9 Identify performance gaps MP-47.10 Feed performance into diagnostic report MP-47.11 Track performance progression MP-47.12 Report performance to leadership	Publish RPT-005 MS/MO/OP RAG dashboard to the executive committee.

E2E-29 · Functional SWOT-to-Improvement Axes

Goal: Conduct function-level SWOT and define improvement axes. **Starts when:** Diagnostic phase of a training engineering engagement or annual functional review. **Ends when:** Validated functional SWOT reports with prioritized improvement axes per function.

Task	Steps	What to type
UFT-29-01 Define function scope R: L&D Analyst	MP-48.1 Define function scope	Function in scope: Assembly & Production (3 sites, 96 people).
UFT-29-02 Conduct function SWOT R: L&D Analyst	MP-48.2 Conduct function SWOT	SWOT workshop held with the function head and 6 supervisors.
UFT-29-03 Identify strengths and weaknesses R: L&D Analyst	MP-48.3 Identify strengths MP-48.4 Identify weaknesses	Strength: experienced team. Weakness: low MES and digital shop-floor tracking usage, paper records. AI run: Strength: experienced team. Weakness: low AI visual inspection of welds and paint usage, paper records.

Task	Steps	What to type
UFT-29-04 Identify opportunities and threats R: L&D Analyst	MP-48.5 Identify opportunities MP-48.6 Identify threats	Opportunity: Supplier portal and EDI. Threat: stricter IATF 16949 audits. AI run: Opportunity: Generative AI for 8D problem solving. Threat: stricter IATF 16949 audits.
UFT-29-05 Define improvement axes R: L&D Business Partner	MP-48.7 Define improvement axes	Axis 1: digitalise shift records with MES and digital shop-floor tracking. Axis 2: certify supervisors on IATF 16949. AI run: Axis 1: digitalise shift records with AI visual inspection of welds and paint. Axis 2: certify supervisors on IATF 16949.
UFT-29-06 Validate with function heads R: L&D Business Partner	MP-48.8 Validate axes with function heads	Validated by the function head on 18 April; axis 2 deadline moved to Q3.
UFT-29-07 Prioritize improvement axes R: L&D Strategist	MP-48.9 Prioritize improvement axes MP-48.10 Feed SWOT into diagnostic report MP-48.11 Track improvement implementation MP-48.12 Report on function performance	Priority: axis 1 (impact 5), axis 2 (impact 4).

E2E-02 · Skills-to-Gap Diagnosis

Goal: Produce a validated skills gap diagnosis. **Starts when:** Approved annual L&D plan or a scheduled skills assessment campaign. **Ends when:** Validated skills gap diagnosis released to needs analysis.

Task	Steps	What to type
UFT-02-01 Maintain competency framework R: L&D Analyst	MP-02.1 Define competency families and levels	Family 'MES and digital shop-floor tracking': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert). AI run: Family 'AI visual inspection of welds and paint': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert).
UFT-02-02 Set target levels per position R: HR Business Partner	MP-02.2 Set target levels per position	Assembly & Production supervisor: MES and digital shop-floor tracking = 3; IATF 16949 = 3. Assembly & Production operator: MES and digital shop-floor tracking = 2. AI run: Assembly & Production supervisor: AI visual inspection of welds and paint = 3; IATF 16949 = 3. Assembly & Production operator: AI visual inspection of welds and paint = 2.
UFT-02-03 Launch assessment campaign R: L&D Analyst	MP-02.3 Launch assessment campaign	Campaign 'Skills 2026': population Assembly & Production and Operations (212 people), 12 competencies, close date 30 April.
UFT-02-04 Collect self and manager assessments R: Manager	MP-02.4 Submit self and manager assessments MP-02.5 Consolidate assessment results	Self-assessment MES and digital shop-floor tracking: 2; manager validation: 2 with comment 'needs practice on live cases'. AI run: Self-assessment AI visual inspection of welds and paint: 2; manager validation: 2 with comment 'needs practice on live cases'.
UFT-02-05 Suggest proficiency from evidence R: L&D Analyst	MP-02.6 Suggest proficiency from evidence	Accept 38 suggested levels, edit 4 (evidence too old), reject 1. Every change carries a note.

Task	Steps	What to type
UFT-02-06 Validate skills inventory R: Head of L&D	MP-02.7 Validate skills inventory	Inventory validated: 212 employees, 96% assessments complete. Justification: sample checked by site.
UFT-02-07 Compute and forecast gaps R: L&D Analyst	MP-03.1 Compute gap matrix MP-03.2 Review gap matrix by site and function MP-28.3 Forecast skill gaps MP-28.1 Build analytics dataset	Critical gaps: MES and digital shop-floor tracking (-1.4 average on supervisors), PLM and digital engineering change (-1.1). Forecast: Supplier portal and EDI becomes critical within 12 months. AI run: Critical gaps: AI visual inspection of welds and paint (-1.4 average on supervisors), Predictive maintenance of press lines (-1.1). Forecast: Generative AI for 8D problem solving becomes critical within 12 months.

E2E-21 · Previous Plan Impact-to-Strategy Update

Goal: Evaluate N-1 plan impact and update strategy. **Starts when:** Start of a new plan cycle with N-1 execution data available. **Ends when:** N-1 impact conclusions fed into the strategy update.

Task	Steps	What to type
UFT-21-01 Load N-1 plan execution data R: L&D Analyst	MP-39.1 Load N-1 plan execution data	Load N-1 plan: 28 sessions planned, 23 delivered, 1,410,000 MAD spent.
UFT-21-02 Define impact criteria R: L&D Analyst	MP-39.2 Define impact criteria	Impact criteria: application on the job, KPI change, satisfaction, cost per learner.
UFT-21-03 Survey participants and managers R: L&D Analyst	MP-39.3 Survey participants and managers MP-09.5 Record on-the-job observation (Level 3)	Survey sent to 190 participants and 34 managers; 61% responded.
UFT-21-04 Compare planned against realized R: L&D Analyst	MP-39.4 Compare planned against realized MP-32.3 Isolate training effect	Planned vs realized: 82% of sessions, 94% of budget; 2 themes not delivered.
UFT-21-05 Review N-1 ROI R: Performance Analyst	MP-32.4 Compute Phillips ROI MP-32.5 Review ROI with finance	N-1 ROI: PLM and digital engineering change 18%; safety theme 35%. AI run: N-1 ROI: Predictive maintenance of press lines 18%; safety theme 35%.
UFT-21-06 Draft impact conclusions R: L&D Analyst	MP-39.5 Draft impact study conclusions	Accept AI conclusions 1-3; rewrite conclusion 4 (sample too small).
UFT-21-07 Feed conclusions to strategy R: Head of L&D	MP-39.6 Feed conclusions to strategy update MP-01.1 Record corporate strategic objectives	Feed to strategy: keep blended format; stop long classroom courses on PLM and digital engineering change. AI run: Feed to strategy: keep blended format; stop long classroom courses on Predictive maintenance of press lines.
UFT-21-08 Update roadmap priorities R: L&D Strategist	MP-04.6 Sequence roadmap initiatives	Roadmap priority updated: MES and digital shop-floor tracking moved to Q2; PLM and digital engineering change to microlearning. AI run: Roadmap priority updated: AI visual inspection of welds and paint moved to Q2; Predictive maintenance of press lines to microlearning.

6.4 Training Engineering Report & plan — gate G3

E2E-01 · Strategy-to-Learning Plan

Goal: Translate corporate strategy into an approved annual L&D plan and budget. **Starts when:** Annual strategy cycle opened or revised corporate objectives published by the board. **Ends when:** Annual L&D plan and budget envelope approved by the Steering Committee and locked.

Task	Steps	What to type
UFT-01-01 Record strategic objectives R: Head of L&D	MP-01.1 Record corporate strategic objectives	SO-1: MES and digital shop-floor tracking used by 80% of Assembly & Production staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on IATF 16949. AI run: SO-1: AI visual inspection of welds and paint used by 80% of Assembly & Production staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on IATF 16949.
UFT-01-02 Link objectives to functions and sites R: L&D Strategist	MP-01.2 Link objectives to functions and sites	SO-1 → Assembly & Production, Operations, Information Systems (all sites). SO-2 → Quality & HSE, Assembly & Production.
UFT-01-03 Frame skills priorities R: L&D Analyst	MP-02.1 Define competency families and levels MP-02.2 Set target levels per position	Priority competency families: MES and digital shop-floor tracking; PLM and digital engineering change; IATF 16949 compliance. Target level 3 (Autonomous) for supervisors. AI run: Priority competency families: AI visual inspection of welds and paint; Predictive maintenance of press lines; IATF 16949 compliance. Target level 3 (Autonomous) for supervisors.
UFT-01-04 Pre-scope training needs R: L&D Analyst	MP-03.1 Compute gap matrix MP-03.2 Review gap matrix by site and function	Pre-scoped needs: 42% of Assembly & Production supervisors below target on MES and digital shop-floor tracking; 18 employees below target on IATF 16949. AI run: Pre-scoped needs: 42% of Assembly & Production supervisors below target on AI visual inspection of welds and paint; 18 employees below target on IATF 16949.
UFT-01-05 Define budget envelope R: Finance Manager	MP-01.3 Define L&D budget envelope MP-18.1 Allocate budget by theme and site MP-18.2 Forecast OFPPT refunds	Gross L&D budget 2026: 1,850,000 MAD; forecast refund (OFPPT/CSF): 520,000 MAD; net envelope: 1,330,000 MAD.
UFT-01-06 Plan change and adoption R: Change Manager	MP-19.1 Assess change impact MP-19.2 Build adoption plan	Change impact: high for Assembly & Production supervisors (new MES and digital shop-floor tracking routines). Sponsors: Operations Director. Champions: one per site. AI run: Change impact: high for Assembly & Production supervisors (new AI visual inspection of welds and paint routines). Sponsors: Operations Director. Champions: one per site.
UFT-01-07 Compile plan approval pack R: Head of L&D	MP-01.4 Schedule Steering Committee milestones MP-01.5 Compile plan approval pack MP-04.1 Consolidate feeder outputs	Approval pack: 2 objectives, net budget 1,330,000 MAD, 6 priority themes, committee date 15 March 2026.
UFT-01-08 Approve and lock annual L&D plan R: HR Director	MP-01.6 Record Steering Committee decision MP-01.7 Lock and distribute approved plan	Decision: Approve. Justification: aligned with SO-1 and SO-2; budget within envelope. Plan locked as version 1.

E2E-03 · Needs-to-Training Engineering Report & Roadmap

Goal: Produce the Training Engineering Report and the prioritized training roadmap. **Starts when:** Validated skills gap diagnosis, consolidated demands, approved Scope of Work or diagnostic findings available. **Ends when:** Training Engineering Report and prioritized roadmap approved and published.

Task	Steps	What to type
UFT-03-01 Plan diagnostic interviews R: L&D Analyst	MP-03.3 Plan diagnostic interviews	Interview plan: 14 semi-structured interviews (4 MS, 6 MO, 4 OP), 45 minutes each, weeks 10-11.
UFT-03-02 Record interview findings R: L&D Analyst	MP-03.4 Record interview findings	Finding (MO, Assembly & Production): 'Supervisors do not trust MES and digital shop-floor tracking data; they re-enter figures on paper.' AI run: Finding (MO, Assembly & Production): 'Supervisors do not trust AI visual inspection of welds and paint data; they re-enter figures on paper.'
UFT-03-03 Cluster needs into themes R: L&D Analyst	MP-03.5 Cluster needs into training themes	Accept theme 'MES and digital shop-floor tracking for supervisors'; merge two duplicate themes on PLM and digital engineering change; split 'IATF 16949' into awareness and auditor tracks. AI run: Accept theme 'AI visual inspection of welds and paint for supervisors'; merge two duplicate themes on Predictive maintenance of press lines; split 'IATF 16949' into awareness and auditor tracks.
UFT-03-04 Prioritize needs by impact R: L&D Strategist	MP-03.6 Prioritize needs by business impact	MES and digital shop-floor tracking: impact 5, urgency 4. PLM and digital engineering change: impact 4, urgency 3. IATF 16949: impact 4, urgency 5. AI run: AI visual inspection of welds and paint: impact 5, urgency 4. Predictive maintenance of press lines: impact 4, urgency 3. IATF 16949: impact 4, urgency 5.
UFT-03-05 Validate needs register R: Head of L&D	MP-03.7 Validate needs register	Needs register validated: 23 needs, 6 themes. Justification: covers SO-1 and SO-2; sponsor reviewed.
UFT-03-06 Consolidate engineering inputs R: L&D Analyst	MP-04.1 Consolidate feeder outputs MP-04.2 Check input completeness	Inputs complete: Scope of Work, 187 responses, gap matrix, RAG dashboard, SWOT, demands. Missing: none.
UFT-03-07 Draft Training Engineering Report R: L&D Strategist	MP-04.3 Generate report draft MP-04.4 Edit and complete report sections	Section 3 'Diagnostic': edit the AI draft, add the interview quote on MES and digital shop-floor tracking, keep the RAG table. AI run: Section 3 'Diagnostic': edit the AI draft, add the interview quote on AI visual inspection of welds and paint, keep the RAG table.
UFT-03-08 Run quality review R: Quality Manager	MP-04.5 Run quality review of report MP-20.5 Run periodic quality review	Quality review: 11/12 checklist items met; fix item 'sources cited for every figure'. Result: pass after correction.
UFT-03-09 Sequence and budget roadmap R: L&D Strategist	MP-04.6 Sequence roadmap initiatives MP-18.1 Allocate budget by theme and site	Roadmap: Q2 MES and digital shop-floor tracking (6 groups); Q3 IATF 16949 (4 groups); Q4 PLM and digital engineering change (3 groups). Total 1,240,000 MAD. AI run: Roadmap: Q2 AI visual inspection of welds and paint (6 groups); Q3 IATF 16949 (4 groups); Q4 Predictive maintenance of press lines (3 groups). Total 1,240,000 MAD.

Task	Steps	What to type
UFT-03-10 Approve and publish report and roadmap R: Head of L&D	MP-04.7 Submit roadmap for approval MP-04.8 Record roadmap approval MP-04.9 Publish approved report and roadmap MP-01.6 Record Steering Committee decision	Decision: Approve report and roadmap v1. Justification: within budget, linked to SO-1/SO-2. Publish to all stakeholders.

E2E-30 · Prioritization-to-Resource Plan

Goal: Prioritize themes and plan days, groups, trainers, budget. **Starts when:** Consolidated training themes requiring prioritization and resource planning. **Ends when:** Approved prioritized training plan with days per theme, group planning, trainer allocation, and budget.

Task	Steps	What to type
UFT-30-01 Consolidate training themes R: L&D Analyst	MP-49.1 Consolidate training themes	Consolidated list: 9 themes from needs, demands, GPEC and SWOT.
UFT-30-02 Define prioritization criteria R: L&D Strategist	MP-49.2 Define prioritization criteria	Criteria: strategic impact 40%, urgency 30%, number of learners 20%, cost 10%.
UFT-30-03 Prioritize themes R: L&D Strategist	MP-49.3 Prioritize themes	Rank 1 MES and digital shop-floor tracking (score 86); rank 2 IATF 16949 (81); rank 3 PLM and digital engineering change (74). AI run: Rank 1 AI visual inspection of welds and paint (score 86); rank 2 IATF 16949 (81); rank 3 Predictive maintenance of press lines (74).
UFT-30-04 Estimate days per theme R: L&D Planner	MP-49.4 Estimate days per theme	MES and digital shop-floor tracking: 3 days per group; IATF 16949: 2 days; PLM and digital engineering change: 1.5 days. AI run: AI visual inspection of welds and paint: 3 days per group; IATF 16949: 2 days; Predictive maintenance of press lines: 1.5 days.
UFT-30-05 Define groups per theme R: L&D Planner	MP-49.5 Define number of groups per theme MP-49.6 Allocate trainers	MES and digital shop-floor tracking: 6 groups of 12; IATF 16949: 4 groups; PLM and digital engineering change: 3 groups. AI run: AI visual inspection of welds and paint: 6 groups of 12; IATF 16949: 4 groups; Predictive maintenance of press lines: 3 groups.
UFT-30-06 Allocate trainers and budget R: Finance Manager	MP-49.7 Estimate plan budget MP-49.8 Sequence delivery MP-49.9 Validate plan with governance	Trainers: 2 internal, vendor A; budget 1,240,000 MAD (within envelope).
UFT-30-07 Publish prioritized training plan R: L&D Leader	MP-49.10 Publish prioritized plan MP-49.11 Track plan execution MP-49.12 Report on resource utilization	Publish RPT-002 Prioritized Training Plan 2026 to all stakeholders.

E2E-22 · Multi-Site Plan-to-Deployment

Goal: Adapt and deploy plans across sites. **Starts when:** Approved roadmap for an organization with several sites or entities. **Ends when:** Site plans adapted, validated and deployed, with deviations escalated.

Task	Steps	What to type
UFT-22-01 Split plan by site R: Head of L&D	MP-40.1 Split plan by site	Split plan into 3 sites: Casablanca 55%, Tanger 30%, Agadir 15%.
UFT-22-02 Adapt site plan to local constraints R: Site L&D Coordinator	MP-40.2 Adapt site plan to local constraints	Tanger: shift constraints → sessions of 4 hours instead of full days.
UFT-22-03 Localize site materials R: Instructional Designer	MP-23.1 Request translation MP-23.3 Validate translation MP-23.6 Review participation equity MP-23.7 Record inclusion actions	Agadir materials translated to AR; validated by the site expert.
UFT-22-04 Validate site plan R: Head of L&D	MP-40.3 Validate site plan	Site plans validated centrally; budget deviation within ±5%.
UFT-22-05 Schedule site sessions R: Training Administrator	MP-07.1 Create training session MP-11.1 Book rooms and equipment	Tanger schedule: 8 sessions, rooms booked, 2 trainers.
UFT-22-06 Deploy site schedule R: Site L&D Coordinator	MP-40.4 Deploy site schedule	Schedules deployed and communicated to site managers.
UFT-22-07 Consolidate site status R: Head of L&D	MP-40.5 Consolidate site status	Status: Casablanca 70%, Tanger 45%, Agadir 20% delivered.
UFT-22-08 Escalate site deviation R: Head of L&D	MP-40.6 Escalate site deviation	Escalate Agadir deviation (-25%) to the HR Director with a recovery plan.

E2E-23 · Regulatory Submission-to-Validation

Goal: Submit and validate training plans with regulatory bodies. **Starts when:** Approved plan requiring external validation or funding (e.g. OFPPT, GIAC-Agro). **Ends when:** Plan validated by the regulatory body and evidence archived.

Task	Steps	What to type
UFT-23-01 Select regulatory template R: Compliance Officer	MP-41.1 Select regulatory template	Template: OFPPT special training contracts (CSF) — plan file.
UFT-23-02 Generate submission file R: Compliance Officer	MP-41.2 Generate submission file MP-20.5 Run periodic quality review	Submission file generated: plan, themes, providers, costs; quality check passed.
UFT-23-03 Submit plan to regulatory body R: Compliance Officer	MP-41.3 Submit plan to regulatory body	Submitted to the regional funding committee on 5 March; reference GSF-2026-118.
UFT-23-04 Track submission status R: Compliance Officer	MP-41.4 Track submission status	Status: additional document requested (provider accreditation) — sent on 12 March.
UFT-23-05 Record regulator decision R: Compliance Officer	MP-41.5 Record regulator decision MP-14.1 Register regulatory requirement	Decision: approved with a cap of 520,000 MAD.

Task	Steps	What to type
UFT-23-06 Submit refund claims R: Finance Manager	MP-18.5 Submit refund claims	Refund claims submitted for 12 delivered actions: 318,000 MAD.
UFT-23-07 Archive submission evidence R: Compliance Officer	MP-41.6 Archive submission evidence MP-18.6 Close budget period	Archive file, decision and claims; retention 10 years.

E2E-16 · Vendor-to-Finance

Goal: Manage vendors from selection to payment. **Starts when:** Training need requiring an external provider. **Ends when:** Vendor selected, order issued and payment approved against attendance.

Task	Steps	What to type
UFT-16-01 Issue request for proposal R: Purchasing Officer	MP-15.1 Issue request for proposal	RFP 'Training on MES and digital shop-floor tracking' sent to 4 vendors, answers due 15 May. AI run: RFP 'Training on AI visual inspection of welds and paint' sent to 4 vendors, answers due 15 May.
UFT-16-02 Score vendor proposals R: Purchasing Officer	MP-15.2 Score vendor proposals	Scores: vendor A 82, vendor B 76, vendor C 64 (price 40%, expertise 40%, references 20%).
UFT-16-03 Register and verify vendor R: Purchasing Officer	MP-15.3 Register vendor record MP-15.4 Verify vendor accreditation	Register vendor A; accreditation OFPPT verified, valid until December.
UFT-16-04 Issue purchase order R: Purchasing Officer	MP-15.5 Issue purchase order MP-18.3 Record committed and actual costs	Purchase order PO-2026-044: 180,000 MAD on budget line 'MES and digital shop-floor tracking'. AI run: Purchase order PO-2026-044: 180,000 MAD on budget line 'AI visual inspection of welds and paint'.
UFT-16-05 Match invoice to order and attendance R: Training Administrator	MP-15.6 Match invoice to order and attendance MP-11.5 Reconcile attendance with invoices	Invoice matched with PO and attendance (3 days × 12 learners): OK.
UFT-16-06 Approve vendor payment R: Finance Manager	MP-15.7 Approve vendor payment MP-18.4 Compare spend against budget	Approve payment 180,000 MAD; vendor performance rating 4/5.

AUTO-E2E-02 · Automotive Critical-Skills-to-Transformation Plan

Goal: Turn critical-skill gaps and digital and AI use cases into a transformation plan.. **Starts when:** Annual plan cycle or technology change in Automotive. **Ends when:** Transformation learning paths approved.

Task	Steps	What to type
UFT-AUTO-E2-01 List critical Assembly & Production skills R: L&D Analyst	MP-02.1 Define competency families and levels MP-03.1 Compute gap matrix	Critical skills: 6 for Assembly & Production, each with target level 3.
UFT-AUTO-E2-02 List digital and AI use cases R: L&D Strategist	MP-03.3 Plan diagnostic interviews	Use cases: MES and digital shop-floor tracking; PLM and digital engineering change; Supplier portal and EDI. AI run: Use cases: AI visual inspection of welds and paint; Predictive maintenance of press lines; Generative AI for 8D problem solving.

Task	Steps	What to type
UFT-AUTO-E2-03 Forecast impacted roles R: Performance Analyst	MP-03.5 Cluster needs into training themes MP-28.3 Forecast skill gaps	Impacted roles: supervisors (high), operators (medium); accept the AI forecast.
UFT-AUTO-E2-04 Approve transformation paths R: Instructional Designer	MP-05.2 Define learning path and modules MP-05.7 Approve design document	Approve 2 transformation paths: 'MES and digital shop-floor tracking for supervisors', 'PLM and digital engineering change for operators'. AI run: Approve 2 transformation paths: 'AI visual inspection of welds and paint for supervisors', 'Predictive maintenance of press lines for operators'.

6.5 Design & delivery — gate G4

E2E-04 · Roadmap-to-Curriculum Design

Goal: Convert roadmap into curriculum maps, learning paths, design documents. **Starts when:** Approved Training Engineering Report and roadmap published. **Ends when:** Approved curriculum maps, learning paths and design documents.

Task	Steps	What to type
UFT-04-01 Create curriculum map R: Instructional Designer	MP-05.1 Create curriculum map from roadmap	Curriculum map 'MES and digital shop-floor tracking': 3 learning paths (operators, supervisors, managers), 9 modules. AI run: Curriculum map 'AI visual inspection of welds and paint': 3 learning paths (operators, supervisors, managers), 9 modules.
UFT-04-02 Define learning paths and modules R: Instructional Designer	MP-05.2 Define learning path and modules	Path 'Supervisors — MES and digital shop-floor tracking': 4 modules, 3 days blended (1 day e-learning, 2 days workshop). AI run: Path 'Supervisors — AI visual inspection of welds and paint': 4 modules, 3 days blended (1 day e-learning, 2 days workshop).
UFT-04-03 Write learning objectives R: Instructional Designer	MP-05.3 Write learning objectives per module	Objective M1: 'By the end, the supervisor reads the MES and digital shop-floor tracking dashboard and decides the shift action in 5 minutes.' AI run: Objective M1: 'By the end, the supervisor reads the AI visual inspection of welds and paint dashboard and decides the shift action in 5 minutes.'
UFT-04-04 Propose module structure R: Instructional Designer	MP-05.4 Propose module structure	Accept the proposed structure (intro, demo, practice, quiz); replace the quiz by a live case from Assembly & Production.
UFT-04-05 Set assessment strategy R: Instructional Designer	MP-05.5 Set assessment strategy	Assessment: pre/post test (Level 2) and manager observation after 30 days (Level 3).
UFT-04-06 Develop and tag content R: Content Developer	MP-06.1 Upload content assets MP-06.2 Validate package format MP-06.5 Tag content with competencies	Upload 'M1_MES and digital shop-floor tracking.pptx' and 'M1_video.mp4'; tag competency 'MES and digital shop-floor tracking' level 3. AI run: Upload 'M1_AI visual inspection of welds and paint.pptx' and 'M1_video.mp4'; tag competency 'AI visual inspection of welds and paint' level 3.
UFT-04-07 Localize and check accessibility R: Instructional Designer	MP-23.1 Request translation MP-23.2 Draft machine translation MP-23.3 Validate translation MP-23.4 Run accessibility check MP-23.5 Fix accessibility issues	Request FR and AR versions; validate the AI draft translation; accessibility check: 0 blocking issues.

Task	Steps	What to type
UFT-04-08 Approve design document R: Head of L&D	MP-05.6 Review design with subject matter expert MP-05.7 Approve design document	Decision: design approved. Comment: SME review done on 12 May; ready for delivery.

E2E-05 · Design-to-Delivery

Goal: Deliver training across all modalities. **Starts when:** Approved design document and prioritized training plan.

Ends when: Training delivered across all modalities with attendance and completion recorded.

Task	Steps	What to type
UFT-05-01 Publish content to catalog R: Content Developer	MP-06.3 Route content for expert review MP-06.4 Record review decision MP-06.6 Publish content to catalog	Publish module 'M1 MES and digital shop-floor tracking' to the catalog; audience: supervisors; languages EN/FR/AR. AI run: Publish module 'M1 AI visual inspection of welds and paint' to the catalog; audience: supervisors; languages EN/FR/AR.
UFT-05-02 Book logistics R: Training Administrator	MP-11.1 Book rooms and equipment MP-11.2 Manage trainer calendars	Room 'Training A' (20 seats) 3-5 June; projector; trainer calendar blocked.
UFT-05-03 Schedule sessions R: Training Administrator	MP-07.1 Create training session MP-07.2 Check scheduling conflicts	Session S-01 'MES and digital shop-floor tracking — supervisors', 3-5 June, 12 seats, no conflict reported. AI run: Session S-01 'AI visual inspection of welds and paint — supervisors', 3-5 June, 12 seats, no conflict reported.
UFT-05-04 Enroll learners and send convocations R: Training Administrator	MP-07.3 Enroll learners into session MP-07.4 Send convocations MP-17.1 Provision users via SSO	Enroll 12 supervisors; convocations sent by e-mail and SMS in each learner's language.
UFT-05-05 Push microlearning capsules R: Instructional Designer	MP-25.1 Author microlearning capsule MP-25.2 Generate capsule draft from source MP-25.3 Push capsule to collaboration channel MP-25.4 Consume capsule on mobile MP-25.5 Track capsule completion	Capsule '5-minute PLM and digital engineering change check' pushed to the Teams channel of Assembly & Production; 48 views in week 1. AI run: Capsule '5-minute Predictive maintenance of press lines check' pushed to the Teams channel of Assembly & Production; 48 views in week 1.
UFT-05-06 Run immersive simulations R: Trainer	MP-30.1 Define simulation scenario MP-30.2 Configure simulation scoring MP-30.3 Launch simulation session MP-30.4 Capture simulation performance MP-30.5 Debrief learner MP-30.6 Record simulation evidence	Simulation 'Assembly & Production incident': score 78/100; debrief notes recorded; evidence saved.
UFT-05-07 Record attendance R: Trainer	MP-07.5 Record attendance	Attendance S-01: 11 present, 1 absent (justified). Signature sheet attached.
UFT-05-08 Close sessions R: Training Administrator	MP-07.6 Close session and record completion	Close S-01: 11 completions recorded; certificate issued to each participant.
UFT-05-09 Reconcile and archive period R: Training Administrator	MP-11.5 Reconcile attendance with invoices MP-11.6 Archive period records MP-11.3 Import external training records MP-11.4 Correct training record with justification	Reconcile invoice INV-2026-118 (3 days × 12 learners) with attendance; archive period Q2.

E2E-06 · Learner-Journey-to-Engagement

Goal: Deliver personalized, engaging learning experience. **Starts when:** Learner enrolled in a learning path or session. **Ends when:** Personalized learning journey completed with engagement measured.

Task	Steps	What to type
UFT-06-01 Generate personal learning plan R: L&D Analyst	MP-08.1 Generate personal learning plan	Personal plan generated for each learner: 3 items on MES and digital shop-floor tracking, 1 capsule on PLM and digital engineering change. AI run: Personal plan generated for each learner: 3 items on AI visual inspection of welds and paint, 1 capsule on Predictive maintenance of press lines.
UFT-06-02 Recommend learning items R: Learner	MP-08.2 Recommend learning items MP-24.1 Enable personalization per scope	Accept 2 recommendations, reject 1 ('already mastered'). The outcome is logged.
UFT-06-03 Adapt path to performance R: Instructional Designer	MP-24.2 Set adaptation rules MP-24.3 Adapt path to learner performance MP-24.4 Record learner response to adaptation	Rule: if the quiz score < 60%, add the remedial capsule 'MES and digital shop-floor tracking basics'. AI run: Rule: if the quiz score < 60%, add the remedial capsule 'AI visual inspection of welds and paint basics'.
UFT-06-04 Animate social learning R: Knowledge Manager	MP-26.1 Create learning cohort group MP-26.2 Invite group members MP-26.3 Post question or answer MP-26.4 Endorse expert answer MP-26.5 Flag inappropriate content MP-26.6 Resolve moderation flag	Create cohort 'MES and digital shop-floor tracking supervisors 2026' and invite 12 members; first question posted. AI run: Create cohort 'AI visual inspection of welds and paint supervisors 2026' and invite 12 members; first question posted.
UFT-06-05 Run gamification R: Instructional Designer	MP-27.1 Define points and badge rules MP-27.2 Configure leaderboard scope MP-27.3 Award points on completion MP-27.4 Unlock badge MP-27.6 Adjust gamification rules	Badge 'MES and digital shop-floor tracking Practitioner' for completing 3 modules; 10 points per capsule. AI run: Badge 'AI visual inspection of welds and paint Practitioner' for completing 3 modules; 10 points per capsule.
UFT-06-06 Match and run coaching R: L&D Business Partner	MP-21.1 Request coaching MP-21.2 Match coach to learner MP-21.3 Schedule coaching sessions MP-21.4 Log coaching session notes MP-21.5 Evaluate coaching outcomes MP-21.6 Close coaching engagement	Match coach 'Senior Assembly & Production supervisor' to 3 learners; 4 sessions of 1 hour.
UFT-06-07 Collect learner feedback R: Learner	MP-08.3 Enroll in recommended item MP-08.4 Submit learning feedback	Feedback: 4.4/5; comment 'more real cases from Assembly & Production'.
UFT-06-08 Monitor engagement and nudge R: L&D Analyst	MP-08.5 Monitor engagement indicators MP-08.6 Trigger re-engagement nudge MP-24.5 Review recommendation acceptance MP-27.5 Review engagement uplift MP-24.6 Tune personalization settings MP-28.4 Predict learner drop-out risk MP-28.5 Review predictions with L&D MP-28.6 Create preventive action	Engagement 81%; nudge sent to 9 inactive learners; drop-out risk high for 2 learners.

E2E-13 · Content-Curate-to-Retire

Goal: Publish, maintain, retire content. **Starts when:** New content published or content past its review date. **Ends when:** Catalog curated, maintained and outdated content retired.

Task	Steps	What to type
UFT-13-01 Aggregate provider catalogs R: Content Curator	MP-29.1 Aggregate provider catalogs	Aggregate 2 provider catalogs (LinkedIn Learning, Coursera): 1,240 items imported.
UFT-13-02 Recommend curated items R: Content Curator	MP-29.2 Recommend curated items	Keep the 15 top-ranked items on MES and digital shop-floor tracking; reject 3 items older than 3 years. AI run: Keep the 15 top-ranked items on AI visual inspection of welds and paint; reject 3 items older than 3 years.
UFT-13-03 Approve and organize collections R: Content Curator	MP-29.3 Approve curated item MP-29.4 Organize curated collection	Collection 'MES and digital shop-floor tracking starter kit': 8 items, audience supervisors, review date in 12 months. AI run: Collection 'AI visual inspection of welds and paint starter kit': 8 items, audience supervisors, review date in 12 months.
UFT-13-04 Review peer content R: Subject Matter Expert	MP-33.1 Submit user-generated content MP-33.2 Check content against policy MP-33.3 Peer review content	Peer video 'How we use PLM and digital engineering change on shift' reviewed by an expert: approved with 1 correction. AI run: Peer video 'How we use Predictive maintenance of press lines on shift' reviewed by an expert: approved with 1 correction.
UFT-13-05 Promote and rate content R: Knowledge Manager	MP-33.5 Send approved content to curation MP-33.6 Rate user-generated item	Send approved peer content to curation; average learner rating 4.5/5.
UFT-13-06 Flag content past review date R: Content Curator	MP-29.5 Flag content past review date	14 items past review date flagged; owners notified.
UFT-13-07 Retire outdated content R: Content Curator	MP-29.6 Retire outdated content MP-25.6 Retire low-value capsule	Retire 6 outdated items and 2 low-value capsules; library health 92%.

E2E-14 · Extended-Enterprise-Training

Goal: Certify partners and train customers. **Starts when:** Partner, reseller or customer training program launched.

Ends when: External learners trained, paid and certified.

Task	Steps	What to type
UFT-14-01 Create external sub-portal R: Extended Enterprise Manager	MP-22.1 Create external sub-portal	Sub-portal 'Partners Academy — Atlas Motors Kénitra' created for distributors and installers.
UFT-14-02 Configure catalog and pricing R: Extended Enterprise Manager	MP-22.2 Configure external catalog and pricing MP-18.1 Allocate budget by theme and site	Catalog: 'IATF 16949 for partners' 1,200 MAD; 'MES and digital shop-floor tracking certification' 2,400 MAD. AI run: Catalog: 'IATF 16949 for partners' 1,200 MAD; 'AI visual inspection of welds and paint certification' 2,400 MAD.
UFT-14-03 Process payment and enroll R: Extended Enterprise Manager	MP-22.3 Process online payment MP-22.4 Enroll external learner	18 online payments processed; 18 external learners enrolled.
UFT-14-04 Deliver external sessions R: Training Administrator	MP-07.1 Create training session MP-07.5 Record attendance	Session P-01 (virtual), 18 invited, 16 present.

Task	Steps	What to type
UFT-14-05 Track external completion R: Extended Enterprise Manager	MP-22.5 Track external completion	Completion: 15 of 16 passed the final quiz.
UFT-14-06 Issue partner certification R: Extended Enterprise Manager	MP-22.6 Issue partner certification MP-14.4 Issue certificate on completion	Issue 15 partner certificates valid 2 years.
UFT-14-07 Reconcile external revenue R: Finance Manager	MP-18.3 Record committed and actual costs MP-18.4 Compare spend against budget	Revenue 43,200 MAD reconciled with the ERP; 0 unpaid.

6.6 Evaluation, compliance & impact — gate G5

E2E-07 · Assessment-to-Evaluation

Goal: Measure training effectiveness and skill progression. **Starts when:** Training session or path completed. **Ends when:** Effectiveness measured on Kirkpatrick levels 1-3 and skill progression computed.

Task	Steps	What to type
UFT-07-01 Create assessment instrument R: Instructional Designer	MP-09.1 Create assessment instrument	Instrument 'Test MES and digital shop-floor tracking M1': 15 questions, pass mark 70%. AI run: Instrument 'Test AI visual inspection of welds and paint M1': 15 questions, pass mark 70%.
UFT-07-02 Draft question bank R: Instructional Designer	MP-09.2 Generate question bank draft	Keep 12 AI-drafted questions, rewrite 3 with Assembly & Production vocabulary; validate each one.
UFT-07-03 Collect reaction survey (Level 1) R: L&D Analyst	MP-09.3 Collect reaction survey (Level 1)	Reaction survey S-01: 11 responses, satisfaction 4.3/5.
UFT-07-04 Record learning results (Level 2) R: Trainer	MP-09.4 Record learning results (Level 2)	Level 2: average pre-test 48%, post-test 81% (+33 points).
UFT-07-05 Record on-the-job observation (Level 3) R: Manager	MP-09.5 Record on-the-job observation (Level 3)	Level 3 (day 30): 9 of 11 supervisors apply the MES and digital shop-floor tracking routine daily. AI run: Level 3 (day 30): 9 of 11 supervisors apply the AI visual inspection of welds and paint routine daily.
UFT-07-06 Compute skill progression R: L&D Analyst	MP-09.6 Compute skill progression MP-10.3 Refresh KPI computation	Skill progression: MES and digital shop-floor tracking from 1.8 to 2.7 (target 3). AI run: Skill progression: AI visual inspection of welds and paint from 1.8 to 2.7 (target 3).
UFT-07-07 Review evaluation results R: L&D Analyst	MP-09.7 Review evaluation results MP-20.5 Run periodic quality review	Review: module M3 below 70% pass rate → improvement action assigned to the designer.
UFT-07-08 Publish evaluation report R: L&D Analyst	MP-10.4 Export report MP-10.6 Share insight with stakeholders MP-10.2 Configure dashboard widgets	Export RPT-016 Kirkpatrick report (PDF) and share with the Steering Committee.

E2E-08 · Learning-to-ROI

Goal: Validate ROI and business impact. **Starts when:** Evaluation results available for a theme selected for an ROI study. **Ends when:** Phillips ROI validated with finance and business impact report published.

Task	Steps	What to type
UFT-08-01 Select theme for ROI study R: Performance Analyst	MP-32.1 Select theme for ROI study	ROI study on theme 'MES and digital shop-floor tracking' — population: 36 supervisors, 3 sites. AI run: ROI study on theme 'AI visual inspection of welds and paint' — population: 36 supervisors, 3 sites.
UFT-08-02 Define business indicators R: Performance Analyst	MP-32.2 Define business indicators MP-10.1 Define KPI set per audience	Indicators: rework rate, downtime minutes per shift, data re-entry hours.
UFT-08-03 Collect cost data R: Finance Manager	MP-18.3 Record committed and actual costs MP-18.4 Compare spend against budget	Costs: design 60,000 MAD; delivery 180,000 MAD; participants' time 95,000 MAD.
UFT-08-04 Isolate training effect R: Performance Analyst	MP-32.3 Isolate training effect MP-09.6 Compute skill progression	Control group: site B (not trained). Isolated benefit: 410,000 MAD per year.
UFT-08-05 Compute Phillips ROI R: Performance Analyst	MP-32.4 Compute Phillips ROI	$ROI = (410,000 - 335,000) / 335,000 = 22\%$; benefit-cost ratio 1.22.
UFT-08-06 Review ROI with finance R: Finance Manager	MP-32.5 Review ROI with finance	Finance review: assumptions accepted; downtime valued at 180 MAD per minute.
UFT-08-07 Publish business impact report R: Head of L&D	MP-32.6 Publish business impact report MP-10.4 Export report MP-10.5 Query data via AI Assistant	Publish RPT-012 ROI & Business Impact Report to executive leadership.

E2E-09 · Compliance-to-Certification

Goal: Ensure compliant workforce with valid certifications. **Starts when:** New regulatory requirement or certification nearing expiry. **Ends when:** Compliant workforce with valid certifications and an audit extract available.

Task	Steps	What to type
UFT-09-01 Register regulatory requirement R: Compliance Officer	MP-14.1 Register regulatory requirement	Requirement 'IATF 16949 awareness', every 24 months, source: IATF 16949 clause on competence.
UFT-09-02 Assign mandatory training R: Compliance Officer	MP-14.2 Assign mandatory training by position	Assign to positions: Assembly & Production operator, Assembly & Production supervisor, quality inspector.
UFT-09-03 Deliver mandatory sessions R: Training Administrator	MP-07.3 Enroll learners into session MP-07.5 Record attendance	Enroll 24 employees in session 'IATF 16949 awareness'; attendance recorded.
UFT-09-04 Assess and certify R: Trainer	MP-09.4 Record learning results (Level 2) MP-14.4 Issue certificate on completion	Result 86%; certificate 'IATF 16949 awareness' issued, valid until 2026+2.

Task	Steps	What to type
UFT-09-05 Compute certification validity R: Compliance Officer	MP-14.3 Compute certification validity	Validity: 212 valid, 9 expire within 60 days, 3 expired.
UFT-09-06 Manage renewals R: Compliance Officer	MP-14.5 Launch renewal enrollment MP-14.6 Confirm renewal completion	Launch renewal for the 12 employees; confirm 10 completions, 2 rescheduled.
UFT-09-07 Produce compliance audit extract R: Compliance Officer	MP-14.7 Produce compliance audit extract MP-10.4 Export report	Export compliance audit extract for IATF 16949 (XLSX) for the external auditor.

AUTO-E2E-01 · Automotive Compliance-to-Certification Readiness

Goal: Keep Automotive regulated roles certified against IATF 16949.. **Starts when:** New IATF 16949 requirement or certification expiry. **Ends when:** Sector compliance extract issued with every critical role certified.

Task	Steps	What to type
UFT-AUTO-E1-01 Register IATF 16949 obligations R: Compliance Officer	MP-01.1 Record corporate strategic objectives MP-14.1 Register regulatory requirement	Obligation 'IATF 16949 training', every 12 months, owner Compliance Officer.
UFT-AUTO-E1-02 Link obligations to positions R: HR Business Partner	MP-01.2 Link objectives to functions and sites MP-14.2 Assign mandatory training by position	Linked to 5 Assembly & Production positions (38 employees).
UFT-AUTO-E1-03 Track certification validity R: Compliance Officer	MP-02.1 Define competency families and levels MP-14.3 Compute certification validity	Validity: 33 valid, 5 expire within 60 days.
UFT-AUTO-E1-04 Issue sector compliance extract R: Compliance Officer	MP-02.2 Set target levels per position MP-14.7 Produce compliance audit extract	Extract issued for the IATF 16949 audit on 15 October.

6.7 Talent, knowledge & continuous improvement — gate G6

E2E-10 · Talent-to-Mobility

Goal: Enable internal mobility and career progression. **Starts when:** Internal opening published or annual career review. **Ends when:** Internal move decided with a reskilling plan assigned.

Task	Steps	What to type
UFT-10-01 Model career paths R: HR Director	MP-13.1 Model career path MP-13.2 Link path steps to competency targets	Career path: Assembly & Production operator → team leader → supervisor, with competency targets per step.
UFT-10-02 Publish internal opening R: HR Business Partner	MP-31.1 Publish internal opening MP-31.2 Define required skills	Opening 'Assembly & Production team leader', required skills: MES and digital shop-floor tracking level 3, leadership level 2. AI run: Opening 'Assembly & Production team leader', required skills: AI visual inspection of welds and paint level 3, leadership level 2.

Task	Steps	What to type
UFT-10-03 Match employees to opening R: HR Business Partner	MP-31.3 Match employees to opening MP-02.7 Validate skills inventory	Review 6 AI matches; keep 4 candidates with match score above 75%.
UFT-10-04 Apply to internal opening R: Employee	MP-31.4 Apply to internal opening	Application with motivation note and consent of the current manager.
UFT-10-05 Shortlist candidates R: Hiring Manager	MP-31.5 Shortlist candidates	Shortlist: 2 candidates; interviews on 20 and 21 June.
UFT-10-06 Plan individual development R: Manager	MP-13.3 Create individual development plan MP-13.4 Suggest development actions MP-42.3 Build leadership development plan MP-42.4 Suggest leadership development actions	Development plan: 2 modules MES and digital shop-floor tracking, 1 leadership workshop, 3 months mentoring. AI run: Development plan: 2 modules AI visual inspection of welds and paint, 1 leadership workshop, 3 months mentoring.
UFT-10-07 Assign reskilling plan R: HR Business Partner	MP-31.6 Assign reskilling plan MP-08.1 Generate personal learning plan	Assign reskilling path 'MES and digital shop-floor tracking for team leaders' to the selected candidate. AI run: Assign reskilling path 'AI visual inspection of welds and paint for team leaders' to the selected candidate.
UFT-10-08 Review career and succession R: HR Director	MP-13.5 Run career review MP-13.6 Update succession readiness MP-42.5 Review leadership pipeline MP-42.6 Reassess leadership maturity	Succession readiness updated: 2 ready now, 3 ready within 12 months.

E2E-11 · Onboarding-to-Productivity

Goal: Accelerate time-to-productivity. **Starts when:** New hire or internal mover confirmed. **Ends when:** Employee productive within target time and onboarding closed.

Task	Steps	What to type
UFT-11-01 Create onboarding record R: Hiring Manager	MP-35.1 Create onboarding record	Onboarding record for the new Assembly & Production technician, start date 1 July, buddy assigned.
UFT-11-02 Generate 30-60-90 day path R: HR Business Partner	MP-35.2 Generate 30-60-90 day path MP-08.1 Generate personal learning plan	30-60-90 path: day 30 safety and IATF 16949; day 60 MES and digital shop-floor tracking; day 90 autonomy on shift. AI run: 30-60-90 path: day 30 safety and IATF 16949; day 60 AI visual inspection of welds and paint; day 90 autonomy on shift.
UFT-11-03 Enroll in onboarding sessions R: Training Administrator	MP-07.3 Enroll learners into session MP-07.4 Send convocations	Enroll in the induction session of 2 July; convocation sent.
UFT-11-04 Complete onboarding tasks R: Employee	MP-35.3 Complete onboarding tasks	Tasks done: badge, IT account, safety tour, meeting with the team.
UFT-11-05 Hold milestone check-ins R: Hiring Manager	MP-35.4 Hold milestone check-in MP-21.3 Schedule coaching sessions	Day-30 check-in: on track; coaching needed on MES and digital shop-floor tracking data entry. AI run: Day-30 check-in: on track; coaching needed on AI visual inspection of welds and paint data entry.

Task	Steps	What to type
UFT-11-06 Assess time to productivity R: Hiring Manager	MP-35.5 Assess time to productivity	Time to productivity: 74 days (target 90).
UFT-11-07 Close onboarding R: HR Business Partner	MP-35.6 Close onboarding MP-13.3 Create individual development plan	Close onboarding; link the individual development plan for year 1.

E2E-12 · Knowledge-Capture-to-Transfer

Goal: Capture and transfer institutional knowledge. **Starts when:** Critical expert identified as leaving, retiring or holding at-risk knowledge. **Ends when:** Knowledge captured, published and transferred to a validated successor.

Task	Steps	What to type
UFT-12-01 Identify critical experts R: HR Business Partner	MP-34.1 Identify critical experts	Critical expert: senior Assembly & Production engineer retiring in 8 months; knowledge risk: high.
UFT-12-02 Plan capture sessions R: Knowledge Manager	MP-34.2 Plan capture sessions	Capture plan: 4 sessions of 90 minutes on troubleshooting and IATF 16949 practices.
UFT-12-03 Record expert interview R: Knowledge Manager	MP-34.3 Record expert interview	Interview 1 recorded (82 minutes); transcript attached.
UFT-12-04 Structure knowledge R: Knowledge Manager	MP-34.4 Structure knowledge from transcript	Accept the AI structure: 5 failure modes, 12 checks, 3 decision rules; correct 2 technical terms.
UFT-12-05 Publish knowledge article R: Knowledge Manager	MP-12.1 Publish knowledge article MP-12.2 Index article for retrieval MP-33.4 Approve publication	Publish article 'Troubleshooting guide — Assembly & Production' in EN/FR/AR; indexed for search.
UFT-12-06 Assign successor learning path R: Manager	MP-34.5 Assign successor learning path MP-06.6 Publish content to catalog	Assign the successor path: article + 3 shadowing sessions with the expert.
UFT-12-07 Validate transfer completion R: Subject Matter Expert	MP-34.6 Validate transfer completion	Transfer validated: successor solved 4 of 5 test cases alone.

E2E-31 · Engagement-to-Roadmap

Goal: Define post-engagement roadmap and continuous improvement. **Starts when:** Closure of the current training engineering engagement (E2E-19). **Ends when:** Approved post-engagement roadmap with future missions and continuous improvement plan.

Task	Steps	What to type
UFT-31-01 Consolidate engagement findings R: Consultant PM	MP-50.1 Consolidate engagement findings	Findings: 6 deliverables, 3 lessons learned, 2 open topics (IS, org design).
UFT-31-02 Define future perspectives R: Consultant PM	MP-50.2 Define future perspectives	Perspectives: Supplier portal and EDI programme, second wave for OP level. AI run: Perspectives: Generative AI for 8D problem solving programme, second wave for OP level.

Task	Steps	What to type
UFT-31-03 Plan One-to-One coaching R: L&D Strategist	MP-50.3 Plan One-to-One coaching	One-to-One coaching: 6 managers, 6 sessions each over 6 months.
UFT-31-04 Plan organizational optimization R: Org Design Consultant	MP-50.4 Plan organizational optimization	Organizational optimization: merge 2 planning cells; update 11 descriptions.
UFT-31-05 Plan IS rehabilitation R: IT Architect	MP-50.5 Plan IS rehabilitation	IS rehabilitation: connect HRIS and training platform; retire 2 spreadsheets.
UFT-31-06 Define KPIs and dashboards R: Performance Analyst	MP-50.6 Define KPIs and dashboards	KPIs: training coverage, time to competency, ROI per theme; monthly dashboard.
UFT-31-07 Prioritize future missions R: Consultant PM	MP-50.7 Prioritize future missions MP-50.8 Validate roadmap with leadership	Priority missions: 1 IS rehabilitation, 2 coaching, 3 org optimization.
UFT-31-08 Publish roadmap R: Consultant PM	MP-50.9 Publish post-engagement roadmap MP-50.10 Track roadmap execution MP-50.11 Improve roadmap continuously MP-50.12 Report on roadmap progress	Publish RPT-010 Post-Engagement Roadmap to the executive committee.

7. SMEs (any sector)

This part follows Tanger Auto Parts, a SME in the Automotive sector (85 employees, Tanger, independent). Sign in as headld@tangerautoparts.ma. The same steps apply to any organization of this type: replace the names, figures and themes with your own.

Item	Digital skills run	AI skills run
Project	Digital Skills Full Run 2026 — Tanger Auto Parts	AI Skills Full Run 2026 — Tanger Auto Parts
Mode and track	SME · SME-T3	SME · SME-T3
Processes and tasks	38 processes · 277 tasks	38 processes · 277 tasks

Phase	Gate	End-to-end processes
Enablers (run across all phases)	—	E2E-15, E2E-17, E2E-18
Scope & evidence	G1	E2E-32, E2E-33, E2E-19, E2E-24, SME-E2E-01
Diagnosis	G2	E2E-20, E2E-25, E2E-26, E2E-27, E2E-28, E2E-29, E2E-02, E2E-21
Training Engineering Report & plan	G3	E2E-01, E2E-03, E2E-30, E2E-22, E2E-23, E2E-16, AUTO-E2E-02, SME-E2E-02
Design & delivery	G4	E2E-04, E2E-05, E2E-06, E2E-13, E2E-14, SME-E2E-03
Evaluation, compliance & impact	G5	E2E-07, E2E-08, E2E-09, AUTO-E2E-01
Talent, knowledge & continuous improvement	G6	E2E-10, E2E-11, E2E-12, E2E-31

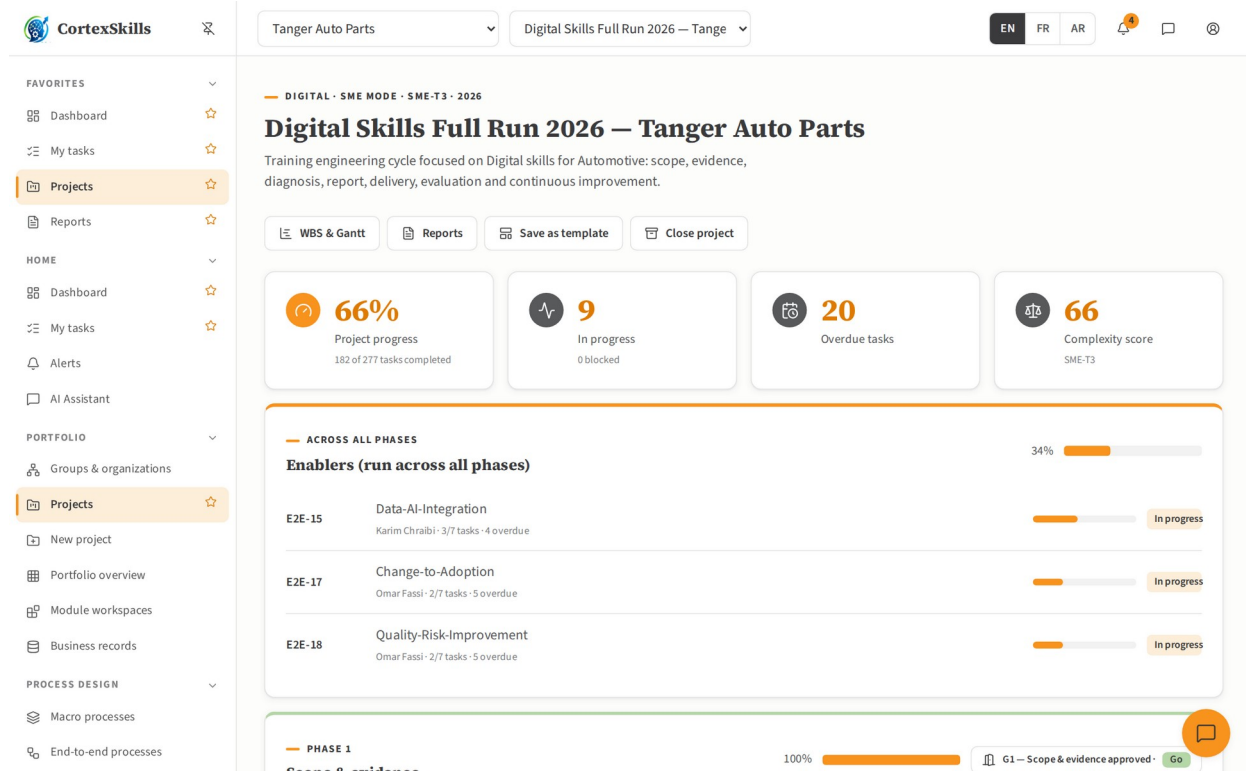


Figure — Workspace of the SME Digital run (Tanger Auto Parts)

7.1 Enablers (run across all phases)

E2E-15 · Data-AI-Integration

Goal: Govern data, AI, integrations. **Starts when:** New integration, data source or AI use case to govern. **Ends when:** Integrations, data and AI governed with health, retention and usage reviewed.

Task	Steps	What to type
UFT-15-01 Register external integration R: Platform Administrator	MP-16.1 Register external integration	Register integration 'HRIS — Workday' (INT-HR-01); credential reference stored encrypted.
UFT-15-02 Map fields and check health R: IT Architect	MP-16.2 Map integration fields MP-16.3 Check integration health	Map fields: employee_id → matricule; position → poste. Health check: success.
UFT-15-03 Run HRIS synchronisation R: IT Architect	MP-16.4 Run HRIS synchronisation MP-16.5 Review synchronisation rejections	Sync run: 1,204 records updated, 3 rejected (missing position) — corrected.
UFT-15-04 Set data retention rule R: Data Protection Officer	MP-16.6 Set data retention rule	Retention: questionnaire responses 3 years; training records 10 years.
UFT-15-05 Maintain AI use case register R: Platform Administrator	MP-16.7 Maintain AI use case register	Add custom use case 'Shift-report summarizer' (Assistive), version 1.
UFT-15-06 Set AI activation per scope R: Platform Administrator	MP-16.8 Set AI activation per scope MP-24.1 Enable personalization per scope	Activate AIUC-35 and AIUC-36 for the organization; override Off for pilot project B.
UFT-15-07 Review AI usage log R: IT Architect	MP-16.9 Review AI usage log MP-28.2 Validate dataset quality	Usage review: 412 suggestions — 71% accepted, 20% edited, 9% rejected.

E2E-17 · Change-to-Adoption

Goal: Drive sustained adoption and culture change. **Starts when:** Approved plan or new platform capability requiring adoption. **Ends when:** Sustained adoption reached with low-adoption groups reinforced.

Task	Steps	What to type
UFT-17-01 Assess change impact R: Change Manager	MP-19.1 Assess change impact	Impact: Assembly & Production supervisors high, operators medium, support functions low.
UFT-17-02 Build adoption plan R: Change Manager	MP-19.2 Build adoption plan	Adoption plan: sponsor message, 6 champions, weekly 15-minute huddles for 8 weeks.
UFT-17-03 Launch communication campaign R: Change Manager	MP-19.3 Launch communication campaign	Campaign 'MES and digital shop-floor tracking — why it matters' on e-mail, intranet and screens. AI run: Campaign 'AI visual inspection of welds and paint — why it matters' on e-mail, intranet and screens.
UFT-17-04 Open community space R: Knowledge Manager	MP-12.3 Create community space MP-12.4 Moderate community posts MP-26.1 Create learning cohort group	Community space 'MES and digital shop-floor tracking Q&A' opened; moderation rules published. AI run: Community space 'AI visual inspection of welds and paint Q&A' opened; moderation rules published.

Task	Steps	What to type
UFT-17-05 Track adoption usage R: L&D Analyst	MP-19.4 Track adoption usage MP-08.5 Monitor engagement indicators	Weekly active users: 64% of the target population.
UFT-17-06 Identify low-adoption groups R: Change Manager	MP-19.5 Identify low-adoption groups	Low adoption confirmed for night shift (31%); one group rejected as false positive.
UFT-17-07 Run reinforcement actions R: Change Manager	MP-19.6 Run reinforcement actions MP-08.6 Trigger re-engagement nudge	Reinforcement: night-shift coaching sessions; adoption reached 58% after 4 weeks.

E2E-18 · Quality-Risk-Improvement

Goal: Improve processes and mitigate risk. **Starts when:** Risk logged, periodic quality review due or control test scheduled. **Ends when:** Risks mitigated, actions evaluated by a different person, controls rated.

Task	Steps	What to type
UFT-18-01 Log risk or opportunity R: Quality Manager	MP-20.1 Log risk or opportunity	Risk 'Trainers unavailable in Q3': likelihood 3, impact 4, score 12.
UFT-18-02 Assign mitigation action R: Quality Manager	MP-20.2 Assign mitigation action	Action: contract a second vendor; owner Purchasing Officer; evaluator Quality Manager.
UFT-18-03 Execute improvement action R: Action Owner	MP-20.3 Execute improvement action	Action done: framework contract signed with vendor B; evidence attached.
UFT-18-04 Evaluate action effectiveness R: Action Evaluator	MP-20.4 Evaluate action effectiveness	Verdict: effective. The evaluator is a different user from the owner.
UFT-18-05 Review access and security R: IT Architect	MP-17.4 Review access violation log MP-17.6 Enforce login rate limit MP-17.2 Assign roles to user MP-17.3 Edit permission matrix MP-17.5 Issue signed session token	Access review: 2 dormant accounts disabled; 0 cross-tenant attempts.
UFT-18-06 Run periodic quality review R: Quality Manager	MP-20.5 Run periodic quality review MP-09.7 Review evaluation results	Quality review minutes: 3 KPIs red, 2 actions opened, next review in 30 days.
UFT-18-07 Update control effectiveness R: Quality Manager	MP-20.6 Update control effectiveness rating	Control CTRL-002 effectiveness: Effective; CTRL-031: Partially effective.

7.2 Scope & evidence — gate G1

E2E-32 · Scope-of-Work-to-Engineering-Plan

Goal: Define and approve the structured scope of work and stakeholder register. **Starts when:** New training engineering engagement, annual plan cycle, or executive request. **Ends when:** Approved Scope of Work with criteria matrix and stakeholder register released to questionnaire design (E2E-33) and needs analysis (E2E-03).

Task	Steps	What to type
UFT-32-01 Define scope frame R: Head of L&D	MP-53.1 Define scope frame (Group Yes/No) MP-53.2 Select Organization	Group scope: No. Organization: Tanger Auto Parts.
UFT-32-02 Select sector R: L&D Analyst	MP-53.3 Select sector	Sector: Automotive.
UFT-32-03 Select decision levels R: L&D Analyst	MP-53.4 Select decision level (MS/MO/OP/Custom)	Decision levels: MS, MO, OP (no custom level).
UFT-32-04 Map functions × decision levels R: L&D Analyst	MP-53.5 Map functions × decision level	Matrix: Assembly & Production × MS/MO/OP; Quality × MO/OP; Finance × MS/MO; HR × MS/MO.
UFT-32-05 Select focus and add custom criteria R: Head of L&D	MP-53.6 Select focus (All/Digital/AI/Custom) MP-53.7 Add custom criteria	Focus: Digital. Custom criterion: 'Readiness for MES and digital shop-floor tracking' (weight 2.00). AI run: Focus: AI. Custom criterion: 'Readiness for AI visual inspection of welds and paint' (weight 2.00).
UFT-32-06 Identify stakeholders R: HR Business Partner	MP-53.8 Identify stakeholders	Register 40 stakeholders: name, role, function, level, site, preferred channel (Email, Face-to-Face or Hybrid).
UFT-32-07 Validate scope R: Head of L&D	MP-53.9 Validate and approve scope	Validation: every function in scope has at least 3 stakeholders; completeness 100%.
UFT-32-08 Approve scope R: HR Director / Consultant PM	MP-53.9 Validate and approve scope MP-53.10 Publish scope and register stakeholders	Approval status: Approved (version 1). Justification: scope aligned with SO-1 and SO-2.
UFT-32-09 Publish scope and register stakeholders R: L&D Analyst	MP-53.10 Publish scope and register stakeholders	Generate the SOW document (RPT-033) and release scope and stakeholders to the questionnaire studio.

E2E-33 · Questionnaire-to-Response-Collection

Goal: Design, distribute and collect questionnaire responses across channels. **Starts when:** An approved Scope of Work becomes available (end of E2E-32). **Ends when:** Consolidated, validated questionnaire response dataset feeding needs analysis (E2E-03), diagnostic (E2E-20) and demand collection (E2E-27).

Task	Steps	What to type
UFT-33-01 Select questionnaire template R: L&D Analyst	MP-54.1 Select questionnaire template by focus	Template: 'Digital needs — Automotive' in the user's language, 5 sections. AI run: Template: 'AI needs — Automotive' in the user's language, 5 sections.
UFT-33-02 Elaborate questionnaire R: L&D Analyst	MP-54.2 Elaborate questionnaire (Load/AI/Manual)	Elaboration mode: AI. 24 questions generated from the approved Scope of Work.
UFT-33-03 Tailor and validate content R: L&D Analyst	MP-54.3 Tailor to sector and focus	Validate each question; reword 5 with Assembly & Production vocabulary; delete 2 duplicates.

Task	Steps	What to type
UFT-33-04 Allocate RACSI R: Head of L&D	MP-54.4 Allocate RACSI per section	Section 'Digital practices': R L&D Analyst, A Head of L&D, C Consultant PM, S IT, I CHRO (one Accountable only).
UFT-33-05 Select distribution channels R: Survey Administrator	MP-54.5 Select distribution channels	Channels: MS and MO by Email; OP Face-to-Face with tablets; night shift Hybrid.
UFT-33-06 Distribute questionnaire R: Survey Administrator	MP-54.6 Distribute to stakeholders	Distribute to 40 stakeholders; 40 dispatches logged.
UFT-33-07 Send reminders R: Survey Administrator	MP-54.7 Send reminders on cadence	Reminder 1 on day 5 to 17 non-respondents; reminder 2 on day 10 to 8.
UFT-33-08 Collect responses R: Stakeholders	MP-54.8 Collect responses	Responses: 34 collected (22 online, 12 offline synchronised).
UFT-33-09 Validate completeness R: L&D Analyst	MP-54.9 Validate completeness and consent	Completeness: 31 complete, 3 incomplete flagged.
UFT-33-10 Consolidate responses R: L&D Analyst	MP-54.10 Consolidate responses	Consolidated dataset: 31 responses, 24 questions, by function and level.
UFT-33-11 Check consent and release dataset R: L&D Analyst	MP-54.11 Feed responses to needs analysis and diagnostic MP-54.12 Report on response rate and engagement	Consent given for 31 of 31 stored responses; release to needs analysis, diagnostic and demand collection.
UFT-33-12 Report on response and engagement R: L&D Analyst	MP-54.12 Report on response rate and engagement	Response rate 85%; engagement rate 78%; completeness 91% (RPT-034).

E2E-19 · Consulting Engagement-to-Closure

Goal: Manage full consulting engagement lifecycle. **Starts when:** Client purchase order or engagement request received. **Ends when:** Engagement closed with client acceptance and REX recorded.

Task	Steps	What to type
UFT-19-01 Register engagement and purchase order R: Consultant PM	MP-36.1 Register engagement and purchase order	Engagement 'Training engineering 2026 — Tanger Auto Parts', PO-CL-221, 45 consulting days.
UFT-19-02 Hold kickoff meeting R: Consultant PM	MP-36.2 Hold kickoff meeting	Kickoff held on 10 February with HR Director, Head of L&D and 4 function heads.
UFT-19-03 Draft meeting minutes R: Consultant PM	MP-36.3 Draft meeting minutes	Review the AI minutes: 6 decisions, 9 actions, RACSI extracted; correct 1 owner name.

Task	Steps	What to type
UFT-19-04 Align with client strategy R: Consultant PM	MP-01.1 Record corporate strategic objectives MP-01.2 Link objectives to functions and sites	Client objectives recorded: MES and digital shop-floor tracking and IATF 16949 compliance for Assembly & Production. AI run: Client objectives recorded: AI visual inspection of welds and paint and IATF 16949 compliance for Assembly & Production.
UFT-19-05 Plan engagement work breakdown R: Consultant PM	MP-36.4 Plan engagement work breakdown	WBS: 6 phases, 14 deliverables, Gantt from February to November.
UFT-19-06 Plan change support R: Change Manager	MP-19.1 Assess change impact MP-19.2 Build adoption plan	Change plan: 3 sponsor messages, champion network, 2 town-halls.
UFT-19-07 Track engagement deliverables R: Consultant PM	MP-36.5 Track engagement deliverables MP-20.5 Run periodic quality review	Deliverables: 9 of 14 delivered on time, 1 late (SWOT), 4 planned.
UFT-19-08 Deliver final report and obtain acceptance R: Consultant PM	MP-36.6 Deliver final report MP-36.7 Obtain client acceptance	Final report delivered; acceptance signed by the HR Director on 28 November.
UFT-19-09 Record engagement REX R: Consultant PM	MP-36.8 Record engagement REX MP-12.6 Record REX entry MP-12.5 Prompt REX at closure	REX: went well — stakeholder register; did not — late SWOT inputs; root cause — no function-head backup; rating 4/5.

E2E-24 · Competitive Intelligence-to-Strategy

Goal: Analyze external environment and feed L&D strategy. **Starts when:** Annual strategy cycle or executive request for market positioning analysis. **Ends when:** Validated competitive intelligence report feeding into L&D strategy and organizational diagnostic.

Task	Steps	What to type
UFT-24-01 Define intelligence scope R: Strategy Analyst	MP-43.1 Define intelligence scope	Scope: Automotive market in Morocco and export markets; horizon 3 years; focus on MES and digital shop-floor tracking and PLM and digital engineering change. AI run: Scope: Automotive market in Morocco and export markets; horizon 3 years; focus on AI visual inspection of welds and paint and Predictive maintenance of press lines.
UFT-24-02 Conduct Porter's Five Forces R: Strategy Analyst	MP-43.2 Conduct Porter's Five Forces analysis	Rivalry 4/5; new entrants 3/5; substitutes 2/5; supplier power 3/5; buyer power 4/5.
UFT-24-03 Map market segments R: Market Analyst	MP-43.3 Map market segments	Segments: key accounts (55% revenue), resellers (30%), direct small customers (15%).
UFT-24-04 Analyze competitor positioning R: Market Analyst	MP-43.4 Analyze competitor positioning	Competitor A leads on MES and digital shop-floor tracking; competitor B cheaper but weaker on IATF 16949. AI run: Competitor A leads on AI visual inspection of welds and paint; competitor B cheaper but weaker on IATF 16949.

Task	Steps	What to type
UFT-24-05 Monitor regulatory and technology trends R: Regulatory Analyst	MP-43.5 Monitor regulatory changes MP-43.6 Track technology trends MP-43.7 Benchmark against industry	Trends: revision of IATF 16949 expected next year; fast growth of Supplier portal and EDI. AI run: Trends: revision of IATF 16949 expected next year; fast growth of Generative AI for 8D problem solving.
UFT-24-06 Identify L&D implications R: L&D Strategist	MP-43.8 Identify strategic implications for L&D	L&D implication: build MES and digital shop-floor tracking skills for key-account teams before competitor A scales. AI run: L&D implication: build AI visual inspection of welds and paint skills for key-account teams before competitor A scales.
UFT-24-07 Publish intelligence report R: Strategy Analyst	MP-43.9 Produce intelligence report MP-43.10 Feed intelligence into strategy and diagnostic MP-43.11 Update intelligence continuously MP-43.12 Report to executive leadership	Publish RPT-007 Competitive Intelligence Report to the executive committee.

SME-E2E-01 · SME Snapshot-to-Plan in 30 days

Goal: Turn a one-day needs snapshot into a short, funded plan.. **Starts when:** SME onboarding started. **Ends when:** Short plan approved by the owner-manager.

Task	Steps	What to type
UFT-SME1-01 Interview the owner-manager R: Head of L&D	SME-MP-01.1 Record business priorities SME-MP-01.2 Record key roles and headcount	Priorities: win 2 new customers; reduce rework. Headcount SME: owner, 3 team leaders, operators.
UFT-SME1-02 Send the needs snapshot R: L&D Analyst	SME-MP-01.3 Send short needs questionnaire MP-54.6 Distribute to stakeholders	Send the 10-question snapshot to all employees by WhatsApp link or paper.
UFT-SME1-03 Summarize top needs R: L&D Analyst	SME-MP-01.4 Summarize top needs	Top needs: MES and digital shop-floor tracking; PLM and digital engineering change; customer service. Accept the AI summary. AI run: Top needs: AI visual inspection of welds and paint; Predictive maintenance of press lines; customer service. Accept the AI summary.
UFT-SME1-04 Approve the short plan R: HR Director	MP-53.9 Validate and approve scope	Short plan approved: 3 themes, 6 training days, 45,000 MAD.

7.3 Diagnosis — gate G2

E2E-20 · Multi-Axis Diagnostic-to-Maturity Report

Goal: Conduct 5-axis diagnostic + CMM maturity + leadership assessment. **Starts when:** Engagement kickoff or approved Scope of Work requesting a diagnostic. **Ends when:** 5-axis diagnostic, CMM maturity and leadership maturity report validated with the sponsor.

Task	Steps	What to type
UFT-20-01 Define diagnostic axes and sample R: Consultant PM	MP-37.1 Define diagnostic axes and sample	Axes: strategy, organization, processes, people, information systems. Sample: 40 people (MS 8, MO 16, OP 16).

Task	Steps	What to type
UFT-20-02 Deploy diagnostic questionnaire R: Consultant PM	MP-37.2 Deploy diagnostic questionnaire MP-37.4 Collect questionnaire responses	Diagnostic questionnaire deployed to 40 people; 34 responses (85%).
UFT-20-03 Conduct semi-structured interviews R: Consultant	MP-37.3 Conduct semi-structured interviews	Interview notes (OP, Assembly & Production): 'Procedures exist but are not updated since 2023.'
UFT-20-04 Score diagnostic axes R: Consultant	MP-37.5 Score diagnostic axes	Axis scores (1-5): strategy 3.4, organization 2.8, processes 2.6, people 3.1, IS 2.2.
UFT-20-05 Select maturity model R: Consultant	MP-38.1 Select maturity model levels MP-38.2 Define evidence criteria per level	Maturity model: CMM 5 levels; evidence for level 3 = documented and applied process.
UFT-20-06 Rate process maturity R: Consultant	MP-38.3 Rate maturity per process area MP-38.4 Compute maturity profile	Maturity: training management level 2; Assembly & Production processes level 3.
UFT-20-07 Assess leadership maturity R: HR Business Partner	MP-42.1 Launch leadership 360 assessment MP-42.2 Compute leadership maturity level	Leadership 360: average level 3 (Team Leadership) across 18 managers.
UFT-20-08 Cross-check skills and needs R: L&D Analyst	MP-02.7 Validate skills inventory MP-03.2 Review gap matrix by site and function	Cross-check: IS axis weakness confirmed by the MES and digital shop-floor tracking gap (-1.4). AI run: Cross-check: IS axis weakness confirmed by the AI visual inspection of welds and paint gap (-1.4).
UFT-20-09 Draft diagnostic findings R: Consultant	MP-37.6 Draft diagnostic findings MP-38.5 Produce maturity report	Edit AI findings: keep 5, merge 2, add one on IATF 16949 documentation.
UFT-20-10 Validate findings with sponsor R: Consultant PM	MP-37.7 Validate findings with sponsor MP-38.6 Agree target maturity	Findings validated with the sponsor; target maturity level 3 by 2026+1.

E2E-25 · Job Architecture-to-Competency Map

Goal: Manage organizational charts, position descriptions, gap analysis. **Starts when:** Organizational change, new role creation, or annual job architecture review. **Ends when:** Approved organizational charts, position descriptions, and competency maps with gap analysis.

Task	Steps	What to type
UFT-25-01 Map organizational structure R: HR Analyst	MP-44.1 Map organizational structure	Structure: 6 functions, 14 departments, 3 sites; 212 positions.
UFT-25-02 Design organizational charts R: Org Design Consultant	MP-44.2 Design organizational charts	Org chart 'Assembly & Production': director → 3 managers → 9 supervisors → operators.

Task	Steps	What to type
UFT-25-03 Conduct job analysis R: Job Analyst	MP-44.3 Conduct job analysis	Job analysis 'Assembly & Production supervisor': 8 main activities, 2 of them now supported by MES and digital shop-floor tracking. AI run: Job analysis 'Assembly & Production supervisor': 8 main activities, 2 of them now supported by AI visual inspection of welds and paint.
UFT-25-04 Draft position descriptions R: Job Analyst	MP-44.4 Draft position descriptions	Position description drafted: mission, activities, competencies (MES and digital shop-floor tracking level 3, IATF 16949 level 3), KPIs. AI run: Position description drafted: mission, activities, competencies (AI visual inspection of welds and paint level 3, IATF 16949 level 3), KPIs.
UFT-25-05 Validate with managers R: HR Business Partner	MP-44.5 Validate descriptions with managers	Validated by the Assembly & Production manager with 2 changes on activities.
UFT-25-06 Conduct gap analysis R: Job Analyst	MP-44.6 Conduct gap analysis existing versus real	Gap existing vs real: 11 descriptions outdated; 4 roles with new MES and digital shop-floor tracking tasks. AI run: Gap existing vs real: 11 descriptions outdated; 4 roles with new AI visual inspection of welds and paint tasks.
UFT-25-07 Identify roles to develop R: HR Business Partner	MP-44.7 Identify roles to develop MP-44.8 Update job architecture MP-44.9 Align with competency framework	Roles 'To develop': data-literate supervisor, maintenance technician 4.0.
UFT-25-08 Publish approved architecture R: HR Director	MP-44.10 Publish approved position descriptions MP-44.11 Track job architecture changes MP-44.12 Report on architecture health	Publish 212 approved descriptions and the architecture map to all employees.

E2E-26 · GPEC-to-Training Plan

Goal: Integrate Forward Planning of Jobs and Skills into L&D. **Starts when:** Annual HR strategic planning cycle or GPEC (Forward Planning of Jobs and Skills) review. **Ends when:** Training plan aligned with GPEC and HR strategic orientations.

Task	Steps	What to type
UFT-26-01 Define GPEC scope R: GPEC Specialist	MP-45.1 Define GPEC scope	GPEC scope: Assembly & Production and Information Systems jobs; horizon 3 years.
UFT-26-02 Map HR strategic orientations R: HR Director	MP-45.2 Map HR strategic orientations MP-45.3 Align training with GPEC	HR orientations: internal mobility first; 30% of promotions from internal talent.
UFT-26-03 Update development foundation R: HR Business Partner	MP-45.4 Update development foundation MP-45.5 Support human capital development	Development foundation updated: descriptions, annual objectives, evaluation grid.
UFT-26-04 Update Jobs and Skills Directory (REC) R: GPEC Specialist	MP-45.6 Update Jobs and Skills Directory (REC)	REC updated: 42 jobs, 3 new jobs linked to MES and digital shop-floor tracking. AI run: REC updated: 42 jobs, 3 new jobs linked to AI visual inspection of welds and paint.

Task	Steps	What to type
UFT-26-05 Redynamize periodic evaluations R: HR Business Partner	MP-45.7 Redynamize periodic evaluations	Periodic evaluation redesigned: 2 reviews per year, competency section added.
UFT-26-06 Design career paths R: HR Director	MP-45.8 Design career paths	Career path: operator → team leader → supervisor → Assembly & Production manager.
UFT-26-07 Document career management R: HR Director	MP-45.9 Document career management process MP-45.10 Implement collective compensation	Career management procedure documented (v1): eligibility, committee, calendar.
UFT-26-08 Align training with GPEC R: L&D Strategist	MP-45.11 Feed GPEC into training needs MP-45.12 Report on GPEC integration	Training aligned with GPEC: 4 themes cover the 3 new jobs; 2 themes removed.

E2E-27 · Demand Collection-to-Consolidation

Goal: Collect individual and collective training demands. **Starts when:** Annual training plan cycle or ad-hoc demand collection request. **Ends when:** Consolidated and prioritized demand repository integrated into the training needs analysis.

Task	Steps	What to type
UFT-27-01 Design demand collection forms R: L&D Analyst	MP-46.1 Design demand collection forms	Forms: individual form (5 questions) and collective form per team (3 questions).
UFT-27-02 Deploy individual demand collection R: L&D Analyst	MP-46.2 Deploy individual demand collection	Individual collection open 1-20 March; 146 demands received.
UFT-27-03 Deploy collective demand collection R: L&D Analyst	MP-46.3 Deploy collective demand collection	Collective collection: 18 team demands received.
UFT-27-04 Collect manager recommendations R: L&D Business Partner	MP-46.4 Collect manager recommendations	Manager recommendations: 24 received, 9 flagged as priority.
UFT-27-05 Consolidate demands by function R: L&D Analyst	MP-46.5 Consolidate demands by function	Consolidated: Assembly & Production 64 demands, Operations 41, Quality 22, others 37.
UFT-27-06 Map demands to competencies R: L&D Analyst	MP-46.6 Map demands to competencies MP-46.7 Prioritize demands	Accept AI mapping for 139 demands; map 7 manually to 'PLM and digital engineering change'. AI run: Accept AI mapping for 139 demands; map 7 manually to 'Predictive maintenance of press lines'.

Task	Steps	What to type
UFT-27-07 Prioritize and validate demands R: L&D Business Partner	MP-46.8 Validate demands with managers MP-46.9 Integrate demands into needs analysis MP-46.10 Report on demand patterns MP-46.11 Track demand fulfillment MP-46.12 Improve demand collection	Validated: 112 demands (High 38, Medium 51, Low 23); 34 rejected with reason.

E2E-28 · Performance Assessment-to-RAG Dashboard

Goal: Assess MS/MO/OP performance with RAG ratings. **Starts when:** Annual performance cycle or management request for performance visualization. **Ends when:** Validated MS/MO/OP (Strategic Management / Operational Management / Operational Level) performance assessment with RAG (Green/Amber/Red) dashboards.

Task	Steps	What to type
UFT-28-01 Define MS/MO/OP framework R: Performance Analyst	MP-47.1 Define MS/MO/OP framework	MS = executive committee; MO = managers and supervisors; OP = operators and technicians.
UFT-28-02 Define RAG criteria R: Performance Analyst	MP-47.2 Define RAG criteria	Green $\geq$ 90% of target; Amber 70-89%; Red < 70%.
UFT-28-03 Collect performance data by function R: Performance Analyst	MP-47.3 Collect performance data by function	Data collected for 6 functions: 18 KPIs, last 12 months.
UFT-28-04 Assess MS performance R: Performance Analyst	MP-47.4 Assess MS performance	MS: strategy deployment Amber (78%); governance Green (92%).
UFT-28-05 Assess MO performance R: Performance Analyst	MP-47.5 Assess MO performance	MO: Assembly & Production team management Red (64%); planning Amber (81%).
UFT-28-06 Assess OP performance R: Performance Analyst	MP-47.6 Assess OP performance MP-47.7 Apply RAG ratings	OP: IATF 16949 compliance Amber (85%); productivity Green (93%).
UFT-28-07 Publish RAG dashboard R: Performance Analyst	MP-47.8 Visualize performance dashboards MP-47.9 Identify performance gaps MP-47.10 Feed performance into diagnostic report MP-47.11 Track performance progression MP-47.12 Report performance to leadership	Publish RPT-005 MS/MO/OP RAG dashboard to the executive committee.

E2E-29 · Functional SWOT-to-Improvement Axes

Goal: Conduct function-level SWOT and define improvement axes. **Starts when:** Diagnostic phase of a training engineering engagement or annual functional review. **Ends when:** Validated functional SWOT reports with prioritized improvement axes per function.

Task	Steps	What to type
UFT-29-01 Define function scope R: L&D Analyst	MP-48.1 Define function scope	Function in scope: Assembly & Production (3 sites, 96 people).
UFT-29-02 Conduct function SWOT R: L&D Analyst	MP-48.2 Conduct function SWOT	SWOT workshop held with the function head and 6 supervisors.
UFT-29-03 Identify strengths and weaknesses R: L&D Analyst	MP-48.3 Identify strengths MP-48.4 Identify weaknesses	Strength: experienced team. Weakness: low MES and digital shop-floor tracking usage, paper records. AI run: Strength: experienced team. Weakness: low AI visual inspection of welds and paint usage, paper records.
UFT-29-04 Identify opportunities and threats R: L&D Analyst	MP-48.5 Identify opportunities MP-48.6 Identify threats	Opportunity: Supplier portal and EDI. Threat: stricter IATF 16949 audits. AI run: Opportunity: Generative AI for 8D problem solving. Threat: stricter IATF 16949 audits.
UFT-29-05 Define improvement axes R: L&D Business Partner	MP-48.7 Define improvement axes	Axis 1: digitalise shift records with MES and digital shop-floor tracking. Axis 2: certify supervisors on IATF 16949. AI run: Axis 1: digitalise shift records with AI visual inspection of welds and paint. Axis 2: certify supervisors on IATF 16949.
UFT-29-06 Validate with function heads R: L&D Business Partner	MP-48.8 Validate axes with function heads	Validated by the function head on 18 April; axis 2 deadline moved to Q3.
UFT-29-07 Prioritize improvement axes R: L&D Strategist	MP-48.9 Prioritize improvement axes MP-48.10 Feed SWOT into diagnostic report MP-48.11 Track improvement implementation MP-48.12 Report on function performance	Priority: axis 1 (impact 5), axis 2 (impact 4).

E2E-02 · Skills-to-Gap Diagnosis

Goal: Produce a validated skills gap diagnosis. **Starts when:** Approved annual L&D plan or a scheduled skills assessment campaign. **Ends when:** Validated skills gap diagnosis released to needs analysis.

Task	Steps	What to type
UFT-02-01 Maintain competency framework R: L&D Analyst	MP-02.1 Define competency families and levels	Family 'MES and digital shop-floor tracking': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert). AI run: Family 'AI visual inspection of welds and paint': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert).
UFT-02-02 Set target levels per position R: HR Business Partner	MP-02.2 Set target levels per position	Assembly & Production supervisor: MES and digital shop-floor tracking = 3; IATF 16949 = 3. Assembly & Production operator: MES and digital shop-floor tracking = 2. AI run: Assembly & Production supervisor: AI visual inspection of welds and paint = 3; IATF 16949 = 3. Assembly & Production operator: AI visual inspection of welds and paint = 2.
UFT-02-03 Launch assessment campaign R: L&D Analyst	MP-02.3 Launch assessment campaign	Campaign 'Skills 2026': population Assembly & Production and Operations (212 people), 12 competencies, close date 30 April.

Task	Steps	What to type
UFT-02-04 Collect self and manager assessments R: Manager	MP-02.4 Submit self and manager assessments MP-02.5 Consolidate assessment results	Self-assessment MES and digital shop-floor tracking: 2; manager validation: 2 with comment 'needs practice on live cases'. AI run: Self-assessment AI visual inspection of welds and paint: 2; manager validation: 2 with comment 'needs practice on live cases'.
UFT-02-05 Suggest proficiency from evidence R: L&D Analyst	MP-02.6 Suggest proficiency from evidence	Accept 38 suggested levels, edit 4 (evidence too old), reject 1. Every change carries a note.
UFT-02-06 Validate skills inventory R: Head of L&D	MP-02.7 Validate skills inventory	Inventory validated: 212 employees, 96% assessments complete. Justification: sample checked by site.
UFT-02-07 Compute and forecast gaps R: L&D Analyst	MP-03.1 Compute gap matrix MP-03.2 Review gap matrix by site and function MP-28.3 Forecast skill gaps MP-28.1 Build analytics dataset	Critical gaps: MES and digital shop-floor tracking (-1.4 average on supervisors), PLM and digital engineering change (-1.1). Forecast: Supplier portal and EDI becomes critical within 12 months. AI run: Critical gaps: AI visual inspection of welds and paint (-1.4 average on supervisors), Predictive maintenance of press lines (-1.1). Forecast: Generative AI for 8D problem solving becomes critical within 12 months.

E2E-21 · Previous Plan Impact-to-Strategy Update

Goal: Evaluate N-1 plan impact and update strategy. **Starts when:** Start of a new plan cycle with N-1 execution data available. **Ends when:** N-1 impact conclusions fed into the strategy update.

Task	Steps	What to type
UFT-21-01 Load N-1 plan execution data R: L&D Analyst	MP-39.1 Load N-1 plan execution data	Load N-1 plan: 28 sessions planned, 23 delivered, 1,410,000 MAD spent.
UFT-21-02 Define impact criteria R: L&D Analyst	MP-39.2 Define impact criteria	Impact criteria: application on the job, KPI change, satisfaction, cost per learner.
UFT-21-03 Survey participants and managers R: L&D Analyst	MP-39.3 Survey participants and managers MP-09.5 Record on-the-job observation (Level 3)	Survey sent to 190 participants and 34 managers; 61% responded.
UFT-21-04 Compare planned against realized R: L&D Analyst	MP-39.4 Compare planned against realized MP-32.3 Isolate training effect	Planned vs realized: 82% of sessions, 94% of budget; 2 themes not delivered.
UFT-21-05 Review N-1 ROI R: Performance Analyst	MP-32.4 Compute Phillips ROI MP-32.5 Review ROI with finance	N-1 ROI: PLM and digital engineering change 18%; safety theme 35%. AI run: N-1 ROI: Predictive maintenance of press lines 18%; safety theme 35%.
UFT-21-06 Draft impact conclusions R: L&D Analyst	MP-39.5 Draft impact study conclusions	Accept AI conclusions 1-3; rewrite conclusion 4 (sample too small).

Task	Steps	What to type
UFT-21-07 Feed conclusions to strategy R: Head of L&D	MP-39.6 Feed conclusions to strategy update MP-01.1 Record corporate strategic objectives	Feed to strategy: keep blended format; stop long classroom courses on PLM and digital engineering change. AI run: Feed to strategy: keep blended format; stop long classroom courses on Predictive maintenance of press lines.
UFT-21-08 Update roadmap priorities R: L&D Strategist	MP-04.6 Sequence roadmap initiatives	Roadmap priority updated: MES and digital shop-floor tracking moved to Q2; PLM and digital engineering change to microlearning. AI run: Roadmap priority updated: AI visual inspection of welds and paint moved to Q2; Predictive maintenance of press lines to microlearning.

7.4 Training Engineering Report & plan — gate G3

E2E-01 · Strategy-to-Learning Plan

Goal: Translate corporate strategy into an approved annual L&D plan and budget. **Starts when:** Annual strategy cycle opened or revised corporate objectives published by the board. **Ends when:** Annual L&D plan and budget envelope approved by the Steering Committee and locked.

Task	Steps	What to type
UFT-01-01 Record strategic objectives R: Head of L&D	MP-01.1 Record corporate strategic objectives	SO-1: MES and digital shop-floor tracking used by 80% of Assembly & Production staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on IATF 16949. AI run: SO-1: AI visual inspection of welds and paint used by 80% of Assembly & Production staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on IATF 16949.
UFT-01-02 Link objectives to functions and sites R: L&D Strategist	MP-01.2 Link objectives to functions and sites	SO-1 → Assembly & Production, Operations, Information Systems (all sites). SO-2 → Quality & HSE, Assembly & Production.
UFT-01-03 Frame skills priorities R: L&D Analyst	MP-02.1 Define competency families and levels MP-02.2 Set target levels per position	Priority competency families: MES and digital shop-floor tracking; PLM and digital engineering change; IATF 16949 compliance. Target level 3 (Autonomous) for supervisors. AI run: Priority competency families: AI visual inspection of welds and paint; Predictive maintenance of press lines; IATF 16949 compliance. Target level 3 (Autonomous) for supervisors.
UFT-01-04 Pre-scope training needs R: L&D Analyst	MP-03.1 Compute gap matrix MP-03.2 Review gap matrix by site and function	Pre-scoped needs: 42% of Assembly & Production supervisors below target on MES and digital shop-floor tracking; 18 employees below target on IATF 16949. AI run: Pre-scoped needs: 42% of Assembly & Production supervisors below target on AI visual inspection of welds and paint; 18 employees below target on IATF 16949.
UFT-01-05 Define budget envelope R: Finance Manager	MP-01.3 Define L&D budget envelope MP-18.1 Allocate budget by theme and site MP-18.2 Forecast OFPPT refunds	Gross L&D budget 2026: 1,850,000 MAD; forecast refund (OFPPT/CSF): 520,000 MAD; net envelope: 1,330,000 MAD.

Task	Steps	What to type
UFT-01-06 Plan change and adoption R: Change Manager	MP-19.1 Assess change impact MP-19.2 Build adoption plan	Change impact: high for Assembly & Production supervisors (new MES and digital shop-floor tracking routines). Sponsors: Operations Director. Champions: one per site. AI run: Change impact: high for Assembly & Production supervisors (new AI visual inspection of welds and paint routines). Sponsors: Operations Director. Champions: one per site.
UFT-01-07 Compile plan approval pack R: Head of L&D	MP-01.4 Schedule Steering Committee milestones MP-01.5 Compile plan approval pack MP-04.1 Consolidate feeder outputs	Approval pack: 2 objectives, net budget 1,330,000 MAD, 6 priority themes, committee date 15 March 2026.
UFT-01-08 Approve and lock annual L&D plan R: HR Director	MP-01.6 Record Steering Committee decision MP-01.7 Lock and distribute approved plan	Decision: Approve. Justification: aligned with SO-1 and SO-2; budget within envelope. Plan locked as version 1.

E2E-03 · Needs-to-Training Engineering Report & Roadmap

Goal: Produce the Training Engineering Report and the prioritized training roadmap. **Starts when:** Validated skills gap diagnosis, consolidated demands, approved Scope of Work or diagnostic findings available. **Ends when:** Training Engineering Report and prioritized roadmap approved and published.

Task	Steps	What to type
UFT-03-01 Plan diagnostic interviews R: L&D Analyst	MP-03.3 Plan diagnostic interviews	Interview plan: 14 semi-structured interviews (4 MS, 6 MO, 4 OP), 45 minutes each, weeks 10-11.
UFT-03-02 Record interview findings R: L&D Analyst	MP-03.4 Record interview findings	Finding (MO, Assembly & Production): 'Supervisors do not trust MES and digital shop-floor tracking data; they re-enter figures on paper.' AI run: Finding (MO, Assembly & Production): 'Supervisors do not trust AI visual inspection of welds and paint data; they re-enter figures on paper.'
UFT-03-03 Cluster needs into themes R: L&D Analyst	MP-03.5 Cluster needs into training themes	Accept theme 'MES and digital shop-floor tracking for supervisors'; merge two duplicate themes on PLM and digital engineering change; split 'IATF 16949' into awareness and auditor tracks. AI run: Accept theme 'AI visual inspection of welds and paint for supervisors'; merge two duplicate themes on Predictive maintenance of press lines; split 'IATF 16949' into awareness and auditor tracks.
UFT-03-04 Prioritize needs by impact R: L&D Strategist	MP-03.6 Prioritize needs by business impact	MES and digital shop-floor tracking: impact 5, urgency 4. PLM and digital engineering change: impact 4, urgency 3. IATF 16949: impact 4, urgency 5. AI run: AI visual inspection of welds and paint: impact 5, urgency 4. Predictive maintenance of press lines: impact 4, urgency 3. IATF 16949: impact 4, urgency 5.
UFT-03-05 Validate needs register R: Head of L&D	MP-03.7 Validate needs register	Needs register validated: 23 needs, 6 themes. Justification: covers SO-1 and SO-2; sponsor reviewed.
UFT-03-06 Consolidate engineering inputs R: L&D Analyst	MP-04.1 Consolidate feeder outputs MP-04.2 Check input completeness	Inputs complete: Scope of Work, 187 responses, gap matrix, RAG dashboard, SWOT, demands. Missing: none.

Task	Steps	What to type
UFT-03-07 Draft Training Engineering Report R: L&D Strategist	MP-04.3 Generate report draft MP-04.4 Edit and complete report sections	Section 3 'Diagnostic': edit the AI draft, add the interview quote on MES and digital shop-floor tracking, keep the RAG table. AI run: Section 3 'Diagnostic': edit the AI draft, add the interview quote on AI visual inspection of welds and paint, keep the RAG table.
UFT-03-08 Run quality review R: Quality Manager	MP-04.5 Run quality review of report MP-20.5 Run periodic quality review	Quality review: 11/12 checklist items met; fix item 'sources cited for every figure'. Result: pass after correction.
UFT-03-09 Sequence and budget roadmap R: L&D Strategist	MP-04.6 Sequence roadmap initiatives MP-18.1 Allocate budget by theme and site	Roadmap: Q2 MES and digital shop-floor tracking (6 groups); Q3 IATF 16949 (4 groups); Q4 PLM and digital engineering change (3 groups). Total 1,240,000 MAD. AI run: Roadmap: Q2 AI visual inspection of welds and paint (6 groups); Q3 IATF 16949 (4 groups); Q4 Predictive maintenance of press lines (3 groups). Total 1,240,000 MAD.
UFT-03-10 Approve and publish report and roadmap R: Head of L&D	MP-04.7 Submit roadmap for approval MP-04.8 Record roadmap approval MP-04.9 Publish approved report and roadmap MP-01.6 Record Steering Committee decision	Decision: Approve report and roadmap v1. Justification: within budget, linked to SO-1/SO-2. Publish to all stakeholders.

E2E-30 · Prioritization-to-Resource Plan

Goal: Prioritize themes and plan days, groups, trainers, budget. **Starts when:** Consolidated training themes requiring prioritization and resource planning. **Ends when:** Approved prioritized training plan with days per theme, group planning, trainer allocation, and budget.

Task	Steps	What to type
UFT-30-01 Consolidate training themes R: L&D Analyst	MP-49.1 Consolidate training themes	Consolidated list: 9 themes from needs, demands, GPEC and SWOT.
UFT-30-02 Define prioritization criteria R: L&D Strategist	MP-49.2 Define prioritization criteria	Criteria: strategic impact 40%, urgency 30%, number of learners 20%, cost 10%.
UFT-30-03 Prioritize themes R: L&D Strategist	MP-49.3 Prioritize themes	Rank 1 MES and digital shop-floor tracking (score 86); rank 2 IATF 16949 (81); rank 3 PLM and digital engineering change (74). AI run: Rank 1 AI visual inspection of welds and paint (score 86); rank 2 IATF 16949 (81); rank 3 Predictive maintenance of press lines (74).
UFT-30-04 Estimate days per theme R: L&D Planner	MP-49.4 Estimate days per theme	MES and digital shop-floor tracking: 3 days per group; IATF 16949: 2 days; PLM and digital engineering change: 1.5 days. AI run: AI visual inspection of welds and paint: 3 days per group; IATF 16949: 2 days; Predictive maintenance of press lines: 1.5 days.
UFT-30-05 Define groups per theme R: L&D Planner	MP-49.5 Define number of groups per theme MP-49.6 Allocate trainers	MES and digital shop-floor tracking: 6 groups of 12; IATF 16949: 4 groups; PLM and digital engineering change: 3 groups. AI run: AI visual inspection of welds and paint: 6 groups of 12; IATF 16949: 4 groups; Predictive maintenance of press lines: 3 groups.

Task	Steps	What to type
UFT-30-06 Allocate trainers and budget R: Finance Manager	MP-49.7 Estimate plan budget MP-49.8 Sequence delivery MP-49.9 Validate plan with governance	Trainers: 2 internal, vendor A; budget 1,240,000 MAD (within envelope).
UFT-30-07 Publish prioritized training plan R: L&D Leader	MP-49.10 Publish prioritized plan MP-49.11 Track plan execution MP-49.12 Report on resource utilization	Publish RPT-002 Prioritized Training Plan 2026 to all stakeholders.

E2E-22 · Multi-Site Plan-to-Deployment

Goal: Adapt and deploy plans across sites. **Starts when:** Approved roadmap for an organization with several sites or entities. **Ends when:** Site plans adapted, validated and deployed, with deviations escalated.

Task	Steps	What to type
UFT-22-01 Split plan by site R: Head of L&D	MP-40.1 Split plan by site	Split plan into 3 sites: Casablanca 55%, Tanger 30%, Agadir 15%.
UFT-22-02 Adapt site plan to local constraints R: Site L&D Coordinator	MP-40.2 Adapt site plan to local constraints	Tanger: shift constraints → sessions of 4 hours instead of full days.
UFT-22-03 Localize site materials R: Instructional Designer	MP-23.1 Request translation MP-23.3 Validate translation MP-23.6 Review participation equity MP-23.7 Record inclusion actions	Agadir materials translated to AR; validated by the site expert.
UFT-22-04 Validate site plan R: Head of L&D	MP-40.3 Validate site plan	Site plans validated centrally; budget deviation within ±5%.
UFT-22-05 Schedule site sessions R: Training Administrator	MP-07.1 Create training session MP-11.1 Book rooms and equipment	Tanger schedule: 8 sessions, rooms booked, 2 trainers.
UFT-22-06 Deploy site schedule R: Site L&D Coordinator	MP-40.4 Deploy site schedule	Schedules deployed and communicated to site managers.
UFT-22-07 Consolidate site status R: Head of L&D	MP-40.5 Consolidate site status	Status: Casablanca 70%, Tanger 45%, Agadir 20% delivered.
UFT-22-08 Escalate site deviation R: Head of L&D	MP-40.6 Escalate site deviation	Escalate Agadir deviation (-25%) to the HR Director with a recovery plan.

E2E-23 · Regulatory Submission-to-Validation

Goal: Submit and validate training plans with regulatory bodies. **Starts when:** Approved plan requiring external validation or funding (e.g. OFPPT, GIAC-Agro). **Ends when:** Plan validated by the regulatory body and evidence archived.

Task	Steps	What to type
UFT-23-01 Select regulatory template R: Compliance Officer	MP-41.1 Select regulatory template	Template: OFPPT special training contracts (CSF) — plan file.

Task	Steps	What to type
UFT-23-02 Generate submission file R: Compliance Officer	MP-41.2 Generate submission file MP-20.5 Run periodic quality review	Submission file generated: plan, themes, providers, costs; quality check passed.
UFT-23-03 Submit plan to regulatory body R: Compliance Officer	MP-41.3 Submit plan to regulatory body	Submitted to the regional funding committee on 5 March; reference GSF-2026-118.
UFT-23-04 Track submission status R: Compliance Officer	MP-41.4 Track submission status	Status: additional document requested (provider accreditation) — sent on 12 March.
UFT-23-05 Record regulator decision R: Compliance Officer	MP-41.5 Record regulator decision MP-14.1 Register regulatory requirement	Decision: approved with a cap of 520,000 MAD.
UFT-23-06 Submit refund claims R: Finance Manager	MP-18.5 Submit refund claims	Refund claims submitted for 12 delivered actions: 318,000 MAD.
UFT-23-07 Archive submission evidence R: Compliance Officer	MP-41.6 Archive submission evidence MP-18.6 Close budget period	Archive file, decision and claims; retention 10 years.

E2E-16 · Vendor-to-Finance

Goal: Manage vendors from selection to payment. **Starts when:** Training need requiring an external provider. **Ends when:** Vendor selected, order issued and payment approved against attendance.

Task	Steps	What to type
UFT-16-01 Issue request for proposal R: Purchasing Officer	MP-15.1 Issue request for proposal	RFP 'Training on MES and digital shop-floor tracking' sent to 4 vendors, answers due 15 May. AI run: RFP 'Training on AI visual inspection of welds and paint' sent to 4 vendors, answers due 15 May.
UFT-16-02 Score vendor proposals R: Purchasing Officer	MP-15.2 Score vendor proposals	Scores: vendor A 82, vendor B 76, vendor C 64 (price 40%, expertise 40%, references 20%).
UFT-16-03 Register and verify vendor R: Purchasing Officer	MP-15.3 Register vendor record MP-15.4 Verify vendor accreditation	Register vendor A; accreditation OFPPT verified, valid until December.
UFT-16-04 Issue purchase order R: Purchasing Officer	MP-15.5 Issue purchase order MP-18.3 Record committed and actual costs	Purchase order PO-2026-044: 180,000 MAD on budget line 'MES and digital shop-floor tracking'. AI run: Purchase order PO-2026-044: 180,000 MAD on budget line 'AI visual inspection of welds and paint'.
UFT-16-05 Match invoice to order and attendance R: Training Administrator	MP-15.6 Match invoice to order and attendance MP-11.5 Reconcile attendance with invoices	Invoice matched with PO and attendance (3 days × 12 learners): OK.
UFT-16-06 Approve vendor payment R: Finance Manager	MP-15.7 Approve vendor payment MP-18.4 Compare spend against budget	Approve payment 180,000 MAD; vendor performance rating 4/5.

AUTO-E2E-02 · Automotive Critical-Skills-to-Transformation Plan

Goal: Turn critical-skill gaps and digital and AI use cases into a transformation plan.. **Starts when:** Annual plan cycle or technology change in Automotive. **Ends when:** Transformation learning paths approved.

Task	Steps	What to type
UFT-AUTO-E2-01 List critical Assembly & Production skills R: L&D Analyst	MP-02.1 Define competency families and levels MP-03.1 Compute gap matrix	Critical skills: 6 for Assembly & Production, each with target level 3.
UFT-AUTO-E2-02 List digital and AI use cases R: L&D Strategist	MP-03.3 Plan diagnostic interviews	Use cases: MES and digital shop-floor tracking; PLM and digital engineering change; Supplier portal and EDI. AI run: Use cases: AI visual inspection of welds and paint; Predictive maintenance of press lines; Generative AI for 8D problem solving.
UFT-AUTO-E2-03 Forecast impacted roles R: Performance Analyst	MP-03.5 Cluster needs into training themes MP-28.3 Forecast skill gaps	Impacted roles: supervisors (high), operators (medium); accept the AI forecast.
UFT-AUTO-E2-04 Approve transformation paths R: Instructional Designer	MP-05.2 Define learning path and modules MP-05.7 Approve design document	Approve 2 transformation paths: 'MES and digital shop-floor tracking for supervisors', 'PLM and digital engineering change for operators'. AI run: Approve 2 transformation paths: 'AI visual inspection of welds and paint for supervisors', 'Predictive maintenance of press lines for operators'.

SME-E2E-02 · SME Funding-to-Refund

Goal: Secure funding and recover the refunds of the plan.. **Starts when:** Short plan approved. **Ends when:** Refund received and recorded.

Task	Steps	What to type
UFT-SME2-01 Select eligible themes R: L&D Analyst	SME-MP-02.1 Select eligible themes	Eligible themes: MES and digital shop-floor tracking and IATF 16949 (funding rules met). AI run: Eligible themes: AI visual inspection of welds and paint and IATF 16949 (funding rules met).
UFT-SME2-02 Build the funding file R: Finance Manager	SME-MP-02.2 Build funding file MP-41.2 Generate submission file	Funding file: plan, quotes, provider accreditation, attendance model.
UFT-SME2-03 Submit the refund claim R: Finance Manager	SME-MP-02.3 Submit refund claim MP-18.5 Submit refund claims	Refund claim submitted: 28,000 MAD with signed attendance sheets.
UFT-SME2-04 Record the refund R: Finance Manager	SME-MP-02.4 Track refund payment	Refund received: 28,000 MAD on 20 November; file closed.

7.5 Design & delivery — gate G4

E2E-04 · Roadmap-to-Curriculum Design

Goal: Convert roadmap into curriculum maps, learning paths, design documents. **Starts when:** Approved Training Engineering Report and roadmap published. **Ends when:** Approved curriculum maps, learning paths and design documents.

Task	Steps	What to type
UFT-04-01 Create curriculum map R: Instructional Designer	MP-05.1 Create curriculum map from roadmap	Curriculum map 'MES and digital shop-floor tracking': 3 learning paths (operators, supervisors, managers), 9 modules. AI run: Curriculum map 'AI visual inspection of welds and paint': 3 learning paths (operators, supervisors, managers), 9 modules.
UFT-04-02 Define learning paths and modules R: Instructional Designer	MP-05.2 Define learning path and modules	Path 'Supervisors — MES and digital shop-floor tracking': 4 modules, 3 days blended (1 day e-learning, 2 days workshop). AI run: Path 'Supervisors — AI visual inspection of welds and paint': 4 modules, 3 days blended (1 day e-learning, 2 days workshop).
UFT-04-03 Write learning objectives R: Instructional Designer	MP-05.3 Write learning objectives per module	Objective M1: 'By the end, the supervisor reads the MES and digital shop-floor tracking dashboard and decides the shift action in 5 minutes.' AI run: Objective M1: 'By the end, the supervisor reads the AI visual inspection of welds and paint dashboard and decides the shift action in 5 minutes.'
UFT-04-04 Propose module structure R: Instructional Designer	MP-05.4 Propose module structure	Accept the proposed structure (intro, demo, practice, quiz); replace the quiz by a live case from Assembly & Production.
UFT-04-05 Set assessment strategy R: Instructional Designer	MP-05.5 Set assessment strategy	Assessment: pre/post test (Level 2) and manager observation after 30 days (Level 3).
UFT-04-06 Develop and tag content R: Content Developer	MP-06.1 Upload content assets MP-06.2 Validate package format MP-06.5 Tag content with competencies	Upload 'M1_MES and digital shop-floor tracking.pptx' and 'M1_video.mp4'; tag competency 'MES and digital shop-floor tracking' level 3. AI run: Upload 'M1_AI visual inspection of welds and paint.pptx' and 'M1_video.mp4'; tag competency 'AI visual inspection of welds and paint' level 3.
UFT-04-07 Localize and check accessibility R: Instructional Designer	MP-23.1 Request translation MP-23.2 Draft machine translation MP-23.3 Validate translation MP-23.4 Run accessibility check MP-23.5 Fix accessibility issues	Request FR and AR versions; validate the AI draft translation; accessibility check: 0 blocking issues.
UFT-04-08 Approve design document R: Head of L&D	MP-05.6 Review design with subject matter expert MP-05.7 Approve design document	Decision: design approved. Comment: SME review done on 12 May; ready for delivery.

E2E-05 · Design-to-Delivery

Goal: Deliver training across all modalities. **Starts when:** Approved design document and prioritized training plan.

Ends when: Training delivered across all modalities with attendance and completion recorded.

Task	Steps	What to type
UFT-05-01 Publish content to catalog R: Content Developer	MP-06.3 Route content for expert review MP-06.4 Record review decision MP-06.6 Publish content to catalog	Publish module 'M1 MES and digital shop-floor tracking' to the catalog; audience: supervisors; languages EN/FR/AR. AI run: Publish module 'M1 AI visual inspection of welds and paint' to the catalog; audience: supervisors; languages EN/FR/AR.
UFT-05-02 Book logistics R: Training Administrator	MP-11.1 Book rooms and equipment MP-11.2 Manage trainer calendars	Room 'Training A' (20 seats) 3-5 June; projector; trainer calendar blocked.

Task	Steps	What to type
UFT-05-03 Schedule sessions R: Training Administrator	MP-07.1 Create training session MP-07.2 Check scheduling conflicts	Session S-01 'MES and digital shop-floor tracking — supervisors', 3-5 June, 12 seats, no conflict reported. AI run: Session S-01 'AI visual inspection of welds and paint — supervisors', 3-5 June, 12 seats, no conflict reported.
UFT-05-04 Enroll learners and send convocations R: Training Administrator	MP-07.3 Enroll learners into session MP-07.4 Send convocations MP-17.1 Provision users via SSO	Enroll 12 supervisors; convocations sent by e-mail and SMS in each learner's language.
UFT-05-05 Push microlearning capsules R: Instructional Designer	MP-25.1 Author microlearning capsule MP-25.2 Generate capsule draft from source MP-25.3 Push capsule to collaboration channel MP-25.4 Consume capsule on mobile MP-25.5 Track capsule completion	Capsule '5-minute PLM and digital engineering change check' pushed to the Teams channel of Assembly & Production; 48 views in week 1. AI run: Capsule '5-minute Predictive maintenance of press lines check' pushed to the Teams channel of Assembly & Production; 48 views in week 1.
UFT-05-06 Run immersive simulations R: Trainer	MP-30.1 Define simulation scenario MP-30.2 Configure simulation scoring MP-30.3 Launch simulation session MP-30.4 Capture simulation performance MP-30.5 Debrief learner MP-30.6 Record simulation evidence	Simulation 'Assembly & Production incident': score 78/100; debrief notes recorded; evidence saved.
UFT-05-07 Record attendance R: Trainer	MP-07.5 Record attendance	Attendance S-01: 11 present, 1 absent (justified). Signature sheet attached.
UFT-05-08 Close sessions R: Training Administrator	MP-07.6 Close session and record completion	Close S-01: 11 completions recorded; certificate issued to each participant.
UFT-05-09 Reconcile and archive period R: Training Administrator	MP-11.5 Reconcile attendance with invoices MP-11.6 Archive period records MP-11.3 Import external training records MP-11.4 Correct training record with justification	Reconcile invoice INV-2026-118 (3 days × 12 learners) with attendance; archive period Q2.

E2E-06 · Learner-Journey-to-Engagement

Goal: Deliver personalized, engaging learning experience. **Starts when:** Learner enrolled in a learning path or session. **Ends when:** Personalized learning journey completed with engagement measured.

Task	Steps	What to type
UFT-06-01 Generate personal learning plan R: L&D Analyst	MP-08.1 Generate personal learning plan	Personal plan generated for each learner: 3 items on MES and digital shop-floor tracking, 1 capsule on PLM and digital engineering change. AI run: Personal plan generated for each learner: 3 items on AI visual inspection of welds and paint, 1 capsule on Predictive maintenance of press lines.
UFT-06-02 Recommend learning items R: Learner	MP-08.2 Recommend learning items MP-24.1 Enable personalization per scope	Accept 2 recommendations, reject 1 ('already mastered'). The outcome is logged.

Task	Steps	What to type
UFT-06-03 Adapt path to performance R: Instructional Designer	MP-24.2 Set adaptation rules MP-24.3 Adapt path to learner performance MP-24.4 Record learner response to adaptation	Rule: if the quiz score < 60%, add the remedial capsule 'MES and digital shop-floor tracking basics'. AI run: Rule: if the quiz score < 60%, add the remedial capsule 'AI visual inspection of welds and paint basics'.
UFT-06-04 Animate social learning R: Knowledge Manager	MP-26.1 Create learning cohort group MP-26.2 Invite group members MP-26.3 Post question or answer MP-26.4 Endorse expert answer MP-26.5 Flag inappropriate content MP-26.6 Resolve moderation flag	Create cohort 'MES and digital shop-floor tracking supervisors 2026' and invite 12 members; first question posted. AI run: Create cohort 'AI visual inspection of welds and paint supervisors 2026' and invite 12 members; first question posted.
UFT-06-05 Run gamification R: Instructional Designer	MP-27.1 Define points and badge rules MP-27.2 Configure leaderboard scope MP-27.3 Award points on completion MP-27.4 Unlock badge MP-27.6 Adjust gamification rules	Badge 'MES and digital shop-floor tracking Practitioner' for completing 3 modules; 10 points per capsule. AI run: Badge 'AI visual inspection of welds and paint Practitioner' for completing 3 modules; 10 points per capsule.
UFT-06-06 Match and run coaching R: L&D Business Partner	MP-21.1 Request coaching MP-21.2 Match coach to learner MP-21.3 Schedule coaching sessions MP-21.4 Log coaching session notes MP-21.5 Evaluate coaching outcomes MP-21.6 Close coaching engagement	Match coach 'Senior Assembly & Production supervisor' to 3 learners; 4 sessions of 1 hour.
UFT-06-07 Collect learner feedback R: Learner	MP-08.3 Enroll in recommended item MP-08.4 Submit learning feedback	Feedback: 4.4/5; comment 'more real cases from Assembly & Production'.
UFT-06-08 Monitor engagement and nudge R: L&D Analyst	MP-08.5 Monitor engagement indicators MP-08.6 Trigger re-engagement nudge MP-24.5 Review recommendation acceptance MP-27.5 Review engagement uplift MP-24.6 Tune personalization settings MP-28.4 Predict learner drop-out risk MP-28.5 Review predictions with L&D MP-28.6 Create preventive action	Engagement 81%; nudge sent to 9 inactive learners; drop-out risk high for 2 learners.

E2E-13 · Content-Curate-to-Retire

Goal: Publish, maintain, retire content. **Starts when:** New content published or content past its review date. **Ends when:** Catalog curated, maintained and outdated content retired.

Task	Steps	What to type
UFT-13-01 Aggregate provider catalogs R: Content Curator	MP-29.1 Aggregate provider catalogs	Aggregate 2 provider catalogs (LinkedIn Learning, Coursera): 1,240 items imported.
UFT-13-02 Recommend curated items R: Content Curator	MP-29.2 Recommend curated items	Keep the 15 top-ranked items on MES and digital shop-floor tracking; reject 3 items older than 3 years. AI run: Keep the 15 top-ranked items on AI visual inspection of welds and paint; reject 3 items older than 3 years.

Task	Steps	What to type
UFT-13-03 Approve and organize collections R: Content Curator	MP-29.3 Approve curated item MP-29.4 Organize curated collection	Collection 'MES and digital shop-floor tracking starter kit': 8 items, audience supervisors, review date in 12 months. AI run: Collection 'AI visual inspection of welds and paint starter kit': 8 items, audience supervisors, review date in 12 months.
UFT-13-04 Review peer content R: Subject Matter Expert	MP-33.1 Submit user-generated content MP-33.2 Check content against policy MP-33.3 Peer review content	Peer video 'How we use PLM and digital engineering change on shift' reviewed by an expert: approved with 1 correction. AI run: Peer video 'How we use Predictive maintenance of press lines on shift' reviewed by an expert: approved with 1 correction.
UFT-13-05 Promote and rate content R: Knowledge Manager	MP-33.5 Send approved content to curation MP-33.6 Rate user-generated item	Send approved peer content to curation; average learner rating 4.5/5.
UFT-13-06 Flag content past review date R: Content Curator	MP-29.5 Flag content past review date	14 items past review date flagged; owners notified.
UFT-13-07 Retire outdated content R: Content Curator	MP-29.6 Retire outdated content MP-25.6 Retire low-value capsule	Retire 6 outdated items and 2 low-value capsules; library health 92%.

E2E-14 · Extended-Enterprise-Training

Goal: Certify partners and train customers. **Starts when:** Partner, reseller or customer training program launched.

Ends when: External learners trained, paid and certified.

Task	Steps	What to type
UFT-14-01 Create external sub-portal R: Extended Enterprise Manager	MP-22.1 Create external sub-portal	Sub-portal 'Partners Academy — Tanger Auto Parts' created for distributors and installers.
UFT-14-02 Configure catalog and pricing R: Extended Enterprise Manager	MP-22.2 Configure external catalog and pricing MP-18.1 Allocate budget by theme and site	Catalog: 'IATF 16949 for partners' 1,200 MAD; 'MES and digital shop-floor tracking certification' 2,400 MAD. AI run: Catalog: 'IATF 16949 for partners' 1,200 MAD; 'AI visual inspection of welds and paint certification' 2,400 MAD.
UFT-14-03 Process payment and enroll R: Extended Enterprise Manager	MP-22.3 Process online payment MP-22.4 Enroll external learner	18 online payments processed; 18 external learners enrolled.
UFT-14-04 Deliver external sessions R: Training Administrator	MP-07.1 Create training session MP-07.5 Record attendance	Session P-01 (virtual), 18 invited, 16 present.
UFT-14-05 Track external completion R: Extended Enterprise Manager	MP-22.5 Track external completion	Completion: 15 of 16 passed the final quiz.
UFT-14-06 Issue partner certification R: Extended Enterprise Manager	MP-22.6 Issue partner certification MP-14.4 Issue certificate on completion	Issue 15 partner certificates valid 2 years.

Task	Steps	What to type
UFT-14-07 Reconcile external revenue R: Finance Manager	MP-18.3 Record committed and actual costs MP-18.4 Compare spend against budget	Revenue 43,200 MAD reconciled with the ERP; 0 unpaid.

SME-E2E-03 · SME Upskill-to-Adoption

Goal: Make sure new digital and AI skills are used at work.. **Starts when:** Funded plan launched. **Ends when:** Adoption confirmed and owner-manager coached.

Task	Steps	What to type
UFT-SME3-01 Assign microlearning capsules R: Training Administrator	SME-MP-03.1 Assign microlearning capsules MP-25.3 Push capsule to collaboration channel	Assign 4 capsules 'MES and digital shop-floor tracking in 10 minutes' to each employee. AI run: Assign 4 capsules 'AI visual inspection of welds and paint in 10 minutes' to each employee.
UFT-SME3-02 Coach on the job R: Trainer	SME-MP-03.2 Coach employees on the job	On-the-job coaching: 2 hours per team leader per week for 4 weeks.
UFT-SME3-03 Measure adoption R: L&D Analyst	SME-MP-03.3 Measure tool usage	Adoption: 9 of 12 employees use the new tool every day.
UFT-SME3-04 Coach the owner-manager R: Consultant PM	SME-MP-04.1 Hold monthly coaching session SME-MP-04.2 Update skills dashboard	Monthly coaching with the owner-manager; skills dashboard updated.

7.6 Evaluation, compliance & impact — gate G5

E2E-07 · Assessment-to-Evaluation

Goal: Measure training effectiveness and skill progression. **Starts when:** Training session or path completed. **Ends when:** Effectiveness measured on Kirkpatrick levels 1-3 and skill progression computed.

Task	Steps	What to type
UFT-07-01 Create assessment instrument R: Instructional Designer	MP-09.1 Create assessment instrument	Instrument 'Test MES and digital shop-floor tracking M1': 15 questions, pass mark 70%. AI run: Instrument 'Test AI visual inspection of welds and paint M1': 15 questions, pass mark 70%.
UFT-07-02 Draft question bank R: Instructional Designer	MP-09.2 Generate question bank draft	Keep 12 AI-drafted questions, rewrite 3 with Assembly & Production vocabulary; validate each one.
UFT-07-03 Collect reaction survey (Level 1) R: L&D Analyst	MP-09.3 Collect reaction survey (Level 1)	Reaction survey S-01: 11 responses, satisfaction 4.3/5.
UFT-07-04 Record learning results (Level 2) R: Trainer	MP-09.4 Record learning results (Level 2)	Level 2: average pre-test 48%, post-test 81% (+33 points).

Task	Steps	What to type
UFT-07-05 Record on-the-job observation (Level 3) R: Manager	MP-09.5 Record on-the-job observation (Level 3)	Level 3 (day 30): 9 of 11 supervisors apply the MES and digital shop-floor tracking routine daily. AI run: Level 3 (day 30): 9 of 11 supervisors apply the AI visual inspection of welds and paint routine daily.
UFT-07-06 Compute skill progression R: L&D Analyst	MP-09.6 Compute skill progression MP-10.3 Refresh KPI computation	Skill progression: MES and digital shop-floor tracking from 1.8 to 2.7 (target 3). AI run: Skill progression: AI visual inspection of welds and paint from 1.8 to 2.7 (target 3).
UFT-07-07 Review evaluation results R: L&D Analyst	MP-09.7 Review evaluation results MP-20.5 Run periodic quality review	Review: module M3 below 70% pass rate → improvement action assigned to the designer.
UFT-07-08 Publish evaluation report R: L&D Analyst	MP-10.4 Export report MP-10.6 Share insight with stakeholders MP-10.2 Configure dashboard widgets	Export RPT-016 Kirkpatrick report (PDF) and share with the Steering Committee.

E2E-08 · Learning-to-ROI

Goal: Validate ROI and business impact. **Starts when:** Evaluation results available for a theme selected for an ROI study. **Ends when:** Phillips ROI validated with finance and business impact report published.

Task	Steps	What to type
UFT-08-01 Select theme for ROI study R: Performance Analyst	MP-32.1 Select theme for ROI study	ROI study on theme 'MES and digital shop-floor tracking' — population: 36 supervisors, 3 sites. AI run: ROI study on theme 'AI visual inspection of welds and paint' — population: 36 supervisors, 3 sites.
UFT-08-02 Define business indicators R: Performance Analyst	MP-32.2 Define business indicators MP-10.1 Define KPI set per audience	Indicators: rework rate, downtime minutes per shift, data re-entry hours.
UFT-08-03 Collect cost data R: Finance Manager	MP-18.3 Record committed and actual costs MP-18.4 Compare spend against budget	Costs: design 60,000 MAD; delivery 180,000 MAD; participants' time 95,000 MAD.
UFT-08-04 Isolate training effect R: Performance Analyst	MP-32.3 Isolate training effect MP-09.6 Compute skill progression	Control group: site B (not trained). Isolated benefit: 410,000 MAD per year.
UFT-08-05 Compute Phillips ROI R: Performance Analyst	MP-32.4 Compute Phillips ROI	$ROI = (410,000 - 335,000) / 335,000 = 22\%$; benefit-cost ratio 1.22.
UFT-08-06 Review ROI with finance R: Finance Manager	MP-32.5 Review ROI with finance	Finance review: assumptions accepted; downtime valued at 180 MAD per minute.
UFT-08-07 Publish business impact report R: Head of L&D	MP-32.6 Publish business impact report MP-10.4 Export report MP-10.5 Query data via AI Assistant	Publish RPT-012 ROI & Business Impact Report to executive leadership.

E2E-09 · Compliance-to-Certification

Goal: Ensure compliant workforce with valid certifications. **Starts when:** New regulatory requirement or certification nearing expiry. **Ends when:** Compliant workforce with valid certifications and an audit extract available.

Task	Steps	What to type
UFT-09-01 Register regulatory requirement R: Compliance Officer	MP-14.1 Register regulatory requirement	Requirement 'IATF 16949 awareness', every 24 months, source: IATF 16949 clause on competence.
UFT-09-02 Assign mandatory training R: Compliance Officer	MP-14.2 Assign mandatory training by position	Assign to positions: Assembly & Production operator, Assembly & Production supervisor, quality inspector.
UFT-09-03 Deliver mandatory sessions R: Training Administrator	MP-07.3 Enroll learners into session MP-07.5 Record attendance	Enroll 24 employees in session 'IATF 16949 awareness'; attendance recorded.
UFT-09-04 Assess and certify R: Trainer	MP-09.4 Record learning results (Level 2) MP-14.4 Issue certificate on completion	Result 86%; certificate 'IATF 16949 awareness' issued, valid until 2026+2.
UFT-09-05 Compute certification validity R: Compliance Officer	MP-14.3 Compute certification validity	Validity: 212 valid, 9 expire within 60 days, 3 expired.
UFT-09-06 Manage renewals R: Compliance Officer	MP-14.5 Launch renewal enrollment MP-14.6 Confirm renewal completion	Launch renewal for the 12 employees; confirm 10 completions, 2 rescheduled.
UFT-09-07 Produce compliance audit extract R: Compliance Officer	MP-14.7 Produce compliance audit extract MP-10.4 Export report	Export compliance audit extract for IATF 16949 (XLSX) for the external auditor.

AUTO-E2E-01 · Automotive Compliance-to-Certification Readiness

Goal: Keep Automotive regulated roles certified against IATF 16949.. **Starts when:** New IATF 16949 requirement or certification expiry. **Ends when:** Sector compliance extract issued with every critical role certified.

Task	Steps	What to type
UFT-AUTO-E1-01 Register IATF 16949 obligations R: Compliance Officer	MP-01.1 Record corporate strategic objectives MP-14.1 Register regulatory requirement	Obligation 'IATF 16949 training', every 12 months, owner Compliance Officer.
UFT-AUTO-E1-02 Link obligations to positions R: HR Business Partner	MP-01.2 Link objectives to functions and sites MP-14.2 Assign mandatory training by position	Linked to 5 Assembly & Production positions (38 employees).
UFT-AUTO-E1-03 Track certification validity R: Compliance Officer	MP-02.1 Define competency families and levels MP-14.3 Compute certification validity	Validity: 33 valid, 5 expire within 60 days.
UFT-AUTO-E1-04 Issue sector compliance extract R: Compliance Officer	MP-02.2 Set target levels per position MP-14.7 Produce compliance audit extract	Extract issued for the IATF 16949 audit on 15 October.

7.7 Talent, knowledge & continuous improvement — gate G6

E2E-10 · Talent-to-Mobility

Goal: Enable internal mobility and career progression. **Starts when:** Internal opening published or annual career review. **Ends when:** Internal move decided with a reskilling plan assigned.

Task	Steps	What to type
UFT-10-01 Model career paths R: HR Director	MP-13.1 Model career path MP-13.2 Link path steps to competency targets	Career path: Assembly & Production operator → team leader → supervisor, with competency targets per step.
UFT-10-02 Publish internal opening R: HR Business Partner	MP-31.1 Publish internal opening MP-31.2 Define required skills	Opening 'Assembly & Production team leader', required skills: MES and digital shop-floor tracking level 3, leadership level 2. AI run: Opening 'Assembly & Production team leader', required skills: AI visual inspection of welds and paint level 3, leadership level 2.
UFT-10-03 Match employees to opening R: HR Business Partner	MP-31.3 Match employees to opening MP-02.7 Validate skills inventory	Review 6 AI matches; keep 4 candidates with match score above 75%.
UFT-10-04 Apply to internal opening R: Employee	MP-31.4 Apply to internal opening	Application with motivation note and consent of the current manager.
UFT-10-05 Shortlist candidates R: Hiring Manager	MP-31.5 Shortlist candidates	Shortlist: 2 candidates; interviews on 20 and 21 June.
UFT-10-06 Plan individual development R: Manager	MP-13.3 Create individual development plan MP-13.4 Suggest development actions MP-42.3 Build leadership development plan MP-42.4 Suggest leadership development actions	Development plan: 2 modules MES and digital shop-floor tracking, 1 leadership workshop, 3 months mentoring. AI run: Development plan: 2 modules AI visual inspection of welds and paint, 1 leadership workshop, 3 months mentoring.
UFT-10-07 Assign reskilling plan R: HR Business Partner	MP-31.6 Assign reskilling plan MP-08.1 Generate personal learning plan	Assign reskilling path 'MES and digital shop-floor tracking for team leaders' to the selected candidate. AI run: Assign reskilling path 'AI visual inspection of welds and paint for team leaders' to the selected candidate.
UFT-10-08 Review career and succession R: HR Director	MP-13.5 Run career review MP-13.6 Update succession readiness MP-42.5 Review leadership pipeline MP-42.6 Reassess leadership maturity	Succession readiness updated: 2 ready now, 3 ready within 12 months.

E2E-11 · Onboarding-to-Productivity

Goal: Accelerate time-to-productivity. **Starts when:** New hire or internal mover confirmed. **Ends when:** Employee productive within target time and onboarding closed.

Task	Steps	What to type
UFT-11-01 Create onboarding record R: Hiring Manager	MP-35.1 Create onboarding record	Onboarding record for the new Assembly & Production technician, start date 1 July, buddy assigned.

Task	Steps	What to type
UFT-11-02 Generate 30-60-90 day path R: HR Business Partner	MP-35.2 Generate 30-60-90 day path MP-08.1 Generate personal learning plan	30-60-90 path: day 30 safety and IATF 16949; day 60 MES and digital shop-floor tracking; day 90 autonomy on shift. AI run: 30-60-90 path: day 30 safety and IATF 16949; day 60 AI visual inspection of welds and paint; day 90 autonomy on shift.
UFT-11-03 Enroll in onboarding sessions R: Training Administrator	MP-07.3 Enroll learners into session MP-07.4 Send convocations	Enroll in the induction session of 2 July; convocation sent.
UFT-11-04 Complete onboarding tasks R: Employee	MP-35.3 Complete onboarding tasks	Tasks done: badge, IT account, safety tour, meeting with the team.
UFT-11-05 Hold milestone check-ins R: Hiring Manager	MP-35.4 Hold milestone check-in MP-21.3 Schedule coaching sessions	Day-30 check-in: on track; coaching needed on MES and digital shop-floor tracking data entry. AI run: Day-30 check-in: on track; coaching needed on AI visual inspection of welds and paint data entry.
UFT-11-06 Assess time to productivity R: Hiring Manager	MP-35.5 Assess time to productivity	Time to productivity: 74 days (target 90).
UFT-11-07 Close onboarding R: HR Business Partner	MP-35.6 Close onboarding MP-13.3 Create individual development plan	Close onboarding; link the individual development plan for year 1.

E2E-12 · Knowledge-Capture-to-Transfer

Goal: Capture and transfer institutional knowledge. **Starts when:** Critical expert identified as leaving, retiring or holding at-risk knowledge. **Ends when:** Knowledge captured, published and transferred to a validated successor.

Task	Steps	What to type
UFT-12-01 Identify critical experts R: HR Business Partner	MP-34.1 Identify critical experts	Critical expert: senior Assembly & Production engineer retiring in 8 months; knowledge risk: high.
UFT-12-02 Plan capture sessions R: Knowledge Manager	MP-34.2 Plan capture sessions	Capture plan: 4 sessions of 90 minutes on troubleshooting and IATF 16949 practices.
UFT-12-03 Record expert interview R: Knowledge Manager	MP-34.3 Record expert interview	Interview 1 recorded (82 minutes); transcript attached.
UFT-12-04 Structure knowledge R: Knowledge Manager	MP-34.4 Structure knowledge from transcript	Accept the AI structure: 5 failure modes, 12 checks, 3 decision rules; correct 2 technical terms.
UFT-12-05 Publish knowledge article R: Knowledge Manager	MP-12.1 Publish knowledge article MP-12.2 Index article for retrieval MP-33.4 Approve publication	Publish article 'Troubleshooting guide — Assembly & Production' in EN/FR/AR; indexed for search.
UFT-12-06 Assign successor learning path R: Manager	MP-34.5 Assign successor learning path MP-06.6 Publish content to catalog	Assign the successor path: article + 3 shadowing sessions with the expert.
UFT-12-07 Validate transfer completion R: Subject Matter Expert	MP-34.6 Validate transfer completion	Transfer validated: successor solved 4 of 5 test cases alone.

E2E-31 · Engagement-to-Roadmap

Goal: Define post-engagement roadmap and continuous improvement. **Starts when:** Closure of the current training engineering engagement (E2E-19). **Ends when:** Approved post-engagement roadmap with future missions and continuous improvement plan.

Task	Steps	What to type
UFT-31-01 Consolidate engagement findings R: Consultant PM	MP-50.1 Consolidate engagement findings	Findings: 6 deliverables, 3 lessons learned, 2 open topics (IS, org design).
UFT-31-02 Define future perspectives R: Consultant PM	MP-50.2 Define future perspectives	Perspectives: Supplier portal and EDI programme, second wave for OP level. AI run: Perspectives: Generative AI for 8D problem solving programme, second wave for OP level.
UFT-31-03 Plan One-to-One coaching R: L&D Strategist	MP-50.3 Plan One-to-One coaching	One-to-One coaching: 6 managers, 6 sessions each over 6 months.
UFT-31-04 Plan organizational optimization R: Org Design Consultant	MP-50.4 Plan organizational optimization	Organizational optimization: merge 2 planning cells; update 11 descriptions.
UFT-31-05 Plan IS rehabilitation R: IT Architect	MP-50.5 Plan IS rehabilitation	IS rehabilitation: connect HRIS and training platform; retire 2 spreadsheets.
UFT-31-06 Define KPIs and dashboards R: Performance Analyst	MP-50.6 Define KPIs and dashboards	KPIs: training coverage, time to competency, ROI per theme; monthly dashboard.
UFT-31-07 Prioritize future missions R: Consultant PM	MP-50.7 Prioritize future missions MP-50.8 Validate roadmap with leadership	Priority missions: 1 IS rehabilitation, 2 coaching, 3 org optimization.
UFT-31-08 Publish roadmap R: Consultant PM	MP-50.9 Publish post-engagement roadmap MP-50.10 Track roadmap execution MP-50.11 Improve roadmap continuously MP-50.12 Report on roadmap progress	Publish RPT-010 Post-Engagement Roadmap to the executive committee.

8. SMEs in AEC (architecture, engineering, construction)

This part follows Souss BTP Solutions, a SME in the AEC & Construction sector (42 employees, Agadir, member of Souss-Massa SME Network). Sign in as headld@soussbtpsolutions.ma. The same steps apply to any organization of this type: replace the names, figures and themes with your own.

Item	Digital skills run	AI skills run
Project	Digital Skills Full Run 2026 — Souss BTP Solutions	AI Skills Full Run 2026 — Souss BTP Solutions
Mode and track	SME · SME-T2	SME · SME-T2
Processes and tasks	38 processes · 277 tasks	38 processes · 277 tasks

Phase	Gate	End-to-end processes
Enablers (run across all phases)	—	E2E-15, E2E-17, E2E-18
Scope & evidence	G1	E2E-32, E2E-33, E2E-19, E2E-24, SME-E2E-01
Diagnosis	G2	E2E-20, E2E-25, E2E-26, E2E-27, E2E-28, E2E-29, E2E-02, E2E-21
Training Engineering Report & plan	G3	E2E-01, E2E-03, E2E-30, E2E-22, E2E-23, E2E-16, AEC-E2E-02, SME-E2E-02
Design & delivery	G4	E2E-04, E2E-05, E2E-06, E2E-13, E2E-14, SME-E2E-03
Evaluation, compliance & impact	G5	E2E-07, E2E-08, E2E-09, AEC-E2E-01
Talent, knowledge & continuous improvement	G6	E2E-10, E2E-11, E2E-12, E2E-31

8.1 Enablers (run across all phases)

E2E-15 · Data-AI-Integration

Goal: Govern data, AI, integrations. **Starts when:** New integration, data source or AI use case to govern. **Ends when:** Integrations, data and AI governed with health, retention and usage reviewed.

Task	Steps	What to type
UFT-15-01 Register external integration R: Platform Administrator	MP-16.1 Register external integration	Register integration 'HRIS — Workday' (INT-HR-01); credential reference stored encrypted.
UFT-15-02 Map fields and check health R: IT Architect	MP-16.2 Map integration fields MP-16.3 Check integration health	Map fields: employee_id → matricule; position → poste. Health check: success.
UFT-15-03 Run HRIS synchronisation R: IT Architect	MP-16.4 Run HRIS synchronisation MP-16.5 Review synchronisation rejections	Sync run: 1,204 records updated, 3 rejected (missing position) — corrected.
UFT-15-04 Set data retention rule R: Data Protection Officer	MP-16.6 Set data retention rule	Retention: questionnaire responses 3 years; training records 10 years.

Task	Steps	What to type
UFT-15-05 Maintain AI use case register R: Platform Administrator	MP-16.7 Maintain AI use case register	Add custom use case 'Shift-report summarizer' (Assistive), version 1.
UFT-15-06 Set AI activation per scope R: Platform Administrator	MP-16.8 Set AI activation per scope MP-24.1 Enable personalization per scope	Activate AIUC-35 and AIUC-36 for the organization; override Off for pilot project B.
UFT-15-07 Review AI usage log R: IT Architect	MP-16.9 Review AI usage log MP-28.2 Validate dataset quality	Usage review: 412 suggestions — 71% accepted, 20% edited, 9% rejected.

E2E-17 · Change-to-Adoption

Goal: Drive sustained adoption and culture change. **Starts when:** Approved plan or new platform capability requiring adoption. **Ends when:** Sustained adoption reached with low-adoption groups reinforced.

Task	Steps	What to type
UFT-17-01 Assess change impact R: Change Manager	MP-19.1 Assess change impact	Impact: Site Works & Project Delivery supervisors high, operators medium, support functions low.
UFT-17-02 Build adoption plan R: Change Manager	MP-19.2 Build adoption plan	Adoption plan: sponsor message, 6 champions, weekly 15-minute huddles for 8 weeks.
UFT-17-03 Launch communication campaign R: Change Manager	MP-19.3 Launch communication campaign	Campaign 'BIM modelling and ISO 19650 workflows — why it matters' on e-mail, intranet and screens. AI run: Campaign 'AI clash detection and model checking — why it matters' on e-mail, intranet and screens.
UFT-17-04 Open community space R: Knowledge Manager	MP-12.3 Create community space MP-12.4 Moderate community posts MP-26.1 Create learning cohort group	Community space 'BIM modelling and ISO 19650 workflows Q&A' opened; moderation rules published. AI run: Community space 'AI clash detection and model checking Q&A' opened; moderation rules published.
UFT-17-05 Track adoption usage R: L&D Analyst	MP-19.4 Track adoption usage MP-08.5 Monitor engagement indicators	Weekly active users: 64% of the target population.
UFT-17-06 Identify low-adoption groups R: Change Manager	MP-19.5 Identify low-adoption groups	Low adoption confirmed for night shift (31%); one group rejected as false positive.
UFT-17-07 Run reinforcement actions R: Change Manager	MP-19.6 Run reinforcement actions MP-08.6 Trigger re-engagement nudge	Reinforcement: night-shift coaching sessions; adoption reached 58% after 4 weeks.

E2E-18 · Quality-Risk-Improvement

Goal: Improve processes and mitigate risk. **Starts when:** Risk logged, periodic quality review due or control test scheduled. **Ends when:** Risks mitigated, actions evaluated by a different person, controls rated.

Task	Steps	What to type
UFT-18-01 Log risk or opportunity R: Quality Manager	MP-20.1 Log risk or opportunity	Risk 'Trainers unavailable in Q3': likelihood 3, impact 4, score 12.

Task	Steps	What to type
UFT-18-02 Assign mitigation action R: Quality Manager	MP-20.2 Assign mitigation action	Action: contract a second vendor; owner Purchasing Officer; evaluator Quality Manager.
UFT-18-03 Execute improvement action R: Action Owner	MP-20.3 Execute improvement action	Action done: framework contract signed with vendor B; evidence attached.
UFT-18-04 Evaluate action effectiveness R: Action Evaluator	MP-20.4 Evaluate action effectiveness	Verdict: effective. The evaluator is a different user from the owner.
UFT-18-05 Review access and security R: IT Architect	MP-17.4 Review access violation log MP-17.6 Enforce login rate limit MP-17.2 Assign roles to user MP-17.3 Edit permission matrix MP-17.5 Issue signed session token	Access review: 2 dormant accounts disabled; 0 cross-tenant attempts.
UFT-18-06 Run periodic quality review R: Quality Manager	MP-20.5 Run periodic quality review MP-09.7 Review evaluation results	Quality review minutes: 3 KPIs red, 2 actions opened, next review in 30 days.
UFT-18-07 Update control effectiveness R: Quality Manager	MP-20.6 Update control effectiveness rating	Control CTRL-002 effectiveness: Effective; CTRL-031: Partially effective.

8.2 Scope & evidence — gate G1

E2E-32 · Scope-of-Work-to-Engineering-Plan

Goal: Define and approve the structured scope of work and stakeholder register. **Starts when:** New training engineering engagement, annual plan cycle, or executive request. **Ends when:** Approved Scope of Work with criteria matrix and stakeholder register released to questionnaire design (E2E-33) and needs analysis (E2E-03).

Task	Steps	What to type
UFT-32-01 Define scope frame R: Head of L&D	MP-53.1 Define scope frame (Group Yes/No) MP-53.2 Select Organization	Group scope: No. Organization: Souss BTP Solutions.
UFT-32-02 Select sector R: L&D Analyst	MP-53.3 Select sector	Sector: AEC & Construction.
UFT-32-03 Select decision levels R: L&D Analyst	MP-53.4 Select decision level (MS/MO/OP/Custom)	Decision levels: MS, MO, OP (no custom level).
UFT-32-04 Map functions × decision levels R: L&D Analyst	MP-53.5 Map functions × decision level	Matrix: Site Works & Project Delivery × MS/MO/OP; Quality × MO/OP; Finance × MS/MO; HR × MS/MO.
UFT-32-05 Select focus and add custom criteria R: Head of L&D	MP-53.6 Select focus (All/Digital/AI/Custom) MP-53.7 Add custom criteria	Focus: Digital. Custom criterion: 'Readiness for BIM modelling and ISO 19650 workflows' (weight 2.00). AI run: Focus: AI. Custom criterion: 'Readiness for AI clash detection and model checking' (weight 2.00).
UFT-32-06 Identify stakeholders R: HR Business Partner	MP-53.8 Identify stakeholders	Register 40 stakeholders: name, role, function, level, site, preferred channel (Email, Face-to-Face or Hybrid).

Task	Steps	What to type
UFT-32-07 Validate scope R: Head of L&D	MP-53.9 Validate and approve scope	Validation: every function in scope has at least 3 stakeholders; completeness 100%.
UFT-32-08 Approve scope R: HR Director / Consultant PM	MP-53.9 Validate and approve scope MP-53.10 Publish scope and register stakeholders	Approval status: Approved (version 1). Justification: scope aligned with SO-1 and SO-2.
UFT-32-09 Publish scope and register stakeholders R: L&D Analyst	MP-53.10 Publish scope and register stakeholders	Generate the SOW document (RPT-033) and release scope and stakeholders to the questionnaire studio.

E2E-33 · Questionnaire-to-Response-Collection

Goal: Design, distribute and collect questionnaire responses across channels. **Starts when:** An approved Scope of Work becomes available (end of E2E-32). **Ends when:** Consolidated, validated questionnaire response dataset feeding needs analysis (E2E-03), diagnostic (E2E-20) and demand collection (E2E-27).

Task	Steps	What to type
UFT-33-01 Select questionnaire template R: L&D Analyst	MP-54.1 Select questionnaire template by focus	Template: 'Digital needs — AEC & Construction' in the user's language, 5 sections. AI run: Template: 'AI needs — AEC & Construction' in the user's language, 5 sections.
UFT-33-02 Elaborate questionnaire R: L&D Analyst	MP-54.2 Elaborate questionnaire (Load/AI/Manual)	Elaboration mode: AI. 24 questions generated from the approved Scope of Work.
UFT-33-03 Tailor and validate content R: L&D Analyst	MP-54.3 Tailor to sector and focus	Validate each question; reword 5 with Site Works & Project Delivery vocabulary; delete 2 duplicates.
UFT-33-04 Allocate RACSI R: Head of L&D	MP-54.4 Allocate RACSI per section	Section 'Digital practices': R L&D Analyst, A Head of L&D, C Consultant PM, S IT, I CHRO (one Accountable only).
UFT-33-05 Select distribution channels R: Survey Administrator	MP-54.5 Select distribution channels	Channels: MS and MO by Email; OP Face-to-Face with tablets; night shift Hybrid.
UFT-33-06 Distribute questionnaire R: Survey Administrator	MP-54.6 Distribute to stakeholders	Distribute to 40 stakeholders; 40 dispatches logged.
UFT-33-07 Send reminders R: Survey Administrator	MP-54.7 Send reminders on cadence	Reminder 1 on day 5 to 17 non-respondents; reminder 2 on day 10 to 8.
UFT-33-08 Collect responses R: Stakeholders	MP-54.8 Collect responses	Responses: 34 collected (22 online, 12 offline synchronised).
UFT-33-09 Validate completeness R: L&D Analyst	MP-54.9 Validate completeness and consent	Completeness: 31 complete, 3 incomplete flagged.
UFT-33-10 Consolidate responses R: L&D Analyst	MP-54.10 Consolidate responses	Consolidated dataset: 31 responses, 24 questions, by function and level.

Task	Steps	What to type
UFT-33-11 Check consent and release dataset R: L&D Analyst	MP-54.11 Feed responses to needs analysis and diagnostic MP-54.12 Report on response rate and engagement	Consent given for 31 of 31 stored responses; release to needs analysis, diagnostic and demand collection.
UFT-33-12 Report on response and engagement R: L&D Analyst	MP-54.12 Report on response rate and engagement	Response rate 85%; engagement rate 78%; completeness 91% (RPT-034).

E2E-19 · Consulting Engagement-to-Closure

Goal: Manage full consulting engagement lifecycle. **Starts when:** Client purchase order or engagement request received. **Ends when:** Engagement closed with client acceptance and REX recorded.

Task	Steps	What to type
UFT-19-01 Register engagement and purchase order R: Consultant PM	MP-36.1 Register engagement and purchase order	Engagement 'Training engineering 2026 — Souss BTP Solutions', PO-CL-221, 45 consulting days.
UFT-19-02 Hold kickoff meeting R: Consultant PM	MP-36.2 Hold kickoff meeting	Kickoff held on 10 February with HR Director, Head of L&D and 4 function heads.
UFT-19-03 Draft meeting minutes R: Consultant PM	MP-36.3 Draft meeting minutes	Review the AI minutes: 6 decisions, 9 actions, RACSI extracted; correct 1 owner name.
UFT-19-04 Align with client strategy R: Consultant PM	MP-01.1 Record corporate strategic objectives MP-01.2 Link objectives to functions and sites	Client objectives recorded: BIM modelling and ISO 19650 workflows and ISO 19650 compliance for Site Works & Project Delivery. AI run: Client objectives recorded: AI clash detection and model checking and ISO 19650 compliance for Site Works & Project Delivery.
UFT-19-05 Plan engagement work breakdown R: Consultant PM	MP-36.4 Plan engagement work breakdown	WBS: 6 phases, 14 deliverables, Gantt from February to November.
UFT-19-06 Plan change support R: Change Manager	MP-19.1 Assess change impact MP-19.2 Build adoption plan	Change plan: 3 sponsor messages, champion network, 2 town-halls.
UFT-19-07 Track engagement deliverables R: Consultant PM	MP-36.5 Track engagement deliverables MP-20.5 Run periodic quality review	Deliverables: 9 of 14 delivered on time, 1 late (SWOT), 4 planned.
UFT-19-08 Deliver final report and obtain acceptance R: Consultant PM	MP-36.6 Deliver final report MP-36.7 Obtain client acceptance	Final report delivered; acceptance signed by the HR Director on 28 November.
UFT-19-09 Record engagement REX R: Consultant PM	MP-36.8 Record engagement REX MP-12.6 Record REX entry MP-12.5 Prompt REX at closure	REX: went well — stakeholder register; did not — late SWOT inputs; root cause — no function-head backup; rating 4/5.

E2E-24 · Competitive Intelligence-to-Strategy

Goal: Analyze external environment and feed L&D strategy. **Starts when:** Annual strategy cycle or executive request for market positioning analysis. **Ends when:** Validated competitive intelligence report feeding into L&D strategy and organizational diagnostic.

Task	Steps	What to type
UFT-24-01 Define intelligence scope R: Strategy Analyst	MP-43.1 Define intelligence scope	Scope: AEC & Construction market in Morocco and export markets; horizon 3 years; focus on BIM modelling and ISO 19650 workflows and Digital site diary and field reporting. AI run: Scope: AEC & Construction market in Morocco and export markets; horizon 3 years; focus on AI clash detection and model checking and AI safety monitoring with site cameras.
UFT-24-02 Conduct Porter's Five Forces R: Strategy Analyst	MP-43.2 Conduct Porter's Five Forces analysis	Rivalry 4/5; new entrants 3/5; substitutes 2/5; supplier power 3/5; buyer power 4/5.
UFT-24-03 Map market segments R: Market Analyst	MP-43.3 Map market segments	Segments: key accounts (55% revenue), resellers (30%), direct small customers (15%).
UFT-24-04 Analyze competitor positioning R: Market Analyst	MP-43.4 Analyze competitor positioning	Competitor A leads on BIM modelling and ISO 19650 workflows; competitor B cheaper but weaker on ISO 19650. AI run: Competitor A leads on AI clash detection and model checking; competitor B cheaper but weaker on ISO 19650.
UFT-24-05 Monitor regulatory and technology trends R: Regulatory Analyst	MP-43.5 Monitor regulatory changes MP-43.6 Track technology trends MP-43.7 Benchmark against industry	Trends: revision of ISO 19650 expected next year; fast growth of Drone surveying and 3D site scans. AI run: Trends: revision of ISO 19650 expected next year; fast growth of AI cost and schedule forecasting.
UFT-24-06 Identify L&D implications R: L&D Strategist	MP-43.8 Identify strategic implications for L&D	L&D implication: build BIM modelling and ISO 19650 workflows skills for key-account teams before competitor A scales. AI run: L&D implication: build AI clash detection and model checking skills for key-account teams before competitor A scales.
UFT-24-07 Publish intelligence report R: Strategy Analyst	MP-43.9 Produce intelligence report MP-43.10 Feed intelligence into strategy and diagnostic MP-43.11 Update intelligence continuously MP-43.12 Report to executive leadership	Publish RPT-007 Competitive Intelligence Report to the executive committee.

SME-E2E-01 · SME Snapshot-to-Plan in 30 days

Goal: Turn a one-day needs snapshot into a short, funded plan.. **Starts when:** SME onboarding started. **Ends when:** Short plan approved by the owner-manager.

Task	Steps	What to type
UFT-SME1-01 Interview the owner-manager R: Head of L&D	SME-MP-01.1 Record business priorities SME-MP-01.2 Record key roles and headcount	Priorities: win 2 new customers; reduce rework. Headcount SME: owner, 3 team leaders, operators.
UFT-SME1-02 Send the needs snapshot R: L&D Analyst	SME-MP-01.3 Send short needs questionnaire MP-54.6 Distribute to stakeholders	Send the 10-question snapshot to all employees by WhatsApp link or paper.

Task	Steps	What to type
UFT-SME1-03 Summarize top needs R: L&D Analyst	SME-MP-01.4 Summarize top needs	Top needs: BIM modelling and ISO 19650 workflows; Digital site diary and field reporting; customer service. Accept the AI summary. AI run: Top needs: AI clash detection and model checking; AI safety monitoring with site cameras; customer service. Accept the AI summary.
UFT-SME1-04 Approve the short plan R: HR Director	MP-53.9 Validate and approve scope	Short plan approved: 3 themes, 6 training days, 45,000 MAD.

8.3 Diagnosis — gate G2

E2E-20 · Multi-Axis Diagnostic-to-Maturity Report

Goal: Conduct 5-axis diagnostic + CMM maturity + leadership assessment. **Starts when:** Engagement kickoff or approved Scope of Work requesting a diagnostic. **Ends when:** 5-axis diagnostic, CMM maturity and leadership maturity report validated with the sponsor.

Task	Steps	What to type
UFT-20-01 Define diagnostic axes and sample R: Consultant PM	MP-37.1 Define diagnostic axes and sample	Axes: strategy, organization, processes, people, information systems. Sample: 40 people (MS 8, MO 16, OP 16).
UFT-20-02 Deploy diagnostic questionnaire R: Consultant PM	MP-37.2 Deploy diagnostic questionnaire MP-37.4 Collect questionnaire responses	Diagnostic questionnaire deployed to 40 people; 34 responses (85%).
UFT-20-03 Conduct semi-structured interviews R: Consultant	MP-37.3 Conduct semi-structured interviews	Interview notes (OP, Site Works & Project Delivery): 'Procedures exist but are not updated since 2023.'
UFT-20-04 Score diagnostic axes R: Consultant	MP-37.5 Score diagnostic axes	Axis scores (1-5): strategy 3.4, organization 2.8, processes 2.6, people 3.1, IS 2.2.
UFT-20-05 Select maturity model R: Consultant	MP-38.1 Select maturity model levels MP-38.2 Define evidence criteria per level	Maturity model: CMM 5 levels; evidence for level 3 = documented and applied process.
UFT-20-06 Rate process maturity R: Consultant	MP-38.3 Rate maturity per process area MP-38.4 Compute maturity profile	Maturity: training management level 2; Site Works & Project Delivery processes level 3.
UFT-20-07 Assess leadership maturity R: HR Business Partner	MP-42.1 Launch leadership 360 assessment MP-42.2 Compute leadership maturity level	Leadership 360: average level 3 (Team Leadership) across 18 managers.
UFT-20-08 Cross-check skills and needs R: L&D Analyst	MP-02.7 Validate skills inventory MP-03.2 Review gap matrix by site and function	Cross-check: IS axis weakness confirmed by the BIM modelling and ISO 19650 workflows gap (-1.4). AI run: Cross-check: IS axis weakness confirmed by the AI clash detection and model checking gap (-1.4).
UFT-20-09 Draft diagnostic findings R: Consultant	MP-37.6 Draft diagnostic findings MP-38.5 Produce maturity report	Edit AI findings: keep 5, merge 2, add one on ISO 19650 documentation.

Task	Steps	What to type
UFT-20-10 Validate findings with sponsor R: Consultant PM	MP-37.7 Validate findings with sponsor MP-38.6 Agree target maturity	Findings validated with the sponsor; target maturity level 3 by 2026+1.

E2E-25 · Job Architecture-to-Competency Map

Goal: Manage organizational charts, position descriptions, gap analysis. **Starts when:** Organizational change, new role creation, or annual job architecture review. **Ends when:** Approved organizational charts, position descriptions, and competency maps with gap analysis.

Task	Steps	What to type
UFT-25-01 Map organizational structure R: HR Analyst	MP-44.1 Map organizational structure	Structure: 6 functions, 14 departments, 3 sites; 212 positions.
UFT-25-02 Design organizational charts R: Org Design Consultant	MP-44.2 Design organizational charts	Org chart 'Site Works & Project Delivery': director → 3 managers → 9 supervisors → operators.
UFT-25-03 Conduct job analysis R: Job Analyst	MP-44.3 Conduct job analysis	Job analysis 'Site Works & Project Delivery supervisor': 8 main activities, 2 of them now supported by BIM modelling and ISO 19650 workflows. AI run: Job analysis 'Site Works & Project Delivery supervisor': 8 main activities, 2 of them now supported by AI clash detection and model checking.
UFT-25-04 Draft position descriptions R: Job Analyst	MP-44.4 Draft position descriptions	Position description drafted: mission, activities, competencies (BIM modelling and ISO 19650 workflows level 3, ISO 19650 level 3), KPIs. AI run: Position description drafted: mission, activities, competencies (AI clash detection and model checking level 3, ISO 19650 level 3), KPIs.
UFT-25-05 Validate with managers R: HR Business Partner	MP-44.5 Validate descriptions with managers	Validated by the Site Works & Project Delivery manager with 2 changes on activities.
UFT-25-06 Conduct gap analysis R: Job Analyst	MP-44.6 Conduct gap analysis existing versus real	Gap existing vs real: 11 descriptions outdated; 4 roles with new BIM modelling and ISO 19650 workflows tasks. AI run: Gap existing vs real: 11 descriptions outdated; 4 roles with new AI clash detection and model checking tasks.
UFT-25-07 Identify roles to develop R: HR Business Partner	MP-44.7 Identify roles to develop MP-44.8 Update job architecture MP-44.9 Align with competency framework	Roles 'To develop': data-literate supervisor, maintenance technician 4.0.
UFT-25-08 Publish approved architecture R: HR Director	MP-44.10 Publish approved position descriptions MP-44.11 Track job architecture changes MP-44.12 Report on architecture health	Publish 212 approved descriptions and the architecture map to all employees.

E2E-26 · GPEC-to-Training Plan

Goal: Integrate Forward Planning of Jobs and Skills into L&D. **Starts when:** Annual HR strategic planning cycle or GPEC (Forward Planning of Jobs and Skills) review. **Ends when:** Training plan aligned with GPEC and HR strategic orientations.

Task	Steps	What to type
UFT-26-01 Define GPEC scope R: GPEC Specialist	MP-45.1 Define GPEC scope	GPEC scope: Site Works & Project Delivery and Information Systems jobs; horizon 3 years.
UFT-26-02 Map HR strategic orientations R: HR Director	MP-45.2 Map HR strategic orientations MP-45.3 Align training with GPEC	HR orientations: internal mobility first; 30% of promotions from internal talent.
UFT-26-03 Update development foundation R: HR Business Partner	MP-45.4 Update development foundation MP-45.5 Support human capital development	Development foundation updated: descriptions, annual objectives, evaluation grid.
UFT-26-04 Update Jobs and Skills Directory (REC) R: GPEC Specialist	MP-45.6 Update Jobs and Skills Directory (REC)	REC updated: 42 jobs, 3 new jobs linked to BIM modelling and ISO 19650 workflows. AI run: REC updated: 42 jobs, 3 new jobs linked to AI clash detection and model checking.
UFT-26-05 Redynamize periodic evaluations R: HR Business Partner	MP-45.7 Redynamize periodic evaluations	Periodic evaluation redesigned: 2 reviews per year, competency section added.
UFT-26-06 Design career paths R: HR Director	MP-45.8 Design career paths	Career path: operator → team leader → supervisor → Site Works & Project Delivery manager.
UFT-26-07 Document career management R: HR Director	MP-45.9 Document career management process MP-45.10 Implement collective compensation	Career management procedure documented (v1): eligibility, committee, calendar.
UFT-26-08 Align training with GPEC R: L&D Strategist	MP-45.11 Feed GPEC into training needs MP-45.12 Report on GPEC integration	Training aligned with GPEC: 4 themes cover the 3 new jobs; 2 themes removed.

E2E-27 · Demand Collection-to-Consolidation

Goal: Collect individual and collective training demands. **Starts when:** Annual training plan cycle or ad-hoc demand collection request. **Ends when:** Consolidated and prioritized demand repository integrated into the training needs analysis.

Task	Steps	What to type
UFT-27-01 Design demand collection forms R: L&D Analyst	MP-46.1 Design demand collection forms	Forms: individual form (5 questions) and collective form per team (3 questions).
UFT-27-02 Deploy individual demand collection R: L&D Analyst	MP-46.2 Deploy individual demand collection	Individual collection open 1-20 March; 146 demands received.
UFT-27-03 Deploy collective demand collection R: L&D Analyst	MP-46.3 Deploy collective demand collection	Collective collection: 18 team demands received.

Task	Steps	What to type
UFT-27-04 Collect manager recommendations R: L&D Business Partner	MP-46.4 Collect manager recommendations	Manager recommendations: 24 received, 9 flagged as priority.
UFT-27-05 Consolidate demands by function R: L&D Analyst	MP-46.5 Consolidate demands by function	Consolidated: Site Works & Project Delivery 64 demands, Operations 41, Quality 22, others 37.
UFT-27-06 Map demands to competencies R: L&D Analyst	MP-46.6 Map demands to competencies MP-46.7 Prioritize demands	Accept AI mapping for 139 demands; map 7 manually to 'Digital site diary and field reporting'. AI run: Accept AI mapping for 139 demands; map 7 manually to 'AI safety monitoring with site cameras'.
UFT-27-07 Prioritize and validate demands R: L&D Business Partner	MP-46.8 Validate demands with managers MP-46.9 Integrate demands into needs analysis MP-46.10 Report on demand patterns MP-46.11 Track demand fulfillment MP-46.12 Improve demand collection	Validated: 112 demands (High 38, Medium 51, Low 23); 34 rejected with reason.

E2E-28 · Performance Assessment-to-RAG Dashboard

Goal: Assess MS/MO/OP performance with RAG ratings. **Starts when:** Annual performance cycle or management request for performance visualization. **Ends when:** Validated MS/MO/OP (Strategic Management / Operational Management / Operational Level) performance assessment with RAG (Green/Amber/Red) dashboards.

Task	Steps	What to type
UFT-28-01 Define MS/MO/OP framework R: Performance Analyst	MP-47.1 Define MS/MO/OP framework	MS = executive committee; MO = managers and supervisors; OP = operators and technicians.
UFT-28-02 Define RAG criteria R: Performance Analyst	MP-47.2 Define RAG criteria	Green ≥ 90% of target; Amber 70-89%; Red < 70%.
UFT-28-03 Collect performance data by function R: Performance Analyst	MP-47.3 Collect performance data by function	Data collected for 6 functions: 18 KPIs, last 12 months.
UFT-28-04 Assess MS performance R: Performance Analyst	MP-47.4 Assess MS performance	MS: strategy deployment Amber (78%); governance Green (92%).
UFT-28-05 Assess MO performance R: Performance Analyst	MP-47.5 Assess MO performance	MO: Site Works & Project Delivery team management Red (64%); planning Amber (81%).
UFT-28-06 Assess OP performance R: Performance Analyst	MP-47.6 Assess OP performance MP-47.7 Apply RAG ratings	OP: ISO 19650 compliance Amber (85%); productivity Green (93%).

Task	Steps	What to type
UFT-28-07 Publish RAG dashboard R: Performance Analyst	MP-47.8 Visualize performance dashboards MP-47.9 Identify performance gaps MP-47.10 Feed performance into diagnostic report MP-47.11 Track performance progression MP-47.12 Report performance to leadership	Publish RPT-005 MS/MO/OP RAG dashboard to the executive committee.

E2E-29 · Functional SWOT-to-Improvement Axes

Goal: Conduct function-level SWOT and define improvement axes. **Starts when:** Diagnostic phase of a training engineering engagement or annual functional review. **Ends when:** Validated functional SWOT reports with prioritized improvement axes per function.

Task	Steps	What to type
UFT-29-01 Define function scope R: L&D Analyst	MP-48.1 Define function scope	Function in scope: Site Works & Project Delivery (3 sites, 96 people).
UFT-29-02 Conduct function SWOT R: L&D Analyst	MP-48.2 Conduct function SWOT	SWOT workshop held with the function head and 6 supervisors.
UFT-29-03 Identify strengths and weaknesses R: L&D Analyst	MP-48.3 Identify strengths MP-48.4 Identify weaknesses	Strength: experienced team. Weakness: low BIM modelling and ISO 19650 workflows usage, paper records. AI run: Strength: experienced team. Weakness: low AI clash detection and model checking usage, paper records.
UFT-29-04 Identify opportunities and threats R: L&D Analyst	MP-48.5 Identify opportunities MP-48.6 Identify threats	Opportunity: Drone surveying and 3D site scans. Threat: stricter ISO 19650 audits. AI run: Opportunity: AI cost and schedule forecasting. Threat: stricter ISO 19650 audits.
UFT-29-05 Define improvement axes R: L&D Business Partner	MP-48.7 Define improvement axes	Axis 1: digitalise shift records with BIM modelling and ISO 19650 workflows. Axis 2: certify supervisors on ISO 19650. AI run: Axis 1: digitalise shift records with AI clash detection and model checking. Axis 2: certify supervisors on ISO 19650.
UFT-29-06 Validate with function heads R: L&D Business Partner	MP-48.8 Validate axes with function heads	Validated by the function head on 18 April; axis 2 deadline moved to Q3.
UFT-29-07 Prioritize improvement axes R: L&D Strategist	MP-48.9 Prioritize improvement axes MP-48.10 Feed SWOT into diagnostic report MP-48.11 Track improvement implementation MP-48.12 Report on function performance	Priority: axis 1 (impact 5), axis 2 (impact 4).

E2E-02 · Skills-to-Gap Diagnosis

Goal: Produce a validated skills gap diagnosis. **Starts when:** Approved annual L&D plan or a scheduled skills assessment campaign. **Ends when:** Validated skills gap diagnosis released to needs analysis.

Task	Steps	What to type
UFT-02-01 Maintain competency framework R: L&D Analyst	MP-02.1 Define competency families and levels	Family 'BIM modelling and ISO 19650 workflows': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert). AI run: Family 'AI clash detection and model checking': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert).
UFT-02-02 Set target levels per position R: HR Business Partner	MP-02.2 Set target levels per position	Site Works & Project Delivery supervisor: BIM modelling and ISO 19650 workflows = 3; ISO 19650 = 3. Site Works & Project Delivery operator: BIM modelling and ISO 19650 workflows = 2. AI run: Site Works & Project Delivery supervisor: AI clash detection and model checking = 3; ISO 19650 = 3. Site Works & Project Delivery operator: AI clash detection and model checking = 2.
UFT-02-03 Launch assessment campaign R: L&D Analyst	MP-02.3 Launch assessment campaign	Campaign 'Skills 2026': population Site Works & Project Delivery and Operations (212 people), 12 competencies, close date 30 April.
UFT-02-04 Collect self and manager assessments R: Manager	MP-02.4 Submit self and manager assessments MP-02.5 Consolidate assessment results	Self-assessment BIM modelling and ISO 19650 workflows: 2; manager validation: 2 with comment 'needs practice on live cases'. AI run: Self-assessment AI clash detection and model checking: 2; manager validation: 2 with comment 'needs practice on live cases'.
UFT-02-05 Suggest proficiency from evidence R: L&D Analyst	MP-02.6 Suggest proficiency from evidence	Accept 38 suggested levels, edit 4 (evidence too old), reject 1. Every change carries a note.
UFT-02-06 Validate skills inventory R: Head of L&D	MP-02.7 Validate skills inventory	Inventory validated: 212 employees, 96% assessments complete. Justification: sample checked by site.
UFT-02-07 Compute and forecast gaps R: L&D Analyst	MP-03.1 Compute gap matrix MP-03.2 Review gap matrix by site and function MP-28.3 Forecast skill gaps MP-28.1 Build analytics dataset	Critical gaps: BIM modelling and ISO 19650 workflows (-1.4 average on supervisors), Digital site diary and field reporting (-1.1). Forecast: Drone surveying and 3D site scans becomes critical within 12 months. AI run: Critical gaps: AI clash detection and model checking (-1.4 average on supervisors), AI safety monitoring with site cameras (-1.1). Forecast: AI cost and schedule forecasting becomes critical within 12 months.

E2E-21 · Previous Plan Impact-to-Strategy Update

Goal: Evaluate N-1 plan impact and update strategy. **Starts when:** Start of a new plan cycle with N-1 execution data available. **Ends when:** N-1 impact conclusions fed into the strategy update.

Task	Steps	What to type
UFT-21-01 Load N-1 plan execution data R: L&D Analyst	MP-39.1 Load N-1 plan execution data	Load N-1 plan: 28 sessions planned, 23 delivered, 1,410,000 MAD spent.
UFT-21-02 Define impact criteria R: L&D Analyst	MP-39.2 Define impact criteria	Impact criteria: application on the job, KPI change, satisfaction, cost per learner.

Task	Steps	What to type
UFT-21-03 Survey participants and managers R: L&D Analyst	MP-39.3 Survey participants and managers MP-09.5 Record on-the-job observation (Level 3)	Survey sent to 190 participants and 34 managers; 61% responded.
UFT-21-04 Compare planned against realized R: L&D Analyst	MP-39.4 Compare planned against realized MP-32.3 Isolate training effect	Planned vs realized: 82% of sessions, 94% of budget; 2 themes not delivered.
UFT-21-05 Review N-1 ROI R: Performance Analyst	MP-32.4 Compute Phillips ROI MP-32.5 Review ROI with finance	N-1 ROI: Digital site diary and field reporting 18%; safety theme 35%. AI run: N-1 ROI: AI safety monitoring with site cameras 18%; safety theme 35%.
UFT-21-06 Draft impact conclusions R: L&D Analyst	MP-39.5 Draft impact study conclusions	Accept AI conclusions 1-3; rewrite conclusion 4 (sample too small).
UFT-21-07 Feed conclusions to strategy R: Head of L&D	MP-39.6 Feed conclusions to strategy update MP-01.1 Record corporate strategic objectives	Feed to strategy: keep blended format; stop long classroom courses on Digital site diary and field reporting. AI run: Feed to strategy: keep blended format; stop long classroom courses on AI safety monitoring with site cameras.
UFT-21-08 Update roadmap priorities R: L&D Strategist	MP-04.6 Sequence roadmap initiatives	Roadmap priority updated: BIM modelling and ISO 19650 workflows moved to Q2; Digital site diary and field reporting to microlearning. AI run: Roadmap priority updated: AI clash detection and model checking moved to Q2; AI safety monitoring with site cameras to microlearning.

8.4 Training Engineering Report & plan — gate G3

E2E-01 · Strategy-to-Learning Plan

Goal: Translate corporate strategy into an approved annual L&D plan and budget. **Starts when:** Annual strategy cycle opened or revised corporate objectives published by the board. **Ends when:** Annual L&D plan and budget envelope approved by the Steering Committee and locked.

Task	Steps	What to type
UFT-01-01 Record strategic objectives R: Head of L&D	MP-01.1 Record corporate strategic objectives	SO-1: BIM modelling and ISO 19650 workflows used by 80% of Site Works & Project Delivery staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on ISO 19650. AI run: SO-1: AI clash detection and model checking used by 80% of Site Works & Project Delivery staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on ISO 19650.
UFT-01-02 Link objectives to functions and sites R: L&D Strategist	MP-01.2 Link objectives to functions and sites	SO-1 → Site Works & Project Delivery, Operations, Information Systems (all sites). SO-2 → Quality & HSE, Site Works & Project Delivery.

Task	Steps	What to type
UFT-01-03 Frame skills priorities R: L&D Analyst	MP-02.1 Define competency families and levels MP-02.2 Set target levels per position	Priority competency families: BIM modelling and ISO 19650 workflows; Digital site diary and field reporting; ISO 19650 compliance. Target level 3 (Autonomous) for supervisors. AI run: Priority competency families: AI clash detection and model checking; AI safety monitoring with site cameras; ISO 19650 compliance. Target level 3 (Autonomous) for supervisors.
UFT-01-04 Pre-scope training needs R: L&D Analyst	MP-03.1 Compute gap matrix MP-03.2 Review gap matrix by site and function	Pre-scoped needs: 42% of Site Works & Project Delivery supervisors below target on BIM modelling and ISO 19650 workflows; 18 employees below target on ISO 19650. AI run: Pre-scoped needs: 42% of Site Works & Project Delivery supervisors below target on AI clash detection and model checking; 18 employees below target on ISO 19650.
UFT-01-05 Define budget envelope R: Finance Manager	MP-01.3 Define L&D budget envelope MP-18.1 Allocate budget by theme and site MP-18.2 Forecast OFPPT refunds	Gross L&D budget 2026: 1,850,000 MAD; forecast refund (OFPPT/CSF): 520,000 MAD; net envelope: 1,330,000 MAD.
UFT-01-06 Plan change and adoption R: Change Manager	MP-19.1 Assess change impact MP-19.2 Build adoption plan	Change impact: high for Site Works & Project Delivery supervisors (new BIM modelling and ISO 19650 workflows routines). Sponsors: Operations Director. Champions: one per site. AI run: Change impact: high for Site Works & Project Delivery supervisors (new AI clash detection and model checking routines). Sponsors: Operations Director. Champions: one per site.
UFT-01-07 Compile plan approval pack R: Head of L&D	MP-01.4 Schedule Steering Committee milestones MP-01.5 Compile plan approval pack MP-04.1 Consolidate feeder outputs	Approval pack: 2 objectives, net budget 1,330,000 MAD, 6 priority themes, committee date 15 March 2026.
UFT-01-08 Approve and lock annual L&D plan R: HR Director	MP-01.6 Record Steering Committee decision MP-01.7 Lock and distribute approved plan	Decision: Approve. Justification: aligned with SO-1 and SO-2; budget within envelope. Plan locked as version 1.

E2E-03 · Needs-to-Training Engineering Report & Roadmap

Goal: Produce the Training Engineering Report and the prioritized training roadmap. **Starts when:** Validated skills gap diagnosis, consolidated demands, approved Scope of Work or diagnostic findings available. **Ends when:** Training Engineering Report and prioritized roadmap approved and published.

Task	Steps	What to type
UFT-03-01 Plan diagnostic interviews R: L&D Analyst	MP-03.3 Plan diagnostic interviews	Interview plan: 14 semi-structured interviews (4 MS, 6 MO, 4 OP), 45 minutes each, weeks 10-11.
UFT-03-02 Record interview findings R: L&D Analyst	MP-03.4 Record interview findings	Finding (MO, Site Works & Project Delivery): 'Supervisors do not trust BIM modelling and ISO 19650 workflows data; they re-enter figures on paper.' AI run: Finding (MO, Site Works & Project Delivery): 'Supervisors do not trust AI clash detection and model checking data; they re-enter figures on paper.'

Task	Steps	What to type
UFT-03-03 Cluster needs into themes R: L&D Analyst	MP-03.5 Cluster needs into training themes	Accept theme 'BIM modelling and ISO 19650 workflows for supervisors'; merge two duplicate themes on Digital site diary and field reporting; split 'ISO 19650' into awareness and auditor tracks. AI run: Accept theme 'AI clash detection and model checking for supervisors'; merge two duplicate themes on AI safety monitoring with site cameras; split 'ISO 19650' into awareness and auditor tracks.
UFT-03-04 Prioritize needs by impact R: L&D Strategist	MP-03.6 Prioritize needs by business impact	BIM modelling and ISO 19650 workflows: impact 5, urgency 4. Digital site diary and field reporting: impact 4, urgency 3. ISO 19650: impact 4, urgency 5. AI run: AI clash detection and model checking: impact 5, urgency 4. AI safety monitoring with site cameras: impact 4, urgency 3. ISO 19650: impact 4, urgency 5.
UFT-03-05 Validate needs register R: Head of L&D	MP-03.7 Validate needs register	Needs register validated: 23 needs, 6 themes. Justification: covers SO-1 and SO-2; sponsor reviewed.
UFT-03-06 Consolidate engineering inputs R: L&D Analyst	MP-04.1 Consolidate feeder outputs MP-04.2 Check input completeness	Inputs complete: Scope of Work, 187 responses, gap matrix, RAG dashboard, SWOT, demands. Missing: none.
UFT-03-07 Draft Training Engineering Report R: L&D Strategist	MP-04.3 Generate report draft MP-04.4 Edit and complete report sections	Section 3 'Diagnostic': edit the AI draft, add the interview quote on BIM modelling and ISO 19650 workflows, keep the RAG table. AI run: Section 3 'Diagnostic': edit the AI draft, add the interview quote on AI clash detection and model checking, keep the RAG table.
UFT-03-08 Run quality review R: Quality Manager	MP-04.5 Run quality review of report MP-20.5 Run periodic quality review	Quality review: 11/12 checklist items met; fix item 'sources cited for every figure'. Result: pass after correction.
UFT-03-09 Sequence and budget roadmap R: L&D Strategist	MP-04.6 Sequence roadmap initiatives MP-18.1 Allocate budget by theme and site	Roadmap: Q2 BIM modelling and ISO 19650 workflows (6 groups); Q3 ISO 19650 (4 groups); Q4 Digital site diary and field reporting (3 groups). Total 1,240,000 MAD. AI run: Roadmap: Q2 AI clash detection and model checking (6 groups); Q3 ISO 19650 (4 groups); Q4 AI safety monitoring with site cameras (3 groups). Total 1,240,000 MAD.
UFT-03-10 Approve and publish report and roadmap R: Head of L&D	MP-04.7 Submit roadmap for approval MP-04.8 Record roadmap approval MP-04.9 Publish approved report and roadmap MP-01.6 Record Steering Committee decision	Decision: Approve report and roadmap v1. Justification: within budget, linked to SO-1/SO-2. Publish to all stakeholders.

E2E-30 · Prioritization-to-Resource Plan

Goal: Prioritize themes and plan days, groups, trainers, budget. **Starts when:** Consolidated training themes requiring prioritization and resource planning. **Ends when:** Approved prioritized training plan with days per theme, group planning, trainer allocation, and budget.

Task	Steps	What to type
UFT-30-01 Consolidate training themes R: L&D Analyst	MP-49.1 Consolidate training themes	Consolidated list: 9 themes from needs, demands, GPEC and SWOT.
UFT-30-02 Define prioritization criteria R: L&D Strategist	MP-49.2 Define prioritization criteria	Criteria: strategic impact 40%, urgency 30%, number of learners 20%, cost 10%.
UFT-30-03 Prioritize themes R: L&D Strategist	MP-49.3 Prioritize themes	Rank 1 BIM modelling and ISO 19650 workflows (score 86); rank 2 ISO 19650 (81); rank 3 Digital site diary and field reporting (74). AI run: Rank 1 AI clash detection and model checking (score 86); rank 2 ISO 19650 (81); rank 3 AI safety monitoring with site cameras (74).
UFT-30-04 Estimate days per theme R: L&D Planner	MP-49.4 Estimate days per theme	BIM modelling and ISO 19650 workflows: 3 days per group; ISO 19650: 2 days; Digital site diary and field reporting: 1.5 days. AI run: AI clash detection and model checking: 3 days per group; ISO 19650: 2 days; AI safety monitoring with site cameras: 1.5 days.
UFT-30-05 Define groups per theme R: L&D Planner	MP-49.5 Define number of groups per theme MP-49.6 Allocate trainers	BIM modelling and ISO 19650 workflows: 6 groups of 12; ISO 19650: 4 groups; Digital site diary and field reporting: 3 groups. AI run: AI clash detection and model checking: 6 groups of 12; ISO 19650: 4 groups; AI safety monitoring with site cameras: 3 groups.
UFT-30-06 Allocate trainers and budget R: Finance Manager	MP-49.7 Estimate plan budget MP-49.8 Sequence delivery MP-49.9 Validate plan with governance	Trainers: 2 internal, vendor A; budget 1,240,000 MAD (within envelope).
UFT-30-07 Publish prioritized training plan R: L&D Leader	MP-49.10 Publish prioritized plan MP-49.11 Track plan execution MP-49.12 Report on resource utilization	Publish RPT-002 Prioritized Training Plan 2026 to all stakeholders.

E2E-22 · Multi-Site Plan-to-Deployment

Goal: Adapt and deploy plans across sites. **Starts when:** Approved roadmap for an organization with several sites or entities. **Ends when:** Site plans adapted, validated and deployed, with deviations escalated.

Task	Steps	What to type
UFT-22-01 Split plan by site R: Head of L&D	MP-40.1 Split plan by site	Split plan into 3 sites: Casablanca 55%, Tanger 30%, Agadir 15%.
UFT-22-02 Adapt site plan to local constraints R: Site L&D Coordinator	MP-40.2 Adapt site plan to local constraints	Tanger: shift constraints → sessions of 4 hours instead of full days.
UFT-22-03 Localize site materials R: Instructional Designer	MP-23.1 Request translation MP-23.3 Validate translation MP-23.6 Review participation equity MP-23.7 Record inclusion actions	Agadir materials translated to AR; validated by the site expert.

Task	Steps	What to type
UFT-22-04 Validate site plan R: Head of L&D	MP-40.3 Validate site plan	Site plans validated centrally; budget deviation within $\pm 5\%$.
UFT-22-05 Schedule site sessions R: Training Administrator	MP-07.1 Create training session MP-11.1 Book rooms and equipment	Tanger schedule: 8 sessions, rooms booked, 2 trainers.
UFT-22-06 Deploy site schedule R: Site L&D Coordinator	MP-40.4 Deploy site schedule	Schedules deployed and communicated to site managers.
UFT-22-07 Consolidate site status R: Head of L&D	MP-40.5 Consolidate site status	Status: Casablanca 70%, Tanger 45%, Agadir 20% delivered.
UFT-22-08 Escalate site deviation R: Head of L&D	MP-40.6 Escalate site deviation	Escalate Agadir deviation (-25%) to the HR Director with a recovery plan.

E2E-23 · Regulatory Submission-to-Validation

Goal: Submit and validate training plans with regulatory bodies. **Starts when:** Approved plan requiring external validation or funding (e.g. OFPPT, GIAC-Agro). **Ends when:** Plan validated by the regulatory body and evidence archived.

Task	Steps	What to type
UFT-23-01 Select regulatory template R: Compliance Officer	MP-41.1 Select regulatory template	Template: OFPPT special training contracts (CSF) — plan file.
UFT-23-02 Generate submission file R: Compliance Officer	MP-41.2 Generate submission file MP-20.5 Run periodic quality review	Submission file generated: plan, themes, providers, costs; quality check passed.
UFT-23-03 Submit plan to regulatory body R: Compliance Officer	MP-41.3 Submit plan to regulatory body	Submitted to the regional funding committee on 5 March; reference GSF-2026-118.
UFT-23-04 Track submission status R: Compliance Officer	MP-41.4 Track submission status	Status: additional document requested (provider accreditation) — sent on 12 March.
UFT-23-05 Record regulator decision R: Compliance Officer	MP-41.5 Record regulator decision MP-14.1 Register regulatory requirement	Decision: approved with a cap of 520,000 MAD.
UFT-23-06 Submit refund claims R: Finance Manager	MP-18.5 Submit refund claims	Refund claims submitted for 12 delivered actions: 318,000 MAD.
UFT-23-07 Archive submission evidence R: Compliance Officer	MP-41.6 Archive submission evidence MP-18.6 Close budget period	Archive file, decision and claims; retention 10 years.

E2E-16 · Vendor-to-Finance

Goal: Manage vendors from selection to payment. **Starts when:** Training need requiring an external provider. **Ends when:** Vendor selected, order issued and payment approved against attendance.

Task	Steps	What to type
UFT-16-01 Issue request for proposal R: Purchasing Officer	MP-15.1 Issue request for proposal	RFP 'Training on BIM modelling and ISO 19650 workflows' sent to 4 vendors, answers due 15 May. AI run: RFP 'Training on AI clash detection and model checking' sent to 4 vendors, answers due 15 May.
UFT-16-02 Score vendor proposals R: Purchasing Officer	MP-15.2 Score vendor proposals	Scores: vendor A 82, vendor B 76, vendor C 64 (price 40%, expertise 40%, references 20%).
UFT-16-03 Register and verify vendor R: Purchasing Officer	MP-15.3 Register vendor record MP-15.4 Verify vendor accreditation	Register vendor A; accreditation OFPPT verified, valid until December.
UFT-16-04 Issue purchase order R: Purchasing Officer	MP-15.5 Issue purchase order MP-18.3 Record committed and actual costs	Purchase order PO-2026-044: 180,000 MAD on budget line 'BIM modelling and ISO 19650 workflows'. AI run: Purchase order PO-2026-044: 180,000 MAD on budget line 'AI clash detection and model checking'.
UFT-16-05 Match invoice to order and attendance R: Training Administrator	MP-15.6 Match invoice to order and attendance MP-11.5 Reconcile attendance with invoices	Invoice matched with PO and attendance (3 days × 12 learners): OK.
UFT-16-06 Approve vendor payment R: Finance Manager	MP-15.7 Approve vendor payment MP-18.4 Compare spend against budget	Approve payment 180,000 MAD; vendor performance rating 4/5.

AEC-E2E-02 · AEC & Construction Critical-Skills-to-Transformation Plan

Goal: Turn critical-skill gaps and digital and AI use cases into a transformation plan.. **Starts when:** Annual plan cycle or technology change in AEC & Construction. **Ends when:** Transformation learning paths approved.

Task	Steps	What to type
UFT-AEC-E2-01 List critical Site Works & Project Delivery skills R: L&D Analyst	MP-02.1 Define competency families and levels MP-03.1 Compute gap matrix	Critical skills: 6 for Site Works & Project Delivery, each with target level 3.
UFT-AEC-E2-02 List digital and AI use cases R: L&D Strategist	MP-03.3 Plan diagnostic interviews	Use cases: BIM modelling and ISO 19650 workflows; Digital site diary and field reporting; Drone surveying and 3D site scans. AI run: Use cases: AI clash detection and model checking; AI safety monitoring with site cameras; AI cost and schedule forecasting.
UFT-AEC-E2-03 Forecast impacted roles R: Performance Analyst	MP-03.5 Cluster needs into training themes MP-28.3 Forecast skill gaps	Impacted roles: supervisors (high), operators (medium); accept the AI forecast.
UFT-AEC-E2-04 Approve transformation paths R: Instructional Designer	MP-05.2 Define learning path and modules MP-05.7 Approve design document	Approve 2 transformation paths: 'BIM modelling and ISO 19650 workflows for supervisors', 'Digital site diary and field reporting for operators'. AI run: Approve 2 transformation paths: 'AI clash detection and model checking for supervisors', 'AI safety monitoring with site cameras for operators'.

SME-E2E-02 · SME Funding-to-Refund

Goal: Secure funding and recover the refunds of the plan.. **Starts when:** Short plan approved. **Ends when:** Refund received and recorded.

Task	Steps	What to type
UFT-SME2-01 Select eligible themes R: L&D Analyst	SME-MP-02.1 Select eligible themes	Eligible themes: BIM modelling and ISO 19650 workflows and ISO 19650 (funding rules met). AI run: Eligible themes: AI clash detection and model checking and ISO 19650 (funding rules met).
UFT-SME2-02 Build the funding file R: Finance Manager	SME-MP-02.2 Build funding file MP-41.2 Generate submission file	Funding file: plan, quotes, provider accreditation, attendance model.
UFT-SME2-03 Submit the refund claim R: Finance Manager	SME-MP-02.3 Submit refund claim MP-18.5 Submit refund claims	Refund claim submitted: 28,000 MAD with signed attendance sheets.
UFT-SME2-04 Record the refund R: Finance Manager	SME-MP-02.4 Track refund payment	Refund received: 28,000 MAD on 20 November; file closed.

8.5 Design & delivery — gate G4

E2E-04 · Roadmap-to-Curriculum Design

Goal: Convert roadmap into curriculum maps, learning paths, design documents. **Starts when:** Approved Training Engineering Report and roadmap published. **Ends when:** Approved curriculum maps, learning paths and design documents.

Task	Steps	What to type
UFT-04-01 Create curriculum map R: Instructional Designer	MP-05.1 Create curriculum map from roadmap	Curriculum map 'BIM modelling and ISO 19650 workflows': 3 learning paths (operators, supervisors, managers), 9 modules. AI run: Curriculum map 'AI clash detection and model checking': 3 learning paths (operators, supervisors, managers), 9 modules.
UFT-04-02 Define learning paths and modules R: Instructional Designer	MP-05.2 Define learning path and modules	Path 'Supervisors — BIM modelling and ISO 19650 workflows': 4 modules, 3 days blended (1 day e-learning, 2 days workshop). AI run: Path 'Supervisors — AI clash detection and model checking': 4 modules, 3 days blended (1 day e-learning, 2 days workshop).
UFT-04-03 Write learning objectives R: Instructional Designer	MP-05.3 Write learning objectives per module	Objective M1: 'By the end, the supervisor reads the BIM modelling and ISO 19650 workflows dashboard and decides the shift action in 5 minutes.' AI run: Objective M1: 'By the end, the supervisor reads the AI clash detection and model checking dashboard and decides the shift action in 5 minutes.'
UFT-04-04 Propose module structure R: Instructional Designer	MP-05.4 Propose module structure	Accept the proposed structure (intro, demo, practice, quiz); replace the quiz by a live case from Site Works & Project Delivery.
UFT-04-05 Set assessment strategy R: Instructional Designer	MP-05.5 Set assessment strategy	Assessment: pre/post test (Level 2) and manager observation after 30 days (Level 3).

Task	Steps	What to type
UFT-04-06 Develop and tag content R: Content Developer	MP-06.1 Upload content assets MP-06.2 Validate package format MP-06.5 Tag content with competencies	Upload 'M1_BIM modelling and ISO 19650 workflows.pptx' and 'M1_video.mp4'; tag competency 'BIM modelling and ISO 19650 workflows' level 3. AI run: Upload 'M1_AI clash detection and model checking.pptx' and 'M1_video.mp4'; tag competency 'AI clash detection and model checking' level 3.
UFT-04-07 Localize and check accessibility R: Instructional Designer	MP-23.1 Request translation MP-23.2 Draft machine translation MP-23.3 Validate translation MP-23.4 Run accessibility check MP-23.5 Fix accessibility issues	Request FR and AR versions; validate the AI draft translation; accessibility check: 0 blocking issues.
UFT-04-08 Approve design document R: Head of L&D	MP-05.6 Review design with subject matter expert MP-05.7 Approve design document	Decision: design approved. Comment: SME review done on 12 May; ready for delivery.

E2E-05 · Design-to-Delivery

Goal: Deliver training across all modalities. **Starts when:** Approved design document and prioritized training plan.

Ends when: Training delivered across all modalities with attendance and completion recorded.

Task	Steps	What to type
UFT-05-01 Publish content to catalog R: Content Developer	MP-06.3 Route content for expert review MP-06.4 Record review decision MP-06.6 Publish content to catalog	Publish module 'M1 BIM modelling and ISO 19650 workflows' to the catalog; audience: supervisors; languages EN/FR/AR. AI run: Publish module 'M1 AI clash detection and model checking' to the catalog; audience: supervisors; languages EN/FR/AR.
UFT-05-02 Book logistics R: Training Administrator	MP-11.1 Book rooms and equipment MP-11.2 Manage trainer calendars	Room 'Training A' (20 seats) 3-5 June; projector; trainer calendar blocked.
UFT-05-03 Schedule sessions R: Training Administrator	MP-07.1 Create training session MP-07.2 Check scheduling conflicts	Session S-01 'BIM modelling and ISO 19650 workflows — supervisors', 3-5 June, 12 seats, no conflict reported. AI run: Session S-01 'AI clash detection and model checking — supervisors', 3-5 June, 12 seats, no conflict reported.
UFT-05-04 Enroll learners and send convocations R: Training Administrator	MP-07.3 Enroll learners into session MP-07.4 Send convocations MP-17.1 Provision users via SSO	Enroll 12 supervisors; convocations sent by e-mail and SMS in each learner's language.
UFT-05-05 Push microlearning capsules R: Instructional Designer	MP-25.1 Author microlearning capsule MP-25.2 Generate capsule draft from source MP-25.3 Push capsule to collaboration channel MP-25.4 Consume capsule on mobile MP-25.5 Track capsule completion	Capsule '5-minute Digital site diary and field reporting check' pushed to the Teams channel of Site Works & Project Delivery; 48 views in week 1. AI run: Capsule '5-minute AI safety monitoring with site cameras check' pushed to the Teams channel of Site Works & Project Delivery; 48 views in week 1.
UFT-05-06 Run immersive simulations R: Trainer	MP-30.1 Define simulation scenario MP-30.2 Configure simulation scoring MP-30.3 Launch simulation session MP-30.4 Capture simulation performance MP-30.5 Debrief learner MP-30.6 Record simulation evidence	Simulation 'Site Works & Project Delivery incident': score 78/100; debrief notes recorded; evidence saved.

Task	Steps	What to type
UFT-05-07 Record attendance R: Trainer	MP-07.5 Record attendance	Attendance S-01: 11 present, 1 absent (justified). Signature sheet attached.
UFT-05-08 Close sessions R: Training Administrator	MP-07.6 Close session and record completion	Close S-01: 11 completions recorded; certificate issued to each participant.
UFT-05-09 Reconcile and archive period R: Training Administrator	MP-11.5 Reconcile attendance with invoices MP-11.6 Archive period records MP-11.3 Import external training records MP-11.4 Correct training record with justification	Reconcile invoice INV-2026-118 (3 days × 12 learners) with attendance; archive period Q2.

E2E-06 · Learner-Journey-to-Engagement

Goal: Deliver personalized, engaging learning experience. **Starts when:** Learner enrolled in a learning path or session. **Ends when:** Personalized learning journey completed with engagement measured.

Task	Steps	What to type
UFT-06-01 Generate personal learning plan R: L&D Analyst	MP-08.1 Generate personal learning plan	Personal plan generated for each learner: 3 items on BIM modelling and ISO 19650 workflows, 1 capsule on Digital site diary and field reporting. AI run: Personal plan generated for each learner: 3 items on AI clash detection and model checking, 1 capsule on AI safety monitoring with site cameras.
UFT-06-02 Recommend learning items R: Learner	MP-08.2 Recommend learning items MP-24.1 Enable personalization per scope	Accept 2 recommendations, reject 1 ('already mastered'). The outcome is logged.
UFT-06-03 Adapt path to performance R: Instructional Designer	MP-24.2 Set adaptation rules MP-24.3 Adapt path to learner performance MP-24.4 Record learner response to adaptation	Rule: if the quiz score < 60%, add the remedial capsule 'BIM modelling and ISO 19650 workflows basics'. AI run: Rule: if the quiz score < 60%, add the remedial capsule 'AI clash detection and model checking basics'.
UFT-06-04 Animate social learning R: Knowledge Manager	MP-26.1 Create learning cohort group MP-26.2 Invite group members MP-26.3 Post question or answer MP-26.4 Endorse expert answer MP-26.5 Flag inappropriate content MP-26.6 Resolve moderation flag	Create cohort 'BIM modelling and ISO 19650 workflows supervisors 2026' and invite 12 members; first question posted. AI run: Create cohort 'AI clash detection and model checking supervisors 2026' and invite 12 members; first question posted.
UFT-06-05 Run gamification R: Instructional Designer	MP-27.1 Define points and badge rules MP-27.2 Configure leaderboard scope MP-27.3 Award points on completion MP-27.4 Unlock badge MP-27.6 Adjust gamification rules	Badge 'BIM modelling and ISO 19650 workflows Practitioner' for completing 3 modules; 10 points per capsule. AI run: Badge 'AI clash detection and model checking Practitioner' for completing 3 modules; 10 points per capsule.
UFT-06-06 Match and run coaching R: L&D Business Partner	MP-21.1 Request coaching MP-21.2 Match coach to learner MP-21.3 Schedule coaching sessions MP-21.4 Log coaching session notes MP-21.5 Evaluate coaching outcomes MP-21.6 Close coaching engagement	Match coach 'Senior Site Works & Project Delivery supervisor' to 3 learners; 4 sessions of 1 hour.

Task	Steps	What to type
UFT-06-07 Collect learner feedback R: Learner	MP-08.3 Enroll in recommended item MP-08.4 Submit learning feedback	Feedback: 4.4/5; comment 'more real cases from Site Works & Project Delivery'.
UFT-06-08 Monitor engagement and nudge R: L&D Analyst	MP-08.5 Monitor engagement indicators MP-08.6 Trigger re-engagement nudge MP-24.5 Review recommendation acceptance MP-27.5 Review engagement uplift MP-24.6 Tune personalization settings MP-28.4 Predict learner drop-out risk MP-28.5 Review predictions with L&D MP-28.6 Create preventive action	Engagement 81%; nudge sent to 9 inactive learners; drop-out risk high for 2 learners.

E2E-13 · Content-Curate-to-Retire

Goal: Publish, maintain, retire content. **Starts when:** New content published or content past its review date. **Ends when:** Catalog curated, maintained and outdated content retired.

Task	Steps	What to type
UFT-13-01 Aggregate provider catalogs R: Content Curator	MP-29.1 Aggregate provider catalogs	Aggregate 2 provider catalogs (LinkedIn Learning, Coursera): 1,240 items imported.
UFT-13-02 Recommend curated items R: Content Curator	MP-29.2 Recommend curated items	Keep the 15 top-ranked items on BIM modelling and ISO 19650 workflows; reject 3 items older than 3 years. AI run: Keep the 15 top-ranked items on AI clash detection and model checking; reject 3 items older than 3 years.
UFT-13-03 Approve and organize collections R: Content Curator	MP-29.3 Approve curated item MP-29.4 Organize curated collection	Collection 'BIM modelling and ISO 19650 workflows starter kit': 8 items, audience supervisors, review date in 12 months. AI run: Collection 'AI clash detection and model checking starter kit': 8 items, audience supervisors, review date in 12 months.
UFT-13-04 Review peer content R: Subject Matter Expert	MP-33.1 Submit user-generated content MP-33.2 Check content against policy MP-33.3 Peer review content	Peer video 'How we use Digital site diary and field reporting on shift' reviewed by an expert: approved with 1 correction. AI run: Peer video 'How we use AI safety monitoring with site cameras on shift' reviewed by an expert: approved with 1 correction.
UFT-13-05 Promote and rate content R: Knowledge Manager	MP-33.5 Send approved content to curation MP-33.6 Rate user-generated item	Send approved peer content to curation; average learner rating 4.5/5.
UFT-13-06 Flag content past review date R: Content Curator	MP-29.5 Flag content past review date	14 items past review date flagged; owners notified.
UFT-13-07 Retire outdated content R: Content Curator	MP-29.6 Retire outdated content MP-25.6 Retire low-value capsule	Retire 6 outdated items and 2 low-value capsules; library health 92%.

E2E-14 · Extended-Enterprise-Training

Goal: Certify partners and train customers. **Starts when:** Partner, reseller or customer training program launched. **Ends when:** External learners trained, paid and certified.

Task	Steps	What to type
UFT-14-01 Create external sub-portal R: Extended Enterprise Manager	MP-22.1 Create external sub-portal	Sub-portal 'Partners Academy — Souss BTP Solutions' created for distributors and installers.
UFT-14-02 Configure catalog and pricing R: Extended Enterprise Manager	MP-22.2 Configure external catalog and pricing MP-18.1 Allocate budget by theme and site	Catalog: 'ISO 19650 for partners' 1,200 MAD; 'BIM modelling and ISO 19650 workflows certification' 2,400 MAD. AI run: Catalog: 'ISO 19650 for partners' 1,200 MAD; 'AI clash detection and model checking certification' 2,400 MAD.
UFT-14-03 Process payment and enroll R: Extended Enterprise Manager	MP-22.3 Process online payment MP-22.4 Enroll external learner	18 online payments processed; 18 external learners enrolled.
UFT-14-04 Deliver external sessions R: Training Administrator	MP-07.1 Create training session MP-07.5 Record attendance	Session P-01 (virtual), 18 invited, 16 present.
UFT-14-05 Track external completion R: Extended Enterprise Manager	MP-22.5 Track external completion	Completion: 15 of 16 passed the final quiz.
UFT-14-06 Issue partner certification R: Extended Enterprise Manager	MP-22.6 Issue partner certification MP-14.4 Issue certificate on completion	Issue 15 partner certificates valid 2 years.
UFT-14-07 Reconcile external revenue R: Finance Manager	MP-18.3 Record committed and actual costs MP-18.4 Compare spend against budget	Revenue 43,200 MAD reconciled with the ERP; 0 unpaid.

SME-E2E-03 · SME Upskill-to-Adoption

Goal: Make sure new digital and AI skills are used at work.. **Starts when:** Funded plan launched. **Ends when:** Adoption confirmed and owner-manager coached.

Task	Steps	What to type
UFT-SME3-01 Assign microlearning capsules R: Training Administrator	SME-MP-03.1 Assign microlearning capsules MP-25.3 Push capsule to collaboration channel	Assign 4 capsules 'BIM modelling and ISO 19650 workflows in 10 minutes' to each employee. AI run: Assign 4 capsules 'AI clash detection and model checking in 10 minutes' to each employee.
UFT-SME3-02 Coach on the job R: Trainer	SME-MP-03.2 Coach employees on the job	On-the-job coaching: 2 hours per team leader per week for 4 weeks.
UFT-SME3-03 Measure adoption R: L&D Analyst	SME-MP-03.3 Measure tool usage	Adoption: 9 of 12 employees use the new tool every day.
UFT-SME3-04 Coach the owner-manager R: Consultant PM	SME-MP-04.1 Hold monthly coaching session SME-MP-04.2 Update skills dashboard	Monthly coaching with the owner-manager; skills dashboard updated.

8.6 Evaluation, compliance & impact — gate G5

E2E-07 · Assessment-to-Evaluation

Goal: Measure training effectiveness and skill progression. **Starts when:** Training session or path completed. **Ends when:** Effectiveness measured on Kirkpatrick levels 1-3 and skill progression computed.

Task	Steps	What to type
UFT-07-01 Create assessment instrument R: Instructional Designer	MP-09.1 Create assessment instrument	Instrument 'Test BIM modelling and ISO 19650 workflows M1': 15 questions, pass mark 70%. AI run: Instrument 'Test AI clash detection and model checking M1': 15 questions, pass mark 70%.
UFT-07-02 Draft question bank R: Instructional Designer	MP-09.2 Generate question bank draft	Keep 12 AI-drafted questions, rewrite 3 with Site Works & Project Delivery vocabulary; validate each one.
UFT-07-03 Collect reaction survey (Level 1) R: L&D Analyst	MP-09.3 Collect reaction survey (Level 1)	Reaction survey S-01: 11 responses, satisfaction 4.3/5.
UFT-07-04 Record learning results (Level 2) R: Trainer	MP-09.4 Record learning results (Level 2)	Level 2: average pre-test 48%, post-test 81% (+33 points).
UFT-07-05 Record on-the-job observation (Level 3) R: Manager	MP-09.5 Record on-the-job observation (Level 3)	Level 3 (day 30): 9 of 11 supervisors apply the BIM modelling and ISO 19650 workflows routine daily. AI run: Level 3 (day 30): 9 of 11 supervisors apply the AI clash detection and model checking routine daily.
UFT-07-06 Compute skill progression R: L&D Analyst	MP-09.6 Compute skill progression MP-10.3 Refresh KPI computation	Skill progression: BIM modelling and ISO 19650 workflows from 1.8 to 2.7 (target 3). AI run: Skill progression: AI clash detection and model checking from 1.8 to 2.7 (target 3).
UFT-07-07 Review evaluation results R: L&D Analyst	MP-09.7 Review evaluation results MP-20.5 Run periodic quality review	Review: module M3 below 70% pass rate → improvement action assigned to the designer.
UFT-07-08 Publish evaluation report R: L&D Analyst	MP-10.4 Export report MP-10.6 Share insight with stakeholders MP-10.2 Configure dashboard widgets	Export RPT-016 Kirkpatrick report (PDF) and share with the Steering Committee.

E2E-08 · Learning-to-ROI

Goal: Validate ROI and business impact. **Starts when:** Evaluation results available for a theme selected for an ROI study. **Ends when:** Phillips ROI validated with finance and business impact report published.

Task	Steps	What to type
UFT-08-01 Select theme for ROI study R: Performance Analyst	MP-32.1 Select theme for ROI study	ROI study on theme 'BIM modelling and ISO 19650 workflows' — population: 36 supervisors, 3 sites. AI run: ROI study on theme 'AI clash detection and model checking' — population: 36 supervisors, 3 sites.
UFT-08-02 Define business indicators R: Performance Analyst	MP-32.2 Define business indicators MP-10.1 Define KPI set per audience	Indicators: rework rate, downtime minutes per shift, data re-entry hours.

Task	Steps	What to type
UFT-08-03 Collect cost data R: Finance Manager	MP-18.3 Record committed and actual costs MP-18.4 Compare spend against budget	Costs: design 60,000 MAD; delivery 180,000 MAD; participants' time 95,000 MAD.
UFT-08-04 Isolate training effect R: Performance Analyst	MP-32.3 Isolate training effect MP-09.6 Compute skill progression	Control group: site B (not trained). Isolated benefit: 410,000 MAD per year.
UFT-08-05 Compute Phillips ROI R: Performance Analyst	MP-32.4 Compute Phillips ROI	$ROI = (410,000 - 335,000) / 335,000 = 22\%$; benefit-cost ratio 1.22.
UFT-08-06 Review ROI with finance R: Finance Manager	MP-32.5 Review ROI with finance	Finance review: assumptions accepted; downtime valued at 180 MAD per minute.
UFT-08-07 Publish business impact report R: Head of L&D	MP-32.6 Publish business impact report MP-10.4 Export report MP-10.5 Query data via AI Assistant	Publish RPT-012 ROI & Business Impact Report to executive leadership.

E2E-09 · Compliance-to-Certification

Goal: Ensure compliant workforce with valid certifications. **Starts when:** New regulatory requirement or certification nearing expiry. **Ends when:** Compliant workforce with valid certifications and an audit extract available.

Task	Steps	What to type
UFT-09-01 Register regulatory requirement R: Compliance Officer	MP-14.1 Register regulatory requirement	Requirement 'ISO 19650 awareness', every 24 months, source: ISO 19650 clause on competence.
UFT-09-02 Assign mandatory training R: Compliance Officer	MP-14.2 Assign mandatory training by position	Assign to positions: Site Works & Project Delivery operator, Site Works & Project Delivery supervisor, quality inspector.
UFT-09-03 Deliver mandatory sessions R: Training Administrator	MP-07.3 Enroll learners into session MP-07.5 Record attendance	Enroll 24 employees in session 'ISO 19650 awareness'; attendance recorded.
UFT-09-04 Assess and certify R: Trainer	MP-09.4 Record learning results (Level 2) MP-14.4 Issue certificate on completion	Result 86%; certificate 'ISO 19650 awareness' issued, valid until 2026+2.
UFT-09-05 Compute certification validity R: Compliance Officer	MP-14.3 Compute certification validity	Validity: 212 valid, 9 expire within 60 days, 3 expired.
UFT-09-06 Manage renewals R: Compliance Officer	MP-14.5 Launch renewal enrollment MP-14.6 Confirm renewal completion	Launch renewal for the 12 employees; confirm 10 completions, 2 rescheduled.
UFT-09-07 Produce compliance audit extract R: Compliance Officer	MP-14.7 Produce compliance audit extract MP-10.4 Export report	Export compliance audit extract for ISO 19650 (XLSX) for the external auditor.

AEC-E2E-01 · AEC & Construction Compliance-to-Certification Readiness

Goal: Keep AEC & Construction regulated roles certified against ISO 19650.. **Starts when:** New ISO 19650 requirement or certification expiry. **Ends when:** Sector compliance extract issued with every critical role certified.

Task	Steps	What to type
UFT-AEC-E1-01 Register ISO 19650 obligations R: Compliance Officer	MP-01.1 Record corporate strategic objectives MP-14.1 Register regulatory requirement	Obligation 'ISO 19650 training', every 12 months, owner Compliance Officer.
UFT-AEC-E1-02 Link obligations to positions R: HR Business Partner	MP-01.2 Link objectives to functions and sites MP-14.2 Assign mandatory training by position	Linked to 5 Site Works & Project Delivery positions (38 employees).
UFT-AEC-E1-03 Track certification validity R: Compliance Officer	MP-02.1 Define competency families and levels MP-14.3 Compute certification validity	Validity: 33 valid, 5 expire within 60 days.
UFT-AEC-E1-04 Issue sector compliance extract R: Compliance Officer	MP-02.2 Set target levels per position MP-14.7 Produce compliance audit extract	Extract issued for the ISO 19650 audit on 15 October.

8.7 Talent, knowledge & continuous improvement — gate G6

E2E-10 · Talent-to-Mobility

Goal: Enable internal mobility and career progression. **Starts when:** Internal opening published or annual career review. **Ends when:** Internal move decided with a reskilling plan assigned.

Task	Steps	What to type
UFT-10-01 Model career paths R: HR Director	MP-13.1 Model career path MP-13.2 Link path steps to competency targets	Career path: Site Works & Project Delivery operator → team leader → supervisor, with competency targets per step.
UFT-10-02 Publish internal opening R: HR Business Partner	MP-31.1 Publish internal opening MP-31.2 Define required skills	Opening 'Site Works & Project Delivery team leader', required skills: BIM modelling and ISO 19650 workflows level 3, leadership level 2. AI run: Opening 'Site Works & Project Delivery team leader', required skills: AI clash detection and model checking level 3, leadership level 2.
UFT-10-03 Match employees to opening R: HR Business Partner	MP-31.3 Match employees to opening MP-02.7 Validate skills inventory	Review 6 AI matches; keep 4 candidates with match score above 75%.
UFT-10-04 Apply to internal opening R: Employee	MP-31.4 Apply to internal opening	Application with motivation note and consent of the current manager.
UFT-10-05 Shortlist candidates R: Hiring Manager	MP-31.5 Shortlist candidates	Shortlist: 2 candidates; interviews on 20 and 21 June.

Task	Steps	What to type
UFT-10-06 Plan individual development R: Manager	MP-13.3 Create individual development plan MP-13.4 Suggest development actions MP-42.3 Build leadership development plan MP-42.4 Suggest leadership development actions	Development plan: 2 modules BIM modelling and ISO 19650 workflows, 1 leadership workshop, 3 months mentoring. AI run: Development plan: 2 modules AI clash detection and model checking, 1 leadership workshop, 3 months mentoring.
UFT-10-07 Assign reskilling plan R: HR Business Partner	MP-31.6 Assign reskilling plan MP-08.1 Generate personal learning plan	Assign reskilling path 'BIM modelling and ISO 19650 workflows for team leaders' to the selected candidate. AI run: Assign reskilling path 'AI clash detection and model checking for team leaders' to the selected candidate.
UFT-10-08 Review career and succession R: HR Director	MP-13.5 Run career review MP-13.6 Update succession readiness MP-42.5 Review leadership pipeline MP-42.6 Reassess leadership maturity	Succession readiness updated: 2 ready now, 3 ready within 12 months.

E2E-11 · Onboarding-to-Productivity

Goal: Accelerate time-to-productivity. **Starts when:** New hire or internal mover confirmed. **Ends when:** Employee productive within target time and onboarding closed.

Task	Steps	What to type
UFT-11-01 Create onboarding record R: Hiring Manager	MP-35.1 Create onboarding record	Onboarding record for the new Site Works & Project Delivery technician, start date 1 July, buddy assigned.
UFT-11-02 Generate 30-60-90 day path R: HR Business Partner	MP-35.2 Generate 30-60-90 day path MP-08.1 Generate personal learning plan	30-60-90 path: day 30 safety and ISO 19650; day 60 BIM modelling and ISO 19650 workflows; day 90 autonomy on shift. AI run: 30-60-90 path: day 30 safety and ISO 19650; day 60 AI clash detection and model checking; day 90 autonomy on shift.
UFT-11-03 Enroll in onboarding sessions R: Training Administrator	MP-07.3 Enroll learners into session MP-07.4 Send convocations	Enroll in the induction session of 2 July; convocation sent.
UFT-11-04 Complete onboarding tasks R: Employee	MP-35.3 Complete onboarding tasks	Tasks done: badge, IT account, safety tour, meeting with the team.
UFT-11-05 Hold milestone check-ins R: Hiring Manager	MP-35.4 Hold milestone check-in MP-21.3 Schedule coaching sessions	Day-30 check-in: on track; coaching needed on BIM modelling and ISO 19650 workflows data entry. AI run: Day-30 check-in: on track; coaching needed on AI clash detection and model checking data entry.
UFT-11-06 Assess time to productivity R: Hiring Manager	MP-35.5 Assess time to productivity	Time to productivity: 74 days (target 90).
UFT-11-07 Close onboarding R: HR Business Partner	MP-35.6 Close onboarding MP-13.3 Create individual development plan	Close onboarding; link the individual development plan for year 1.

E2E-12 · Knowledge-Capture-to-Transfer

Goal: Capture and transfer institutional knowledge. **Starts when:** Critical expert identified as leaving, retiring or holding at-risk knowledge. **Ends when:** Knowledge captured, published and transferred to a validated successor.

Task	Steps	What to type
UFT-12-01 Identify critical experts R: HR Business Partner	MP-34.1 Identify critical experts	Critical expert: senior Site Works & Project Delivery engineer retiring in 8 months; knowledge risk: high.
UFT-12-02 Plan capture sessions R: Knowledge Manager	MP-34.2 Plan capture sessions	Capture plan: 4 sessions of 90 minutes on troubleshooting and ISO 19650 practices.
UFT-12-03 Record expert interview R: Knowledge Manager	MP-34.3 Record expert interview	Interview 1 recorded (82 minutes); transcript attached.
UFT-12-04 Structure knowledge R: Knowledge Manager	MP-34.4 Structure knowledge from transcript	Accept the AI structure: 5 failure modes, 12 checks, 3 decision rules; correct 2 technical terms.
UFT-12-05 Publish knowledge article R: Knowledge Manager	MP-12.1 Publish knowledge article MP-12.2 Index article for retrieval MP-33.4 Approve publication	Publish article 'Troubleshooting guide — Site Works & Project Delivery' in EN/FR/AR; indexed for search.
UFT-12-06 Assign successor learning path R: Manager	MP-34.5 Assign successor learning path MP-06.6 Publish content to catalog	Assign the successor path: article + 3 shadowing sessions with the expert.
UFT-12-07 Validate transfer completion R: Subject Matter Expert	MP-34.6 Validate transfer completion	Transfer validated: successor solved 4 of 5 test cases alone.

E2E-31 · Engagement-to-Roadmap

Goal: Define post-engagement roadmap and continuous improvement. **Starts when:** Closure of the current training engineering engagement (E2E-19). **Ends when:** Approved post-engagement roadmap with future missions and continuous improvement plan.

Task	Steps	What to type
UFT-31-01 Consolidate engagement findings R: Consultant PM	MP-50.1 Consolidate engagement findings	Findings: 6 deliverables, 3 lessons learned, 2 open topics (IS, org design).
UFT-31-02 Define future perspectives R: Consultant PM	MP-50.2 Define future perspectives	Perspectives: Drone surveying and 3D site scans programme, second wave for OP level. AI run: Perspectives: AI cost and schedule forecasting programme, second wave for OP level.
UFT-31-03 Plan One-to-One coaching R: L&D Strategist	MP-50.3 Plan One-to-One coaching	One-to-One coaching: 6 managers, 6 sessions each over 6 months.
UFT-31-04 Plan organizational optimization R: Org Design Consultant	MP-50.4 Plan organizational optimization	Organizational optimization: merge 2 planning cells; update 11 descriptions.
UFT-31-05 Plan IS rehabilitation R: IT Architect	MP-50.5 Plan IS rehabilitation	IS rehabilitation: connect HRIS and training platform; retire 2 spreadsheets.

Task	Steps	What to type
UFT-31-06 Define KPIs and dashboards R: Performance Analyst	MP-50.6 Define KPIs and dashboards	KPIs: training coverage, time to competency, ROI per theme; monthly dashboard.
UFT-31-07 Prioritize future missions R: Consultant PM	MP-50.7 Prioritize future missions MP-50.8 Validate roadmap with leadership	Priority missions: 1 IS rehabilitation, 2 coaching, 3 org optimization.
UFT-31-08 Publish roadmap R: Consultant PM	MP-50.9 Publish post-engagement roadmap MP-50.10 Track roadmap execution MP-50.11 Improve roadmap continuously MP-50.12 Report on roadmap progress	Publish RPT-010 Post-Engagement Roadmap to the executive committee.

9. SMEs in healthcare

This part follows Clinique Al Amal, a SME in the Healthcare Providers sector (95 employees, Marrakech, member of Souss-Massa SME Network). Sign in as headld@cliniquealamal.ma. The same steps apply to any organization of this type: replace the names, figures and themes with your own.

Item	Digital skills run	AI skills run
Project	Digital Skills Full Run 2026 — Clinique Al Amal	AI Skills Full Run 2026 — Clinique Al Amal
Mode and track	SME · SME-T3	SME · SME-T3
Processes and tasks	38 processes · 277 tasks	38 processes · 277 tasks

Phase	Gate	End-to-end processes
Enablers (run across all phases)	—	E2E-15, E2E-17, E2E-18
Scope & evidence	G1	E2E-32, E2E-33, E2E-19, E2E-24, SME-E2E-01
Diagnosis	G2	E2E-20, E2E-25, E2E-26, E2E-27, E2E-28, E2E-29, E2E-02, E2E-21
Training Engineering Report & plan	G3	E2E-01, E2E-03, E2E-30, E2E-22, E2E-23, E2E-16, HCPR-E2E-02, SME-E2E-02
Design & delivery	G4	E2E-04, E2E-05, E2E-06, E2E-13, E2E-14, SME-E2E-03
Evaluation, compliance & impact	G5	E2E-07, E2E-08, E2E-09, HCPR-E2E-01
Talent, knowledge & continuous improvement	G6	E2E-10, E2E-11, E2E-12, E2E-31

9.1 Enablers (run across all phases)

E2E-15 · Data-AI-Integration

Goal: Govern data, AI, integrations. **Starts when:** New integration, data source or AI use case to govern. **Ends when:** Integrations, data and AI governed with health, retention and usage reviewed.

Task	Steps	What to type
UFT-15-01 Register external integration R: Platform Administrator	MP-16.1 Register external integration	Register integration 'HRIS — Workday' (INT-HR-01); credential reference stored encrypted.
UFT-15-02 Map fields and check health R: IT Architect	MP-16.2 Map integration fields MP-16.3 Check integration health	Map fields: employee_id → matricule; position → poste. Health check: success.
UFT-15-03 Run HRIS synchronisation R: IT Architect	MP-16.4 Run HRIS synchronisation MP-16.5 Review synchronisation rejections	Sync run: 1,204 records updated, 3 rejected (missing position) — corrected.
UFT-15-04 Set data retention rule R: Data Protection Officer	MP-16.6 Set data retention rule	Retention: questionnaire responses 3 years; training records 10 years.

Task	Steps	What to type
UFT-15-05 Maintain AI use case register R: Platform Administrator	MP-16.7 Maintain AI use case register	Add custom use case 'Shift-report summarizer' (Assistive), version 1.
UFT-15-06 Set AI activation per scope R: Platform Administrator	MP-16.8 Set AI activation per scope MP-24.1 Enable personalization per scope	Activate AIUC-35 and AIUC-36 for the organization; override Off for pilot project B.
UFT-15-07 Review AI usage log R: IT Architect	MP-16.9 Review AI usage log MP-28.2 Validate dataset quality	Usage review: 412 suggestions — 71% accepted, 20% edited, 9% rejected.

E2E-17 · Change-to-Adoption

Goal: Drive sustained adoption and culture change. **Starts when:** Approved plan or new platform capability requiring adoption. **Ends when:** Sustained adoption reached with low-adoption groups reinforced.

Task	Steps	What to type
UFT-17-01 Assess change impact R: Change Manager	MP-19.1 Assess change impact	Impact: Clinical Care & Nursing supervisors high, operators medium, support functions low.
UFT-17-02 Build adoption plan R: Change Manager	MP-19.2 Build adoption plan	Adoption plan: sponsor message, 6 champions, weekly 15-minute huddles for 8 weeks.
UFT-17-03 Launch communication campaign R: Change Manager	MP-19.3 Launch communication campaign	Campaign 'Electronic health records (EHR) — why it matters' on e-mail, intranet and screens. AI run: Campaign 'AI triage and clinical decision support — why it matters' on e-mail, intranet and screens.
UFT-17-04 Open community space R: Knowledge Manager	MP-12.3 Create community space MP-12.4 Moderate community posts MP-26.1 Create learning cohort group	Community space 'Electronic health records (EHR) Q&A' opened; moderation rules published. AI run: Community space 'AI triage and clinical decision support Q&A' opened; moderation rules published.
UFT-17-05 Track adoption usage R: L&D Analyst	MP-19.4 Track adoption usage MP-08.5 Monitor engagement indicators	Weekly active users: 64% of the target population.
UFT-17-06 Identify low-adoption groups R: Change Manager	MP-19.5 Identify low-adoption groups	Low adoption confirmed for night shift (31%); one group rejected as false positive.
UFT-17-07 Run reinforcement actions R: Change Manager	MP-19.6 Run reinforcement actions MP-08.6 Trigger re-engagement nudge	Reinforcement: night-shift coaching sessions; adoption reached 58% after 4 weeks.

E2E-18 · Quality-Risk-Improvement

Goal: Improve processes and mitigate risk. **Starts when:** Risk logged, periodic quality review due or control test scheduled. **Ends when:** Risks mitigated, actions evaluated by a different person, controls rated.

Task	Steps	What to type
UFT-18-01 Log risk or opportunity R: Quality Manager	MP-20.1 Log risk or opportunity	Risk 'Trainers unavailable in Q3': likelihood 3, impact 4, score 12.

Task	Steps	What to type
UFT-18-02 Assign mitigation action R: Quality Manager	MP-20.2 Assign mitigation action	Action: contract a second vendor; owner Purchasing Officer; evaluator Quality Manager.
UFT-18-03 Execute improvement action R: Action Owner	MP-20.3 Execute improvement action	Action done: framework contract signed with vendor B; evidence attached.
UFT-18-04 Evaluate action effectiveness R: Action Evaluator	MP-20.4 Evaluate action effectiveness	Verdict: effective. The evaluator is a different user from the owner.
UFT-18-05 Review access and security R: IT Architect	MP-17.4 Review access violation log MP-17.6 Enforce login rate limit MP-17.2 Assign roles to user MP-17.3 Edit permission matrix MP-17.5 Issue signed session token	Access review: 2 dormant accounts disabled; 0 cross-tenant attempts.
UFT-18-06 Run periodic quality review R: Quality Manager	MP-20.5 Run periodic quality review MP-09.7 Review evaluation results	Quality review minutes: 3 KPIs red, 2 actions opened, next review in 30 days.
UFT-18-07 Update control effectiveness R: Quality Manager	MP-20.6 Update control effectiveness rating	Control CTRL-002 effectiveness: Effective; CTRL-031: Partially effective.

9.2 Scope & evidence — gate G1

E2E-32 · Scope-of-Work-to-Engineering-Plan

Goal: Define and approve the structured scope of work and stakeholder register. **Starts when:** New training engineering engagement, annual plan cycle, or executive request. **Ends when:** Approved Scope of Work with criteria matrix and stakeholder register released to questionnaire design (E2E-33) and needs analysis (E2E-03).

Task	Steps	What to type
UFT-32-01 Define scope frame R: Head of L&D	MP-53.1 Define scope frame (Group Yes/No) MP-53.2 Select Organization	Group scope: No. Organization: Clinique Al Amal.
UFT-32-02 Select sector R: L&D Analyst	MP-53.3 Select sector	Sector: Healthcare Providers.
UFT-32-03 Select decision levels R: L&D Analyst	MP-53.4 Select decision level (MS/MO/OP/Custom)	Decision levels: MS, MO, OP (no custom level).
UFT-32-04 Map functions × decision levels R: L&D Analyst	MP-53.5 Map functions × decision level	Matrix: Clinical Care & Nursing × MS/MO/OP; Quality × MO/OP; Finance × MS/MO; HR × MS/MO.
UFT-32-05 Select focus and add custom criteria R: Head of L&D	MP-53.6 Select focus (All/Digital/AI/Custom) MP-53.7 Add custom criteria	Focus: Digital. Custom criterion: 'Readiness for Electronic health records (EHR)' (weight 2.00). AI run: Focus: AI. Custom criterion: 'Readiness for AI triage and clinical decision support' (weight 2.00).
UFT-32-06 Identify stakeholders R: HR Business Partner	MP-53.8 Identify stakeholders	Register 40 stakeholders: name, role, function, level, site, preferred channel (Email, Face-to-Face or Hybrid).

Task	Steps	What to type
UFT-32-07 Validate scope R: Head of L&D	MP-53.9 Validate and approve scope	Validation: every function in scope has at least 3 stakeholders; completeness 100%.
UFT-32-08 Approve scope R: HR Director / Consultant PM	MP-53.9 Validate and approve scope MP-53.10 Publish scope and register stakeholders	Approval status: Approved (version 1). Justification: scope aligned with SO-1 and SO-2.
UFT-32-09 Publish scope and register stakeholders R: L&D Analyst	MP-53.10 Publish scope and register stakeholders	Generate the SOW document (RPT-033) and release scope and stakeholders to the questionnaire studio.

E2E-33 · Questionnaire-to-Response-Collection

Goal: Design, distribute and collect questionnaire responses across channels. **Starts when:** An approved Scope of Work becomes available (end of E2E-32). **Ends when:** Consolidated, validated questionnaire response dataset feeding needs analysis (E2E-03), diagnostic (E2E-20) and demand collection (E2E-27).

Task	Steps	What to type
UFT-33-01 Select questionnaire template R: L&D Analyst	MP-54.1 Select questionnaire template by focus	Template: 'Digital needs — Healthcare Providers' in the user's language, 5 sections. AI run: Template: 'AI needs — Healthcare Providers' in the user's language, 5 sections.
UFT-33-02 Elaborate questionnaire R: L&D Analyst	MP-54.2 Elaborate questionnaire (Load/AI/Manual)	Elaboration mode: AI. 24 questions generated from the approved Scope of Work.
UFT-33-03 Tailor and validate content R: L&D Analyst	MP-54.3 Tailor to sector and focus	Validate each question; reword 5 with Clinical Care & Nursing vocabulary; delete 2 duplicates.
UFT-33-04 Allocate RACSI R: Head of L&D	MP-54.4 Allocate RACSI per section	Section 'Digital practices': R L&D Analyst, A Head of L&D, C Consultant PM, S IT, I CHRO (one Accountable only).
UFT-33-05 Select distribution channels R: Survey Administrator	MP-54.5 Select distribution channels	Channels: MS and MO by Email; OP Face-to-Face with tablets; night shift Hybrid.
UFT-33-06 Distribute questionnaire R: Survey Administrator	MP-54.6 Distribute to stakeholders	Distribute to 40 stakeholders; 40 dispatches logged.
UFT-33-07 Send reminders R: Survey Administrator	MP-54.7 Send reminders on cadence	Reminder 1 on day 5 to 17 non-respondents; reminder 2 on day 10 to 8.
UFT-33-08 Collect responses R: Stakeholders	MP-54.8 Collect responses	Responses: 34 collected (22 online, 12 offline synchronised).
UFT-33-09 Validate completeness R: L&D Analyst	MP-54.9 Validate completeness and consent	Completeness: 31 complete, 3 incomplete flagged.
UFT-33-10 Consolidate responses R: L&D Analyst	MP-54.10 Consolidate responses	Consolidated dataset: 31 responses, 24 questions, by function and level.

Task	Steps	What to type
UFT-33-11 Check consent and release dataset R: L&D Analyst	MP-54.11 Feed responses to needs analysis and diagnostic MP-54.12 Report on response rate and engagement	Consent given for 31 of 31 stored responses; release to needs analysis, diagnostic and demand collection.
UFT-33-12 Report on response and engagement R: L&D Analyst	MP-54.12 Report on response rate and engagement	Response rate 85%; engagement rate 78%; completeness 91% (RPT-034).

E2E-19 · Consulting Engagement-to-Closure

Goal: Manage full consulting engagement lifecycle. **Starts when:** Client purchase order or engagement request received. **Ends when:** Engagement closed with client acceptance and REX recorded.

Task	Steps	What to type
UFT-19-01 Register engagement and purchase order R: Consultant PM	MP-36.1 Register engagement and purchase order	Engagement 'Training engineering 2026 — Clinique Al Amal', PO-CL-221, 45 consulting days.
UFT-19-02 Hold kickoff meeting R: Consultant PM	MP-36.2 Hold kickoff meeting	Kickoff held on 10 February with HR Director, Head of L&D and 4 function heads.
UFT-19-03 Draft meeting minutes R: Consultant PM	MP-36.3 Draft meeting minutes	Review the AI minutes: 6 decisions, 9 actions, RACSI extracted; correct 1 owner name.
UFT-19-04 Align with client strategy R: Consultant PM	MP-01.1 Record corporate strategic objectives MP-01.2 Link objectives to functions and sites	Client objectives recorded: Electronic health records (EHR) and ISO 7101 compliance for Clinical Care & Nursing. AI run: Client objectives recorded: AI triage and clinical decision support and ISO 7101 compliance for Clinical Care & Nursing.
UFT-19-05 Plan engagement work breakdown R: Consultant PM	MP-36.4 Plan engagement work breakdown	WBS: 6 phases, 14 deliverables, Gantt from February to November.
UFT-19-06 Plan change support R: Change Manager	MP-19.1 Assess change impact MP-19.2 Build adoption plan	Change plan: 3 sponsor messages, champion network, 2 town-halls.
UFT-19-07 Track engagement deliverables R: Consultant PM	MP-36.5 Track engagement deliverables MP-20.5 Run periodic quality review	Deliverables: 9 of 14 delivered on time, 1 late (SWOT), 4 planned.
UFT-19-08 Deliver final report and obtain acceptance R: Consultant PM	MP-36.6 Deliver final report MP-36.7 Obtain client acceptance	Final report delivered; acceptance signed by the HR Director on 28 November.
UFT-19-09 Record engagement REX R: Consultant PM	MP-36.8 Record engagement REX MP-12.6 Record REX entry MP-12.5 Prompt REX at closure	REX: went well — stakeholder register; did not — late SWOT inputs; root cause — no function-head backup; rating 4/5.

E2E-24 · Competitive Intelligence-to-Strategy

Goal: Analyze external environment and feed L&D strategy. **Starts when:** Annual strategy cycle or executive request for market positioning analysis. **Ends when:** Validated competitive intelligence report feeding into L&D strategy and organizational diagnostic.

Task	Steps	What to type
UFT-24-01 Define intelligence scope R: Strategy Analyst	MP-43.1 Define intelligence scope	Scope: Healthcare Providers market in Morocco and export markets; horizon 3 years; focus on Electronic health records (EHR) and Telemedicine and remote consultation. AI run: Scope: Healthcare Providers market in Morocco and export markets; horizon 3 years; focus on AI triage and clinical decision support and AI medical imaging assistance.
UFT-24-02 Conduct Porter's Five Forces R: Strategy Analyst	MP-43.2 Conduct Porter's Five Forces analysis	Rivalry 4/5; new entrants 3/5; substitutes 2/5; supplier power 3/5; buyer power 4/5.
UFT-24-03 Map market segments R: Market Analyst	MP-43.3 Map market segments	Segments: key accounts (55% revenue), resellers (30%), direct small customers (15%).
UFT-24-04 Analyze competitor positioning R: Market Analyst	MP-43.4 Analyze competitor positioning	Competitor A leads on Electronic health records (EHR); competitor B cheaper but weaker on ISO 7101. AI run: Competitor A leads on AI triage and clinical decision support; competitor B cheaper but weaker on ISO 7101.
UFT-24-05 Monitor regulatory and technology trends R: Regulatory Analyst	MP-43.5 Monitor regulatory changes MP-43.6 Track technology trends MP-43.7 Benchmark against industry	Trends: revision of ISO 7101 expected next year; fast growth of Digital patient scheduling and billing. AI run: Trends: revision of ISO 7101 expected next year; fast growth of AI bed and staff capacity planning.
UFT-24-06 Identify L&D implications R: L&D Strategist	MP-43.8 Identify strategic implications for L&D	L&D implication: build Electronic health records (EHR) skills for key-account teams before competitor A scales. AI run: L&D implication: build AI triage and clinical decision support skills for key-account teams before competitor A scales.
UFT-24-07 Publish intelligence report R: Strategy Analyst	MP-43.9 Produce intelligence report MP-43.10 Feed intelligence into strategy and diagnostic MP-43.11 Update intelligence continuously MP-43.12 Report to executive leadership	Publish RPT-007 Competitive Intelligence Report to the executive committee.

SME-E2E-01 · SME Snapshot-to-Plan in 30 days

Goal: Turn a one-day needs snapshot into a short, funded plan.. **Starts when:** SME onboarding started. **Ends when:** Short plan approved by the owner-manager.

Task	Steps	What to type
UFT-SME1-01 Interview the owner-manager R: Head of L&D	SME-MP-01.1 Record business priorities SME-MP-01.2 Record key roles and headcount	Priorities: win 2 new customers; reduce rework. Headcount SME: owner, 3 team leaders, operators.
UFT-SME1-02 Send the needs snapshot R: L&D Analyst	SME-MP-01.3 Send short needs questionnaire MP-54.6 Distribute to stakeholders	Send the 10-question snapshot to all employees by WhatsApp link or paper.

Task	Steps	What to type
UFT-SME1-03 Summarize top needs R: L&D Analyst	SME-MP-01.4 Summarize top needs	Top needs: Electronic health records (EHR); Telemedicine and remote consultation; customer service. Accept the AI summary. AI run: Top needs: AI triage and clinical decision support; AI medical imaging assistance; customer service. Accept the AI summary.
UFT-SME1-04 Approve the short plan R: HR Director	MP-53.9 Validate and approve scope	Short plan approved: 3 themes, 6 training days, 45,000 MAD.

9.3 Diagnosis — gate G2

E2E-20 · Multi-Axis Diagnostic-to-Maturity Report

Goal: Conduct 5-axis diagnostic + CMM maturity + leadership assessment. **Starts when:** Engagement kickoff or approved Scope of Work requesting a diagnostic. **Ends when:** 5-axis diagnostic, CMM maturity and leadership maturity report validated with the sponsor.

Task	Steps	What to type
UFT-20-01 Define diagnostic axes and sample R: Consultant PM	MP-37.1 Define diagnostic axes and sample	Axes: strategy, organization, processes, people, information systems. Sample: 40 people (MS 8, MO 16, OP 16).
UFT-20-02 Deploy diagnostic questionnaire R: Consultant PM	MP-37.2 Deploy diagnostic questionnaire MP-37.4 Collect questionnaire responses	Diagnostic questionnaire deployed to 40 people; 34 responses (85%).
UFT-20-03 Conduct semi-structured interviews R: Consultant	MP-37.3 Conduct semi-structured interviews	Interview notes (OP, Clinical Care & Nursing): 'Procedures exist but are not updated since 2023.'
UFT-20-04 Score diagnostic axes R: Consultant	MP-37.5 Score diagnostic axes	Axis scores (1-5): strategy 3.4, organization 2.8, processes 2.6, people 3.1, IS 2.2.
UFT-20-05 Select maturity model R: Consultant	MP-38.1 Select maturity model levels MP-38.2 Define evidence criteria per level	Maturity model: CMM 5 levels; evidence for level 3 = documented and applied process.
UFT-20-06 Rate process maturity R: Consultant	MP-38.3 Rate maturity per process area MP-38.4 Compute maturity profile	Maturity: training management level 2; Clinical Care & Nursing processes level 3.
UFT-20-07 Assess leadership maturity R: HR Business Partner	MP-42.1 Launch leadership 360 assessment MP-42.2 Compute leadership maturity level	Leadership 360: average level 3 (Team Leadership) across 18 managers.
UFT-20-08 Cross-check skills and needs R: L&D Analyst	MP-02.7 Validate skills inventory MP-03.2 Review gap matrix by site and function	Cross-check: IS axis weakness confirmed by the Electronic health records (EHR) gap (-1.4). AI run: Cross-check: IS axis weakness confirmed by the AI triage and clinical decision support gap (-1.4).
UFT-20-09 Draft diagnostic findings R: Consultant	MP-37.6 Draft diagnostic findings MP-38.5 Produce maturity report	Edit AI findings: keep 5, merge 2, add one on ISO 7101 documentation.

Task	Steps	What to type
UFT-20-10 Validate findings with sponsor R: Consultant PM	MP-37.7 Validate findings with sponsor MP-38.6 Agree target maturity	Findings validated with the sponsor; target maturity level 3 by 2026+1.

E2E-25 · Job Architecture-to-Competency Map

Goal: Manage organizational charts, position descriptions, gap analysis. **Starts when:** Organizational change, new role creation, or annual job architecture review. **Ends when:** Approved organizational charts, position descriptions, and competency maps with gap analysis.

Task	Steps	What to type
UFT-25-01 Map organizational structure R: HR Analyst	MP-44.1 Map organizational structure	Structure: 6 functions, 14 departments, 3 sites; 212 positions.
UFT-25-02 Design organizational charts R: Org Design Consultant	MP-44.2 Design organizational charts	Org chart 'Clinical Care & Nursing': director → 3 managers → 9 supervisors → operators.
UFT-25-03 Conduct job analysis R: Job Analyst	MP-44.3 Conduct job analysis	Job analysis 'Clinical Care & Nursing supervisor': 8 main activities, 2 of them now supported by Electronic health records (EHR). AI run: Job analysis 'Clinical Care & Nursing supervisor': 8 main activities, 2 of them now supported by AI triage and clinical decision support.
UFT-25-04 Draft position descriptions R: Job Analyst	MP-44.4 Draft position descriptions	Position description drafted: mission, activities, competencies (Electronic health records (EHR) level 3, ISO 7101 level 3), KPIs. AI run: Position description drafted: mission, activities, competencies (AI triage and clinical decision support level 3, ISO 7101 level 3), KPIs.
UFT-25-05 Validate with managers R: HR Business Partner	MP-44.5 Validate descriptions with managers	Validated by the Clinical Care & Nursing manager with 2 changes on activities.
UFT-25-06 Conduct gap analysis R: Job Analyst	MP-44.6 Conduct gap analysis existing versus real	Gap existing vs real: 11 descriptions outdated; 4 roles with new Electronic health records (EHR) tasks. AI run: Gap existing vs real: 11 descriptions outdated; 4 roles with new AI triage and clinical decision support tasks.
UFT-25-07 Identify roles to develop R: HR Business Partner	MP-44.7 Identify roles to develop MP-44.8 Update job architecture MP-44.9 Align with competency framework	Roles 'To develop': data-literate supervisor, maintenance technician 4.0.
UFT-25-08 Publish approved architecture R: HR Director	MP-44.10 Publish approved position descriptions MP-44.11 Track job architecture changes MP-44.12 Report on architecture health	Publish 212 approved descriptions and the architecture map to all employees.

E2E-26 · GPEC-to-Training Plan

Goal: Integrate Forward Planning of Jobs and Skills into L&D. **Starts when:** Annual HR strategic planning cycle or GPEC (Forward Planning of Jobs and Skills) review. **Ends when:** Training plan aligned with GPEC and HR strategic orientations.

Task	Steps	What to type
UFT-26-01 Define GPEC scope R: GPEC Specialist	MP-45.1 Define GPEC scope	GPEC scope: Clinical Care & Nursing and Information Systems jobs; horizon 3 years.
UFT-26-02 Map HR strategic orientations R: HR Director	MP-45.2 Map HR strategic orientations MP-45.3 Align training with GPEC	HR orientations: internal mobility first; 30% of promotions from internal talent.
UFT-26-03 Update development foundation R: HR Business Partner	MP-45.4 Update development foundation MP-45.5 Support human capital development	Development foundation updated: descriptions, annual objectives, evaluation grid.
UFT-26-04 Update Jobs and Skills Directory (REC) R: GPEC Specialist	MP-45.6 Update Jobs and Skills Directory (REC)	REC updated: 42 jobs, 3 new jobs linked to Electronic health records (EHR). AI run: REC updated: 42 jobs, 3 new jobs linked to AI triage and clinical decision support.
UFT-26-05 Redynamize periodic evaluations R: HR Business Partner	MP-45.7 Redynamize periodic evaluations	Periodic evaluation redesigned: 2 reviews per year, competency section added.
UFT-26-06 Design career paths R: HR Director	MP-45.8 Design career paths	Career path: operator → team leader → supervisor → Clinical Care & Nursing manager.
UFT-26-07 Document career management R: HR Director	MP-45.9 Document career management process MP-45.10 Implement collective compensation	Career management procedure documented (v1): eligibility, committee, calendar.
UFT-26-08 Align training with GPEC R: L&D Strategist	MP-45.11 Feed GPEC into training needs MP-45.12 Report on GPEC integration	Training aligned with GPEC: 4 themes cover the 3 new jobs; 2 themes removed.

E2E-27 · Demand Collection-to-Consolidation

Goal: Collect individual and collective training demands. **Starts when:** Annual training plan cycle or ad-hoc demand collection request. **Ends when:** Consolidated and prioritized demand repository integrated into the training needs analysis.

Task	Steps	What to type
UFT-27-01 Design demand collection forms R: L&D Analyst	MP-46.1 Design demand collection forms	Forms: individual form (5 questions) and collective form per team (3 questions).
UFT-27-02 Deploy individual demand collection R: L&D Analyst	MP-46.2 Deploy individual demand collection	Individual collection open 1-20 March; 146 demands received.
UFT-27-03 Deploy collective demand collection R: L&D Analyst	MP-46.3 Deploy collective demand collection	Collective collection: 18 team demands received.

Task	Steps	What to type
UFT-27-04 Collect manager recommendations R: L&D Business Partner	MP-46.4 Collect manager recommendations	Manager recommendations: 24 received, 9 flagged as priority.
UFT-27-05 Consolidate demands by function R: L&D Analyst	MP-46.5 Consolidate demands by function	Consolidated: Clinical Care & Nursing 64 demands, Operations 41, Quality 22, others 37.
UFT-27-06 Map demands to competencies R: L&D Analyst	MP-46.6 Map demands to competencies MP-46.7 Prioritize demands	Accept AI mapping for 139 demands; map 7 manually to 'Telemedicine and remote consultation'. AI run: Accept AI mapping for 139 demands; map 7 manually to 'AI medical imaging assistance'.
UFT-27-07 Prioritize and validate demands R: L&D Business Partner	MP-46.8 Validate demands with managers MP-46.9 Integrate demands into needs analysis MP-46.10 Report on demand patterns MP-46.11 Track demand fulfillment MP-46.12 Improve demand collection	Validated: 112 demands (High 38, Medium 51, Low 23); 34 rejected with reason.

E2E-28 · Performance Assessment-to-RAG Dashboard

Goal: Assess MS/MO/OP performance with RAG ratings. **Starts when:** Annual performance cycle or management request for performance visualization. **Ends when:** Validated MS/MO/OP (Strategic Management / Operational Management / Operational Level) performance assessment with RAG (Green/Amber/Red) dashboards.

Task	Steps	What to type
UFT-28-01 Define MS/MO/OP framework R: Performance Analyst	MP-47.1 Define MS/MO/OP framework	MS = executive committee; MO = managers and supervisors; OP = operators and technicians.
UFT-28-02 Define RAG criteria R: Performance Analyst	MP-47.2 Define RAG criteria	Green ≥ 90% of target; Amber 70-89%; Red < 70%.
UFT-28-03 Collect performance data by function R: Performance Analyst	MP-47.3 Collect performance data by function	Data collected for 6 functions: 18 KPIs, last 12 months.
UFT-28-04 Assess MS performance R: Performance Analyst	MP-47.4 Assess MS performance	MS: strategy deployment Amber (78%); governance Green (92%).
UFT-28-05 Assess MO performance R: Performance Analyst	MP-47.5 Assess MO performance	MO: Clinical Care & Nursing team management Red (64%); planning Amber (81%).
UFT-28-06 Assess OP performance R: Performance Analyst	MP-47.6 Assess OP performance MP-47.7 Apply RAG ratings	OP: ISO 7101 compliance Amber (85%); productivity Green (93%).

Task	Steps	What to type
UFT-28-07 Publish RAG dashboard R: Performance Analyst	MP-47.8 Visualize performance dashboards MP-47.9 Identify performance gaps MP-47.10 Feed performance into diagnostic report MP-47.11 Track performance progression MP-47.12 Report performance to leadership	Publish RPT-005 MS/MO/OP RAG dashboard to the executive committee.

E2E-29 · Functional SWOT-to-Improvement Axes

Goal: Conduct function-level SWOT and define improvement axes. **Starts when:** Diagnostic phase of a training engineering engagement or annual functional review. **Ends when:** Validated functional SWOT reports with prioritized improvement axes per function.

Task	Steps	What to type
UFT-29-01 Define function scope R: L&D Analyst	MP-48.1 Define function scope	Function in scope: Clinical Care & Nursing (3 sites, 96 people).
UFT-29-02 Conduct function SWOT R: L&D Analyst	MP-48.2 Conduct function SWOT	SWOT workshop held with the function head and 6 supervisors.
UFT-29-03 Identify strengths and weaknesses R: L&D Analyst	MP-48.3 Identify strengths MP-48.4 Identify weaknesses	Strength: experienced team. Weakness: low Electronic health records (EHR) usage, paper records. AI run: Strength: experienced team. Weakness: low AI triage and clinical decision support usage, paper records.
UFT-29-04 Identify opportunities and threats R: L&D Analyst	MP-48.5 Identify opportunities MP-48.6 Identify threats	Opportunity: Digital patient scheduling and billing. Threat: stricter ISO 7101 audits. AI run: Opportunity: AI bed and staff capacity planning. Threat: stricter ISO 7101 audits.
UFT-29-05 Define improvement axes R: L&D Business Partner	MP-48.7 Define improvement axes	Axis 1: digitalise shift records with Electronic health records (EHR). Axis 2: certify supervisors on ISO 7101. AI run: Axis 1: digitalise shift records with AI triage and clinical decision support. Axis 2: certify supervisors on ISO 7101.
UFT-29-06 Validate with function heads R: L&D Business Partner	MP-48.8 Validate axes with function heads	Validated by the function head on 18 April; axis 2 deadline moved to Q3.
UFT-29-07 Prioritize improvement axes R: L&D Strategist	MP-48.9 Prioritize improvement axes MP-48.10 Feed SWOT into diagnostic report MP-48.11 Track improvement implementation MP-48.12 Report on function performance	Priority: axis 1 (impact 5), axis 2 (impact 4).

E2E-02 · Skills-to-Gap Diagnosis

Goal: Produce a validated skills gap diagnosis. **Starts when:** Approved annual L&D plan or a scheduled skills assessment campaign. **Ends when:** Validated skills gap diagnosis released to needs analysis.

Task	Steps	What to type
UFT-02-01 Maintain competency framework R: L&D Analyst	MP-02.1 Define competency families and levels	Family 'Electronic health records (EHR)': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert). AI run: Family 'AI triage and clinical decision support': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert).
UFT-02-02 Set target levels per position R: HR Business Partner	MP-02.2 Set target levels per position	Clinical Care & Nursing supervisor: Electronic health records (EHR) = 3; ISO 7101 = 3. Clinical Care & Nursing operator: Electronic health records (EHR) = 2. AI run: Clinical Care & Nursing supervisor: AI triage and clinical decision support = 3; ISO 7101 = 3. Clinical Care & Nursing operator: AI triage and clinical decision support = 2.
UFT-02-03 Launch assessment campaign R: L&D Analyst	MP-02.3 Launch assessment campaign	Campaign 'Skills 2026': population Clinical Care & Nursing and Operations (212 people), 12 competencies, close date 30 April.
UFT-02-04 Collect self and manager assessments R: Manager	MP-02.4 Submit self and manager assessments MP-02.5 Consolidate assessment results	Self-assessment Electronic health records (EHR): 2; manager validation: 2 with comment 'needs practice on live cases'. AI run: Self-assessment AI triage and clinical decision support: 2; manager validation: 2 with comment 'needs practice on live cases'.
UFT-02-05 Suggest proficiency from evidence R: L&D Analyst	MP-02.6 Suggest proficiency from evidence	Accept 38 suggested levels, edit 4 (evidence too old), reject 1. Every change carries a note.
UFT-02-06 Validate skills inventory R: Head of L&D	MP-02.7 Validate skills inventory	Inventory validated: 212 employees, 96% assessments complete. Justification: sample checked by site.
UFT-02-07 Compute and forecast gaps R: L&D Analyst	MP-03.1 Compute gap matrix MP-03.2 Review gap matrix by site and function MP-28.3 Forecast skill gaps MP-28.1 Build analytics dataset	Critical gaps: Electronic health records (EHR) (-1.4 average on supervisors), Telemedicine and remote consultation (-1.1). Forecast: Digital patient scheduling and billing becomes critical within 12 months. AI run: Critical gaps: AI triage and clinical decision support (-1.4 average on supervisors), AI medical imaging assistance (-1.1). Forecast: AI bed and staff capacity planning becomes critical within 12 months.

E2E-21 · Previous Plan Impact-to-Strategy Update

Goal: Evaluate N-1 plan impact and update strategy. **Starts when:** Start of a new plan cycle with N-1 execution data available. **Ends when:** N-1 impact conclusions fed into the strategy update.

Task	Steps	What to type
UFT-21-01 Load N-1 plan execution data R: L&D Analyst	MP-39.1 Load N-1 plan execution data	Load N-1 plan: 28 sessions planned, 23 delivered, 1,410,000 MAD spent.
UFT-21-02 Define impact criteria R: L&D Analyst	MP-39.2 Define impact criteria	Impact criteria: application on the job, KPI change, satisfaction, cost per learner.

Task	Steps	What to type
UFT-21-03 Survey participants and managers R: L&D Analyst	MP-39.3 Survey participants and managers MP-09.5 Record on-the-job observation (Level 3)	Survey sent to 190 participants and 34 managers; 61% responded.
UFT-21-04 Compare planned against realized R: L&D Analyst	MP-39.4 Compare planned against realized MP-32.3 Isolate training effect	Planned vs realized: 82% of sessions, 94% of budget; 2 themes not delivered.
UFT-21-05 Review N-1 ROI R: Performance Analyst	MP-32.4 Compute Phillips ROI MP-32.5 Review ROI with finance	N-1 ROI: Telemedicine and remote consultation 18%; safety theme 35%. AI run: N-1 ROI: AI medical imaging assistance 18%; safety theme 35%.
UFT-21-06 Draft impact conclusions R: L&D Analyst	MP-39.5 Draft impact study conclusions	Accept AI conclusions 1-3; rewrite conclusion 4 (sample too small).
UFT-21-07 Feed conclusions to strategy R: Head of L&D	MP-39.6 Feed conclusions to strategy update MP-01.1 Record corporate strategic objectives	Feed to strategy: keep blended format; stop long classroom courses on Telemedicine and remote consultation. AI run: Feed to strategy: keep blended format; stop long classroom courses on AI medical imaging assistance.
UFT-21-08 Update roadmap priorities R: L&D Strategist	MP-04.6 Sequence roadmap initiatives	Roadmap priority updated: Electronic health records (EHR) moved to Q2; Telemedicine and remote consultation to microlearning. AI run: Roadmap priority updated: AI triage and clinical decision support moved to Q2; AI medical imaging assistance to microlearning.

9.4 Training Engineering Report & plan — gate G3

E2E-01 · Strategy-to-Learning Plan

Goal: Translate corporate strategy into an approved annual L&D plan and budget. **Starts when:** Annual strategy cycle opened or revised corporate objectives published by the board. **Ends when:** Annual L&D plan and budget envelope approved by the Steering Committee and locked.

Task	Steps	What to type
UFT-01-01 Record strategic objectives R: Head of L&D	MP-01.1 Record corporate strategic objectives	SO-1: Electronic health records (EHR) used by 80% of Clinical Care & Nursing staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on ISO 7101. AI run: SO-1: AI triage and clinical decision support used by 80% of Clinical Care & Nursing staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on ISO 7101.
UFT-01-02 Link objectives to functions and sites R: L&D Strategist	MP-01.2 Link objectives to functions and sites	SO-1 → Clinical Care & Nursing, Operations, Information Systems (all sites). SO-2 → Quality & HSE, Clinical Care & Nursing.

Task	Steps	What to type
UFT-01-03 Frame skills priorities R: L&D Analyst	MP-02.1 Define competency families and levels MP-02.2 Set target levels per position	Priority competency families: Electronic health records (EHR); Telemedicine and remote consultation; ISO 7101 compliance. Target level 3 (Autonomous) for supervisors. AI run: Priority competency families: AI triage and clinical decision support; AI medical imaging assistance; ISO 7101 compliance. Target level 3 (Autonomous) for supervisors.
UFT-01-04 Pre-scope training needs R: L&D Analyst	MP-03.1 Compute gap matrix MP-03.2 Review gap matrix by site and function	Pre-scoped needs: 42% of Clinical Care & Nursing supervisors below target on Electronic health records (EHR); 18 employees below target on ISO 7101. AI run: Pre-scoped needs: 42% of Clinical Care & Nursing supervisors below target on AI triage and clinical decision support; 18 employees below target on ISO 7101.
UFT-01-05 Define budget envelope R: Finance Manager	MP-01.3 Define L&D budget envelope MP-18.1 Allocate budget by theme and site MP-18.2 Forecast OFPPT refunds	Gross L&D budget 2026: 1,850,000 MAD; forecast refund (OFPPT/CSF): 520,000 MAD; net envelope: 1,330,000 MAD.
UFT-01-06 Plan change and adoption R: Change Manager	MP-19.1 Assess change impact MP-19.2 Build adoption plan	Change impact: high for Clinical Care & Nursing supervisors (new Electronic health records (EHR) routines). Sponsors: Operations Director. Champions: one per site. AI run: Change impact: high for Clinical Care & Nursing supervisors (new AI triage and clinical decision support routines). Sponsors: Operations Director. Champions: one per site.
UFT-01-07 Compile plan approval pack R: Head of L&D	MP-01.4 Schedule Steering Committee milestones MP-01.5 Compile plan approval pack MP-04.1 Consolidate feeder outputs	Approval pack: 2 objectives, net budget 1,330,000 MAD, 6 priority themes, committee date 15 March 2026.
UFT-01-08 Approve and lock annual L&D plan R: HR Director	MP-01.6 Record Steering Committee decision MP-01.7 Lock and distribute approved plan	Decision: Approve. Justification: aligned with SO-1 and SO-2; budget within envelope. Plan locked as version 1.

E2E-03 · Needs-to-Training Engineering Report & Roadmap

Goal: Produce the Training Engineering Report and the prioritized training roadmap. **Starts when:** Validated skills gap diagnosis, consolidated demands, approved Scope of Work or diagnostic findings available. **Ends when:** Training Engineering Report and prioritized roadmap approved and published.

Task	Steps	What to type
UFT-03-01 Plan diagnostic interviews R: L&D Analyst	MP-03.3 Plan diagnostic interviews	Interview plan: 14 semi-structured interviews (4 MS, 6 MO, 4 OP), 45 minutes each, weeks 10-11.
UFT-03-02 Record interview findings R: L&D Analyst	MP-03.4 Record interview findings	Finding (MO, Clinical Care & Nursing): 'Supervisors do not trust Electronic health records (EHR) data; they re-enter figures on paper.' AI run: Finding (MO, Clinical Care & Nursing): 'Supervisors do not trust AI triage and clinical decision support data; they re-enter figures on paper.'

Task	Steps	What to type
UFT-03-03 Cluster needs into themes R: L&D Analyst	MP-03.5 Cluster needs into training themes	Accept theme 'Electronic health records (EHR) for supervisors'; merge two duplicate themes on Telemedicine and remote consultation; split 'ISO 7101' into awareness and auditor tracks. AI run: Accept theme 'AI triage and clinical decision support for supervisors'; merge two duplicate themes on AI medical imaging assistance; split 'ISO 7101' into awareness and auditor tracks.
UFT-03-04 Prioritize needs by impact R: L&D Strategist	MP-03.6 Prioritize needs by business impact	Electronic health records (EHR): impact 5, urgency 4. Telemedicine and remote consultation: impact 4, urgency 3. ISO 7101: impact 4, urgency 5. AI run: AI triage and clinical decision support: impact 5, urgency 4. AI medical imaging assistance: impact 4, urgency 3. ISO 7101: impact 4, urgency 5.
UFT-03-05 Validate needs register R: Head of L&D	MP-03.7 Validate needs register	Needs register validated: 23 needs, 6 themes. Justification: covers SO-1 and SO-2; sponsor reviewed.
UFT-03-06 Consolidate engineering inputs R: L&D Analyst	MP-04.1 Consolidate feeder outputs MP-04.2 Check input completeness	Inputs complete: Scope of Work, 187 responses, gap matrix, RAG dashboard, SWOT, demands. Missing: none.
UFT-03-07 Draft Training Engineering Report R: L&D Strategist	MP-04.3 Generate report draft MP-04.4 Edit and complete report sections	Section 3 'Diagnostic': edit the AI draft, add the interview quote on Electronic health records (EHR), keep the RAG table. AI run: Section 3 'Diagnostic': edit the AI draft, add the interview quote on AI triage and clinical decision support, keep the RAG table.
UFT-03-08 Run quality review R: Quality Manager	MP-04.5 Run quality review of report MP-20.5 Run periodic quality review	Quality review: 11/12 checklist items met; fix item 'sources cited for every figure'. Result: pass after correction.
UFT-03-09 Sequence and budget roadmap R: L&D Strategist	MP-04.6 Sequence roadmap initiatives MP-18.1 Allocate budget by theme and site	Roadmap: Q2 Electronic health records (EHR) (6 groups); Q3 ISO 7101 (4 groups); Q4 Telemedicine and remote consultation (3 groups). Total 1,240,000 MAD. AI run: Roadmap: Q2 AI triage and clinical decision support (6 groups); Q3 ISO 7101 (4 groups); Q4 AI medical imaging assistance (3 groups). Total 1,240,000 MAD.
UFT-03-10 Approve and publish report and roadmap R: Head of L&D	MP-04.7 Submit roadmap for approval MP-04.8 Record roadmap approval MP-04.9 Publish approved report and roadmap MP-01.6 Record Steering Committee decision	Decision: Approve report and roadmap v1. Justification: within budget, linked to SO-1/SO-2. Publish to all stakeholders.

E2E-30 · Prioritization-to-Resource Plan

Goal: Prioritize themes and plan days, groups, trainers, budget. **Starts when:** Consolidated training themes requiring prioritization and resource planning. **Ends when:** Approved prioritized training plan with days per theme, group planning, trainer allocation, and budget.

Task	Steps	What to type
UFT-30-01 Consolidate training themes R: L&D Analyst	MP-49.1 Consolidate training themes	Consolidated list: 9 themes from needs, demands, GPEC and SWOT.
UFT-30-02 Define prioritization criteria R: L&D Strategist	MP-49.2 Define prioritization criteria	Criteria: strategic impact 40%, urgency 30%, number of learners 20%, cost 10%.
UFT-30-03 Prioritize themes R: L&D Strategist	MP-49.3 Prioritize themes	Rank 1 Electronic health records (EHR) (score 86); rank 2 ISO 7101 (81); rank 3 Telemedicine and remote consultation (74). AI run: Rank 1 AI triage and clinical decision support (score 86); rank 2 ISO 7101 (81); rank 3 AI medical imaging assistance (74).
UFT-30-04 Estimate days per theme R: L&D Planner	MP-49.4 Estimate days per theme	Electronic health records (EHR): 3 days per group; ISO 7101: 2 days; Telemedicine and remote consultation: 1.5 days. AI run: AI triage and clinical decision support: 3 days per group; ISO 7101: 2 days; AI medical imaging assistance: 1.5 days.
UFT-30-05 Define groups per theme R: L&D Planner	MP-49.5 Define number of groups per theme MP-49.6 Allocate trainers	Electronic health records (EHR): 6 groups of 12; ISO 7101: 4 groups; Telemedicine and remote consultation: 3 groups. AI run: AI triage and clinical decision support: 6 groups of 12; ISO 7101: 4 groups; AI medical imaging assistance: 3 groups.
UFT-30-06 Allocate trainers and budget R: Finance Manager	MP-49.7 Estimate plan budget MP-49.8 Sequence delivery MP-49.9 Validate plan with governance	Trainers: 2 internal, vendor A; budget 1,240,000 MAD (within envelope).
UFT-30-07 Publish prioritized training plan R: L&D Leader	MP-49.10 Publish prioritized plan MP-49.11 Track plan execution MP-49.12 Report on resource utilization	Publish RPT-002 Prioritized Training Plan 2026 to all stakeholders.

E2E-22 · Multi-Site Plan-to-Deployment

Goal: Adapt and deploy plans across sites. **Starts when:** Approved roadmap for an organization with several sites or entities. **Ends when:** Site plans adapted, validated and deployed, with deviations escalated.

Task	Steps	What to type
UFT-22-01 Split plan by site R: Head of L&D	MP-40.1 Split plan by site	Split plan into 3 sites: Casablanca 55%, Tanger 30%, Agadir 15%.
UFT-22-02 Adapt site plan to local constraints R: Site L&D Coordinator	MP-40.2 Adapt site plan to local constraints	Tanger: shift constraints → sessions of 4 hours instead of full days.
UFT-22-03 Localize site materials R: Instructional Designer	MP-23.1 Request translation MP-23.3 Validate translation MP-23.6 Review participation equity MP-23.7 Record inclusion actions	Agadir materials translated to AR; validated by the site expert.
UFT-22-04 Validate site plan R: Head of L&D	MP-40.3 Validate site plan	Site plans validated centrally; budget deviation within ±5%.

Task	Steps	What to type
UFT-22-05 Schedule site sessions R: Training Administrator	MP-07.1 Create training session MP-11.1 Book rooms and equipment	Tanger schedule: 8 sessions, rooms booked, 2 trainers.
UFT-22-06 Deploy site schedule R: Site L&D Coordinator	MP-40.4 Deploy site schedule	Schedules deployed and communicated to site managers.
UFT-22-07 Consolidate site status R: Head of L&D	MP-40.5 Consolidate site status	Status: Casablanca 70%, Tanger 45%, Agadir 20% delivered.
UFT-22-08 Escalate site deviation R: Head of L&D	MP-40.6 Escalate site deviation	Escalate Agadir deviation (-25%) to the HR Director with a recovery plan.

E2E-23 · Regulatory Submission-to-Validation

Goal: Submit and validate training plans with regulatory bodies. **Starts when:** Approved plan requiring external validation or funding (e.g. OFPPT, GIAC-Agro). **Ends when:** Plan validated by the regulatory body and evidence archived.

Task	Steps	What to type
UFT-23-01 Select regulatory template R: Compliance Officer	MP-41.1 Select regulatory template	Template: OFPPT special training contracts (CSF) — plan file.
UFT-23-02 Generate submission file R: Compliance Officer	MP-41.2 Generate submission file MP-20.5 Run periodic quality review	Submission file generated: plan, themes, providers, costs; quality check passed.
UFT-23-03 Submit plan to regulatory body R: Compliance Officer	MP-41.3 Submit plan to regulatory body	Submitted to the regional funding committee on 5 March; reference GSF-2026-118.
UFT-23-04 Track submission status R: Compliance Officer	MP-41.4 Track submission status	Status: additional document requested (provider accreditation) — sent on 12 March.
UFT-23-05 Record regulator decision R: Compliance Officer	MP-41.5 Record regulator decision MP-14.1 Register regulatory requirement	Decision: approved with a cap of 520,000 MAD.
UFT-23-06 Submit refund claims R: Finance Manager	MP-18.5 Submit refund claims	Refund claims submitted for 12 delivered actions: 318,000 MAD.
UFT-23-07 Archive submission evidence R: Compliance Officer	MP-41.6 Archive submission evidence MP-18.6 Close budget period	Archive file, decision and claims; retention 10 years.

E2E-16 · Vendor-to-Finance

Goal: Manage vendors from selection to payment. **Starts when:** Training need requiring an external provider. **Ends when:** Vendor selected, order issued and payment approved against attendance.

Task	Steps	What to type
UFT-16-01 Issue request for proposal R: Purchasing Officer	MP-15.1 Issue request for proposal	RFP 'Training on Electronic health records (EHR)' sent to 4 vendors, answers due 15 May. AI run: RFP 'Training on AI triage and clinical decision support' sent to 4 vendors, answers due 15 May.
UFT-16-02 Score vendor proposals R: Purchasing Officer	MP-15.2 Score vendor proposals	Scores: vendor A 82, vendor B 76, vendor C 64 (price 40%, expertise 40%, references 20%).
UFT-16-03 Register and verify vendor R: Purchasing Officer	MP-15.3 Register vendor record MP-15.4 Verify vendor accreditation	Register vendor A; accreditation OFPPT verified, valid until December.
UFT-16-04 Issue purchase order R: Purchasing Officer	MP-15.5 Issue purchase order MP-18.3 Record committed and actual costs	Purchase order PO-2026-044: 180,000 MAD on budget line 'Electronic health records (EHR)'. AI run: Purchase order PO-2026-044: 180,000 MAD on budget line 'AI triage and clinical decision support'.
UFT-16-05 Match invoice to order and attendance R: Training Administrator	MP-15.6 Match invoice to order and attendance MP-11.5 Reconcile attendance with invoices	Invoice matched with PO and attendance (3 days × 12 learners): OK.
UFT-16-06 Approve vendor payment R: Finance Manager	MP-15.7 Approve vendor payment MP-18.4 Compare spend against budget	Approve payment 180,000 MAD; vendor performance rating 4/5.

HCPR-E2E-02 · Healthcare Providers Critical-Skills-to-Transformation Plan

Goal: Turn critical-skill gaps and digital and AI use cases into a transformation plan.. **Starts when:** Annual plan cycle or technology change in Healthcare Providers. **Ends when:** Transformation learning paths approved.

Task	Steps	What to type
UFT-HCPR-E2-01 List critical Clinical Care & Nursing skills R: L&D Analyst	MP-02.1 Define competency families and levels MP-03.1 Compute gap matrix	Critical skills: 6 for Clinical Care & Nursing, each with target level 3.
UFT-HCPR-E2-02 List digital and AI use cases R: L&D Strategist	MP-03.3 Plan diagnostic interviews	Use cases: Electronic health records (EHR); Telemedicine and remote consultation; Digital patient scheduling and billing. AI run: Use cases: AI triage and clinical decision support; AI medical imaging assistance; AI bed and staff capacity planning.
UFT-HCPR-E2-03 Forecast impacted roles R: Performance Analyst	MP-03.5 Cluster needs into training themes MP-28.3 Forecast skill gaps	Impacted roles: supervisors (high), operators (medium); accept the AI forecast.
UFT-HCPR-E2-04 Approve transformation paths R: Instructional Designer	MP-05.2 Define learning path and modules MP-05.7 Approve design document	Approve 2 transformation paths: 'Electronic health records (EHR) for supervisors', 'Telemedicine and remote consultation for operators'. AI run: Approve 2 transformation paths: 'AI triage and clinical decision support for supervisors', 'AI medical imaging assistance for operators'.

SME-E2E-02 · SME Funding-to-Refund

Goal: Secure funding and recover the refunds of the plan.. **Starts when:** Short plan approved. **Ends when:** Refund received and recorded.

Task	Steps	What to type
UFT-SME2-01 Select eligible themes R: L&D Analyst	SME-MP-02.1 Select eligible themes	Eligible themes: Electronic health records (EHR) and ISO 7101 (funding rules met). AI run: Eligible themes: AI triage and clinical decision support and ISO 7101 (funding rules met).
UFT-SME2-02 Build the funding file R: Finance Manager	SME-MP-02.2 Build funding file MP-41.2 Generate submission file	Funding file: plan, quotes, provider accreditation, attendance model.
UFT-SME2-03 Submit the refund claim R: Finance Manager	SME-MP-02.3 Submit refund claim MP-18.5 Submit refund claims	Refund claim submitted: 28,000 MAD with signed attendance sheets.
UFT-SME2-04 Record the refund R: Finance Manager	SME-MP-02.4 Track refund payment	Refund received: 28,000 MAD on 20 November; file closed.

9.5 Design & delivery — gate G4

E2E-04 · Roadmap-to-Curriculum Design

Goal: Convert roadmap into curriculum maps, learning paths, design documents. **Starts when:** Approved Training Engineering Report and roadmap published. **Ends when:** Approved curriculum maps, learning paths and design documents.

Task	Steps	What to type
UFT-04-01 Create curriculum map R: Instructional Designer	MP-05.1 Create curriculum map from roadmap	Curriculum map 'Electronic health records (EHR)': 3 learning paths (operators, supervisors, managers), 9 modules. AI run: Curriculum map 'AI triage and clinical decision support': 3 learning paths (operators, supervisors, managers), 9 modules.
UFT-04-02 Define learning paths and modules R: Instructional Designer	MP-05.2 Define learning path and modules	Path 'Supervisors — Electronic health records (EHR)': 4 modules, 3 days blended (1 day e-learning, 2 days workshop). AI run: Path 'Supervisors — AI triage and clinical decision support': 4 modules, 3 days blended (1 day e-learning, 2 days workshop).
UFT-04-03 Write learning objectives R: Instructional Designer	MP-05.3 Write learning objectives per module	Objective M1: 'By the end, the supervisor reads the Electronic health records (EHR) dashboard and decides the shift action in 5 minutes.' AI run: Objective M1: 'By the end, the supervisor reads the AI triage and clinical decision support dashboard and decides the shift action in 5 minutes.'
UFT-04-04 Propose module structure R: Instructional Designer	MP-05.4 Propose module structure	Accept the proposed structure (intro, demo, practice, quiz); replace the quiz by a live case from Clinical Care & Nursing.
UFT-04-05 Set assessment strategy R: Instructional Designer	MP-05.5 Set assessment strategy	Assessment: pre/post test (Level 2) and manager observation after 30 days (Level 3).
UFT-04-06 Develop and tag content R: Content Developer	MP-06.1 Upload content assets MP-06.2 Validate package format MP-06.5 Tag content with competencies	Upload 'M1_Electronic health records (EHR).pptx' and 'M1_video.mp4'; tag competency 'Electronic health records (EHR)' level 3. AI run: Upload 'M1_AI triage and clinical decision support.pptx' and 'M1_video.mp4'; tag competency 'AI triage and clinical decision support' level 3.

Task	Steps	What to type
UFT-04-07 Localize and check accessibility R: Instructional Designer	MP-23.1 Request translation MP-23.2 Draft machine translation MP-23.3 Validate translation MP-23.4 Run accessibility check MP-23.5 Fix accessibility issues	Request FR and AR versions; validate the AI draft translation; accessibility check: 0 blocking issues.
UFT-04-08 Approve design document R: Head of L&D	MP-05.6 Review design with subject matter expert MP-05.7 Approve design document	Decision: design approved. Comment: SME review done on 12 May; ready for delivery.

E2E-05 · Design-to-Delivery

Goal: Deliver training across all modalities. **Starts when:** Approved design document and prioritized training plan.

Ends when: Training delivered across all modalities with attendance and completion recorded.

Task	Steps	What to type
UFT-05-01 Publish content to catalog R: Content Developer	MP-06.3 Route content for expert review MP-06.4 Record review decision MP-06.6 Publish content to catalog	Publish module 'M1 Electronic health records (EHR)' to the catalog; audience: supervisors; languages EN/FR/AR. AI run: Publish module 'M1 AI triage and clinical decision support' to the catalog; audience: supervisors; languages EN/FR/AR.
UFT-05-02 Book logistics R: Training Administrator	MP-11.1 Book rooms and equipment MP-11.2 Manage trainer calendars	Room 'Training A' (20 seats) 3-5 June; projector; trainer calendar blocked.
UFT-05-03 Schedule sessions R: Training Administrator	MP-07.1 Create training session MP-07.2 Check scheduling conflicts	Session S-01 'Electronic health records (EHR) — supervisors', 3-5 June, 12 seats, no conflict reported. AI run: Session S-01 'AI triage and clinical decision support — supervisors', 3-5 June, 12 seats, no conflict reported.
UFT-05-04 Enroll learners and send convocations R: Training Administrator	MP-07.3 Enroll learners into session MP-07.4 Send convocations MP-17.1 Provision users via SSO	Enroll 12 supervisors; convocations sent by e-mail and SMS in each learner's language.
UFT-05-05 Push microlearning capsules R: Instructional Designer	MP-25.1 Author microlearning capsule MP-25.2 Generate capsule draft from source MP-25.3 Push capsule to collaboration channel MP-25.4 Consume capsule on mobile MP-25.5 Track capsule completion	Capsule '5-minute Telemedicine and remote consultation check' pushed to the Teams channel of Clinical Care & Nursing; 48 views in week 1. AI run: Capsule '5-minute AI medical imaging assistance check' pushed to the Teams channel of Clinical Care & Nursing; 48 views in week 1.
UFT-05-06 Run immersive simulations R: Trainer	MP-30.1 Define simulation scenario MP-30.2 Configure simulation scoring MP-30.3 Launch simulation session MP-30.4 Capture simulation performance MP-30.5 Debrief learner MP-30.6 Record simulation evidence	Simulation 'Clinical Care & Nursing incident': score 78/100; debrief notes recorded; evidence saved.
UFT-05-07 Record attendance R: Trainer	MP-07.5 Record attendance	Attendance S-01: 11 present, 1 absent (justified). Signature sheet attached.
UFT-05-08 Close sessions R: Training Administrator	MP-07.6 Close session and record completion	Close S-01: 11 completions recorded; certificate issued to each participant.

Task	Steps	What to type
UFT-05-09 Reconcile and archive period R: Training Administrator	MP-11.5 Reconcile attendance with invoices MP-11.6 Archive period records MP-11.3 Import external training records MP-11.4 Correct training record with justification	Reconcile invoice INV-2026-118 (3 days × 12 learners) with attendance; archive period Q2.

E2E-06 · Learner-Journey-to-Engagement

Goal: Deliver personalized, engaging learning experience. **Starts when:** Learner enrolled in a learning path or session. **Ends when:** Personalized learning journey completed with engagement measured.

Task	Steps	What to type
UFT-06-01 Generate personal learning plan R: L&D Analyst	MP-08.1 Generate personal learning plan	Personal plan generated for each learner: 3 items on Electronic health records (EHR), 1 capsule on Telemedicine and remote consultation. AI run: Personal plan generated for each learner: 3 items on AI triage and clinical decision support, 1 capsule on AI medical imaging assistance.
UFT-06-02 Recommend learning items R: Learner	MP-08.2 Recommend learning items MP-24.1 Enable personalization per scope	Accept 2 recommendations, reject 1 ('already mastered'). The outcome is logged.
UFT-06-03 Adapt path to performance R: Instructional Designer	MP-24.2 Set adaptation rules MP-24.3 Adapt path to learner performance MP-24.4 Record learner response to adaptation	Rule: if the quiz score < 60%, add the remedial capsule 'Electronic health records (EHR) basics'. AI run: Rule: if the quiz score < 60%, add the remedial capsule 'AI triage and clinical decision support basics'.
UFT-06-04 Animate social learning R: Knowledge Manager	MP-26.1 Create learning cohort group MP-26.2 Invite group members MP-26.3 Post question or answer MP-26.4 Endorse expert answer MP-26.5 Flag inappropriate content MP-26.6 Resolve moderation flag	Create cohort 'Electronic health records (EHR) supervisors 2026' and invite 12 members; first question posted. AI run: Create cohort 'AI triage and clinical decision support supervisors 2026' and invite 12 members; first question posted.
UFT-06-05 Run gamification R: Instructional Designer	MP-27.1 Define points and badge rules MP-27.2 Configure leaderboard scope MP-27.3 Award points on completion MP-27.4 Unlock badge MP-27.6 Adjust gamification rules	Badge 'Electronic health records (EHR) Practitioner' for completing 3 modules; 10 points per capsule. AI run: Badge 'AI triage and clinical decision support Practitioner' for completing 3 modules; 10 points per capsule.
UFT-06-06 Match and run coaching R: L&D Business Partner	MP-21.1 Request coaching MP-21.2 Match coach to learner MP-21.3 Schedule coaching sessions MP-21.4 Log coaching session notes MP-21.5 Evaluate coaching outcomes MP-21.6 Close coaching engagement	Match coach 'Senior Clinical Care & Nursing supervisor' to 3 learners; 4 sessions of 1 hour.
UFT-06-07 Collect learner feedback R: Learner	MP-08.3 Enroll in recommended item MP-08.4 Submit learning feedback	Feedback: 4.4/5; comment 'more real cases from Clinical Care & Nursing'.

Task	Steps	What to type
UFT-06-08 Monitor engagement and nudge R: L&D Analyst	MP-08.5 Monitor engagement indicators MP-08.6 Trigger re-engagement nudge MP-24.5 Review recommendation acceptance MP-27.5 Review engagement uplift MP-24.6 Tune personalization settings MP-28.4 Predict learner drop-out risk MP-28.5 Review predictions with L&D MP-28.6 Create preventive action	Engagement 81%; nudge sent to 9 inactive learners; drop-out risk high for 2 learners.

E2E-13 · Content-Curate-to-Retire

Goal: Publish, maintain, retire content. **Starts when:** New content published or content past its review date. **Ends when:** Catalog curated, maintained and outdated content retired.

Task	Steps	What to type
UFT-13-01 Aggregate provider catalogs R: Content Curator	MP-29.1 Aggregate provider catalogs	Aggregate 2 provider catalogs (LinkedIn Learning, Coursera): 1,240 items imported.
UFT-13-02 Recommend curated items R: Content Curator	MP-29.2 Recommend curated items	Keep the 15 top-ranked items on Electronic health records (EHR); reject 3 items older than 3 years. AI run: Keep the 15 top-ranked items on AI triage and clinical decision support; reject 3 items older than 3 years.
UFT-13-03 Approve and organize collections R: Content Curator	MP-29.3 Approve curated item MP-29.4 Organize curated collection	Collection 'Electronic health records (EHR) starter kit': 8 items, audience supervisors, review date in 12 months. AI run: Collection 'AI triage and clinical decision support starter kit': 8 items, audience supervisors, review date in 12 months.
UFT-13-04 Review peer content R: Subject Matter Expert	MP-33.1 Submit user-generated content MP-33.2 Check content against policy MP-33.3 Peer review content	Peer video 'How we use Telemedicine and remote consultation on shift' reviewed by an expert: approved with 1 correction. AI run: Peer video 'How we use AI medical imaging assistance on shift' reviewed by an expert: approved with 1 correction.
UFT-13-05 Promote and rate content R: Knowledge Manager	MP-33.5 Send approved content to curation MP-33.6 Rate user-generated item	Send approved peer content to curation; average learner rating 4.5/5.
UFT-13-06 Flag content past review date R: Content Curator	MP-29.5 Flag content past review date	14 items past review date flagged; owners notified.
UFT-13-07 Retire outdated content R: Content Curator	MP-29.6 Retire outdated content MP-25.6 Retire low-value capsule	Retire 6 outdated items and 2 low-value capsules; library health 92%.

E2E-14 · Extended-Enterprise-Training

Goal: Certify partners and train customers. **Starts when:** Partner, reseller or customer training program launched. **Ends when:** External learners trained, paid and certified.

Task	Steps	What to type
UFT-14-01 Create external sub-portal R: Extended Enterprise Manager	MP-22.1 Create external sub-portal	Sub-portal 'Partners Academy — Clinique Al Amal' created for distributors and installers.
UFT-14-02 Configure catalog and pricing R: Extended Enterprise Manager	MP-22.2 Configure external catalog and pricing MP-18.1 Allocate budget by theme and site	Catalog: 'ISO 7101 for partners' 1,200 MAD; 'Electronic health records (EHR) certification' 2,400 MAD. AI run: Catalog: 'ISO 7101 for partners' 1,200 MAD; 'AI triage and clinical decision support certification' 2,400 MAD.
UFT-14-03 Process payment and enroll R: Extended Enterprise Manager	MP-22.3 Process online payment MP-22.4 Enroll external learner	18 online payments processed; 18 external learners enrolled.
UFT-14-04 Deliver external sessions R: Training Administrator	MP-07.1 Create training session MP-07.5 Record attendance	Session P-01 (virtual), 18 invited, 16 present.
UFT-14-05 Track external completion R: Extended Enterprise Manager	MP-22.5 Track external completion	Completion: 15 of 16 passed the final quiz.
UFT-14-06 Issue partner certification R: Extended Enterprise Manager	MP-22.6 Issue partner certification MP-14.4 Issue certificate on completion	Issue 15 partner certificates valid 2 years.
UFT-14-07 Reconcile external revenue R: Finance Manager	MP-18.3 Record committed and actual costs MP-18.4 Compare spend against budget	Revenue 43,200 MAD reconciled with the ERP; 0 unpaid.

SME-E2E-03 · SME Upskill-to-Adoption

Goal: Make sure new digital and AI skills are used at work.. **Starts when:** Funded plan launched. **Ends when:** Adoption confirmed and owner-manager coached.

Task	Steps	What to type
UFT-SME3-01 Assign microlearning capsules R: Training Administrator	SME-MP-03.1 Assign microlearning capsules MP-25.3 Push capsule to collaboration channel	Assign 4 capsules 'Electronic health records (EHR) in 10 minutes' to each employee. AI run: Assign 4 capsules 'AI triage and clinical decision support in 10 minutes' to each employee.
UFT-SME3-02 Coach on the job R: Trainer	SME-MP-03.2 Coach employees on the job	On-the-job coaching: 2 hours per team leader per week for 4 weeks.
UFT-SME3-03 Measure adoption R: L&D Analyst	SME-MP-03.3 Measure tool usage	Adoption: 9 of 12 employees use the new tool every day.
UFT-SME3-04 Coach the owner-manager R: Consultant PM	SME-MP-04.1 Hold monthly coaching session SME-MP-04.2 Update skills dashboard	Monthly coaching with the owner-manager; skills dashboard updated.

9.6 Evaluation, compliance & impact — gate G5

E2E-07 · Assessment-to-Evaluation

Goal: Measure training effectiveness and skill progression. **Starts when:** Training session or path completed. **Ends when:** Effectiveness measured on Kirkpatrick levels 1-3 and skill progression computed.

Task	Steps	What to type
UFT-07-01 Create assessment instrument R: Instructional Designer	MP-09.1 Create assessment instrument	Instrument 'Test Electronic health records (EHR) M1': 15 questions, pass mark 70%. AI run: Instrument 'Test AI triage and clinical decision support M1': 15 questions, pass mark 70%.
UFT-07-02 Draft question bank R: Instructional Designer	MP-09.2 Generate question bank draft	Keep 12 AI-drafted questions, rewrite 3 with Clinical Care & Nursing vocabulary; validate each one.
UFT-07-03 Collect reaction survey (Level 1) R: L&D Analyst	MP-09.3 Collect reaction survey (Level 1)	Reaction survey S-01: 11 responses, satisfaction 4.3/5.
UFT-07-04 Record learning results (Level 2) R: Trainer	MP-09.4 Record learning results (Level 2)	Level 2: average pre-test 48%, post-test 81% (+33 points).
UFT-07-05 Record on-the-job observation (Level 3) R: Manager	MP-09.5 Record on-the-job observation (Level 3)	Level 3 (day 30): 9 of 11 supervisors apply the Electronic health records (EHR) routine daily. AI run: Level 3 (day 30): 9 of 11 supervisors apply the AI triage and clinical decision support routine daily.
UFT-07-06 Compute skill progression R: L&D Analyst	MP-09.6 Compute skill progression MP-10.3 Refresh KPI computation	Skill progression: Electronic health records (EHR) from 1.8 to 2.7 (target 3). AI run: Skill progression: AI triage and clinical decision support from 1.8 to 2.7 (target 3).
UFT-07-07 Review evaluation results R: L&D Analyst	MP-09.7 Review evaluation results MP-20.5 Run periodic quality review	Review: module M3 below 70% pass rate → improvement action assigned to the designer.
UFT-07-08 Publish evaluation report R: L&D Analyst	MP-10.4 Export report MP-10.6 Share insight with stakeholders MP-10.2 Configure dashboard widgets	Export RPT-016 Kirkpatrick report (PDF) and share with the Steering Committee.

E2E-08 · Learning-to-ROI

Goal: Validate ROI and business impact. **Starts when:** Evaluation results available for a theme selected for an ROI study. **Ends when:** Phillips ROI validated with finance and business impact report published.

Task	Steps	What to type
UFT-08-01 Select theme for ROI study R: Performance Analyst	MP-32.1 Select theme for ROI study	ROI study on theme 'Electronic health records (EHR)' — population: 36 supervisors, 3 sites. AI run: ROI study on theme 'AI triage and clinical decision support' — population: 36 supervisors, 3 sites.
UFT-08-02 Define business indicators R: Performance Analyst	MP-32.2 Define business indicators MP-10.1 Define KPI set per audience	Indicators: rework rate, downtime minutes per shift, data re-entry hours.

Task	Steps	What to type
UFT-08-03 Collect cost data R: Finance Manager	MP-18.3 Record committed and actual costs MP-18.4 Compare spend against budget	Costs: design 60,000 MAD; delivery 180,000 MAD; participants' time 95,000 MAD.
UFT-08-04 Isolate training effect R: Performance Analyst	MP-32.3 Isolate training effect MP-09.6 Compute skill progression	Control group: site B (not trained). Isolated benefit: 410,000 MAD per year.
UFT-08-05 Compute Phillips ROI R: Performance Analyst	MP-32.4 Compute Phillips ROI	$ROI = (410,000 - 335,000) / 335,000 = 22\%$; benefit-cost ratio 1.22.
UFT-08-06 Review ROI with finance R: Finance Manager	MP-32.5 Review ROI with finance	Finance review: assumptions accepted; downtime valued at 180 MAD per minute.
UFT-08-07 Publish business impact report R: Head of L&D	MP-32.6 Publish business impact report MP-10.4 Export report MP-10.5 Query data via AI Assistant	Publish RPT-012 ROI & Business Impact Report to executive leadership.

E2E-09 · Compliance-to-Certification

Goal: Ensure compliant workforce with valid certifications. **Starts when:** New regulatory requirement or certification nearing expiry. **Ends when:** Compliant workforce with valid certifications and an audit extract available.

Task	Steps	What to type
UFT-09-01 Register regulatory requirement R: Compliance Officer	MP-14.1 Register regulatory requirement	Requirement 'ISO 7101 awareness', every 24 months, source: ISO 7101 clause on competence.
UFT-09-02 Assign mandatory training R: Compliance Officer	MP-14.2 Assign mandatory training by position	Assign to positions: Clinical Care & Nursing operator, Clinical Care & Nursing supervisor, quality inspector.
UFT-09-03 Deliver mandatory sessions R: Training Administrator	MP-07.3 Enroll learners into session MP-07.5 Record attendance	Enroll 24 employees in session 'ISO 7101 awareness'; attendance recorded.
UFT-09-04 Assess and certify R: Trainer	MP-09.4 Record learning results (Level 2) MP-14.4 Issue certificate on completion	Result 86%; certificate 'ISO 7101 awareness' issued, valid until 2026+2.
UFT-09-05 Compute certification validity R: Compliance Officer	MP-14.3 Compute certification validity	Validity: 212 valid, 9 expire within 60 days, 3 expired.
UFT-09-06 Manage renewals R: Compliance Officer	MP-14.5 Launch renewal enrollment MP-14.6 Confirm renewal completion	Launch renewal for the 12 employees; confirm 10 completions, 2 rescheduled.
UFT-09-07 Produce compliance audit extract R: Compliance Officer	MP-14.7 Produce compliance audit extract MP-10.4 Export report	Export compliance audit extract for ISO 7101 (XLSX) for the external auditor.

HCPR-E2E-01 · Healthcare Providers Compliance-to-Certification Readiness

Goal: Keep Healthcare Providers regulated roles certified against ISO 7101.. **Starts when:** New ISO 7101 requirement or certification expiry. **Ends when:** Sector compliance extract issued with every critical role certified.

Task	Steps	What to type
UFT-HCPR-E1-01 Register ISO 7101 obligations R: Compliance Officer	MP-01.1 Record corporate strategic objectives MP-14.1 Register regulatory requirement	Obligation 'ISO 7101 training', every 12 months, owner Compliance Officer.
UFT-HCPR-E1-02 Link obligations to positions R: HR Business Partner	MP-01.2 Link objectives to functions and sites MP-14.2 Assign mandatory training by position	Linked to 5 Clinical Care & Nursing positions (38 employees).
UFT-HCPR-E1-03 Track certification validity R: Compliance Officer	MP-02.1 Define competency families and levels MP-14.3 Compute certification validity	Validity: 33 valid, 5 expire within 60 days.
UFT-HCPR-E1-04 Issue sector compliance extract R: Compliance Officer	MP-02.2 Set target levels per position MP-14.7 Produce compliance audit extract	Extract issued for the ISO 7101 audit on 15 October.

9.7 Talent, knowledge & continuous improvement — gate G6

E2E-10 · Talent-to-Mobility

Goal: Enable internal mobility and career progression. **Starts when:** Internal opening published or annual career review. **Ends when:** Internal move decided with a reskilling plan assigned.

Task	Steps	What to type
UFT-10-01 Model career paths R: HR Director	MP-13.1 Model career path MP-13.2 Link path steps to competency targets	Career path: Clinical Care & Nursing operator → team leader → supervisor, with competency targets per step.
UFT-10-02 Publish internal opening R: HR Business Partner	MP-31.1 Publish internal opening MP-31.2 Define required skills	Opening 'Clinical Care & Nursing team leader', required skills: Electronic health records (EHR) level 3, leadership level 2. AI run: Opening 'Clinical Care & Nursing team leader', required skills: AI triage and clinical decision support level 3, leadership level 2.
UFT-10-03 Match employees to opening R: HR Business Partner	MP-31.3 Match employees to opening MP-02.7 Validate skills inventory	Review 6 AI matches; keep 4 candidates with match score above 75%.
UFT-10-04 Apply to internal opening R: Employee	MP-31.4 Apply to internal opening	Application with motivation note and consent of the current manager.
UFT-10-05 Shortlist candidates R: Hiring Manager	MP-31.5 Shortlist candidates	Shortlist: 2 candidates; interviews on 20 and 21 June.
UFT-10-06 Plan individual development R: Manager	MP-13.3 Create individual development plan MP-13.4 Suggest development actions MP-42.3 Build leadership development plan MP-42.4 Suggest leadership development actions	Development plan: 2 modules Electronic health records (EHR), 1 leadership workshop, 3 months mentoring. AI run: Development plan: 2 modules AI triage and clinical decision support, 1 leadership workshop, 3 months mentoring.

Task	Steps	What to type
UFT-10-07 Assign reskilling plan R: HR Business Partner	MP-31.6 Assign reskilling plan MP-08.1 Generate personal learning plan	Assign reskilling path 'Electronic health records (EHR) for team leaders' to the selected candidate. AI run: Assign reskilling path 'AI triage and clinical decision support for team leaders' to the selected candidate.
UFT-10-08 Review career and succession R: HR Director	MP-13.5 Run career review MP-13.6 Update succession readiness MP-42.5 Review leadership pipeline MP-42.6 Reassess leadership maturity	Succession readiness updated: 2 ready now, 3 ready within 12 months.

E2E-11 · Onboarding-to-Productivity

Goal: Accelerate time-to-productivity. **Starts when:** New hire or internal mover confirmed. **Ends when:** Employee productive within target time and onboarding closed.

Task	Steps	What to type
UFT-11-01 Create onboarding record R: Hiring Manager	MP-35.1 Create onboarding record	Onboarding record for the new Clinical Care & Nursing technician, start date 1 July, buddy assigned.
UFT-11-02 Generate 30-60-90 day path R: HR Business Partner	MP-35.2 Generate 30-60-90 day path MP-08.1 Generate personal learning plan	30-60-90 path: day 30 safety and ISO 7101; day 60 Electronic health records (EHR); day 90 autonomy on shift. AI run: 30-60-90 path: day 30 safety and ISO 7101; day 60 AI triage and clinical decision support; day 90 autonomy on shift.
UFT-11-03 Enroll in onboarding sessions R: Training Administrator	MP-07.3 Enroll learners into session MP-07.4 Send convocations	Enroll in the induction session of 2 July; convocation sent.
UFT-11-04 Complete onboarding tasks R: Employee	MP-35.3 Complete onboarding tasks	Tasks done: badge, IT account, safety tour, meeting with the team.
UFT-11-05 Hold milestone check-ins R: Hiring Manager	MP-35.4 Hold milestone check-in MP-21.3 Schedule coaching sessions	Day-30 check-in: on track; coaching needed on Electronic health records (EHR) data entry. AI run: Day-30 check-in: on track; coaching needed on AI triage and clinical decision support data entry.
UFT-11-06 Assess time to productivity R: Hiring Manager	MP-35.5 Assess time to productivity	Time to productivity: 74 days (target 90).
UFT-11-07 Close onboarding R: HR Business Partner	MP-35.6 Close onboarding MP-13.3 Create individual development plan	Close onboarding; link the individual development plan for year 1.

E2E-12 · Knowledge-Capture-to-Transfer

Goal: Capture and transfer institutional knowledge. **Starts when:** Critical expert identified as leaving, retiring or holding at-risk knowledge. **Ends when:** Knowledge captured, published and transferred to a validated successor.

Task	Steps	What to type
UFT-12-01 Identify critical experts R: HR Business Partner	MP-34.1 Identify critical experts	Critical expert: senior Clinical Care & Nursing engineer retiring in 8 months; knowledge risk: high.

Task	Steps	What to type
UFT-12-02 Plan capture sessions R: Knowledge Manager	MP-34.2 Plan capture sessions	Capture plan: 4 sessions of 90 minutes on troubleshooting and ISO 7101 practices.
UFT-12-03 Record expert interview R: Knowledge Manager	MP-34.3 Record expert interview	Interview 1 recorded (82 minutes); transcript attached.
UFT-12-04 Structure knowledge R: Knowledge Manager	MP-34.4 Structure knowledge from transcript	Accept the AI structure: 5 failure modes, 12 checks, 3 decision rules; correct 2 technical terms.
UFT-12-05 Publish knowledge article R: Knowledge Manager	MP-12.1 Publish knowledge article MP-12.2 Index article for retrieval MP-33.4 Approve publication	Publish article 'Troubleshooting guide — Clinical Care & Nursing' in EN/FR/AR; indexed for search.
UFT-12-06 Assign successor learning path R: Manager	MP-34.5 Assign successor learning path MP-06.6 Publish content to catalog	Assign the successor path: article + 3 shadowing sessions with the expert.
UFT-12-07 Validate transfer completion R: Subject Matter Expert	MP-34.6 Validate transfer completion	Transfer validated: successor solved 4 of 5 test cases alone.

E2E-31 · Engagement-to-Roadmap

Goal: Define post-engagement roadmap and continuous improvement. **Starts when:** Closure of the current training engineering engagement (E2E-19). **Ends when:** Approved post-engagement roadmap with future missions and continuous improvement plan.

Task	Steps	What to type
UFT-31-01 Consolidate engagement findings R: Consultant PM	MP-50.1 Consolidate engagement findings	Findings: 6 deliverables, 3 lessons learned, 2 open topics (IS, org design).
UFT-31-02 Define future perspectives R: Consultant PM	MP-50.2 Define future perspectives	Perspectives: Digital patient scheduling and billing programme, second wave for OP level. AI run: Perspectives: AI bed and staff capacity planning programme, second wave for OP level.
UFT-31-03 Plan One-to-One coaching R: L&D Strategist	MP-50.3 Plan One-to-One coaching	One-to-One coaching: 6 managers, 6 sessions each over 6 months.
UFT-31-04 Plan organizational optimization R: Org Design Consultant	MP-50.4 Plan organizational optimization	Organizational optimization: merge 2 planning cells; update 11 descriptions.
UFT-31-05 Plan IS rehabilitation R: IT Architect	MP-50.5 Plan IS rehabilitation	IS rehabilitation: connect HRIS and training platform; retire 2 spreadsheets.
UFT-31-06 Define KPIs and dashboards R: Performance Analyst	MP-50.6 Define KPIs and dashboards	KPIs: training coverage, time to competency, ROI per theme; monthly dashboard.

Task	Steps	What to type
UFT-31-07 Prioritize future missions R: Consultant PM	MP-50.7 Prioritize future missions MP-50.8 Validate roadmap with leadership	Priority missions: 1 IS rehabilitation, 2 coaching, 3 org optimization.
UFT-31-08 Publish roadmap R: Consultant PM	MP-50.9 Publish post-engagement roadmap MP-50.10 Track roadmap execution MP-50.11 Improve roadmap continuously MP-50.12 Report on roadmap progress	Publish RPT-010 Post-Engagement Roadmap to the executive committee.

10. Administration

Task	Where	What to type or choose
Add a user	Administration › Users › New user	Name, e-mail in the organization's domain, one or more roles, language. The licence limits the number of active users.
Change what a role can do	Administration › Permissions	Tick or untick a permission for a role. The change applies at once.
Choose the solution pack and add-ons	Administration › Configuration	Pick the pack; switch add-ons on or off. Quotas are shown with their current use.
Activate a compliance standard	Administration › Configuration › Compliance	Read and acknowledge the notice (activation is not a certification), then activate. Controls are created once.
Upload a licence	Administration › Configuration › Licence	Choose the .lic file. The signature and expiry date are checked.
Back up now	Administration › Backups	Click Back up now. Backups are kept 14 days.
Read the audit log	Administration › Audit log	Filter by record, user or date. The log cannot be edited.
Check requirement coverage	Administration › Traceability	Each requirement of the standard with its status and evidence.

Configuration & licence
One Solution Pack, independent add-ons and compliance standards, and the licence.

Usage against quotas

Dimension	Used	Limit
Projects	2	200
OBS nodes	8	1000
Custom AI use cases	3	20
Questionnaires this month	2	∞
Active users	29	600

Licence

Deployment: SAAS
Status: **Active**
Plan: BND-05
Maximum users: 600
Expiry: 3 Nov 2027
Active add-ons: AD-08, AD-11, GDPR, LAW0908, ISO9001
Can create a user: Yes

Warning 30 days before expiry; read-only after expiry.
OnPrem files are verified with the vendor's Ed25519 key.

Solution Packs

- BND-05**
Full Suite
Bundle
- 55**
Modules entitled
- Assistive and Augmented**
AI tier
- Active**
Licence
400 days left

Figure — Administration › Configuration: pack, add-ons, quotas and licence

Appendix — Status colours

Statuses use the same colours everywhere, from red (worst) to green (best):

Colour	Meaning in tasks	Meaning in KPIs
Red	Blocked / overdue	Off target
Amber	In progress	Watch
Yellow	Waiting at a gate	—
Green	Completed	On target
Dark green	Approved / signed off	Above target
