



journi's 8 Transformation Types

How journi implements each archetype, end to end

ERP · Cultural / Values · BPR · Automation · QMS · Operating Model · Compliance · Training & Skills — one manufacturing tenant, Bouregreg Group

8

ARCHETYPES

9

LIVE ALERTS

21

JOURNI MODULES

1

SHARED TENANT

ONE TENANT, EIGHT KINDS OF CHANGE

journi's data model makes this the natural way to show "more than one kind of change"

Bouregreg Group's single tenant holds one Organization, under which every Change Management Project runs — several CM Projects share one Stakeholder Map, one Codebook, and one Permission Matrix, while each keeps its own Lewin phase, ADKAR scores, resistance log, and sustainment record.

- › Every one of the 8 archetypes below runs on a Phase Template with a registered End-to-End lifecycle behind it — not an ad-hoc project structure invented per case.
- › Two of journi's live alerts — Change Saturation (ALT-008) and Communication Overload (ALT-011) — only fire when several of these projects target the same population at once, which is exactly what running all 8 concurrently under one Organization makes real.
- › A ninth case in the same library, Settlat Plant Consolidation & Restructuring, runs on journi's 4 generic core chains instead, since no dedicated lifecycle exists for Restructuring — this guide states that gap plainly rather than imply otherwise.

THE 8 TYPES, AT A GLANCE

Every archetype journey implements with a dedicated lifecycle



ERP Implementation

TPL-ERP-8



Business Process Redesign

TPL-BPR-7



Business Process Automation

TPL-BPA-7



Integrated Management System

TPL-IMS-7



Cultural / Values Transformation

TPL-CULT-7



Operating Model Redesign

TPL-OM-7



Compliance-Driven Change

TPL-COMP-7



Training & Skills Development

TPL-TSD-7



ERP Implementation

A full system cutover across every site at once — the only archetype where all four frameworks matter equally, all the time.

BUSINESS DRIVER

Replacing fragmented, manual, or legacy tooling with one integrated system of record across every site and function.

TARGET POPULATION PATTERN

The broadest population of any archetype — every user of the system being replaced, across every site.


PHASE TEMPLATE

TPL-ERP-8 — 8 phases

1. Discovery
2. Design
3. Build
4. Test

... 4 more (next slide)

TPL-ERP-8: 8 Phases, In Order

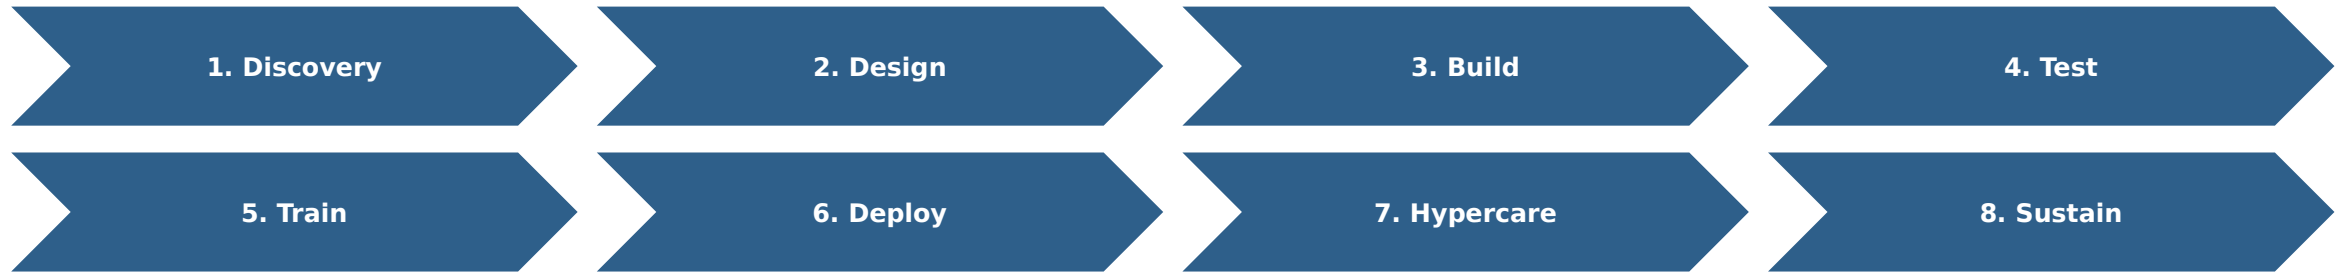

FRAMEWORK WEIGHTING FOR THIS ARCHETYPE

ADKAR + Lewin dominate equally. A system cutover needs organizational readiness (Lewin's Change → Refreeze) and individual capability (ADKAR's Knowledge/Ability) at the same time — neither alone is sufficient, and this is the only archetype where that is true throughout, not just at one phase.

The RACSI Team for This Case

journi's 7-code RACSI role taxonomy (ES/CM/PM/FPO/ITL/SUP/EU), assigned to real, named accounts for this program.

Name	RACSI Code	Role
CFO, Bouregreg Group	ES	Sponsor
Driss El Amrani	CM	Change Manager — owns day-to-day program execution
Ghita Bennis	PM	Practitioner / Contributor — PM-track coordination
Houda Zerouali	FPO	People Manager
Reda Loukili	EU	Employee

Which modules dominate this archetype

M17 (WBS & Gantt)

The 8-phase TPL-ERP-8 template, the longest and most detailed schedule of any archetype.

M5 (ADKAR Engine)

Scored per site/cohort — the direct input to catching site-level divergence (Exception E6).

M9 (Training)

The Train phase's entire content — job aids, sandbox environments, per-site delivery waves.

M12 (Sustainment)

The Hypercare-to-Sustain handoff — the checkpoint that actually justifies closing Lewin at Refreeze.

Bouregreg ERP Adoption Program

3,400 staff, all sites (Casablanca, Kenitra, Settat) · W1-64

Week	Milestone
W1	Discovery opens; Lewin opens at Unfreeze.
W28	Test phase; Casablanca finance cohort fires ALT-001 (Divergence Pattern Detected).
W36-39	Train phase; site-level Composite Readiness Index disaggregation (Exception E6).
W48	Deploy — go-live across all three sites.
W60+	Hypercare exits clean; Sustain phase confirms adoption holds.

What This Case Fires

ALERTS THIS CASE EXERCISES

ALT-001 (Divergence Pattern Detected) · **ALT-009 (Phase Gate No-Go/Conditional, if any gate closes non-Go)**

WHY

The throughline case — the one most likely to exercise a Knowledge/Ability-vs-Bridges divergence, given its scale and duration.

WHAT THIS GUIDE PROVES, CONCRETELY

A real Divergence Pattern catch before go-live, a real cross-site CRI disaggregation, and a Refreeze closed only once Sustain's own evidence supports it.



Business Process Redesign

Redesigning a process independent of any system change — where staff who privately own today's workarounds resist a redesign that makes those workarounds obsolete.

BUSINESS DRIVER

A process that works, technically, but costs the organization real time or money by design — not a tooling problem.

TARGET POPULATION PATTERN

A single function or process family, typically 100-200 staff — narrower than ERP, but often the most emotionally invested population in the library.

PHASE TEMPLATE

TPL-BPR-7 — 7 phases

1. Intake & Diagnosis
2. Clean-Slate Design
3. Build
4. Pilot

... 3 more (next slide)

TPL-BPR-7: 7 Phases, In Order



FRAMEWORK WEIGHTING FOR THIS ARCHETYPE

Kübler-Ross dominates. Staff who built and privately own today's manual workarounds resist a redesign that makes those workarounds obsolete — the Resistance/Anger stage, and the Resistance Log it feeds, is this archetype's central risk, more than any specific skill gap.

The RACSI Team for This Case

journi's 7-code RACSI role taxonomy (ES/CM/PM/FPO/ITL/SUP/EU), assigned to real, named accounts for this program.

Name	RACSI Code	Role
Karim Zniber	ES	Sponsor — VP Finance
Imane Berrada	CM	Change Manager
Othmane Rifai	PM	Program Manager
Salwa Tazi	FPO	Functional Process Owner
Karim Alami	ITL	IT/Technical Lead
Amina Sebti	SUP	Supervisor

Which modules dominate this archetype

M10 (Resistance Log)

The archetype's most-watched module — 3+ open entries fires ALT-004.

M4 (Stakeholder Mapping)

Identifies exactly whose workaround is being redesigned away, by name.

M17 (WBS & Gantt)

The TPL-BPR-7 template — Clean-Slate Design is this archetype's defining phase.

M21 (Field Notes)

Captures the specific, named fear behind a resistance entry, not just its existence.

Order-to-Cash Process Redesign

140 staff, Casablanca finance • 50 weeks (guide numbering)

Week	Milestone
Wk 1	Intake & Diagnosis opens, run alongside the ERP program's own Discovery.
Wk 10	Clean-Slate Design signed off.
Wk 20–24	Pilot on a single process step; third resistance entry lands, firing ALT-004.
Wk 34	Organization-wide rollout.
Wk 50	Sustainment handoff.

What This Case Fires

ALERTS THIS CASE EXERCISES


ALT-004 (Resistance Escalation Threshold Breached)

WHY

Built deliberately to cross the resistance-escalation threshold — the defining alert of this archetype.

WHAT THIS GUIDE PROVES, CONCRETELY

A real ALT-004 firing, resolved through a co-designed accuracy safeguard the resisting staff themselves helped define — not overridden from above.



Business Process Automation

A narrow, well-scoped RPA project with no judgment calls — journi's deliberate low-resistance, fast-moving contrast case.

BUSINESS DRIVER

A repetitive task with no judgment calls involved — a strong automation candidate by nature, not a cultural or process problem.

TARGET POPULATION PATTERN

The narrowest population of any archetype — a single team, often under 20 staff, already bought into the change.

PHASE TEMPLATE

TPL-BPA-7 — 7 phases

1. Automation-Opportunity Assessment
2. Architecture Design
3. Build
4. UAT & Shadow-Mode

... 3 more (next slide)

TPL-BPA-7: 7 Phases, In Order



FRAMEWORK WEIGHTING FOR THIS ARCHETYPE

All four frameworks read favorably from the start, by design. This is journi's deliberate contrast case: a narrow scope, an already-bought-in team, and a visibly active Sponsor mean no framework carries unusual risk — the point being that not every program needs a recovery playbook.

The RACSI Team for This Case

journi's 7-code RACSI role taxonomy (ES/CM/PM/FPO/ITL/SUP/EU), assigned to real, named accounts for this program.

Name	RACSI Code	Role
Hakim Berrada	ES	Sponsor
Salma Ouazzani	CM	Change Manager
Amine Sqalli	PM	Program Manager
Yassine Kabbaj	ITL	IT/Technical Lead
Nawal Fassi	FPO, SUP	Functional Process Owner and Supervisor, combined

Which modules dominate this archetype

M17 (WBS & Gantt)

The shortest phase template in the library — closed in as few as 18-19 weeks.

M5 (ADKAR Engine)

A light-touch score, since the team starts already bought in.

M7 (Sponsor & Coalition)

A visibly active Sponsor from day one — the opposite pattern of the Cultural case.

M21 (Field Notes)

Routine logging — this archetype's data is notable for how little it needs to escalate.

Kenitra Invoice-Matching Automation

18 staff, Kenitra accounts payable · 19 weeks (guide numbering)

Week	Milestone
Wk 1	Opportunity assessment; already-bought-in team confirmed.
Wk 5	Architecture design.
Wk 10	Build complete.
Wk 13-14	UAT and shadow-mode — the bot runs alongside the manual process for two weeks.
Wk 16	Production go-live.
Wk 19	CoE handover — closed without any of journi's 9 live alerts firing.

What This Case Proves By Not Firing

NO LIVE ALERT FIRES IN THIS PROGRAM'S REAL RECORD

Stated plainly, not manufactured — a clean record reported as a clean record.

WHY

None. Closed by design without any of journi's 9 live alerts firing — the clean-close contrast case that proves not every program needs a recovery playbook.

WHAT THIS GUIDE PROVES, CONCRETELY

A clean-close record stated plainly, without a manufactured crisis — the deliberate contrast to every other case in the library.



Integrated Management System

Pursuing ISO 9001/14001 certification on one management system rather than two — sponsored alone, without a guiding coalition.

BUSINESS DRIVER

A customer contract now requires certified quality management; a parallel certification is bundled in for efficiency.

TARGET POPULATION PATTERN

A plant's operations and quality function together — often 300-500 staff, spanning shop floor and back office.

PHASE TEMPLATE

TPL-IMS-7 — 7 phases

1. Intake & Diagnosis
2. Design
3. Implementation
4. Mock-up Audit

... 3 more (next slide)

TPL-IMS-7: 7 Phases, In Order



FRAMEWORK WEIGHTING FOR THIS ARCHETYPE

Lewin never fully closes. Ongoing Surveillance is the longest single-phase tail in the library by design — certification surveillance never formally ends, so Refreeze is the one Lewin stage this archetype treats as a standing state, not a destination.

The RACSI Team for This Case

journi's 7-code RACSI role taxonomy (ES/CM/PM/FPO/ITL/SUP/EU), assigned to real, named accounts for this program.

Name	RACSI Code	Role
Nadia Fassi	ES	Sponsor — Quality Manager
Rania Bensouda	CM	Change Manager
Samir Chraibi	PM	Program Manager
Mehdi Ouahbi	FPO	Functional Process Owner
Yasmine Kadiri	ITL	IT/Technical Lead
Aziz Berrada	SUP	Supervisor

Which modules dominate this archetype

M7 (Sponsor & Coalition)

The archetype's central risk — fewer than 2 coalition members fires ALT-010.

M17 (WBS & Gantt)

The TPL-IMS-7 template — Mock-up and Certifying Audit are external-facing gates.

M12 (Sustainment)

Ongoing Surveillance checkpoints, run indefinitely past program close.

M19 (Charter Registry)

Formal charters carry unusual weight given the external audit stakes.

ISO 9001/14001 Integrated Management System

410 staff, Settat plant operations + quality · 60 weeks (guide numbering)

Week	Milestone
Wk 1	Intake & diagnosis, started alongside the ERP program's own kickoff.
Wk 12	Design.
Wk 26	Implementation; the Quality Manager's coalition gap is logged and ALT-010 fires.
Wk 38	Mock-up audit.
Wk 46	Certifying audit — passes clean.
Wk 50+	Surveillance prep, then ongoing surveillance — never formally closes.

What This Case Fires

ALERTS THIS CASE EXERCISES

ALT-010 (Guiding Coalition Gap)

WHY

Built specifically because a Quality Manager sponsoring alone, without a broader coalition, is a realistic single-sponsor failure mode.

WHAT THIS GUIDE PROVES, CONCRETELY

A real ALT-010 firing, resolved by recruiting a Procurement Director and HR Business Partner as genuine coalition members — not just a wider distribution list.



Cultural / Values Transformation

Aligning two distinct ways of working under one set of values after an acquisition — not a system or process change at all.

BUSINESS DRIVER

A stated acquisition synergy that depends on two separate workforces actually operating as one company within a fixed horizon.

TARGET POPULATION PATTERN

An acquired team plus their new counterparts — identity-level change reaching everyone touched by the integration, not a functional subset.

PHASE TEMPLATE

TPL-CULT-7 — 7 phases

1. Diagnosis
2. Target Values Design
3. Leadership Modeling & Reinforcement Build
4. Pilot Cohort

... 3 more (next slide)

TPL-CULT-7: 7 Phases, In Order



FRAMEWORK WEIGHTING FOR THIS ARCHETYPE

Bridges and Kübler-Ross dominate. Identity and emotional integration matter more than any specific skill here — a newly appointed Sponsor with zero logged actions damages exactly these two frameworks fastest, which is why this archetype is built to fire ALT-003 early.

The RACSI Team for This Case

journi's 7-code RACSI role taxonomy (ES/CM/PM/FPO/ITL/SUP/EU), assigned to real, named accounts for this program.

Name	RACSI Code	Role
Karim Fassi	ES	Sponsor — newly appointed integration Sponsor
Nadia Chraibi	CM	Change Manager
Youssef Idrissi	PM	Integration Program Manager
Amal Ziani	FPO	HR Business Partner for the integration
Hicham Bennani	ITL	Systems/tooling lead
Fatima-Zahra Idrissi	SUP	Tangier Distribution Center site lead
Rachid Amrani	SUP	Casablanca supply chain/logistics lead

Which modules dominate this archetype

M6 (Emotional & Transition Layer)

The heaviest use of Bridges and Kübler-Ross of any archetype — two starting cultures tracked side by side.

M7 (Sponsor & Coalition)

A newly appointed Sponsor starts with zero logged actions — the direct ALT-003 trigger.

M5 (ADKAR Engine)

Desire is the block most exposed here — a named, specific fear (job security) stalls it.

M8 (Communications)

Joint briefings for paired cohorts, not separate messaging for each legacy culture.

One Bouregreg: Post-Acquisition Culture Integration

260 staff (acquired Tangier team) + Bouregreg counterparts · 18-month horizon, W27 onward

Week	Milestone
Wk 1 (org W27)	Diagnosis opens, six months into the ERP program.
Wk 4 (org W30)	Target-values design; ALT-003 fires before the Sponsor's first logged action.
Wk 12 (org W38)	Leadership modeling and reinforcement build begins.
Wk 20 (org W46)	Pilot cohort — one Tangier team paired with one legacy Bouregreg team.
Wk 32 (org W58)	Organization-wide rollout; reinforcement continues well past the ERP program's own close.

What This Case Fires

ALERTS THIS CASE EXERCISES

ALT-003 (Sponsor Coverage Gap)

WHY

Built deliberately around a newly appointed Sponsor's slow start — the archetype most exposed to sponsorship visibility risk.

WHAT THIS GUIDE PROVES, CONCRETELY

A real Sponsor Coverage Gap that fires and is corrected, a real Desire stall traced to a named fear, and a Refreeze signed only once the evidence — not the acquisition's press-release timeline — supports it.



Operating Model Redesign

Realigning reporting lines from site-based to function-based — where the real risk is reversion under pressure, not initial adoption.

BUSINESS DRIVER

A prior program (often ERP) exposes how much duplicated decision-making the old structure causes.

TARGET POPULATION PATTERN

People-manager-level staff across every site — narrower in headcount than ERP, but concentrated at the decision-making layer.

PHASE TEMPLATE

TPL-OM-7 — 7 phases

1. Current Operating Model Assessment
2. TOM Design
3. Detailed Org Design
4. Pilot Transition

... 3 more (next slide)

TPL-OM-7: 7 Phases, In Order



FRAMEWORK WEIGHTING FOR THIS ARCHETYPE

ADKAR Reinforcement dominates. Function Heads can pass every earlier checkpoint and still revert to old decision-making under real operational pressure — this archetype is built specifically to show that failure mode, not initial adoption, is the real test.

The RACSI Team for This Case

journi's 7-code RACSI role taxonomy (ES/CM/PM/FPO/ITL/SUP/EU), assigned to real, named accounts for this program.

Name	RACSI Code	Role
Yassine Berrada	ES	Sponsor — COO
Salma Idrissi	CM	Change Manager
Rachid Alaoui	PM	Program Manager
Amina Sqalli	FPO	Finance Function Head
Nabil Ouazzani	ITL	IT/Technical Lead
Loubna Tazi	SUP	Casablanca pilot site

Which modules dominate this archetype

M12 (Sustainment)

The 30-day post-transition checkpoint — where a High regression risk fires ALT-002.

M5 (ADKAR Engine)

Reinforcement tracked separately from Ability, since this archetype is where the two diverge.

M17 (WBS & Gantt)

The TPL-OM-7 template — Pilot Transition de-risks Full Transition, one site at a time.

M6 (Emotional & Transition Layer)

A premature "New Beginning" reading is exactly what a regression later contradicts.

Regional Operating Model Redesign

95 staff, people managers across 3 sites · 34 weeks (guide numbering)

Week	Milestone
Wk 1	Current operating model assessment opens, once the ERP Build phase exposes duplication.
Wk 8	Target operating model design.
Wk 14	Detailed org design.
Wk 18	Pilot transition — Casablanca Finance first.
Wk 22 / 26	Full transition; the 30-day checkpoint lands High regression risk, firing ALT-002/ALT-015.
Wk 34	Governance adoption tracking and standing rhythm handover, resolved only once a clean checkpoint follows.

What This Case Fires

ALERTS THIS CASE EXERCISES


ALT-002 (Regression Risk Score Critical) · ALT-015 (Sustainment Sign-Off Blocked)

WHY

Built to run past its first sustainment checkpoint with High regression risk — the clearest real-data proof in the library that training completion alone does not guarantee reinforcement.

WHAT THIS GUIDE PROVES, CONCRETELY

A real regression caught by a genuine 30-day checkpoint — not glossed over — and a training-completion record (100% by Week 25) that proves Reinforcement, not Knowledge, was the actual gap.



Compliance-Driven Change

Bringing data handling into compliance with a fixed external deadline — the case where a Phase Gate closing as anything but Go has zero schedule slack to absorb it.

BUSINESS DRIVER

A scheduled regulatory audit with a fixed external deadline, not a discretionary program timeline.

TARGET POPULATION PATTERN

Any function touching the regulated data — often 300+ staff spanning HR, Sales, and Customer Service.

PHASE TEMPLATE

TPL-COMP-7 — 7 phases

1. Regulatory Requirement & Gap Analysis
2. Control Design
3. Control Implementation
4. Internal Audit / Independent Testing

... 3 more (next slide)

TPL-COMP-7: 7 Phases, In Order



FRAMEWORK WEIGHTING FOR THIS ARCHETYPE

Awareness and Ability dominate; Desire matters least of any archetype. Staff do not need to want to comply — they need to know the rule and be able to follow it correctly. The Phase Gate itself is the framework that matters most, since the real risk here is schedule risk, not adoption risk.

The RACSI Team for This Case

journi's 7-code RACSI role taxonomy (ES/CM/PM/FPO/ITL/SUP/EU), assigned to real, named accounts for this program.

Name	RACSI Code	Role
Karim Idrissi	ES	Sponsor — General Counsel/Chief Compliance Officer
Sanaa Bouzoubaa	CM	Change Manager
Hamza Alaoui	PM	Compliance Program Lead
Nadia Squalli	FPO	HR Data Privacy Lead
Reda Fassi	ITL	Data systems and access-control lead
Amine Tazi	SUP	Sales Operations Manager

Which modules dominate this archetype

M17 (WBS & Gantt)

The TPL-COMP-7 template — every phase gate dated against a fixed external deadline.

M5 (ADKAR Engine)

Awareness and Ability scored against specific, checkable rules — not general sentiment.

M19 (Charter Registry)

Formal charters matter more here given the external regulator relationship.

M9 (Training)

Checkable-behavior training — data handling, retention, access requests — not persuasion.

Loi 09-08 Data Protection Compliance Program

310 staff, HR, Sales, Customer Service · 64 weeks (guide numbering)

Week	Milestone
Wk 1	Regulatory requirement and gap analysis, run from the tenant's own start given the fixed deadline.
Wk 14	Control design.
Wk 28	Control implementation.
Wk 40	Internal audit / independent testing.
Wk 48	Controls go live, timed deliberately ahead of the ERP program's own Deploy week.
Wk 52	First monitoring cycle confirms controls hold under real operating conditions.

What This Case Proves By Not Firing

NO LIVE ALERT FIRES IN THIS PROGRAM'S REAL RECORD

Stated plainly, not manufactured — a clean record reported as a clean record.

WHY

None fire in this program's real record — every Phase Gate closes Go, on schedule, which is the entire point: ALT-009 (Phase Gate No-Go/Conditional) matters most here precisely because it does not fire.

WHAT THIS GUIDE PROVES, CONCRETELY

Seven consecutive clean Phase Gate decisions — ALT-009 matters here precisely because it never fires, given zero schedule slack for anything less than Go.



Training & Skills Development

A standalone digital-skills program with no go-live of its own — the only archetype where training is the entire content of every phase, not a supporting track.

BUSINESS DRIVER

A skills gap identified independently of any other program, run to prepare a workforce for years of technology change generally.

TARGET POPULATION PATTERN

Plant-floor staff without prior systems training — often 600+ staff across multiple sites, the largest population of any non-ERP archetype.

PHASE TEMPLATE

TPL-TSD-7 — 7 phases

1. Skills Gap Diagnosis
2. Curriculum Design
3. Training Delivery
4. Competency Verification

... 3 more (next slide)

TPL-TSD-7: 7 Phases, In Order



FRAMEWORK WEIGHTING FOR THIS ARCHETYPE

All five ADKAR blocks dominate equally, in sequence. Reinforcement is engineered by two dedicated phases (Practical Application, On-the-Job Coaching) — the only archetype in the series to build reinforcement deliberately rather than leave it to chance.

The RACSI Team for This Case

journi's 7-code RACSI role taxonomy (ES/CM/PM/FPO/ITL/SUP/EU), assigned to real, named accounts for this program.

Name	RACSI Code	Role
Fouad Belghazi	ES	Sponsor — VP Manufacturing Operations
Houda Amrani	CM	Change Manager
Tarik Benjelloun	PM	Skills Program Lead
Leila Ouahbi	FPO	Learning & Development Lead
Younes Berrada	ITL	Learning-systems and AI-drafting-tool lead
Karima Semlali	SUP	Kenitra Plant Floor Supervisor
Mustapha Idrissi	SUP	Settat Plant Floor Supervisor

Which modules dominate this archetype

M9 (Training)

The heaviest use of any archetype — the entire program's content runs through this module.

M16 (AI Use Case Library)

AI-assisted curriculum drafting — the archetype that most exercises this module.

M5 (ADKAR Engine)

All five blocks tracked in sequence, from Awareness through Reinforcement.

M12 (Sustainment)

Two consecutive clean checkpoints, spaced apart, before the program closes Refreeze.

Plant Digital Skills Upskilling Program

620 staff, plant floor, Kenitra and Settat · 43 weeks (guide numbering)

Week	Milestone
Wk 1	Skills gap diagnosis opens.
Wk 15	Curriculum finalized, AI-assisted via M16.
Wk 23	Pilot cohort validated.
Wk 29	Full deployment complete across both plants.
Wk 31	Competency verification confirms 100% certification.
Wk 43	Two consecutive sustainment checks confirm the skill holds without coaching; program closes.

What This Case Proves By Not Firing

NO LIVE ALERT FIRES IN THIS PROGRAM'S REAL RECORD

Stated plainly, not manufactured — a clean record reported as a clean record.

WHY

None — none of journi's 9 live alerts are built around a standalone skills program with no go-live and no resistance log of its own.

WHAT THIS GUIDE PROVES, CONCRETELY

A skill genuinely verified through hands-on testing (not attendance), and reinforcement engineered on purpose through two dedicated phases — not left to chance.

CROSS-TYPE COMPARISON

Population, duration, and dominant framework, side by side

Archetype	Population	Duration	Dominant Framework
ERP	3	W1-64	ADKAR + Lewin dominate equally
BPR	140 staff	50 weeks (guide numbering)	Kübler-Ross dominates
Automation	18 staff	19 weeks (guide numbering)	All four frameworks read favorably from the start, by design
QMS	410 staff	60 weeks (guide numbering)	Lewin never fully closes
Cultural	260 staff (acquired Tangier team) + Bouregreg counterparts	18-month horizon, W27 onward	Bridges and Kübler-Ross dominate
Operating Model	95 staff	34 weeks (guide numbering)	ADKAR Reinforcement dominates
Compliance	310 staff	64 weeks (guide numbering)	Awareness and Ability dominate; Desire matters least of any archetype
Training & Skills	620 staff	43 weeks (guide numbering)	All five ADKAR blocks dominate equally, in sequence

Which of the 9 live alerts each archetype exercises

Archetype	Alerts Exercised
ERP	ALT-001, ALT-009
BPR	ALT-004
Automation	None (by design)
QMS	ALT-010
Cultural	ALT-003
Operating Model	ALT-002, ALT-015
Compliance	None (by design)
Training & Skills	None (by design)

THE PORTFOLIO VIEW

Two alerts only the portfolio, not any single project, can trigger

ALT-008

Change Saturation Threshold Breached

Fires once a project's population segment is targeted by 2 or more other concurrent initiatives — true almost everywhere in this library by design, since the ERP program, the Operating Model redesign, and the Training & Skills program all reach broad, overlapping populations across the same three sites.

ALT-011

Communication Overload Detected

Fires once combined not-yet-sent communications queued across a population's concurrent initiatives exceed three — realistic here precisely because 8 programs are drafting town halls, FAQs, and go-live messages against overlapping audiences at the same time.



Eight kinds of change. One system of record.

journi implements every archetype with the same rigor: a real phase template, real modules, real frameworks — and honesty about which alerts actually fire, and which don't.
