



Business Process Automation

Kenitra Invoice-Matching Automation

A narrow, well-scoped RPA project with no judgment calls — journi's deliberate low-resistance, fast-moving contrast case.

7

PHASES

19

WEEKS

6

EXCEPTIONS

3

TRAINING TIERS

PART 0 — PURPOSE

What This Guide Is, and How to Use It

WHAT THIS GUIDE IS

This deck follows the Kenitra Invoice-Matching Automation program — journi's Business Process Automation archetype case — from tenant setup through CoE handover, the shortest and cleanest program in the entire scenario library.

HOW TO USE IT

This program runs inside the same Bouregreg Group tenant as every other archetype in this series. A reader with the tenant already set up skips straight to CM Project creation.

Verified Against journi's Real Source

This is journi's own stated case with no alerts in its real record. This deck states that plainly, the same way it documents every real exception in the series' other guides — a clean record reported as a clean record, not dramatized, with six realistic contingency patterns shown as hypothetical precisely because none of them actually occurred.

RACSI CODES USED THROUGHOUT

ES = Executive Sponsor · CM = Change Manager · PM = Program/Project Manager · FPO = Functional Process Owner · ITL = IT/Technical Lead · SUP = Supervisor · EU = End User

Why This Case Matters

Every other guide in this series shows a program working through a real risk. This one proves the opposite point just as concretely: not every Change Management Project needs a recovery playbook, when the scope is narrow, the team is already bought in, and the Sponsor is visibly active from day one.

The Case, in Brief

18 staff, Kenitra accounts payable

19 weeks (guide numbering)

A robotic process automation project matches supplier invoices against purchase orders at the Kenitra plant — a repetitive task with no judgment calls, automated in 19 weeks against an already-bought-in 18-person team.

What This Guide Proves, Concretely

A closed program with zero of journi's 9 live alerts fired, a real two-week shadow-mode validation before go-live, and six honestly-labeled hypothetical contingencies showing exactly how this program could have gone differently, had the conditions been less favorable.

Weighting for This Archetype

All four frameworks read favorably from the start, by design. This is journi's deliberate contrast case: a narrow scope, an already-bought-in team, and a visibly active Sponsor mean no framework carries unusual risk — the point being that not every program needs a recovery playbook.

The Composite Readiness Index, Read for This Case

The Composite Readiness Index reads high and rising from Week 1 with no dip worth naming — Benchmarking reads "Ahead" for most of the program's life, and this guide's own honesty standard applies here just as strictly as anywhere else: a clean trend is reported as a clean trend.

The Existing Tenant, and Reading Paths by Role

THE EXISTING TENANT

This program runs inside the same tenant journi's Master User Guide builds, under the existing Bouregreg Manufacturing Maroc Organization — no new Organization needed.

READING PATHS, BY ROLE

- › A Change Manager running this program day to day: Part 2 once, then Part 4 in full.
- › A Program/Project Manager: Part 4's PM Track column and the Master WBS & Gantt.
- › An Executive Sponsor: Part 1, then Part 4's phase-opening narratives.
- › A Super Admin or Org Admin: Part 3.

The RACSI Team for This Program

Name	RACSI Code	Role
Hakim Berrada	ES	Sponsor
Salma Ouazzani	CM	Change Manager
Amine Sqalli	PM	Program Manager
Yassine Kabbaj	ITL	IT/Technical Lead
Nawal Fassi	FPO, SUP	Functional Process Owner and Supervisor, combined

Creating the CM Project

1 On Module 1 — Hierarchy, create the Kenitra Invoice-Matching Automation CM Project under the existing Bouregreg Manufacturing Maroc Organization.

2 Set Change type: Business Process Automation. Target population: "Kenitra accounts payable, 18 staff." Business driver: "A repetitive task with no judgment calls — a strong automation candidate."

3 Save. Lewin opens at Unfreeze — the team already bought in, unlike every resistance-driven case elsewhere in this series.

4 On Module 17 — WBS & Gantt, load the TPL-BPA-7 phase template: Automation-Opportunity Assessment, Architecture Design, Build, UAT & Shadow-Mode, Production Go-Live, Exception Tuning, CoE Handover.

Charters for This Program

Charter	Accountable	Review Cadence
CHTR-01 Sponsorship / Leadership Charter	Hakim Berrada (ES)	Per Phase Gate
CHTR-08 Pulse / Interview Charter	Salma Ouazzani (CM)	Per phase gate + ad hoc

Setup Checklist

- ☒ Base tenant confirmed (Bouregreg Group, existing Organization)
- ☒ Automation program team accounts created
- ☒ CM Project created, Lewin opened at Unfreeze
- ☒ TPL-BPA-7 phase template loaded on M17
- ☒ Applicable Charters reviewed and accountable owners confirmed

PART 4 — WEEK-BY-WEEK TIMELINE

7 Phases, In Order



Total program length: 19 weeks (guide numbering). Every phase below is walked in detail across the next slides — normal flow first, then six exceptions in full operational detail.

Automation-Opportunity Assessment

Weeks 1-4


NARRATIVE

Confirms the invoice-matching task is genuinely low-exception and judgment-free — the specific test every automation candidate has to pass before Architecture Design begins.

Key Moments in This Phase

Week	What Happens
Week 1	Kickoff; Lewin opens at Unfreeze.
Week 3	Historical invoice data sampled to confirm low exception rate.
Week 4	Opportunity assessment gate closes.

Framework Snapshot

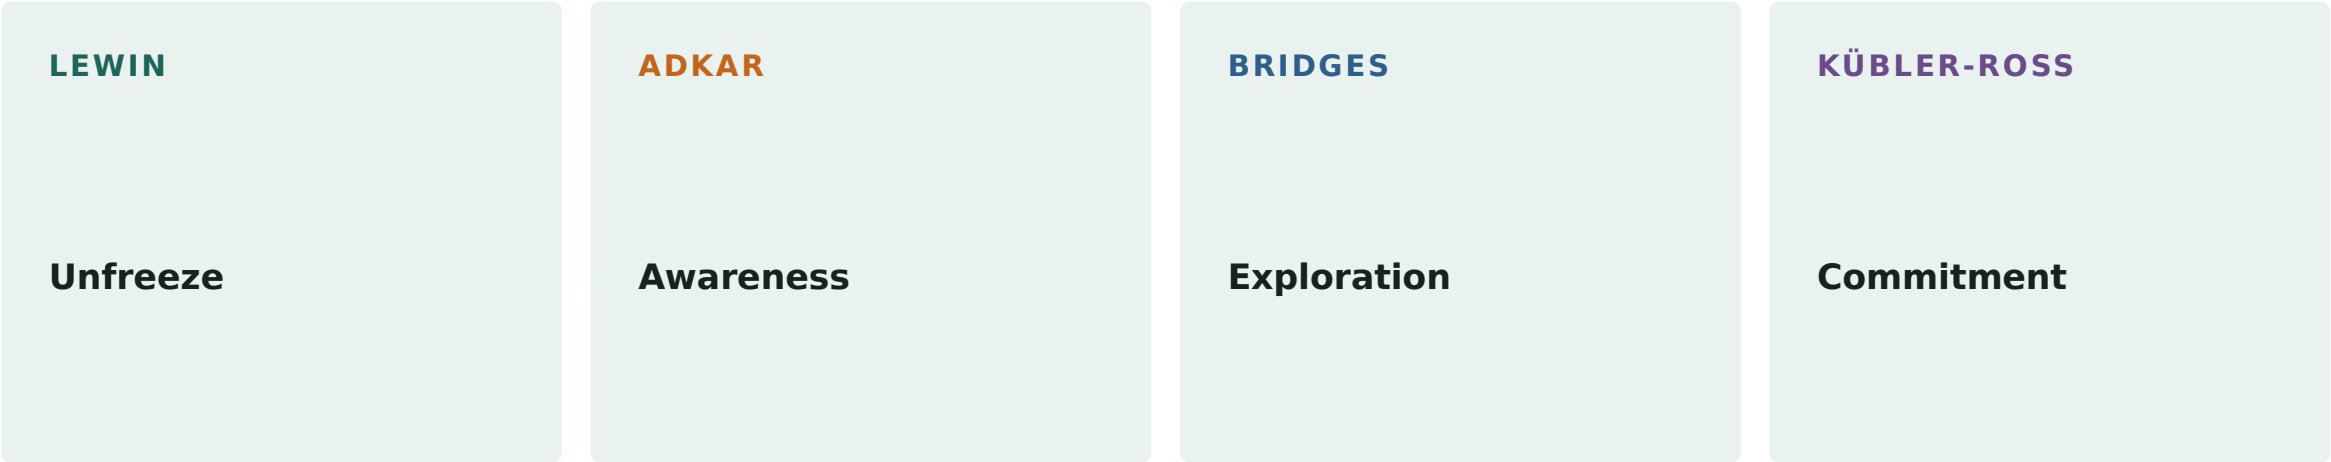

KEY TECHNIQUE THIS PHASE

Exception-rate sampling: Confirm the task is genuinely low-judgment before committing design effort.

Architecture Design

Weeks 4-9

NARRATIVE


Designs the bot's architecture against the confirmed opportunity — where a licensing or platform constraint (Exception C5) could realistically surface.

Key Moments in This Phase

Week	What Happens
Week 5	Bot architecture drafted against the purchase-order matching logic.
Week 9	Architecture design signed off.

PHASE 2 · ARCHITECTURE DESIGN

Framework Snapshot

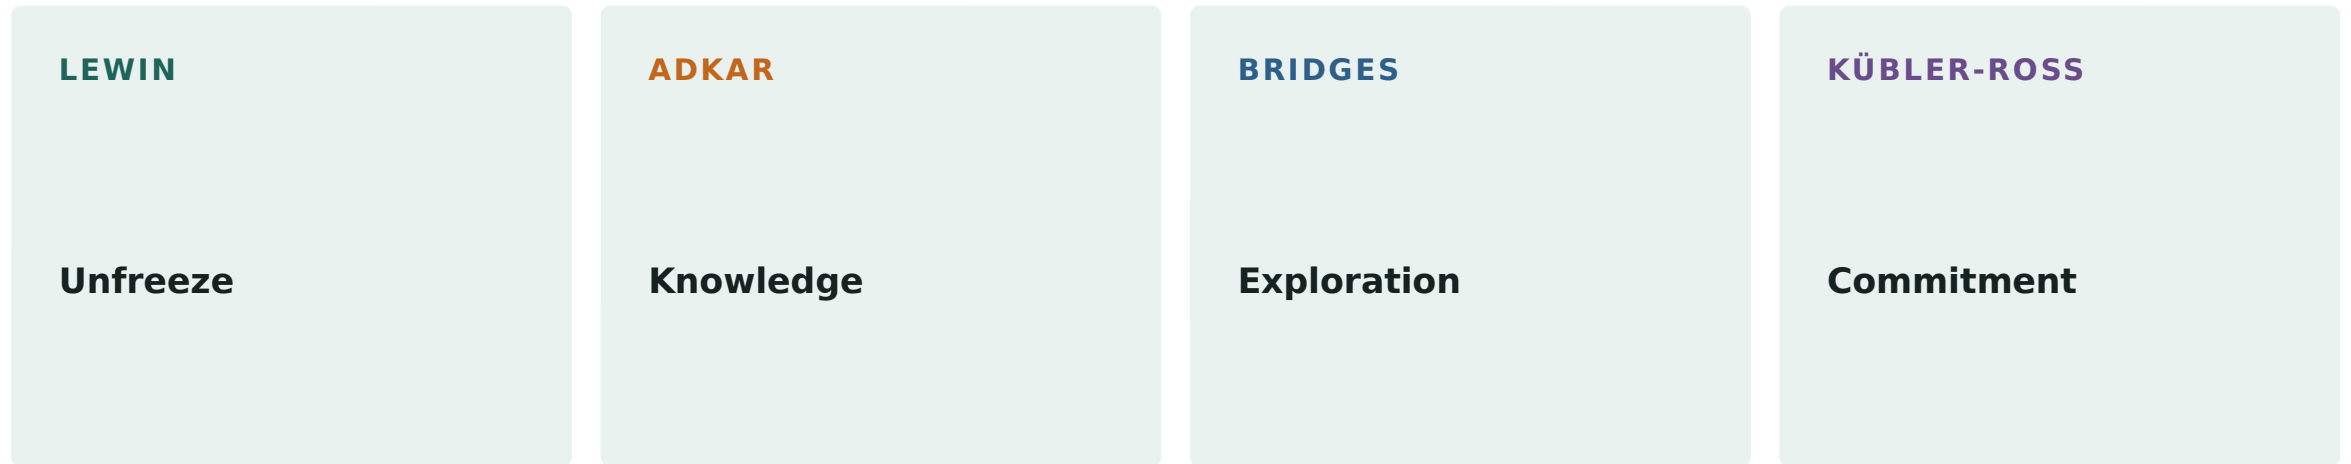

KEY TECHNIQUE THIS PHASE

Bot architecture design against real system constraints: Design against actual platform/licensing limits, not assumed ones.

Build

Weeks 9–12

NARRATIVE


Builds the bot against the signed-off architecture — the phase this guide's contingency patterns C1, C4, and C5 all map to.

Key Moments in This Phase

Week	What Happens
Week 10	Development against the purchase-order matching logic.
Week 12	Build gate closes; internal testing confirms exception-handling rules.

PHASE 3 · BUILD

Framework Snapshot

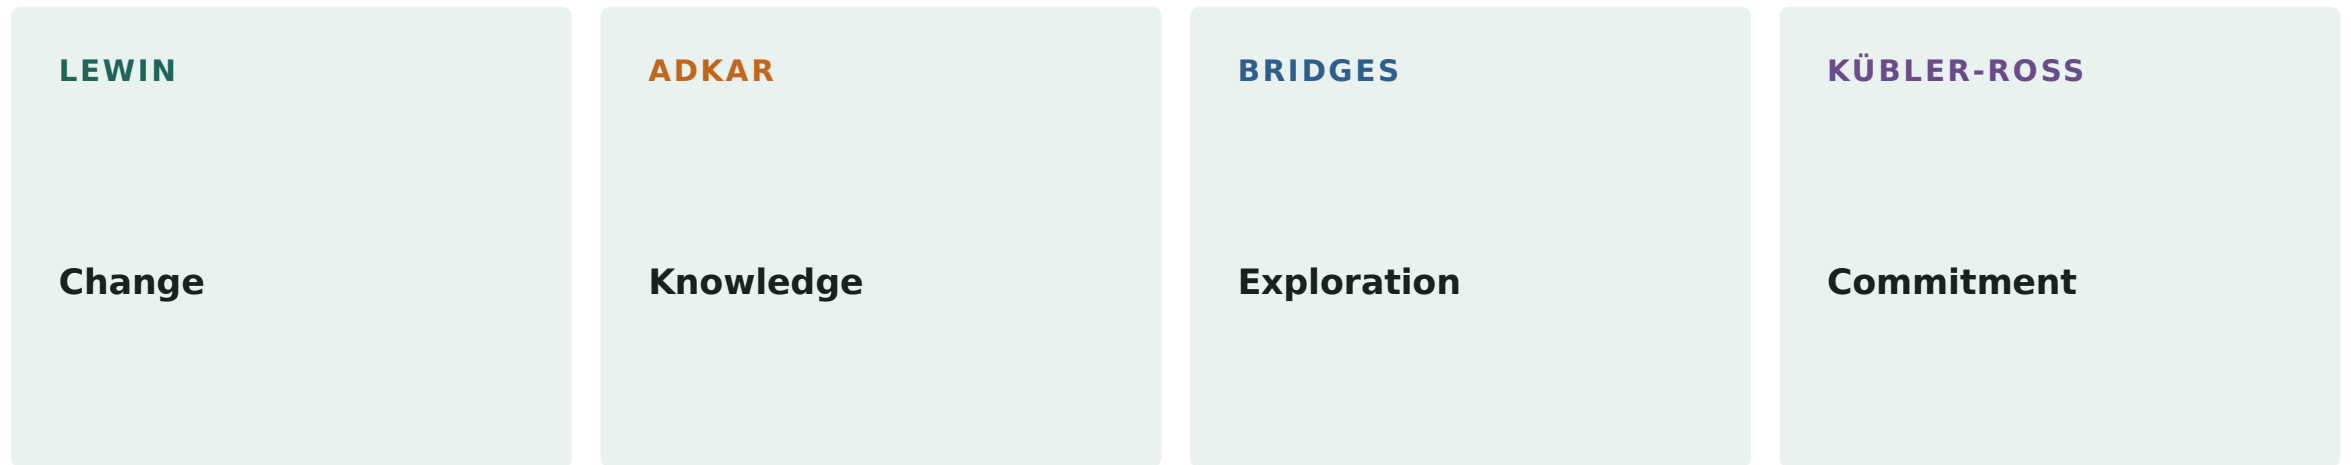

KEY TECHNIQUE THIS PHASE

Iterative build against the matching logic: Build the bot's core matching logic and exception-handling rules together.

UAT & Shadow-Mode

Weeks 12-14

NARRATIVE

Runs the bot alongside the manual process for two weeks — a real, not simulated, validation before any production dependency.

Key Moments in This Phase

Week	What Happens
Week 12	Shadow-mode begins; bot runs in parallel with the manual process.
Week 14	Shadow-mode closes clean; UAT gate passes.

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Two-week parallel shadow-mode run: Validate the bot against real production data with a real fallback still active.

Production Go-Live

Weeks 14-16


NARRATIVE

Cuts the manual process over to the bot in production — the shortest go-live window in the scenario library.

Key Moments in This Phase

Week	What Happens
Week 14	Production go-live.
Week 16	Go-live gate closes; stability confirmed.

Framework Snapshot

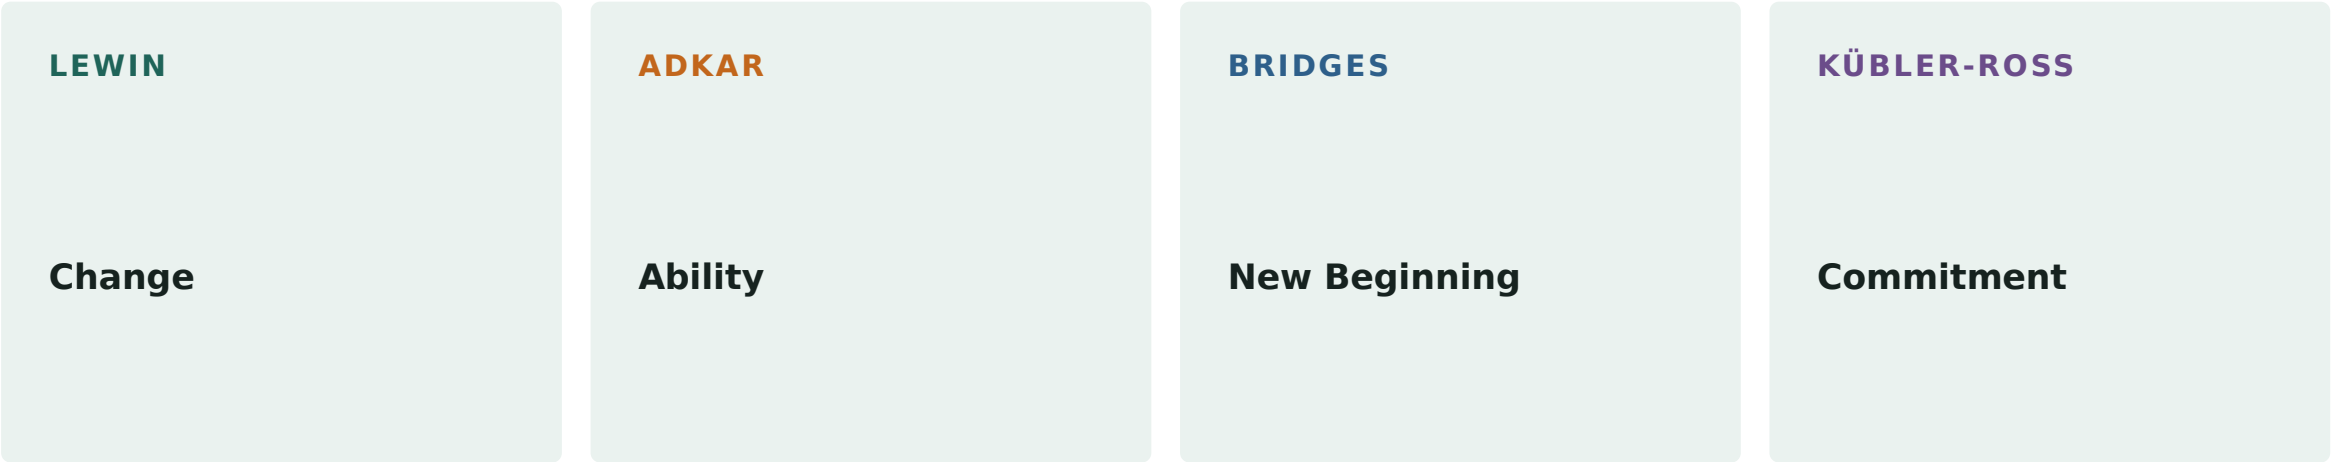

KEY TECHNIQUE THIS PHASE

Direct production cutover: Cut over once shadow-mode has already proven the bot clean.

Exception Tuning

Weeks 16-18


NARRATIVE

Tunes the bot's exception-handling rules against real production volume, not just the test sample.

Key Moments in This Phase

Week	What Happens
Week 16	Real-volume exception patterns reviewed.
Week 18	Exception-handling rules finalized and stable.

Framework Snapshot

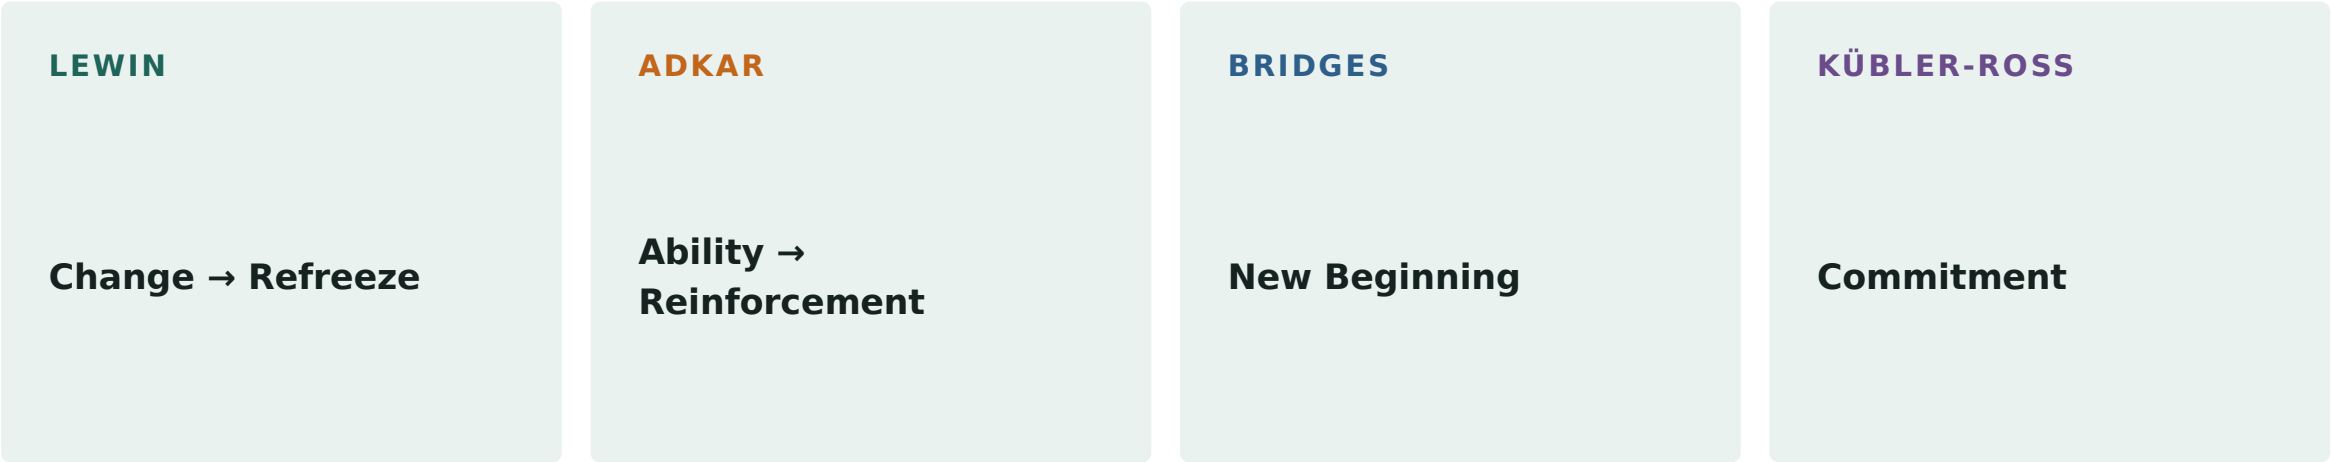

KEY TECHNIQUE THIS PHASE

Real-volume exception review: Tune rules against real production volume, which always differs from the test sample.

CoE Handover

Weeks 18-19


NARRATIVE

Hands the bot's ongoing monitoring to the Center of Excellence — the handover Exception C6 warns can happen on paper without genuinely transferring.

Key Moments in This Phase

Week	What Happens
Week 18	CoE handover package delivered.
Week 19	Program closes with zero alerts fired.

Framework Snapshot

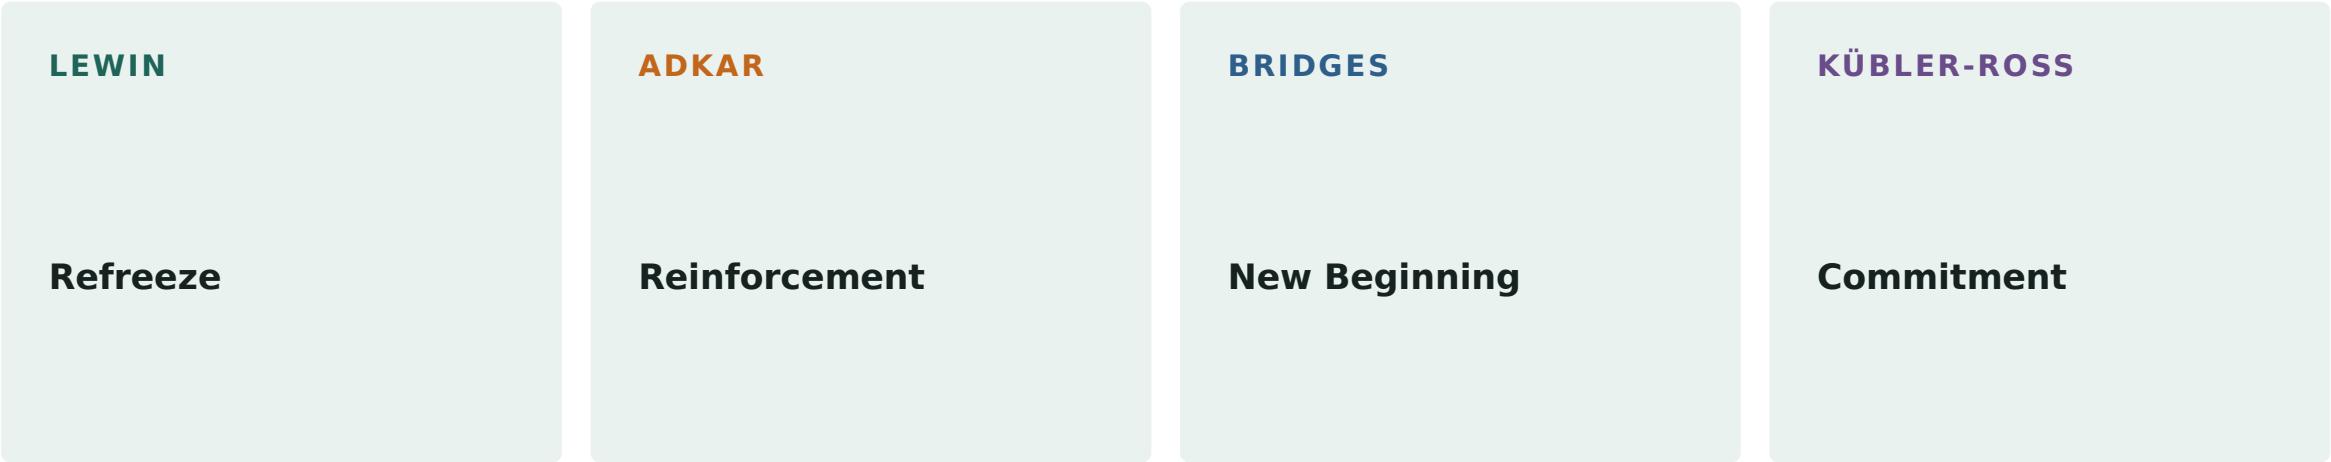

KEY TECHNIQUE THIS PHASE

Genuine capacity-backed handover: Ensure ongoing monitoring ownership actually transfers, not just the paperwork.

Every Phase, Across the Four Frameworks

Phase	Week(s)	Lewin	ADKAR	Bridges	Kübler-Ross
Automation-Opportunity Assessment	Weeks 1-4	Unfreeze	Awareness	Exploration	Commitment
Architecture Design	Weeks 4-9	Unfreeze	Knowledge	Exploration	Commitment
Build	Weeks 9-12	Change	Knowledge	Exploration	Commitment
UAT & Shadow-Mode	Weeks 12-14	Change	Knowledge → Ability	Exploration	Commitment
Production Go-Live	Weeks 14-16	Change	Ability	New Beginning	Commitment
Exception Tuning	Weeks 16-18	Change → Refreeze	Ability → Reinforcement	New Beginning	Commitment
CoE Handover	Weeks 18-19	Refreeze	Reinforcement	New Beginning	Commitment

Every Phase, Techniques and Tools

Phase	Week(s)	Technique	Goal	Tool
Automation-Opportunity Assessment	Weeks 1-4	Exception-rate sampling	Confirm the task is genuinely low-judgment before committing design effort.	M21 (Field Notes)
Architecture Design	Weeks 4-9	Bot architecture design against real system constraints	Design against actual platform/licensing limits, not assumed ones.	M17 (WBS & Gantt)
Build	Weeks 9-12	Iterative build against the matching logic	Build the bot's core matching logic and exception-handling rules together.	M21 (Field Notes)
UAT & Shadow-Mode	Weeks 12-14	Two-week parallel shadow-mode run	Validate the bot against real production data with a real fallback still active.	M9 (Training)
Production Go-Live	Weeks 14-16	Direct production cutover	Cut over once shadow-mode has already proven the bot clean.	M3 (Initiative Registry)
Exception Tuning	Weeks 16-18	Real-volume exception review	Tune rules against real production volume, which always differs from the test sample.	M14 (Analytics)
CoE Handover	Weeks 18-19	Genuine capacity-backed handover	Ensure ongoing monitoring ownership actually transfers, not just the paperwork.	M12 (Sustainment)

PART 4 — SIX EXCEPTIONS, IN DETAIL

Six Realistic Contingencies — None of Which Actually Occurred

Hidden Exception Volume Underestimated

DESCRIPTION

The Phase 1 suitability assessment concludes the task is low-exception; internal testing then reveals a meaningfully higher real exception rate, because the historical sample under-represented a seasonal invoice pattern.

TRIGGER

Internal test exception rate exceeds the threshold set during architecture design.

TIMELINE IMPACT

Would delay the Build gate by one to two weeks, and push shadow-mode from two weeks to three.

RECOVERY TASKS

Redesign exception-handling rules for the newly discovered seasonal pattern before declaring Build complete.

OUTPUTS: An expanded exception-handling rule set; a validated seasonal-pattern test case. **RACSI:** R = PM, ITL · A = CM · C = FPO · S = ES · I = SUP, EU

Shadow-Mode Discrepancy Traced to a Data Quality Issue, Not the Bot

DESCRIPTION

A shadow-mode discrepancy initially looks like a bot logic error; investigation instead finds the discrepancy traces to inconsistent supplier-name formatting in the source system — a data-quality issue the bot correctly flagged.

TRIGGER

A shadow-mode discrepancy rate above the expected noise floor.

TIMELINE IMPACT

No phase-gate delay if resolved within shadow-mode's existing window.

RECOVERY TASKS

Investigate the discrepancy's true source before assuming bot error; correct the upstream data-quality issue.

OUTPUTS: A confirmed root cause; an unmodified, already-correct bot. **RACSI:** R = ITL · A = CM · C = FPO · S = PM · I = ES, SUP

A Single Vocal Staff Member Resists Despite Overall Buy-In

DESCRIPTION

One of the 18 AP staff — often the person who has done the manual match longest — resists individually, even though the rest of the team and the Sponsor are genuinely supportive.

TRIGGER

A single resistance entry from one staff member, with no similar entries from the rest of the cohort.

TIMELINE IMPACT

None to the program timeline if handled directly and early.

RECOVERY TASKS

Address the individual concern directly and early, before it becomes a Phase 5 go-live morale issue.

OUTPUTS: A resolved individual concern; no broader team impact. **RACSI:** R = CM, FPO · A = CM · C = ES · S = SUP · I = PM, EU

IT Change-Freeze Delays Integration

DESCRIPTION

Bouregreg Group's IT function declares a change freeze — commonly tied to a fiscal period close — that blocks the bot's integration work during Build.

TRIGGER

An IT-declared change freeze overlapping Build's planned integration window.

TIMELINE IMPACT

A direct delay equal to the freeze's duration, typically one to three weeks, pushed straight through to UAT and go-live.

RECOVERY TASKS

Plan integration work around known freeze windows where possible; escalate for an exception where the freeze cannot be avoided.

OUTPUTS: A revised integration schedule; a documented freeze-driven delay. **RACSI:** R = PM, ITL · A = PM · C = CM · S = ES · I = FPO, SUP, EU

Platform Licensing or Technical Limitation Discovered Mid-Build

DESCRIPTION

The RPA platform's licensing terms or a technical limitation (a rate limit on the legacy system's API) is discovered mid-Build to constrain the bot's design in a way Architecture Design didn't anticipate.

TRIGGER

A platform constraint discovered during active development that the signed-off architecture didn't account for.

TIMELINE IMPACT

Reopens part of the Architecture Design gate, typically adding one to two weeks.

RECOVERY TASKS

Adjust the design within the newly discovered constraint rather than treat it as a blocking failure.

OUTPUTS: A revised architecture; a documented platform constraint for future automation projects. **RACSI:** R = ITL · A = PM · C = CM · S = FPO · I = ES, SUP, EU

Post-Go-Live Complacency: CoE Ownership Never Really Transfers

DESCRIPTION

The Center of Excellence handover happens on paper — the package delivered, sign-off toggled — but day-to-day monitoring quietly stays with Yassine Kabbaj rather than genuinely transferring, because the CoE was never given real capacity for it.

TRIGGER

A sustainment checkpoint (M12) shows the named CoE owner has logged no monitoring activity since handover.

TIMELINE IMPACT

No impact to this program's own 19-week timeline, since it manifests after formal close.

RECOVERY TASKS

A post-handover checkpoint specifically verifying logged monitoring activity, not just a signed handover document.

OUTPUTS: A verified, capacity-backed CoE handover; an early catch of any silent non-transfer. **RACSI:** R = FPO · A = ES · C = PM, ITL · S = CM · I = SUP, EU

What This Training Covers

Per the E2E-BPA chain, MP-05 is present but light-touch — this archetype's training focuses on operating alongside the bot and handling its flagged exceptions, not persuasion for an already-bought-in team.

Strategic Management

Cohort: Hakim Berrada (Sponsor) · Weeks 1-3

Curriculum Entry	Content Focus
Sponsoring a Low-Risk Automation Project	Why visible sponsorship still matters even when the team is already bought in.
Reading a Clean Program's Own Data	How to confirm a clean record honestly, without assuming it will simply continue.

Operational Management

Cohort: Nawal Fassi (FPO/SUP), Amine Sqalli (PM) · Weeks 3–6

Curriculum Entry	Content Focus
Operating the Bot's Exception Queue	Handling the specific invoice-matching exceptions the bot flags rather than auto-resolves.
Shadow-Mode Validation Procedure	How to compare bot output against the manual process during the two-week parallel run.

Operations (Frontline)

Cohort: All 18 Kenitra AP staff · Weeks 5-13

Curriculum Entry	Content Focus
Working Alongside the Automated Match	What changes and what stays the same in daily AP work once the bot is live.
Escalating a Flagged Exception	The specific steps for routing a bot-flagged invoice back to a human reviewer.

Why This Curriculum Is Shaped This Way

This program's training curriculum is deliberately the lightest in the series — proof that not every automation needs an elaborate change program when the scope is narrow and the team is already on board.

Which journi Modules Dominate This Archetype

M17 (WBS & Gantt)	The shortest phase template in the library — closed in as few as 18-19 weeks.
M5 (ADKAR Engine)	A light-touch score, since the team starts already bought in.
M7 (Sponsor & Coalition)	A visibly active Sponsor from day one — the opposite pattern of the Cultural case.
M21 (Field Notes)	Routine logging — this archetype's data is notable for how little it needs to escalate.
M14 (Analytics)	Confirms a rising, unremarkable CRI trend rather than tracking a recovery.
M12 (Sustainment)	The CoE handover checkpoint — the one place this clean program still needs real verification.

What This Case Proves By Not Firing

NO LIVE ALERT FIRES IN THIS PROGRAM'S REAL RECORD

Stated plainly, not manufactured — a clean record reported as a clean record.

WHY

None. Closed by design without any of journi's 9 live alerts firing — the clean-close contrast case that proves not every program needs a recovery playbook.

KEY TAKEAWAYS

What to Remember About This Archetype

- › A closed program with zero of journi's 9 live alerts fired, a real two-week shadow-mode validation before go-live, and six honestly-labeled hypothetical contingencies showing exactly how this program could have gone differently, had the conditions been less favorable.
- › All four frameworks read favorably from the start, by design. This is journi's deliberate contrast case: a narrow scope, an already-bought-in team, and a visibly active Sponsor mean no framework carries unusual risk — the point being that not every program needs a recovery playbook.
- › None. Closed by design without any of journi's 9 live alerts firing — the clean-close contrast case that proves not every program needs a recovery playbook.



Business Process Automation

Kenitra Invoice-Matching Automation
