



Business Process Redesign

Order-to-Cash Process Redesign

Redesigning a process independent of any system change — where staff who privately own today's workarounds resist a redesign that makes those workarounds obsolete.

7

PHASES

50

WEEKS

6

EXCEPTIONS

3

TRAINING TIERS

PART 0 — PURPOSE

What This Guide Is, and How to Use It

WHAT THIS GUIDE IS

This deck follows the Order-to-Cash Process Redesign — journi's BPR archetype case — from tenant setup through sustainment handoff, showing exactly how a process-only redesign (no system change) is run inside journi, week by week.

HOW TO USE IT

This program runs inside the same Bouregreg Group tenant as every other archetype in this series. A reader with the tenant already set up skips straight to CM Project creation.

Verified Against journi's Real Source

Every journi module, field, and role named here is verified against journi's real source. Order-to-Cash is journi's own stated case for ALT-004 (Resistance Escalation Threshold Breached) — this deck shows exactly how that alert fires and is resolved through co-design, not suppression.

RACSI CODES USED THROUGHOUT

ES = Executive Sponsor · CM = Change Manager · PM = Program/Project Manager · FPO = Functional Process Owner · ITL = IT/Technical Lead · SUP = Supervisor · EU = End User

Why This Case Matters

Finance staff who built and privately own today's manual workarounds resist a redesign that makes those workarounds obsolete — by design, more than any specific skill gap, resistance (Kübler-Ross) is this archetype's central and defining risk.

The Case, in Brief

140 staff, Casablanca finance (AR and AP)

50 weeks (guide numbering)

Casablanca HQ's finance function has run order-to-cash manually since before the ERP program began; this 50-week project redesigns the process itself, independent of any system change, targeting a three-week month-end reconciliation problem self-inflicted by process design, not tooling.

What This Guide Proves, Concretely

A real ALT-004 firing at Week 20-24, resolved through a co-designed accuracy safeguard the resisting staff themselves helped define — and five further exceptions showing exactly how a redesign can go sideways even after the headline resistance risk is handled.

Weighting for This Archetype

Kübler-Ross dominates. Staff who privately own today's workarounds resist a redesign that makes those workarounds obsolete — the Resistance/Anger stage, and the Resistance Log (M10) that feeds it, is this archetype's central risk, more than any specific skill gap ADKAR would otherwise catch first.

The Composite Readiness Index, Read for This Case

The Composite Readiness Index dips visibly during the Pilot phase as the three resistance entries accumulate, then recovers once the co-designed safeguard lands — a real, not cosmetic, trough-and-recovery pattern worth reading as designed evidence, not noise.

The Existing Tenant, and Reading Paths by Role

THE EXISTING TENANT

This program runs inside the same tenant journi's Master User Guide builds, under the existing Bouregreg Manufacturing Maroc Organization — no new Organization needed.

READING PATHS, BY ROLE

- › A Change Manager running this program day to day: Part 2 once, then Part 4 in full.
- › A Program/Project Manager: Part 4's PM Track column and the Master WBS & Gantt.
- › An Executive Sponsor: Part 1, then Part 4's phase-opening narratives.
- › A Super Admin or Org Admin: Part 3.

The RACSI Team for This Program

Name	RACSI Code	Role
Karim Zniber	ES	Sponsor — VP Finance
Imane Berrada	CM	Change Manager
Othmane Rifai	PM	Program Manager
Salwa Tazi	FPO	Casablanca Finance Process Owner
Karim Alami	ITL	IT/Technical Lead
Amina Sebti	SUP	Supervisor

Creating the CM Project

- 1** On Module 1 — Hierarchy, create the Order-to-Cash Process Redesign CM Project under the existing Bouregreg Manufacturing Maroc Organization — no new tenant needed.
- 2** Set Change type: Business Process Redesign. Target population: "Casablanca finance (AR and AP), 140 staff." Business driver: "Three weeks of month-end reconciliation work, self-inflicted by process design."
- 3** Save. Lewin opens at Unfreeze, run alongside the ERP program's own Discovery.
- 4** On Module 17 — WBS & Gantt, load the TPL-BPR-7 phase template: Intake & Diagnosis, Clean-Slate Design, Build, Pilot, Rollout, Stabilization, Sustainment.

Charters for This Program

Charter	Accountable	Review Cadence
CHTR-01 Sponsorship / Leadership Charter	Karim Zniber (ES)	Per Phase Gate
CHTR-04 Organizational Impact Charter	Imane Berrada (CM)	On scope change
CHTR-08 Pulse / Interview Charter	Imane Berrada (CM)	Per phase gate + ad hoc

Setup Checklist

- ☒ Base tenant confirmed (Bouregreg Group, existing Organization)
- ☒ BPR program team accounts created
- ☒ CM Project created, Lewin opened at Unfreeze
- ☒ TPL-BPR-7 phase template loaded on M17
- ☒ Applicable Charters reviewed and accountable owners confirmed

PART 4 — WEEK-BY-WEEK TIMELINE

7 Phases, In Order



Total program length: 50 weeks (guide numbering). Every phase below is walked in detail across the next slides — normal flow first, then six exceptions in full operational detail.

Intake & Diagnosis

Weeks 1-7

NARRATIVE


Characterizes exactly where the three-week reconciliation problem comes from, process step by process step — before any redesign is proposed.

PHASE 1 · INTAKE & DIAGNOSIS

Key Moments in This Phase

Week	What Happens
Week 1	Kickoff; Lewin opens at Unfreeze, run alongside the ERP program's own Discovery.
Week 5	Process-step diagnosis identifies the specific manual workarounds driving the delay.
Week 7	Diagnosis gate closes.

Framework Snapshot

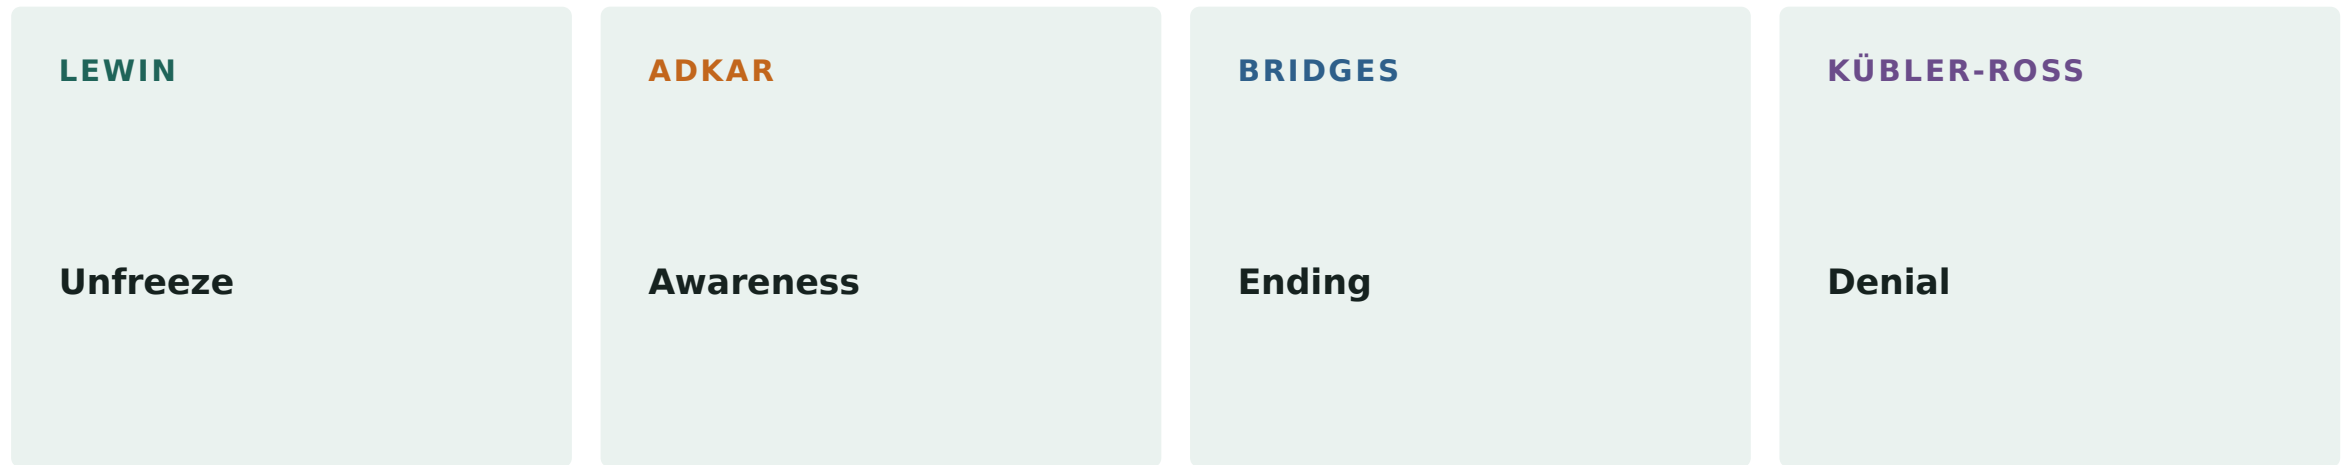

KEY TECHNIQUE THIS PHASE

Process-step root-cause mapping: Trace the three-week delay to specific manual workarounds, by step.

Clean-Slate Design

Weeks 5-8


NARRATIVE

Designs the redesigned process without being anchored to today's workaround-shaped version of it.

Key Moments in This Phase

Week	What Happens
Week 6	Clean-slate design workshop, deliberately excluding today's workaround logic.
Week 8	Clean-slate design signed off by the Steering Committee.

Framework Snapshot

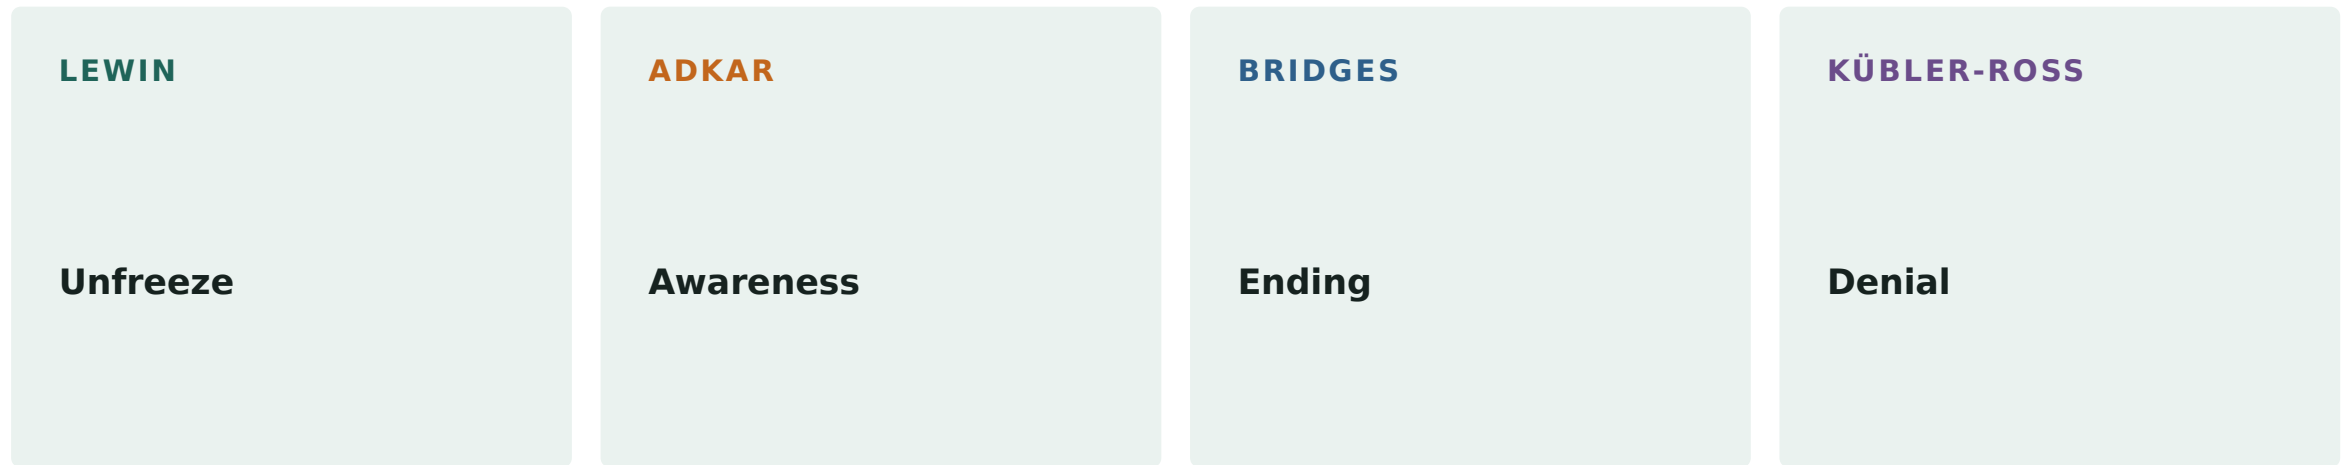

KEY TECHNIQUE THIS PHASE

Clean-slate workshop: Design the new process without anchoring to today's workaround-shaped version.

Build

Weeks 8-16


NARRATIVE

Builds the redesigned process's specific steps, forms, and approval chain — this is where Exception E4's legacy-system constraint surfaces.

Key Moments in This Phase

Week	What Happens
Week 10	A legacy system constraint blocks a required data field — Exception E4 opens.
Week 13	A bounded workaround validated and configured.
Week 16	Build gate closes.

Framework Snapshot

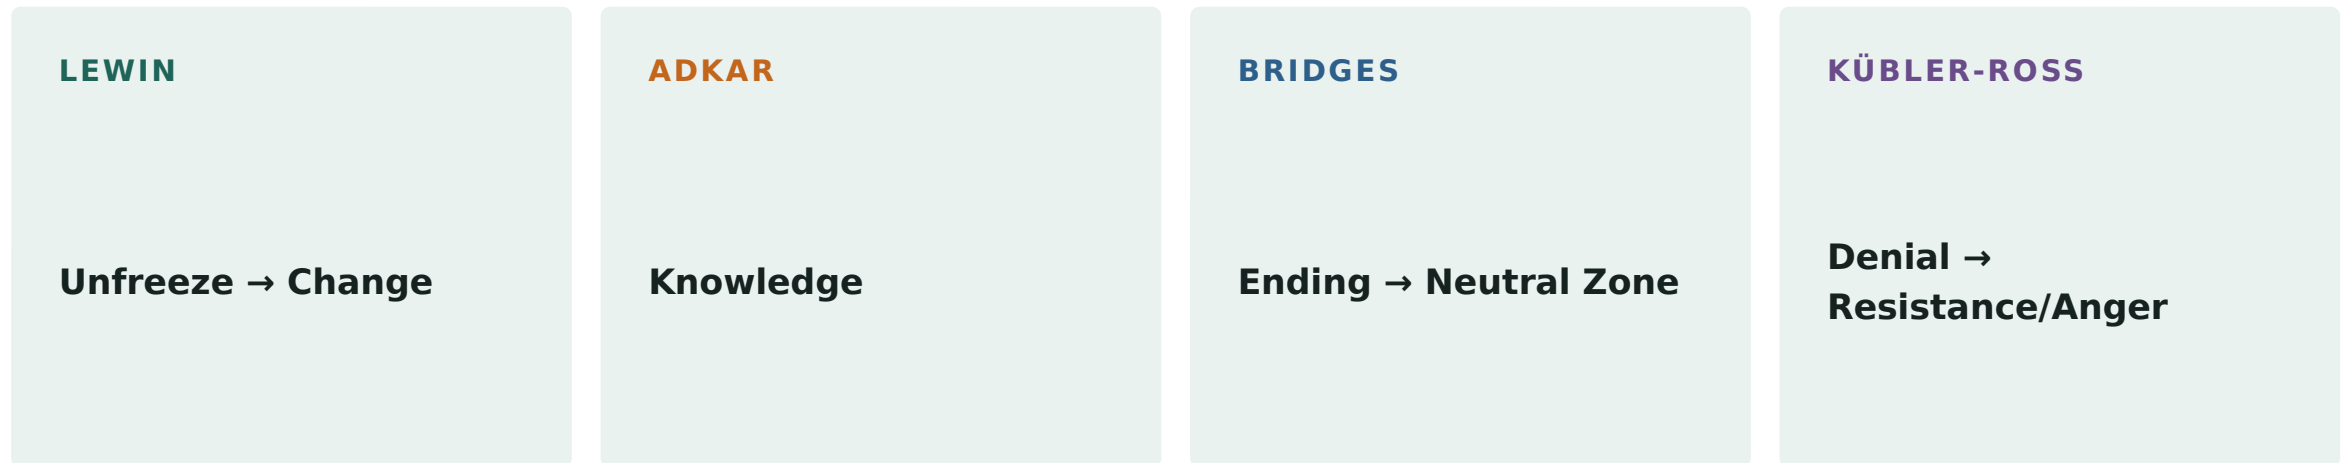

KEY TECHNIQUE THIS PHASE

Bounded technical workaround design: Solve a legacy-system constraint without touching the legacy system directly.

Pilot

Weeks 14-24

NARRATIVE

Pilots the redesigned process on a single process step — the phase this archetype is built to cross the resistance-escalation threshold in.

Key Moments in This Phase

Week	What Happens
Week 20	First resistance entry logged by an AR staff member defending removed manual-control expertise.
Week 24	Third resistance entry lands, firing ALT-004 — Exception E1 opens and resolves within the same week.

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Co-designed accuracy safeguard: Resolve resistance by building the mitigation with the resisting staff, not around them.

Rollout

Weeks 22-32


NARRATIVE

Rolls the redesigned process out organization-wide across AR and AP — where an informal, untracked resistance pattern (Exception E2) can hide.

Key Moments in This Phase

Week	What Happens
Week 26	Adoption metrics lag in a sub-team with no open resistance entries — Exception E2 opens.
Week 28	The co-designed safeguard, tested only against AR's volume, reaches AP — Exception E3 opens.
Week 32	Rollout gate closes.

Framework Snapshot

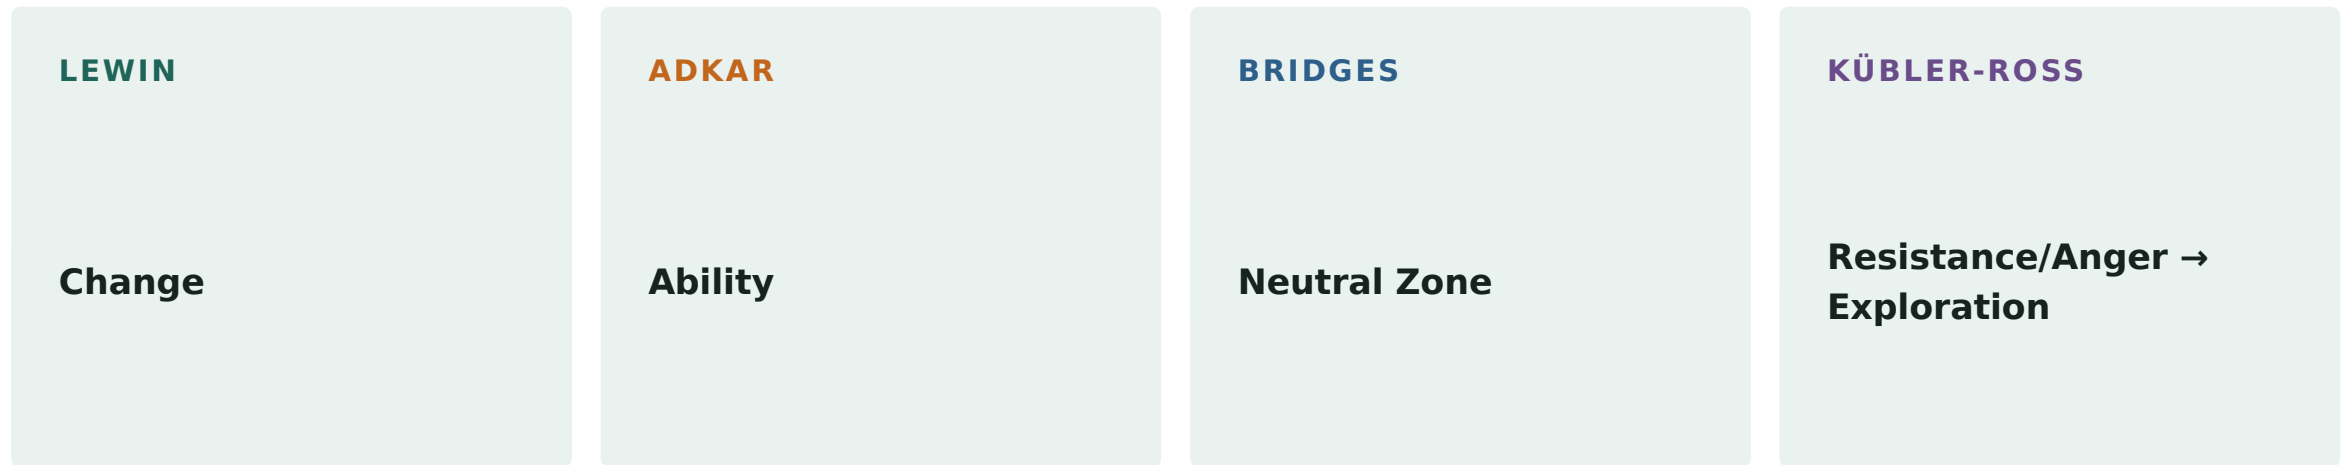

KEY TECHNIQUE THIS PHASE

Adoption-vs-resistance-log cross-check: Catch an informal resistance pattern that never becomes a formal log entry.

Stabilization

Weeks 30-42

NARRATIVE


Confirms the redesigned process holds under real monthly volume — and whether the reconciliation-time target is actually being met.

PHASE 6 · STABILIZATION

Key Moments in This Phase

Week	What Happens
Week 34	Reconciliation time reads two weeks, not the targeted one week — Exception E5 opens.
Week 38	Root-cause disaggregation traces the shortfall to E3's AP-specific safeguard cost.
Week 42	Stabilization gate closes.

Framework Snapshot

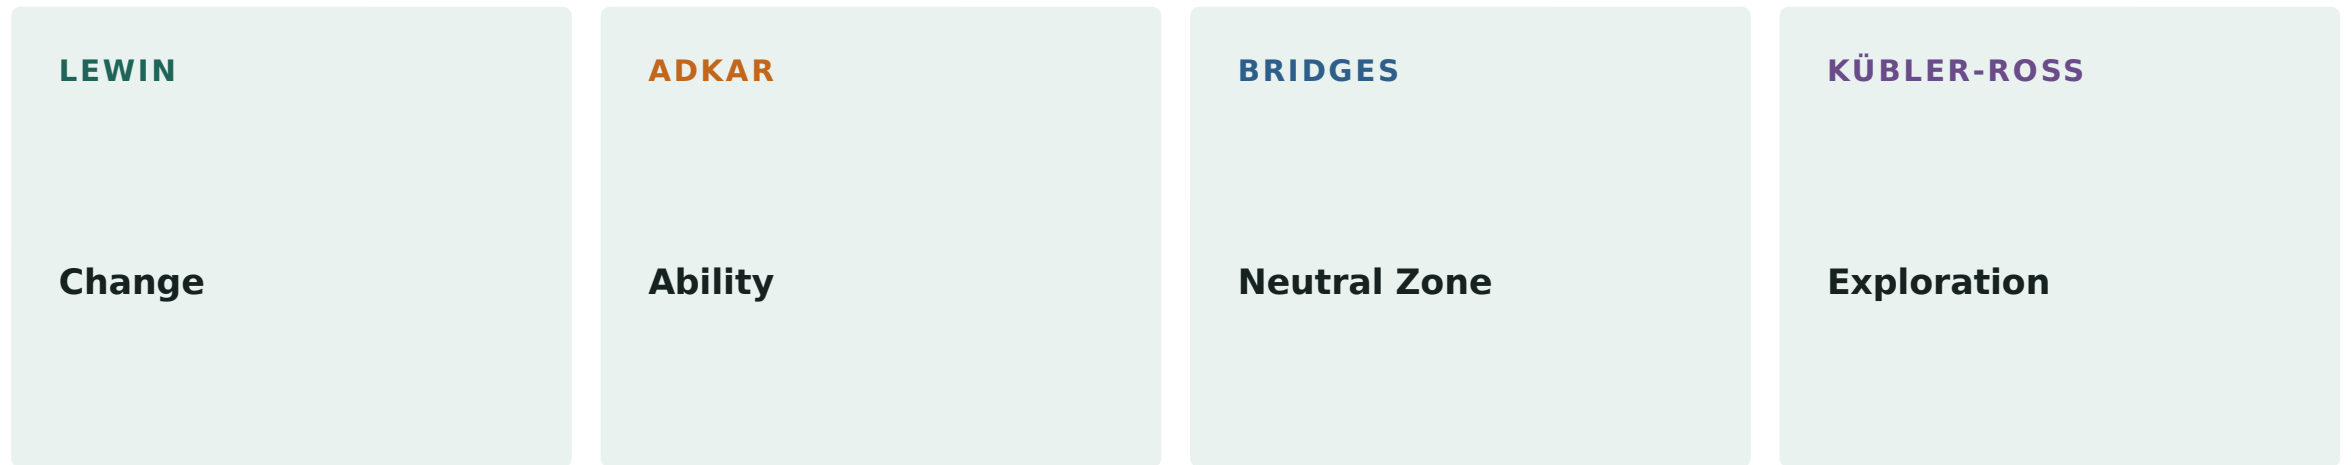

KEY TECHNIQUE THIS PHASE

Reconciliation-time root-cause disaggregation: Separate a real partial shortfall from a hidden, addressable cause.

Sustainment

Weeks 40-50


NARRATIVE

Hands the redesigned process off to standing operations — complicated by the Process Owner's own mid-rollout departure.

Key Moments in This Phase

Week	What Happens
Week 26	Salwa Tazi's departure notice triggers Exception E6's structured handover.
Week 44	A successor Process Owner fully onboarded and RACSI-updated.
Week 50	Sustainment handoff complete; program closes.

Framework Snapshot

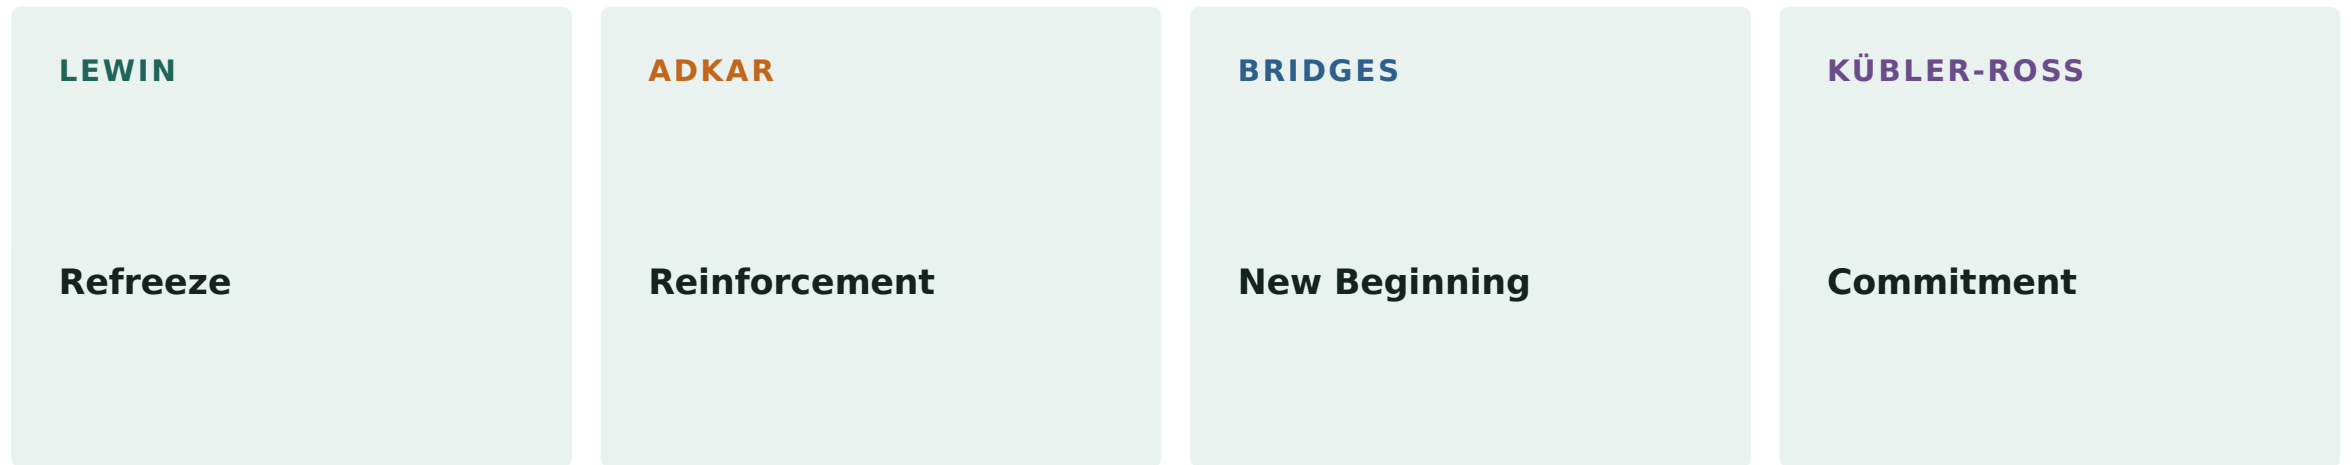

KEY TECHNIQUE THIS PHASE

Decision-rationale handover: Preserve the *why* behind key design decisions, not just the *what*, through a leadership transition.

Every Phase, Across the Four Frameworks

Phase	Week(s)	Lewin	ADKAR	Bridges	Kübler-Ross
Intake & Diagnosis	Weeks 1-7	Unfreeze	Awareness	Ending	Denial
Clean-Slate Design	Weeks 5-8	Unfreeze	Awareness	Ending	Denial
Build	Weeks 8-16	Unfreeze → Change	Knowledge	Ending → Neutral Zone	Denial → Resistance/Anger
Pilot	Weeks 14-24	Change	Knowledge → Ability	Neutral Zone	Resistance/Anger
Rollout	Weeks 22-32	Change	Ability	Neutral Zone	Resistance/Anger → Exploration
Stabilization	Weeks 30-42	Change	Ability	Neutral Zone	Exploration
Sustainment	Weeks 40-50	Refreeze	Reinforcement	New Beginning	Commitment

Every Phase, Techniques and Tools

Phase	Week(s)	Technique	Goal	Tool
Intake & Diagnosis	Weeks 1–7	Process-step root-cause mapping	Trace the three-week delay to specific manual workarounds, by step.	M4 (Stakeholder Mapping)
Clean-Slate Design	Weeks 5–8	Clean-slate workshop	Design the new process without anchoring to today's workaround-shaped version.	M17 (WBS & Gantt)
Build	Weeks 8–16	Bounded technical workaround design	Solve a legacy-system constraint without touching the legacy system directly.	M21 (Field Notes)
Pilot	Weeks 14–24	Co-designed accuracy safeguard	Resolve resistance by building the mitigation with the resisting staff, not around them.	M10 (Resistance Log)
Rollout	Weeks 22–32	Adoption-vs-resistance-log cross-check	Catch an informal resistance pattern that never becomes a formal log entry.	M5 (ADKAR Engine)
Stabilization	Weeks 30–42	Reconciliation-time root-cause disaggregation	Separate a real partial shortfall from a hidden, addressable cause.	M14 (Analytics)
Sustainment	Weeks 40–50	Decision-rationale handover	Preserve the *why* behind key design decisions, not just the *what*, through a leadership transition.	M21 (Field Notes)

PART 4 — SIX EXCEPTIONS, IN DETAIL

Six Realistic Ways This Program Could Have Gone Differently

Resistance Escalation Threshold Breached

DESCRIPTION

Three AR staff, each defending the manual-control expertise the redesigned process removes, logged individually-coded resistance entries within a three-week window — ALT-004's exact condition.

TRIGGER

Three or more open resistance entries accumulated within journi's rolling window.

OUTPUTS: Three closed resistance entries; a co-designed accuracy safeguard folded into the standing rollout design. **RACSI:** R = CM · A = CM · C = FPO, SUP · S = PM · I = ES, EU

TIMELINE IMPACT

No Phase 4 gate delay — resolved within the same phase by Week 24.

RECOVERY TASKS

Direct, individual conversations with each of the three staff; a secondary accuracy-review safeguard co-designed with them, not imposed on them.

A Workaround Champion Undermines the Process Informally

DESCRIPTION

A senior AR staff member who never logged a formal resistance entry quietly tells colleagues to keep a personal shadow spreadsheet "just in case," undermining adoption without ever surfacing as a trackable entry.

TRIGGER

Adoption metrics (M5 Ability) lag in a sub-team despite no open resistance entries there.

OUTPUTS: A newly logged, then closed, resistance entry; a standing practice of cross-checking adoption metrics against the resistance log. **RACSI:** R = CM, SUP · A = CM · C = FPO · S = PM · I = ES, EU

TIMELINE IMPACT

Roughly one week added to that sub-team's rollout confirmation.

RECOVERY TASKS

Investigate the adoption lag directly; identify the informal influence through conversation; convert the informal pattern into a formal, resolvable one.

The Co-Designed Safeguard Slows AP More Than Expected

DESCRIPTION

The safeguard co-designed with AR's resisting staff was tested only against AR's volume; rolled out to AP's significantly higher volume, it adds more processing time than the redesign was meant to save.

TRIGGER

Reconciliation-time monitoring (M14) trends against the business case's own target, not toward it.

OUTPUTS: An AP-specific safeguard threshold; a documented reason the AR-tested design didn't generalize. **RACSI:** R = PM, FPO · A = CM · C = SUP · S = ITL · I = ES, EU

TIMELINE IMPACT

Extends Stabilization by two to three weeks while the safeguard is re-tuned for AP.

RECOVERY TASKS

Confirm the cost specifically in AP; redesign the trigger threshold for AP's volume rather than removing the safeguard; re-test before declaring Stabilization complete.

A Legacy System Constraint Blocks a Required Data Field

DESCRIPTION

The redesigned process requires a new data field (a credit-note reason code) the legacy finance system, still in use pending the separate ERP program's own migration, does not natively support.

TRIGGER

A build-phase technical constraint discovered when the new field's configuration is attempted.

TIMELINE IMPACT

Adds one to two weeks to Build while a bounded workaround is designed and validated.

RECOVERY TASKS

Confirm the constraint is real; design a bounded workaround that doesn't require touching the legacy system; validate it doesn't reintroduce a manual step.

OUTPUTS: A documented constraint and its bounded workaround. **RACSI:** R = ITL, PM · A = PM · C = CM · S = FPO · I = ES, SUP, EU

Reconciliation-Time Reduction Stalls Below Target

DESCRIPTION

The business case targeted a reduction from three weeks to one; Stabilization's readings hold at two weeks — real progress, but short of target.

TRIGGER

Two consecutive monthly readings below the business-case target, without further improving trend.

TIMELINE IMPACT

Extends Stabilization by one monitoring cycle rather than close the gate on a partial result presented as full success.

RECOVERY TASKS

Disaggregate the remaining gap by root cause (largely E3's AP safeguard cost); decide explicitly whether to invest further or revise the target, documented either way.

OUTPUTS: A disaggregated root-cause finding; either a closed gap or an explicitly revised target. **RACSI:** R = CM, FPO · A = ES · C = PM · S = ITL · I = SUP, EU

The Process Owner Departs Mid-Rollout

DESCRIPTION

Salwa Tazi, the Casablanca Finance Process Owner and the person who did the most direct co-design work with the pilot's resisting staff, accepts a role elsewhere mid-rollout.

TRIGGER

A confirmed departure notice from the named Functional Process Owner during an active phase.

OUTPUTS: A documented decision-rationale handover; a successor Process Owner onboarded and RACSI-updated. **RACSI:** R = CM, FPO · A = ES · C = PM · S = SUP · I = ITL, EU

TIMELINE IMPACT

Adds roughly two weeks to Rollout for a structured handover before departure.

RECOVERY TASKS

A structured handover capturing the *why* behind key design decisions; identify and onboard a successor before the departure, not after.

What This Training Covers

Per the E2E-BPR chain, MP-05 is present — training here focuses on the redesigned process's specific new steps, not persuasion about why the redesign is needed (Kübler-Ross's Resistance/Anger stage, not Awareness, is this archetype's real barrier).

Strategic Management

Cohort: Karim Zniber (Sponsor), finance leadership · Weeks 1-4

Curriculum Entry	Content Focus
Sponsoring a Process Redesign Against Owned Workarounds	Why visible sponsorship matters most exactly when staff privately own what's being removed.
Reading a Resistance Log as Real Evidence	How to read three open entries as the system working, not failing.

Operational Management

Cohort: Salwa Tazi (FPO), Amina Sebti (SUP) · Weeks 4-14

Curriculum Entry	Content Focus
Operating the Redesigned Order-to-Cash Process	The specific new steps, forms, and approval chain, replacing the old workaround-shaped version.
Co-Designing a Recovery With Resisting Staff	The specific technique behind Exception E1's resolution.

Operations (Frontline)

Cohort: All 140 AR and AP staff · Weeks 12-28

Curriculum Entry	Content Focus
Using the New Process, Step by Step	Practical training on the redesigned process, delivered ahead of each rollout wave.
The New Accuracy Safeguard, By Volume	AR-specific and later AP-specific versions of the same safeguard.

Why This Curriculum Is Shaped This Way

Training completion here is necessary but not sufficient — Exception E2 shows a fully trained cohort can still undermine adoption informally, which is why the resistance log, not the training-completion rate, is this archetype's real leading indicator.

Which journi Modules Dominate This Archetype

M10 (Resistance Log)	The archetype's most-watched module — 3+ open entries fires ALT-004.
M4 (Stakeholder Mapping)	Identifies exactly whose workaround is being redesigned away, by name.
M17 (WBS & Gantt)	The TPL-BPR-7 template — Clean-Slate Design is this archetype's defining phase.
M21 (Field Notes)	Captures the specific, named fear or rationale behind a resistance entry or handover.
M14 (Analytics)	Reconciliation-time trend monitoring against the business case's own target.
M5 (ADKAR Engine)	Cross-checked against the resistance log to catch informal, untracked resistance.

What This Case Fires

ALERTS THIS CASE EXERCISES

ALT-004 (Resistance Escalation Threshold Breached)

WHY

Built deliberately to cross the resistance-escalation threshold — the defining alert of this archetype.

KEY TAKEAWAYS

What to Remember About This Archetype

- › A real ALT-004 firing at Week 20-24, resolved through a co-designed accuracy safeguard the resisting staff themselves helped define — and five further exceptions showing exactly how a redesign can go sideways even after the headline resistance risk is handled.
- › Kübler-Ross dominates. Staff who privately own today's workarounds resist a redesign that makes those workarounds obsolete — the Resistance/Anger stage, and the Resistance Log (M10) that feeds it, is this archetype's central risk, more than any specific skill gap ADKAR would otherwise catch first.
- › Built deliberately to cross the resistance-escalation threshold — the defining alert of this archetype.



Business Process Redesign

Order-to-Cash Process Redesign
