



ERP Implementation

Bouregreg ERP Adoption Program

A full system cutover across every site at once — the throughline case where all four frameworks matter equally, all the time.

8

PHASES

64

WEEKS

6

EXCEPTIONS

3

TRAINING TIERS

PART 0 — PURPOSE

What This Guide Is, and How to Use It

WHAT THIS GUIDE IS

This deck follows the Bouregreg ERP Adoption Program — journi's own throughline case — from tenant setup through Sustain, showing exactly how a full, vendor-agnostic ERP cutover is run inside journi, week by week, module by module.

HOW TO USE IT

The tenant this deck builds is the same one every other archetype guide in this series extends. A reader who already has the tenant set up can skip straight to the Setup section's CM Project creation step.

Verified Against journi's Real Source

Every journi module, field, and role named here is verified against journi's real source and its own Master User Guide. This is the case most likely to exercise ALT-001 (Divergence Pattern Detected) at UAT and ALT-009 (Phase Gate No-Go/Conditional) at any gate — this deck states plainly which of the two actually fires in the real record, rather than imply both.

RACSI CODES USED THROUGHOUT

ES = Executive Sponsor · CM = Change Manager · PM = Program/Project Manager · FPO = Functional Process Owner · ITL = IT/Technical Lead · SUP = Supervisor · EU = End User

Why This Case Matters

Every other archetype in this series can treat one or two frameworks as dominant. ERP cannot: a full cutover needs organizational readiness (Lewin) and individual capability (ADKAR) at the same time, everywhere, for the program's entire 64-week life — the only archetype where that is true throughout, not just at one phase.

The Case, in Brief

3,400 staff, all sites (Casablanca, Kenitra, Settat)

64 weeks (org calendar W1-64)

Bouregreg Group replaces fragmented, manual, and legacy tooling with one integrated system of record across Order Management, Inventory, and Finance, across all three sites, over 64 weeks — the tenant's own founding program, opened at Unfreeze from Week 1.

What This Guide Proves, Concretely

A real Divergence Pattern catch before go-live (Casablanca, Week 28), a real cross-site Composite Readiness Index disaggregation (Exception E6), and a Refreeze called only once Sustain's own 90-day checkpoint evidence supports it — not the go-live date.

Weighting for This Archetype

ADKAR and Lewin dominate equally, throughout. A system cutover needs organizational readiness (Lewin's Change → Refreeze) and individual capability (ADKAR's Knowledge/Ability) at the same time — neither alone is sufficient, and unlike every other archetype in this series, that is true across all 8 phases, not concentrated in one.

The Composite Readiness Index, Read for This Case

The Composite Readiness Index reads a genuinely different story at each site by mid-Train — Casablanca ahead on Knowledge/Ability given proximity to the program team, Settat behind following a Desire stall, Kenitra solid until a later sentiment regression — exactly the blended-vs-disaggregated tension Exception E6 exists to resolve.

The Existing Tenant, and Reading Paths by Role

THE EXISTING TENANT

This program runs inside the same tenant journi's Master User Guide builds, under the existing Bouregreg Manufacturing Maroc Organization — no new Organization needed.

READING PATHS, BY ROLE

- › A Change Manager running this program day to day: Part 2 once, then Part 4 in full.
- › A Program/Project Manager: Part 4's PM Track column and the Master WBS & Gantt.
- › An Executive Sponsor: Part 1, then Part 4's phase-opening narratives.
- › A Super Admin or Org Admin: Part 3.

The RACSI Team for This Program

Name	RACSI Code	Role
CFO, Bouregreg Group	ES	Sponsor
Driss El Amrani	CM	Change Manager — owns day-to-day program execution
Ghita Bennis	PM	Practitioner / Contributor — PM-track coordination, WBS & Gantt (M17)
Houda Zerouali	FPO	People Manager
Meryem Sabri	Org Admin	Organization-level setup and cross-site CRI disaggregation
Reda Loukili	EU	Employee

Creating the CM Project

- 1 On Module 2 — Users & Roles, seed Bouregreg Group's initial team: Super Admin, Group Admin, Org Admin, then the project-scoped Change Manager, People Manager, Sponsor, Employee, and Practitioner accounts.
- 2 On Module 1 — Hierarchy, create the Bouregreg ERP Adoption Program CM Project, owned by Driss El Amrani, with all 3,400 staff across three sites as target population.
- 3 Save. Lewin opens at Unfreeze — the tenant's founding framework reading, justified against the board-approved business case.
- 4 On Module 17 — WBS & Gantt, load the TPL-ERP-8 phase template: Discovery, Design, Build, Test, Train, Deploy, Hypercare, Sustain.

Charters for This Program


Charter	Accountable	Review Cadence
CHTR-01 Sponsorship / Leadership Charter	CFO, Bouregreg Group (ES)	Per Phase Gate
CHTR-02 Participative Management Charter	Frontline Supervisor role	Per champion briefing
CHTR-05 Team Coaching Charter	People Manager role	At Hypercare sentiment recovery
CHTR-06 One-to-One Coaching Charter	Driss El Amrani (CM)	At Divergence Pattern resolution
CHTR-08 Pulse / Interview Charter	Driss El Amrani (CM)	Per phase gate + ad hoc

Setup Checklist

- ☒ Base tenant confirmed (Bouregreg Group, Bouregreg Manufacturing Maroc Organization)
- ☒ ERP program team accounts created across all RBAC scopes
- ☒ CM Project created, Lewin opened at Unfreeze
- ☒ TPL-ERP-8 phase template loaded on M17
- ☒ Applicable Charters reviewed and accountable owners confirmed

PART 4 — WEEK-BY-WEEK TIMELINE

8 Phases, In Order

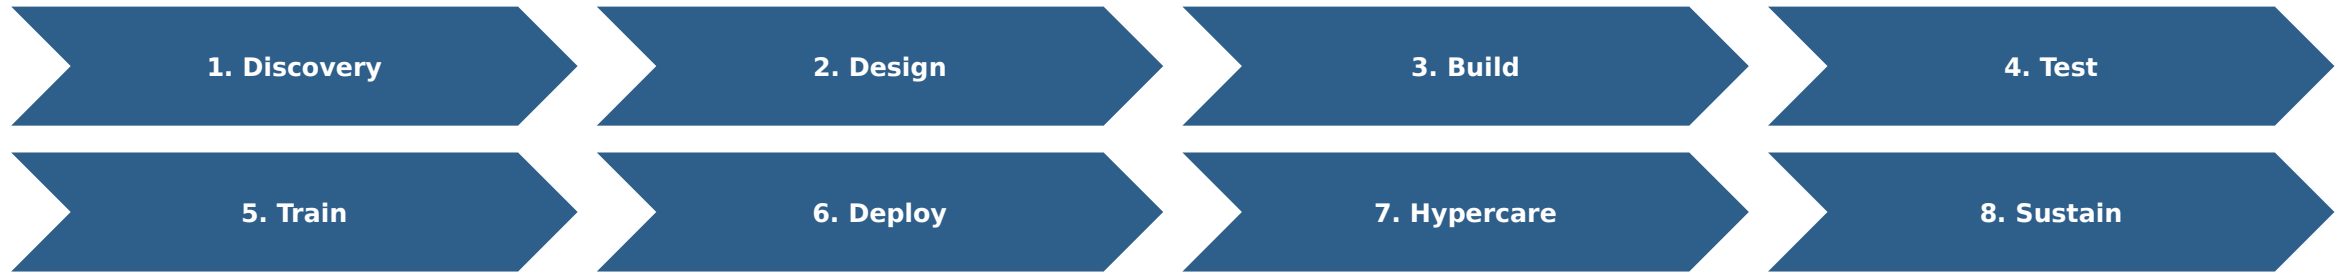

Total program length: 64 weeks (org calendar W1-64). Every phase below is walked in detail across the next slides — normal flow first, then six exceptions in full operational detail.

Discovery

Weeks 1-8

NARRATIVE


Establishes the current-state process map across Order Management, Inventory, and Finance, and confirms the business case driving the cutover.

PHASE 1 · DISCOVERY

Key Moments in This Phase

Week	What Happens
Week 1	Kickoff; Lewin opens at Unfreeze.
Week 5	Current-state process mapping across all three sites.
Week 8	Discovery gate closes; future-state scope confirmed.

Framework Snapshot

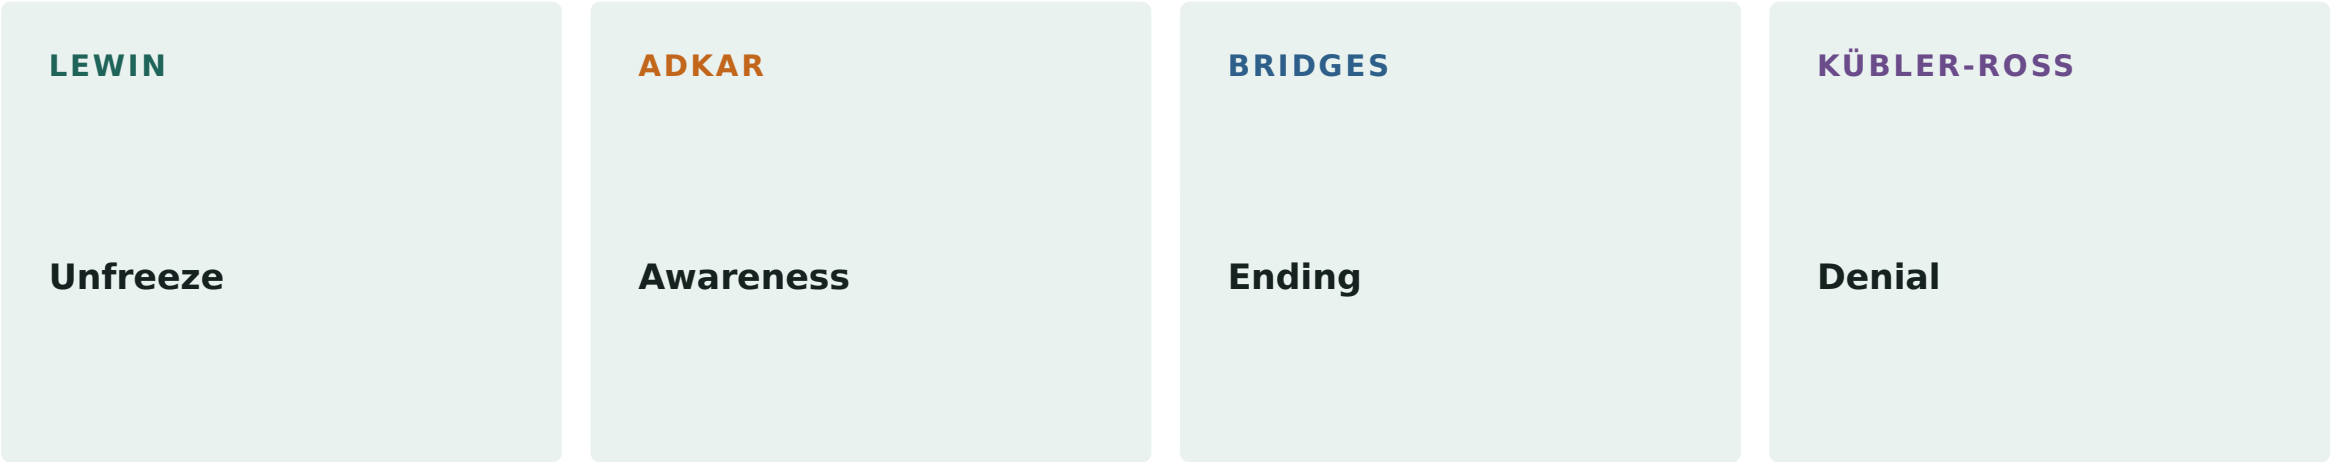

KEY TECHNIQUE THIS PHASE

Current-state process mapping: Establish exactly what today's manual/legacy process actually does, by site.

Design

Weeks 6–17

NARRATIVE


Signs off the future-state design principles the whole build will configure against — starting before Discovery formally closes, since PM and CM tracks run in parallel.

Key Moments in This Phase

Week	What Happens
Week 9	First town hall; first real Awareness scores land, Settat lowest.
Week 13	Design scope signed off by the Steering Committee.
Week 17	Design gate closes.

PHASE 2 · DESIGN

Framework Snapshot

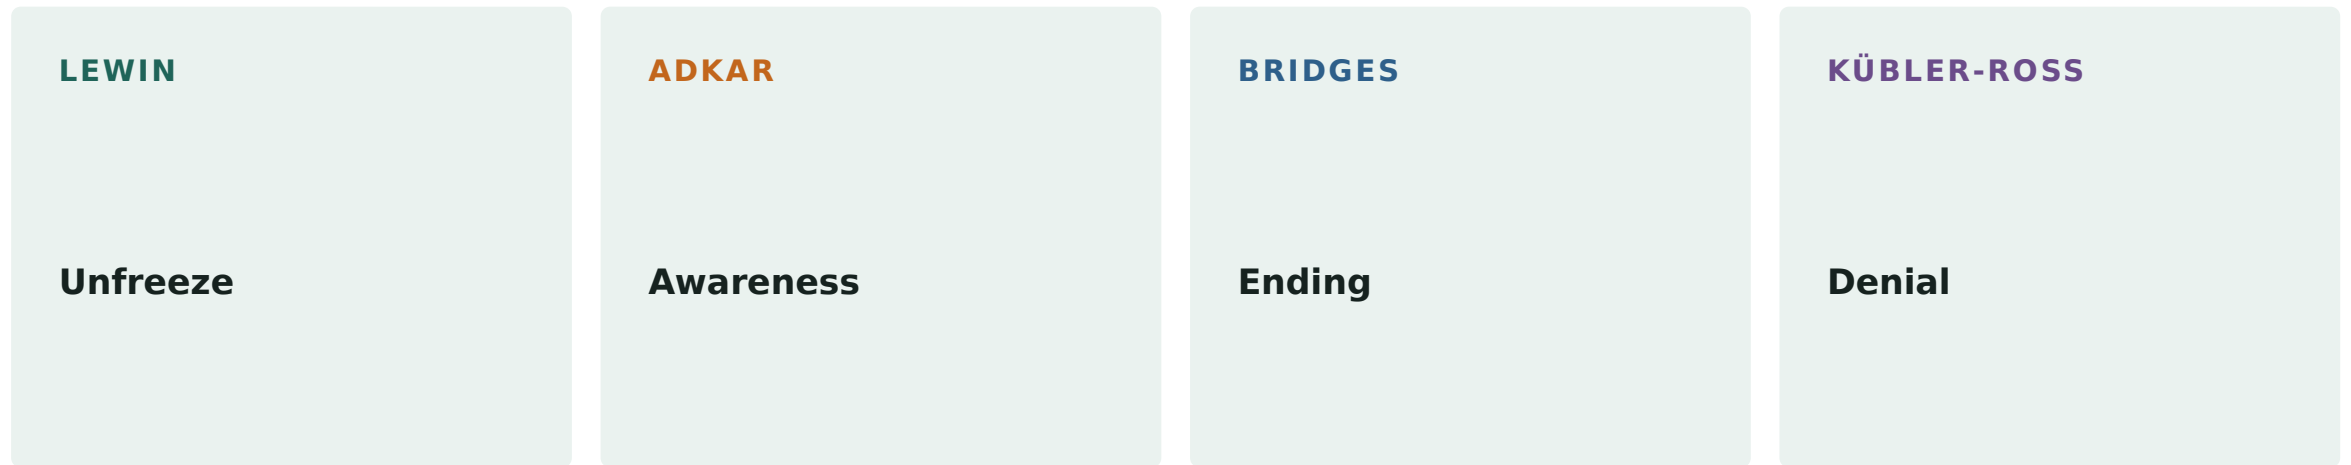

KEY TECHNIQUE THIS PHASE

Future-state design-principle sign-off: Lock the principles every later configuration sprint builds against.

Build

Weeks 14-35

NARRATIVE

The longest phase — four configuration sprints against the signed-off design principles. This is where Exception E1 (Desire Stall at Settat) plays out in full.

PHASE 3 · BUILD

Key Moments in This Phase

Week	What Happens
Week 18-22	Mid-Build; Settats Desire drops to 2, auto-escalating — Exception E1 opens.
Week 22	CFO delivers a direct staffing commitment to the Settats cohort in person.
Week 35	Build gate closes; Lewin call actually moves, backed by evidence.

PHASE 3 · BUILD

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Configuration sprints + barrier-note clustering: Build the system while catching and clustering readiness barriers by root cause, not symptom.

Test

Weeks 28–39

NARRATIVE

The first point a representative slice of end users gets real hands-on exposure — and the first honest opportunity to run the Divergence Pattern check.

Key Moments in This Phase

Week	What Happens
Week 28	SIT test script run: 40 scripted scenarios across all three modules.
Week 31	A Casablanca finance UAT participant fires ALT-001 (Divergence Pattern Detected) — Exception E2 opens.
Week 35	Loss-focused 1:1 held; underlying concern (a role that doesn't exist post-cutover) surfaced and closed.

PHASE 4 · TEST

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Scripted SIT + Divergence Pattern check: Confirm technical correctness and catch a trained-but-not-yet-accepted cohort before go-live.

Train

Weeks 35–42


NARRATIVE

Runs alongside Test rather than strictly after it — Knowledge becomes Ability under increasingly realistic conditions.

Key Moments in This Phase

Week	What Happens
Week 35	Sandbox environment opens for supervised practice, all three sites.
Week 36	Knowledge/Ability scored per cohort: Settat reads meaningfully behind — Exception E6 opens.
Week 37	Composite Readiness Index disaggregated by site for the first time: Casablanca 78%, Kenitra 68%, Settat 54%.

Framework Snapshot

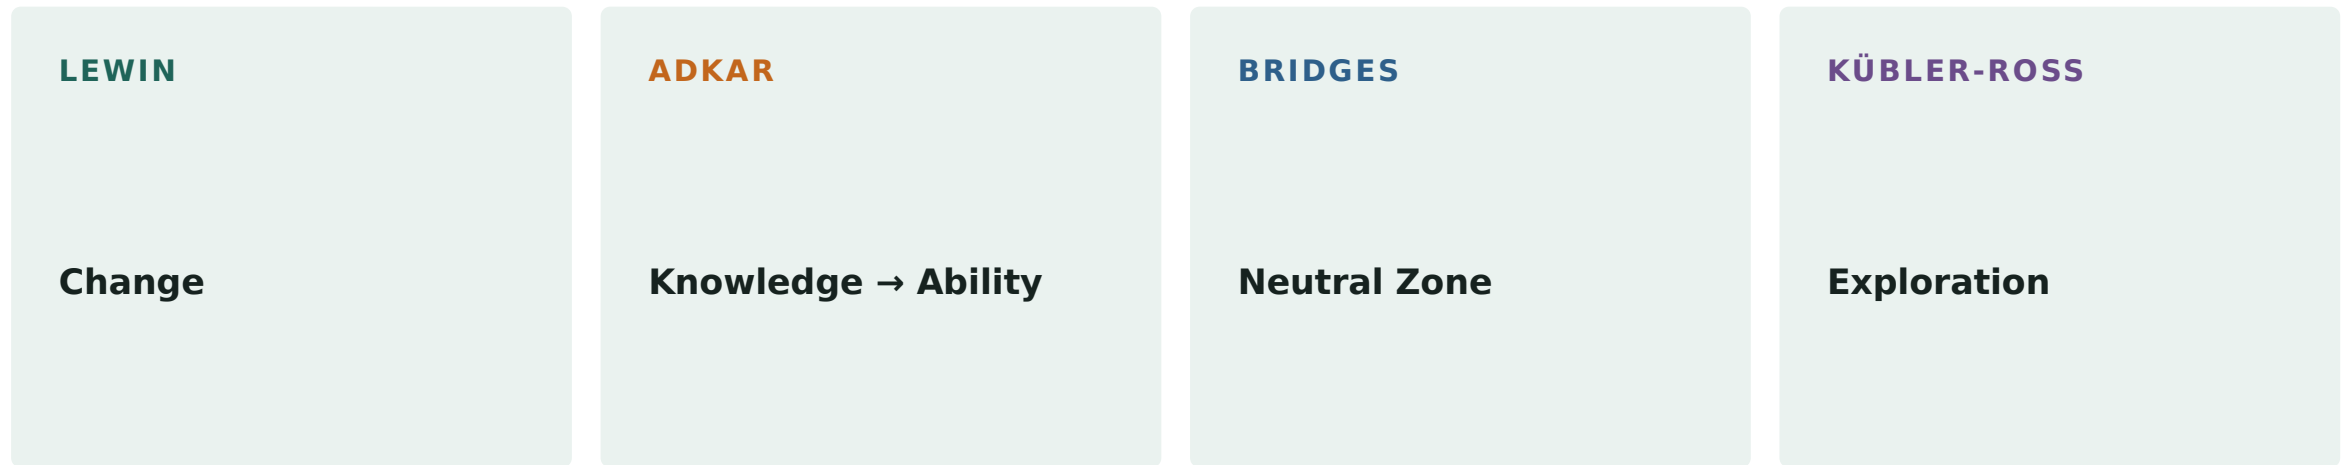

KEY TECHNIQUE THIS PHASE

Sandbox practice + per-cohort Knowledge/Ability scoring: Move Knowledge into Ability under realistic, supervised conditions.

Deploy

Week 43


NARRATIVE

A single, sharp week — the clearest instance of the two-clock problem this series treats as a first-class risk, not an edge case.

Key Moments in This Phase

Week	What Happens
Week 43, Day 1-4	Technical go-live clean across all three sites.
Week 43, Day 5	Hypercare activates; Lewin marked "Change → Refreeze (provisional)," not confirmed — Exception E3 opens by design.

Framework Snapshot

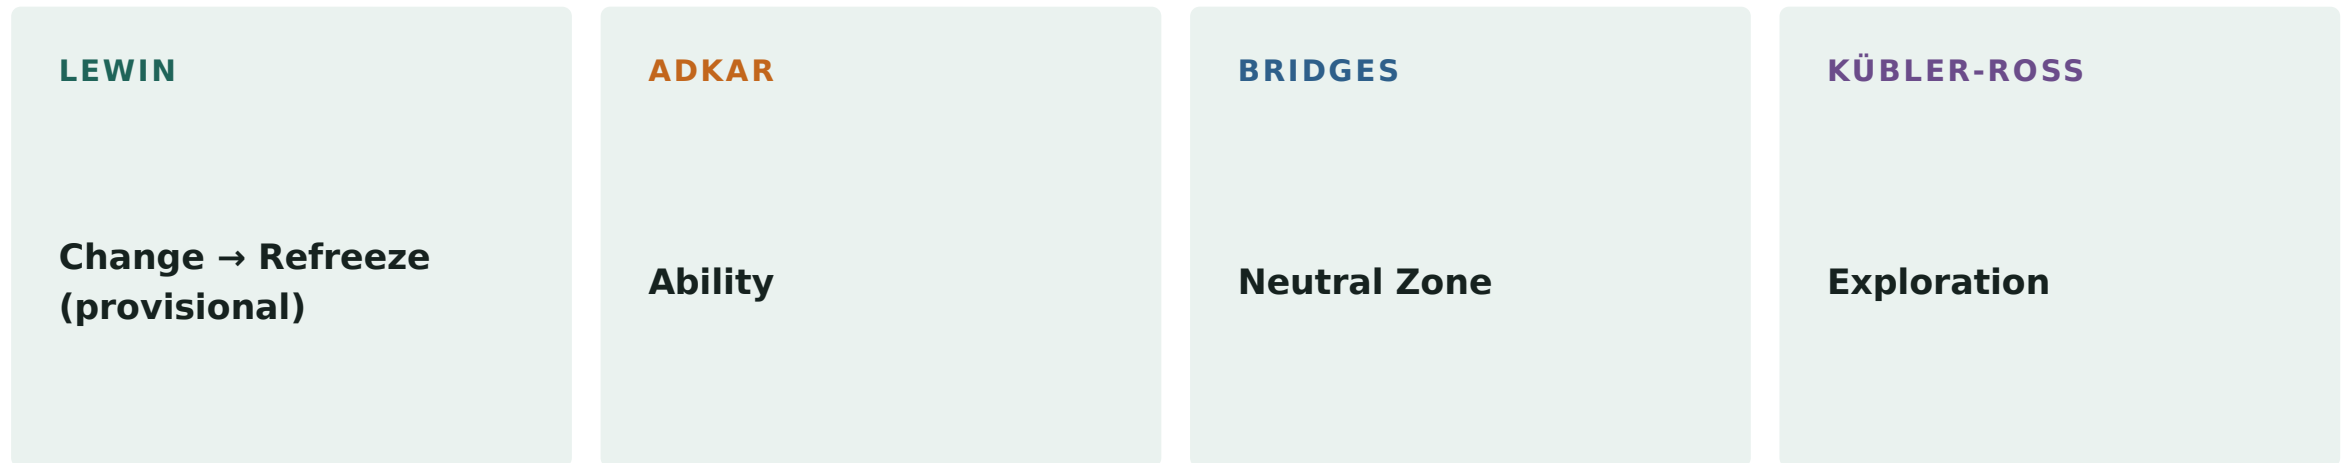

KEY TECHNIQUE THIS PHASE

Two-clock discipline (provisional Refreeze): Separate the technical go-live milestone from the confirmed emotional/behavioral Refreeze call.

Hypercare

Weeks 44-50


NARRATIVE

The last mile of adoption is won or lost here — Kübler-Ross regression during this window is normal, expected behavior, not a data error.

Key Moments in This Phase

Week	What Happens
Week 45	Bridges/Kübler-Ross re-pulse at 2-week mark; Kenitra dips — Exception E4 trigger.
Week 46	Kenitra defect resolved; supervisor holds a team huddle acknowledging the setback directly.
Week 48	Exception E6's disaggregated CRI gap narrows substantially: 82% / 76% / 74%.

Framework Snapshot

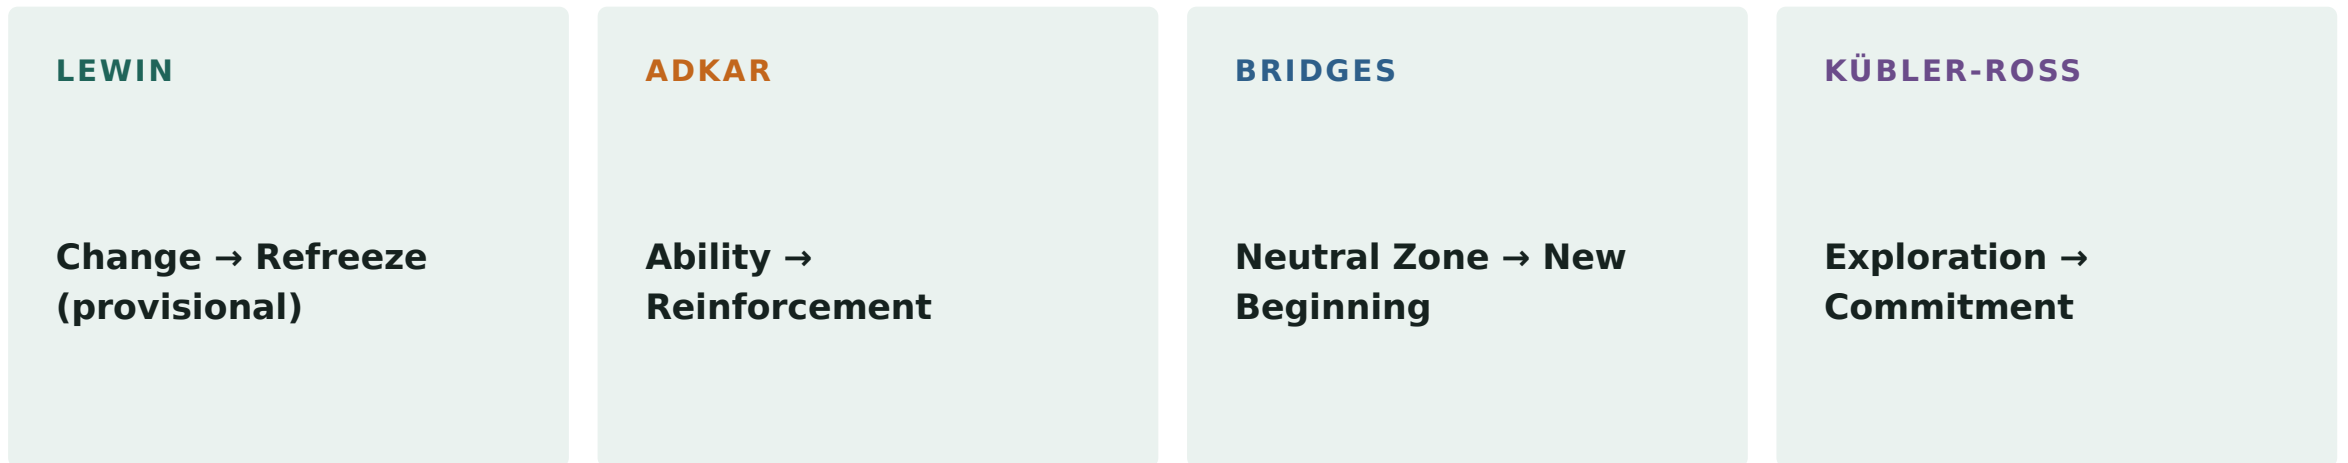

KEY TECHNIQUE THIS PHASE

2- and 4-week Bridges/Kübler-Ross re-pulse: Catch and resolve a sentiment dip before it hardens into lasting resistance.

Sustain

Weeks 51-64


NARRATIVE

Refreeze is called from checkpoint evidence, never the calendar — the discipline that protects against Exception E5 (Reinforcement Gap at Sustain).

Key Moments in This Phase

Week	What Happens
Week 56	Reinforcement stalls below 3 at the 90-day checkpoint — Exception E5 opens.
Week 60	CFO re-authorizes a further checkpoint cadence; champion network re-chartered for reinforcement.
Week 64	Two consecutive healthy checkpoints follow; Refreeze is called from that evidence and program closes.

Framework Snapshot

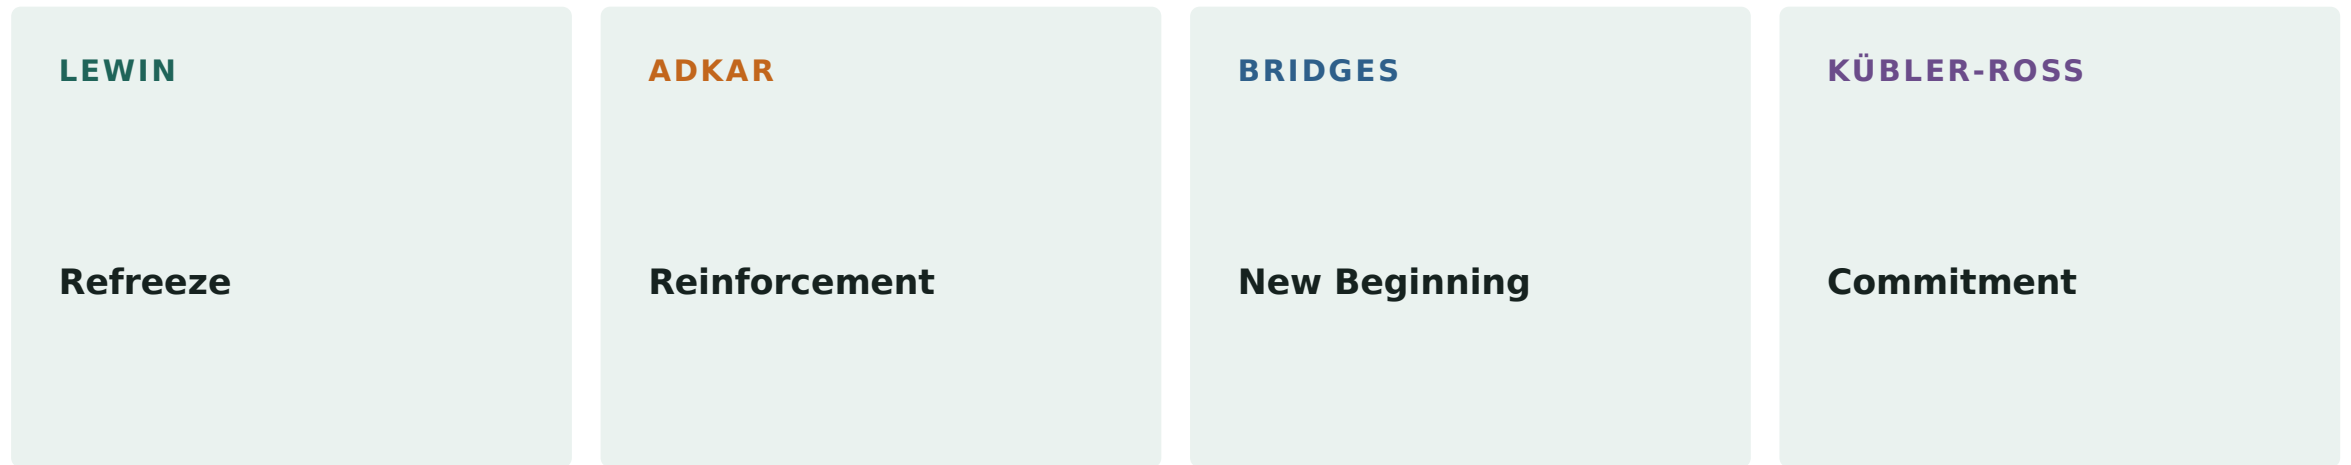

KEY TECHNIQUE THIS PHASE

30/60/90-day sustainment checkpoints: Call Refreeze from evidence, never the calendar.

Every Phase, Across the Four Frameworks

Phase	Week(s)	Lewin	ADKAR	Bridges	Kübler-Ross
Discovery	Weeks 1-8	Unfreeze	Awareness	Ending	Denial
Design	Weeks 6-17	Unfreeze	Awareness	Ending	Denial
Build	Weeks 14-35	Unfreeze → Change	Awareness → Desire	Ending → Neutral Zone	Denial → Resistance/Anger
Test	Weeks 28-39	Change	Knowledge → Ability	Neutral Zone	Resistance/Anger → Exploration
Train	Weeks 35-42	Change	Knowledge → Ability	Neutral Zone	Exploration
Deploy	Week 43	Change → Refreeze (provisional)	Ability	Neutral Zone	Exploration
Hypercare	Weeks 44-50	Change → Refreeze (provisional)	Ability → Reinforcement	Neutral Zone → New Beginning	Exploration → Commitment
Sustain	Weeks 51-64	Refreeze	Reinforcement	New Beginning	Commitment

Every Phase, Techniques and Tools

Phase	Week(s)	Technique	Goal	Tool
Discovery	Weeks 1–8	Current-state process mapping	Establish exactly what today's manual/legacy process actually does, by site.	M4 (Stakeholder Mapping)
Design	Weeks 6–17	Future-state design-principle sign-off	Lock the principles every later configuration sprint builds against.	M17 (WBS & Gantt)
Build	Weeks 14–35	Configuration sprints + barrier-note clustering	Build the system while catching and clustering readiness barriers by root cause, not symptom.	M5 (ADKAR Engine)
Test	Weeks 28–39	Scripted SIT + Divergence Pattern check	Confirm technical correctness and catch a trained-but-not-yet-accepted cohort before go-live.	M6 (Emotional & Transition Layer)
Train	Weeks 35–42	Sandbox practice + per-cohort Knowledge/Ability scoring	Move Knowledge into Ability under realistic, supervised conditions.	M9 (Training)
Deploy	Week 43	Two-clock discipline (provisional Refreeze)	Separate the technical go-live milestone from the confirmed emotional/behavioral Refreeze call.	M3 (Initiative Registry)
Hypercare	Weeks 44–50	2- and 4-week Bridges/Kübler-Ross re-pulse	Catch and resolve a sentiment dip before it hardens into lasting resistance.	M11 (Manager as Coach)
Sustain	Weeks 51–64	30/60/90-day sustainment checkpoints	Call Refreeze from evidence, never the calendar.	M12 (Sustainment)

PART 4 — SIX EXCEPTIONS, IN DETAIL

Six Realistic Ways This Program Could Have Gone Differently

Desire Stall at Settat

DESCRIPTION

Settat's ADKAR Desire score drops to 2, auto-escalating a barrier-reason note citing low visibility into the new inventory workflow and unresolved staffing-level fears.

TRIGGER

Desire logged at 2 or below for the Settat plant-floor cohort on M5, auto-escalating.

TIMELINE IMPACT

No Build gate delay — resolved within the same phase via a direct sponsor intervention.

RECOVERY TASKS

Cluster barrier notes by root cause; run targeted listening sessions confirming position security, not workflow visibility, is the primary driver; CFO delivers a direct staffing commitment in person.

OUTPUTS: A closed barrier note; a documented sponsor intervention; a recovered Desire score. **RACSI:** R = CM · A = ES · C = FPO, SUP · S = PM · I = EU

Divergence Pattern at UAT

DESCRIPTION

A Casablanca finance UAT participant logs Knowledge ≥ 4 and Ability ≥ 4 while Bridges still reads exactly "Ending" — ALT-001's exact condition.

TRIGGER

ALT-001 (Divergence Pattern Detected) fires on M6, cross-referenced against M5.

TIMELINE IMPACT

No gate delay — resolved through a confidential 1:1 within the same week window.

RECOVERY TASKS

Confirm the alert against supervisor observation; hold a loss-focused 1:1; the underlying concern (a role that doesn't exist post-cutover) is surfaced and given an explicit closure moment.

OUTPUTS: A confidential 1:1 outcome logged as a Bridges re-score; a closed divergence. **RACSI:** R = CM · A = CM · C = ES · S = PM · I = FPO, EU

Two-Clock Problem at Deploy

DESCRIPTION

Lewin is technically eligible to call "Refreeze" on the Deploy week's calendar date, while Bridges and Kübler-Ross across most cohorts still read Neutral Zone or lower — the organizational clock and the emotional clock diverging exactly as designed to anticipate.

TRIGGER

Technical go-live succeeds while emotional-layer evidence remains pending re-pulse.

TIMELINE IMPACT

No delay to go-live itself — the discipline costs nothing when there is no lag, and catches the case when there is one.

RECOVERY TASKS

Mark Lewin "Change → Refreeze (provisional)," not confirmed; require the 2- and 4-week Bridges/Kübler-Ross re-pulse across all three sites before calling Refreeze.

OUTPUTS: A provisional Lewin state; confirming evidence at Weeks 45/47/50. **RACSI:** R = CM · A = ES · C = PM · S = FPO · I = SUP, EU

Sentiment Regression During Hypercare

DESCRIPTION

Kenitra's Kübler-Ross reading moves backward from Exploration to Resistance/Anger following a visible, embarrassing stock-count error caused by a configuration defect.

TRIGGER

A cohort's Kübler-Ross reading moves backward on M6 following a specific triggering event.

TIMELINE IMPACT

Resolved within the same week — the defect is fixed and communicated inside Hypercare's own window.

RECOVERY TASKS

Resolve Defect #31; the Kenitra supervisor holds a team huddle acknowledging the incident directly; targeted coaching on the affected stock-count step.

OUTPUTS: A closed defect; a logged coaching action on M11; a confirmed sentiment recovery. **RACSI:** R = SUP · A = ES · C = ITL · S = CM · I = PM, EU

Reinforcement Gap at Sustain

DESCRIPTION

ADKAR Reinforcement stalls below 3 as the program's formal end date approaches, with no forcing deadline prompting continued attention — the exact risk Sustain's evidence-based discipline exists to prevent.

TRIGGER

Reinforcement score stalls below 3 on M5 near the program's formal close.

TIMELINE IMPACT

Extends the Refreeze call past the original close date — accepted, since Refreeze is called from evidence, never the calendar.

RECOVERY TASKS

CFO re-authorizes a further checkpoint cadence at 105 and 120 days; the champion network is re-chartered specifically for reinforcement.

OUTPUTS: Two further consecutive healthy checkpoints; a Refreeze call backed by that evidence. **RACSI:** R = CM · A = ES · C = PM · S = FPO · I = SUP, EU

Cohort Divergence Across Sites

DESCRIPTION

Casablanca, Kenitra, and Settat read genuinely differently across all four frameworks by mid-Train, making the project-level Composite Readiness Index a misleading blend of three very different real situations.

TRIGGER

Site-level ADKAR/Bridges readings diverge sharply enough that a single blended CRI would mislead the Steering Committee.

TIMELINE IMPACT

No gate delay — the fix is a reporting discipline, not a schedule change.

RECOVERY TASKS

Disaggregate the Composite Readiness Index by site using M4's site tags; flag the lagging site for a second training wave; track the three readings separately until they converge.

OUTPUTS: A disaggregated CRI reporting practice, carried forward as the standing reporting standard. **RACSI:** R = CM, PM · A = CM · C = ES · S = FPO · I = SUP, EU

What This Training Covers

Per the E2E-ERP chain, MP-05 runs at full weight across the Train phase — role-based training by cohort, with sandbox practice hours tracked separately from classroom completion.

Strategic Management

Cohort: CFO, Executive Viewer, Site Directors · Weeks 8-17

Curriculum Entry	Content Focus
Sponsoring a Full System Cutover	Why visible, sustained sponsorship matters more here than in any narrower archetype.
Reading a Divergence Pattern Alert	How to read ALT-001 as real evidence, not a false alarm.

Operational Management

Cohort: Driss El Amrani, Houda Zerouali, site supervisors · Weeks 22-39

Curriculum Entry	Content Focus
Barrier-Note Clustering and Response	Turning individual barrier notes into a targeted, root-cause recovery.
Running a Loss-Focused 1:1	The specific coaching technique behind Exception E2's resolution.

Operations (Frontline)

Cohort: All 3,400 end users, by site and cohort · Weeks 35-50

Curriculum Entry	Content Focus
New System Navigation, By Module	Order Management, Inventory, and Finance, each trained separately by cohort.
Sandbox Practice Under Supervision	Hands-on rehearsal before go-live, tracked separately from classroom attendance.

Why This Curriculum Is Shaped This Way

Training completion alone does not close this program — Reinforcement, the slowest-moving ADKAR block, is what Sustain's checkpoints exist to verify, months after the last training session ends.

Which journi Modules Dominate This Archetype

M17 (WBS & Gantt)	The 8-phase TPL-ERP-8 template — the longest, most detailed schedule of any archetype.
M5 (ADKAR Engine)	Scored per site/cohort — the direct input to catching site-level divergence.
M9 (Training)	The Train phase's entire content — job aids, sandbox environments, per-site delivery waves.
M12 (Sustainment)	The Hypercare-to-Sustain handoff — the checkpoint that justifies closing Lewin at Refreeze.
M14 (Analytics)	The Composite Readiness Index, disaggregated by site when a blended number would mislead.
M6 (Emotional & Transition Layer)	Bridges and Kübler-Ross, cross-referenced with ADKAR to compute ALT-001.

What This Case Fires

ALERTS THIS CASE EXERCISES

ALT-001 (Divergence Pattern Detected)

ALT-009 (Phase Gate No-Go/Conditional, if any gate closes non-Go)

WHY

The throughline case — the one most likely to exercise a Knowledge/Ability-vs-Bridges divergence, given its scale and duration.

KEY TAKEAWAYS

What to Remember About This Archetype

- › A real Divergence Pattern catch before go-live (Casablanca, Week 28), a real cross-site Composite Readiness Index disaggregation (Exception E6), and a Refreeze called only once Sustain's own 90-day checkpoint evidence supports it — not the go-live date.
- › ADKAR and Lewin dominate equally, throughout. A system cutover needs organizational readiness (Lewin's Change → Refreeze) and individual capability (ADKAR's Knowledge/Ability) at the same time — neither alone is sufficient, and unlike every other archetype in this series, that is true across all 8 phases, not concentrated in one.
- › The throughline case — the one most likely to exercise a Knowledge/Ability-vs-Bridges divergence, given its scale and duration.



ERP Implementation

Bouregreg ERP Adoption Program
