



Operating Model Redesign

Regional Operating Model Redesign

Realigning reporting lines from site-based to function-based — where the real risk is reversion under pressure, not initial adoption.

7

PHASES

34

WEEKS

6

EXCEPTIONS

3

TRAINING TIERS

PART 0 — PURPOSE

What This Guide Is, and How to Use It

WHAT THIS GUIDE IS

This deck follows the Regional Operating Model Redesign — journi's Operating Model archetype case — from tenant setup through standing rhythm handover, realigning reporting lines from site-based to function-based across Bouregreg Group's three sites.

HOW TO USE IT

This program runs inside the same Bouregreg Group tenant as every other archetype in this series, once the ERP program's own Build phase exposes the site-based structure's duplication. A reader with the tenant already set up skips straight to CM Project creation.

Verified Against journi's Real Source

Every journi module, field, and role named here is verified against journi's real source. This is journi's own stated case for ALT-002 (Regression Risk Score Critical) and ALT-015 (Sustainment Sign-Off Blocked) — this deck shows exactly how a real regression is caught, not glossed over.

RACSI CODES USED THROUGHOUT

ES = Executive Sponsor · CM = Change Manager · PM = Program/Project Manager · FPO = Functional Process Owner · ITL = IT/Technical Lead · SUP = Supervisor · EU = End User

Why This Case Matters

Function Heads can pass every earlier checkpoint and still revert to old decision-making under real operational pressure — this archetype is built specifically to prove that reversion under pressure, not initial adoption, is the real test of an operating-model redesign.

The Case, in Brief

95 staff, people managers across 3 sites

34 weeks (guide numbering)

Bouregreg Group realigns reporting lines across all three sites from site-based to function-based — Finance, Operations, and Quality each reporting centrally rather than to a site director — once the ERP program exposes how much duplicated decision-making the site-based structure was causing.

What This Guide Proves, Concretely

A real 30-day sustainment checkpoint landing High regression risk, and a training-completion record (100% by Week 25) that proves Reinforcement, not Knowledge, was the actual gap — not glossed over as a clean success.

Weighting for This Archetype

ADKAR Reinforcement dominates. Function Heads can pass every earlier checkpoint and still revert to old decision-making under real operational pressure — this archetype is built specifically to show that failure mode, not initial adoption, is the real test.

The Composite Readiness Index, Read for This Case

The Composite Readiness Index reads strong through Pilot Transition, then drops sharply at the 30-day post-Full-Transition checkpoint — a real, not gradual, regression, which is exactly the kind of signal a checkpoint exists to catch rather than a slow drift a trend line would eventually show anyway.

The Existing Tenant, and Reading Paths by Role

THE EXISTING TENANT

This program runs inside the same tenant journi's Master User Guide builds, under the existing Bouregreg Manufacturing Maroc Organization — no new Organization needed.

READING PATHS, BY ROLE

- › A Change Manager running this program day to day: Part 2 once, then Part 4 in full.
- › A Program/Project Manager: Part 4's PM Track column and the Master WBS & Gantt.
- › An Executive Sponsor: Part 1, then Part 4's phase-opening narratives.
- › A Super Admin or Org Admin: Part 3.

The RACSI Team for This Program

Name	RACSI Code	Role
Yassine Berrada	ES	Sponsor — COO
Salma Idrissi	CM	Change Manager
Rachid Alaoui	PM	Program Manager
Amina Sqalli	FPO	Finance Function Head
Nabil Ouazzani	ITL	IT/Technical Lead
Loubna Tazi	SUP	Casablanca pilot site

Creating the CM Project

1

On Module 1 — Hierarchy, create the Regional Operating Model Redesign CM Project under the existing Bouregreg Manufacturing Maroc Organization.

2

Set Change type: Operating Model Redesign. Target population: "All people-manager-level staff across three sites, 95 staff." Business driver: "The ERP program exposed how much duplicated decision-making the site-based structure was causing."

3

Save. Lewin opens at Unfreeze, once the ERP program's own Build phase has exposed the duplication.

4

On Module 17 — WBS & Gantt, load the TPL-OM-7 phase template: Current Operating Model Assessment, TOM Design, Detailed Org Design, Pilot Transition, Full Transition, Governance Adoption Tracking, Standing Rhythm Handover.

Charters for This Program

Charter	Accountable	Review Cadence
CHTR-01 Sponsorship / Leadership Charter	Yassine Berrada (ES)	Per Phase Gate
CHTR-04 Organizational Impact Charter	Salma Idrissi (CM)	On scope change
CHTR-08 Pulse / Interview Charter	Salma Idrissi (CM)	Per phase gate + ad hoc

Setup Checklist

- ☒ Base tenant confirmed (Bouregreg Group, existing Organization)
- ☒ Operating Model program team accounts created across all three sites
- ☒ CM Project created, Lewin opened at Unfreeze
- ☒ TPL-OM-7 phase template loaded on M17
- ☒ Applicable Charters reviewed and accountable owners confirmed

PART 4 — WEEK-BY-WEEK TIMELINE

7 Phases, In Order



Total program length: 34 weeks (guide numbering). Every phase below is walked in detail across the next slides — normal flow first, then six exceptions in full operational detail.

Current Operating Model Assessment

Weeks 1-8


NARRATIVE

Assesses exactly how much duplicated decision-making the site-based structure causes, once the ERP program's Build phase makes it visible.

Key Moments in This Phase

Week	What Happens
Week 1	Kickoff; Lewin opens at Unfreeze.
Week 5	Decision-duplication mapped across all three sites.
Week 8	Assessment gate closes.

Framework Snapshot

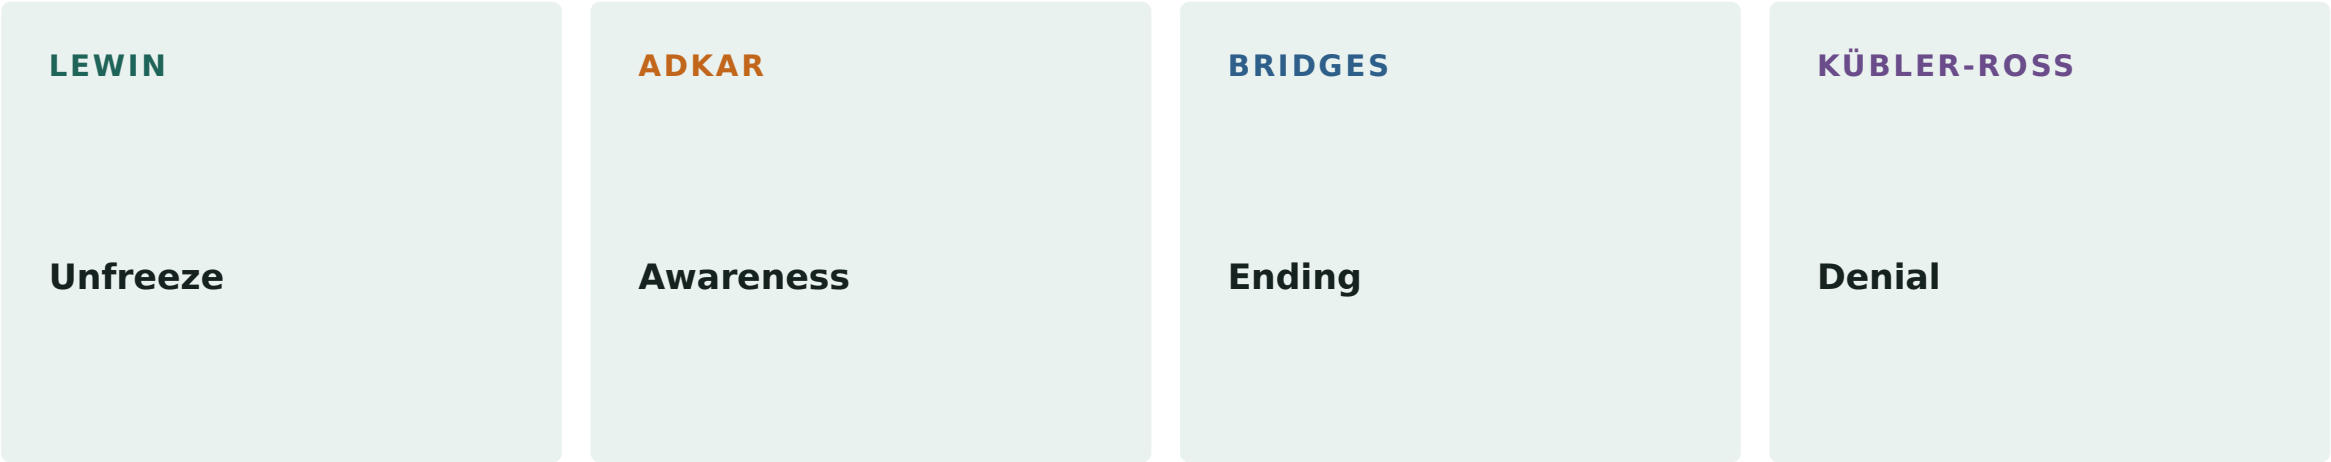

KEY TECHNIQUE THIS PHASE

Decision-duplication mapping: Make the site-based structure's duplicated decision-making visible and countable.

TOM Design

Weeks 6-14


NARRATIVE

Designs the target function-based operating model — Finance, Operations, and Quality reporting centrally.

Key Moments in This Phase

Week	What Happens
Week 10	Target operating model drafted against the assessment findings.
Week 14	TOM design signed off.

Framework Snapshot

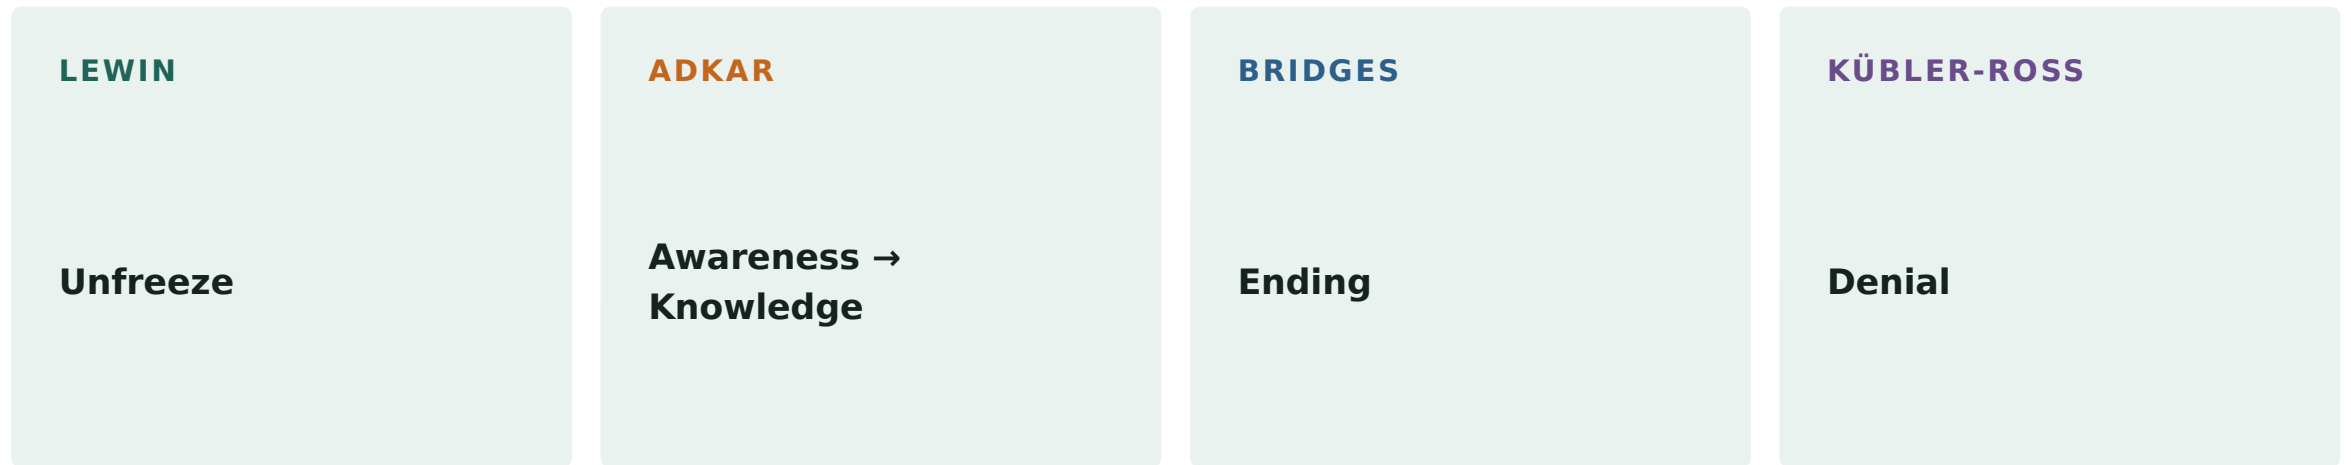

KEY TECHNIQUE THIS PHASE

Target operating model drafting: Design a function-based reporting structure against the assessment's own findings.

Detailed Org Design

Weeks 12-18


NARRATIVE

Details the specific reporting lines, decision rights, and role changes the redesign requires.

Key Moments in This Phase

Week	What Happens
Week 15	Decision-rights matrix drafted per function.
Week 18	Detailed org design gate closes.

Framework Snapshot

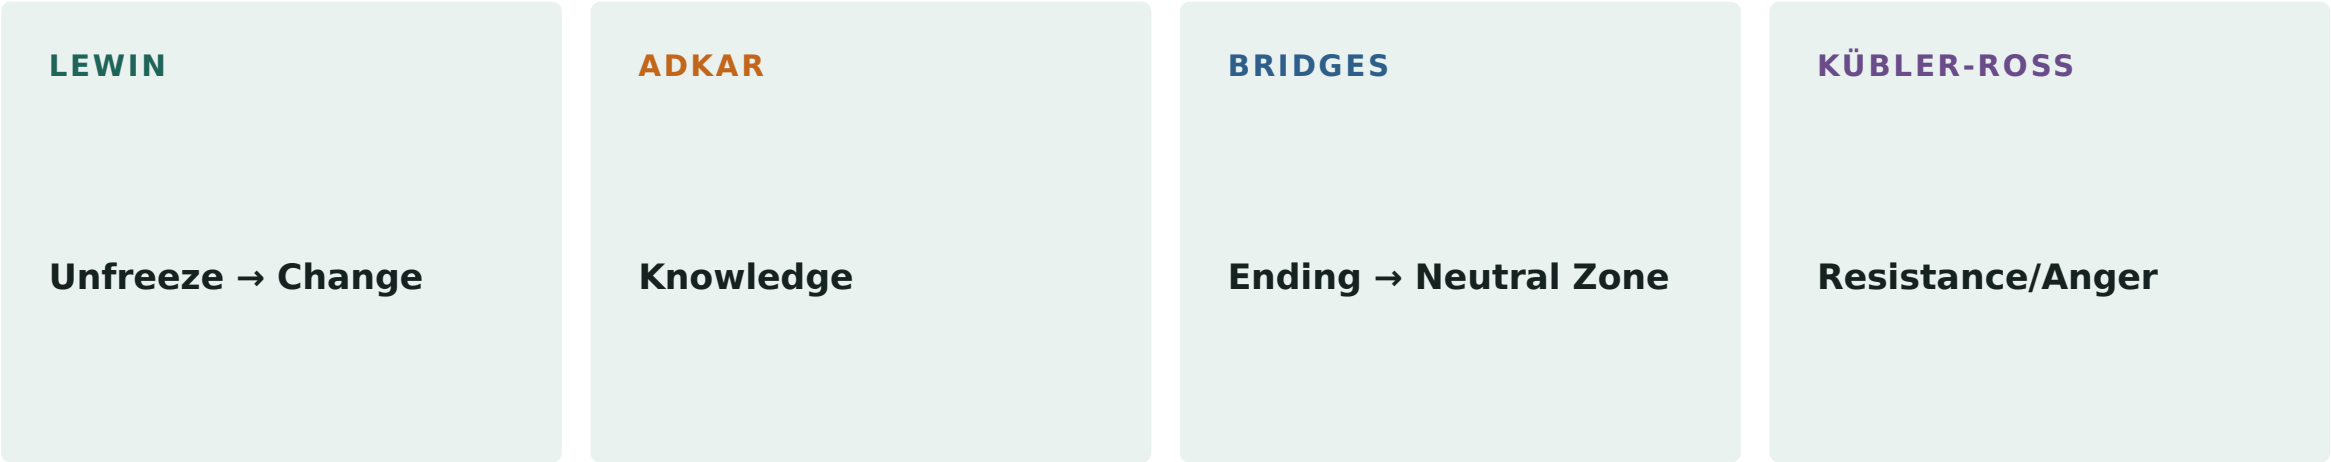

KEY TECHNIQUE THIS PHASE

Decision-rights matrix design: Specify exactly which decisions route where under the new structure.

Pilot Transition

Weeks 17-22

NARRATIVE

Pilots the new reporting structure at Casablanca Finance first — Exception E2's pilot-success-masks-risk pattern originates here.

Key Moments in This Phase

Week	What Happens
Week 18	Casablanca Finance transitions first.
Week 22	Pilot succeeds cleanly — but on a pressure profile unlike Kenitra or Settat's.

PHASE 4 · PILOT TRANSITION

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Single-site piloting: De-risk the full transition by testing on one site before all three.

Full Transition

Weeks 21-27

NARRATIVE


Extends the new reporting structure to Kenitra and Settat — where the pilot's clean success starts to look different.

PHASE 5 · FULL TRANSITION

Key Moments in This Phase

Week	What Happens
Week 23	Amina Sqalli, now receiving escalations from all three sites, shows early capacity strain — Exception E3 opens.
Week 24	A site director continues deciding unofficially — Exception E4 opens.
Week 27	Full transition gate closes.

Framework Snapshot

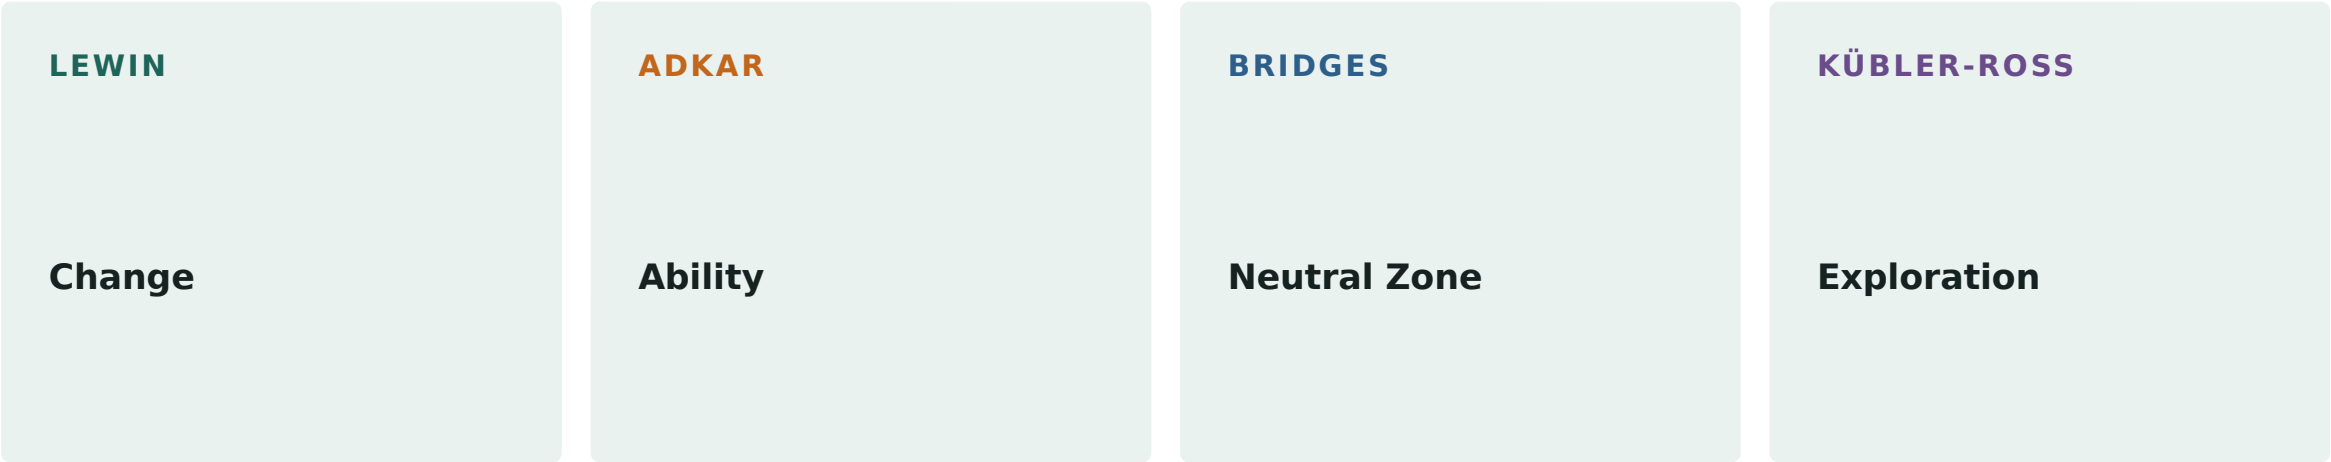

KEY TECHNIQUE THIS PHASE

Staged multi-site rollout: Extend the piloted structure to the remaining two sites.

Governance Adoption Tracking

Weeks 26-32


NARRATIVE

Tracks the new governance rhythm's real adoption — where the program's defining regression actually lands.

Key Moments in This Phase

Week	What Happens
Week 26	The first 30-day sustainment checkpoint lands High regression risk — Exception E1 opens, firing ALT-002/ALT-015.
Week 29	Root cause traced to Kenitra and Settat's unpredictable operational-pressure profile.
Week 32	A clean checkpoint follows; sign-off unblocks.

Framework Snapshot

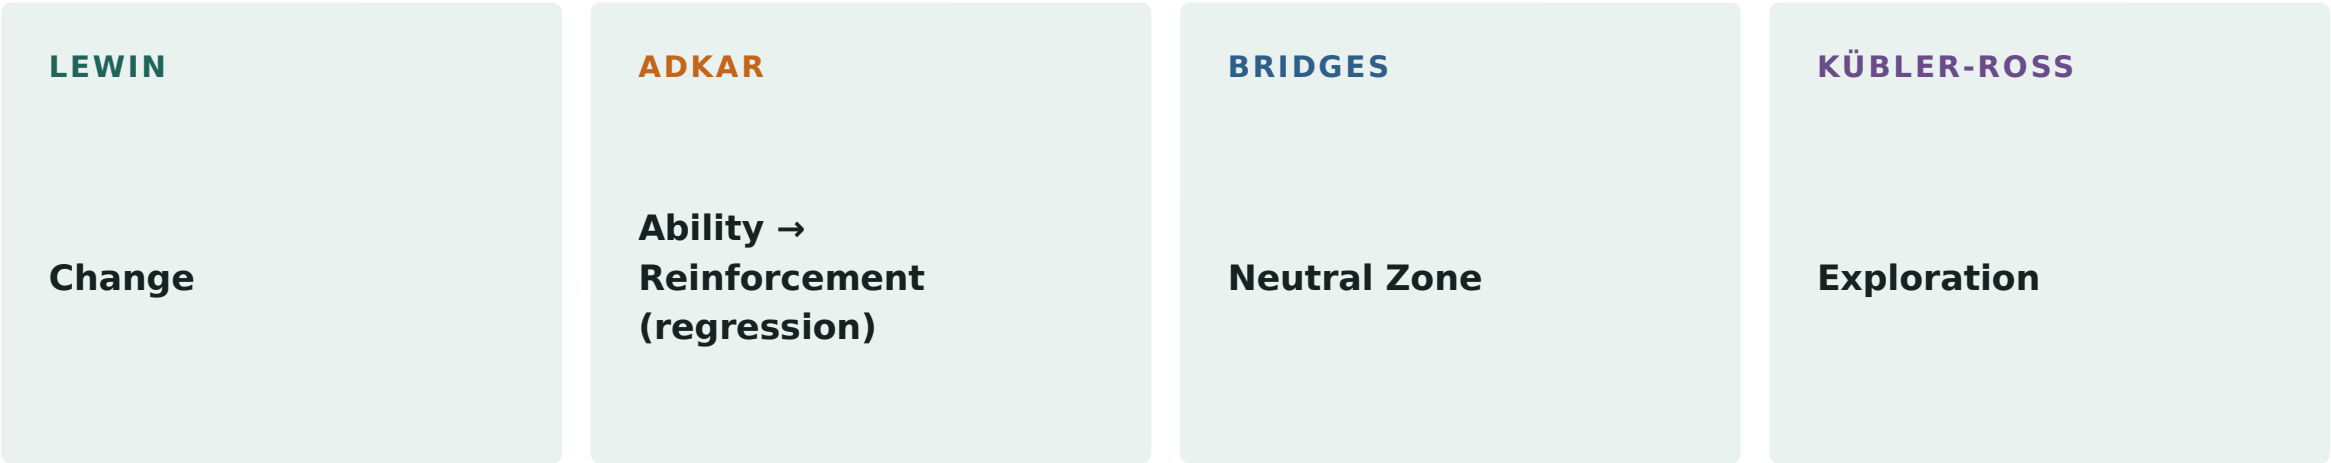

KEY TECHNIQUE THIS PHASE

30-day sustainment checkpoint: Catch a real reversion under operational pressure before it becomes permanent.

Standing Rhythm Handover

Weeks 30-34


NARRATIVE

Hands the new reporting structure off to a standing monthly governance rhythm — tested by a second, smaller regression signal.

Key Moments in This Phase

Week	What Happens
Week 31	Standing monthly rhythm confirmed and documented.
Week 34+	A follow-up check three months later finds a partial slip at one site — Exception E6 opens.

Framework Snapshot

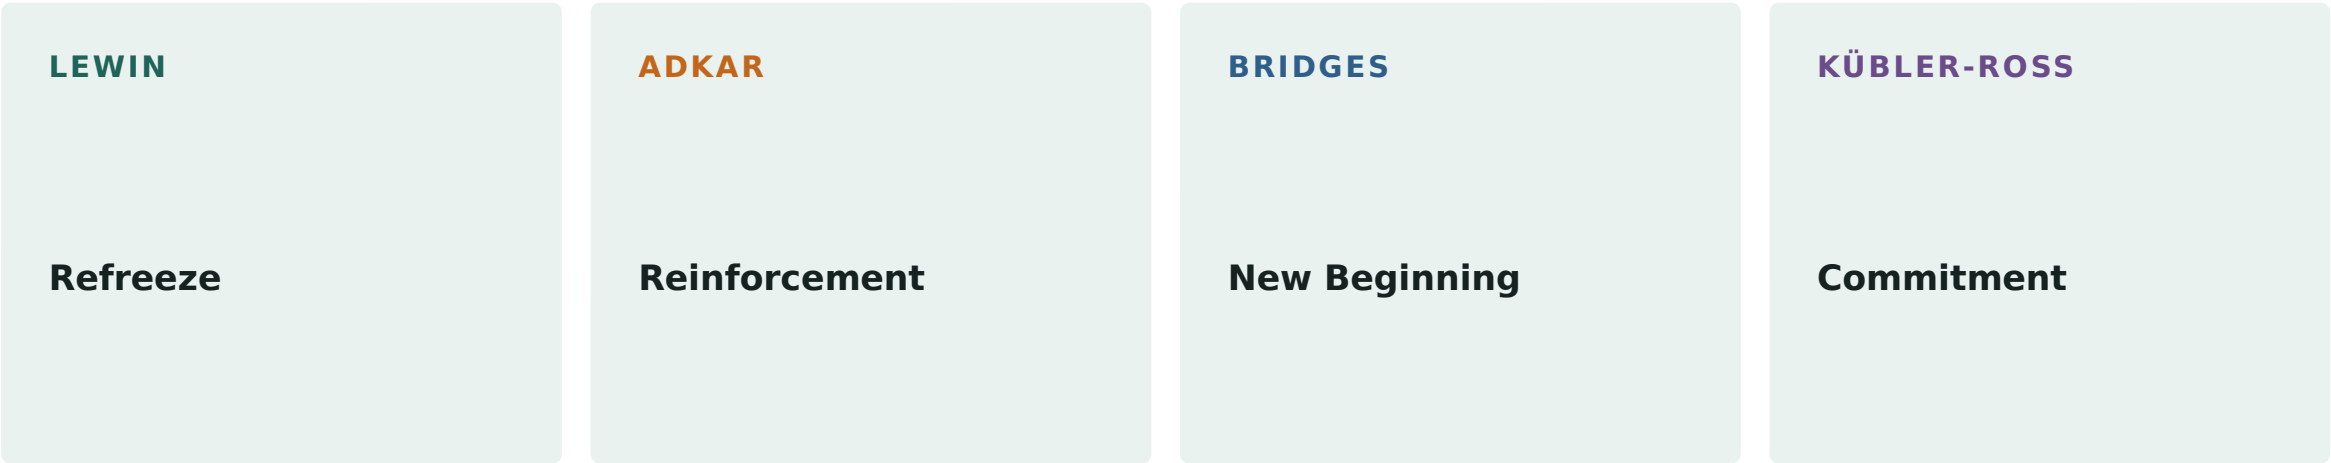

KEY TECHNIQUE THIS PHASE

Standing monthly governance rhythm: Replace a dedicated program team's oversight with a durable, ongoing rhythm.

Every Phase, Across the Four Frameworks

Phase	Week(s)	Lewin	ADKAR	Bridges	Kübler-Ross
Current Operating Model Assessment	Weeks 1-8	Unfreeze	Awareness	Ending	Denial
TOM Design	Weeks 6-14	Unfreeze	Awareness → Knowledge	Ending	Denial
Detailed Org Design	Weeks 12-18	Unfreeze → Change	Knowledge	Ending → Neutral Zone	Resistance/Anger
Pilot Transition	Weeks 17-22	Change	Knowledge → Ability	Neutral Zone	Resistance/Anger → Exploration
Full Transition	Weeks 21-27	Change	Ability	Neutral Zone	Exploration
Governance Adoption Tracking	Weeks 26-32	Change	Ability → Reinforcement (regression)	Neutral Zone	Exploration
Standing Rhythm Handover	Weeks 30-34	Refreeze	Reinforcement	New Beginning	Commitment

Every Phase, Techniques and Tools

Phase	Week(s)	Technique	Goal	Tool
Current Operating Model Assessment	Weeks 1–8	Decision-duplication mapping	Make the site-based structure's duplicated decision-making visible and countable.	M4 (Stakeholder Mapping)
TOM Design	Weeks 6–14	Target operating model drafting	Design a function-based reporting structure against the assessment's own findings.	M17 (WBS & Gantt)
Detailed Org Design	Weeks 12–18	Decision-rights matrix design	Specify exactly which decisions route where under the new structure.	M21 (Field Notes)
Pilot Transition	Weeks 17–22	Single-site piloting	De-risk the full transition by testing on one site before all three.	M5 (ADKAR Engine)
Full Transition	Weeks 21–27	Staged multi-site rollout	Extend the piloted structure to the remaining two sites.	M17 (WBS & Gantt)
Governance Adoption Tracking	Weeks 26–32	30-day sustainment checkpoint	Catch a real reversion under operational pressure before it becomes permanent.	M12 (Sustainment)
Standing Rhythm Handover	Weeks 30–34	Standing monthly governance rhythm	Replace a dedicated program team's oversight with a durable, ongoing rhythm.	M12 (Sustainment)

PART 4 — SIX EXCEPTIONS, IN DETAIL

Six Realistic Ways This Program Could Have Gone Differently

Regression Risk Score Critical / Sustainment Sign-Off Blocked

DESCRIPTION

The program's first 30-day sustainment checkpoint found decisions at several sites quietly reverting to the old site-director escalation path under real operational pressure — ALT-002's exact condition, with ALT-015 following automatically.

TRIGGER

A sustainment checkpoint on M12 is marked complete with regression risk logged as High.

TIMELINE IMPACT

Blocks sign-off until a clean checkpoint follows — roughly one further monitoring cycle.

RECOVERY TASKS

Root-cause the reversion to Kenitra/Settat's unpredictable operational-pressure profile; reinforce the new decision-rights matrix directly with the reverting sites.

OUTPUTS: A clean follow-up checkpoint; an unblocked sustainment sign-off. **RACSI:** R = CM, SUP · A = CM · C = FPO · S = PM · I = ES, EU

Pilot Success Masks a Site-Specific Risk

DESCRIPTION

Casablanca Finance's pilot succeeds cleanly, but Casablanca's steady, predictable finance-cycle pressure profile doesn't resemble Kenitra or Settat's plant-floor pressure profile — the exact difference that later drives Exception E1's regression at those sites specifically.

TRIGGER

A pilot site's clean success is used to assume readiness at sites with a materially different pressure profile.

TIMELINE IMPACT

No delay if caught before Full Transition — a planning correction, not a schedule change.

RECOVERY TASKS

Explicitly assess each remaining site's own pressure profile rather than assume the pilot's success generalizes.

OUTPUTS: A site-specific readiness assessment ahead of Full Transition. **RACSI:** R = CM, PM · A = CM · C = SUP · S = FPO · I = ES, EU

A Function Head Overwhelmed by Centralized Decision Volume

DESCRIPTION

Amina Sqalli, now receiving escalations from all three sites rather than one, cannot process the real decision volume alone — a capacity problem distinct from E1's habit-reversion problem, though both can look similar from outside.

TRIGGER

A Function Head's escalation backlog grows visibly following multi-site centralization.

TIMELINE IMPACT

Adds roughly one to two weeks while additional decision-support capacity is arranged.

RECOVERY TASKS

Add delegated decision authority for lower-stakes items; confirm the distinction between a capacity problem and a habit-reversion problem before prescribing a fix.

OUTPUTS: A revised decision-delegation threshold; a sustainable Function Head workload. **RACSI:** R = FPO, PM · A = CM · C = ES · S = SUP · I = ITL, EU

A Site Director Continues Deciding Unofficially

DESCRIPTION

A site director who lost formal decision authority continues making the same decisions informally — staff still bring them the question out of habit, and the director, not wanting to seem unhelpful, answers rather than redirecting.

TRIGGER

Decisions observed flowing through the old informal path despite the formal structure change.

TIMELINE IMPACT

No formal delay, but requires a direct conversation before it hardens into a permanent workaround.

RECOVERY TASKS

A direct conversation with the site director about redirecting rather than answering; reinforce the new path with staff directly.

OUTPUTS: A corrected decision-routing pattern. **RACSI:** R = CM, ES · A = ES · C = FPO · S = PM · I = SUP, EU

Reporting-Line Systems Lag Behind the Organizational Change

DESCRIPTION

HR and IT systems still show the old site-based reporting lines for several weeks after the organizational change takes effect, creating confusion about who formally approves what.

TRIGGER

A systems audit finds the org chart in HR/IT systems doesn't match the new reporting lines.

TIMELINE IMPACT

Adds roughly one week while systems are updated to match the organizational change.

RECOVERY TASKS

Update HR and IT systems promptly; communicate the interim gap directly so staff aren't confused by the mismatch.

OUTPUTS: Systems-of-record matching the real organizational structure. **RACSI:** R = ITL · A = PM · C = CM · S = FPO · I = ES, SUP, EU

A Second, Smaller Regression Signal After Handover

DESCRIPTION

A follow-up check three months after handover finds a partial slip at one site — not the full reversion E1 caught, but a specific decision type quietly drifting back, testing whether the standing monthly rhythm actually catches what the dedicated program team used to.

TRIGGER

A standing-rhythm governance check finds a partial, decision-type-specific drift.

TIMELINE IMPACT

No formal delay — resolved within the standing rhythm's own next cycle.

RECOVERY TASKS

Address the specific decision type directly; confirm the standing rhythm itself is catching what it's designed to catch.

OUTPUTS: A corrected drift; confirmed standing-rhythm effectiveness. **RACSI:** R = SUP, FPO · A = ES · C = CM · S = PM · I = ITL, EU

What This Training Covers

Per the E2E-OM chain, MP-05 is present — this training focuses on the new reporting-line mechanics and decision rights, not on convincing anyone the structure is correct.

Strategic Management

Cohort: Yassine Berrada (Sponsor) · Weeks 1-14

Curriculum Entry	Content Focus
Sponsoring a Reporting-Line Change	Why an operating model redesign needs sustained reinforcement, not a one-time announcement, to hold.
Reading M12's Regression-Risk Flag	How to read a sustainment checkpoint as real evidence — a blocked sign-off is the system working, not failing.

Operational Management

Cohort: Amina Sqalli (FPO), Loubna Tazi (SUP), other site directors' successors · Weeks 8-22

Curriculum Entry	Content Focus
Operating the New Decision-Rights Matrix	Exactly which decisions route where under the new structure — the direct prerequisite to avoiding Exception E1's reversion.
Redirecting Under Pressure	Specific coaching for the exact moment E1's regression happens — practicing the new routing rather than defaulting to habit.

Operations (Frontline)

Cohort: All 95 people-manager-level staff · Weeks 15-25

Curriculum Entry	Content Focus
Using the New Reporting Structure	Who to escalate to under the new model, reinforced with the same decision-rights reference card later redeployed in E1's recovery.

Why This Curriculum Is Shaped This Way

Training completion reaches 100% by Week 25 — before the Week 26 checkpoint reveals the regression. A fully trained population can still regress under real operational pressure, because Knowledge and Ability were never this case's binding constraint — Reinforcement was.

Which journi Modules Dominate This Archetype

M12 (Sustainment)	The 30-day post-transition checkpoint — where a High regression risk fires ALT-002.
M5 (ADKAR Engine)	Reinforcement tracked separately from Ability, since this archetype is where the two diverge.
M17 (WBS & Gantt)	The TPL-OM-7 template — Pilot Transition de-risks Full Transition, one site at a time.
M6 (Emotional & Transition Layer)	A premature "New Beginning" reading is exactly what a regression later contradicts.
M21 (Field Notes)	The decision-rights matrix and site-specific readiness findings, documented directly.
M14 (Analytics)	The Composite Readiness Index drop at the 30-day checkpoint — a real, not gradual, signal.

What This Case Fires

ALERTS THIS CASE EXERCISES

ALT-002 (Regression Risk Score Critical)

ALT-015 (Sustainment Sign-Off Blocked)

WHY

Built to run past its first sustainment checkpoint with High regression risk — the clearest real-data proof in the library that training completion alone does not guarantee reinforcement.

KEY TAKEAWAYS

What to Remember About This Archetype

- › A real 30-day sustainment checkpoint landing High regression risk, and a training-completion record (100% by Week 25) that proves Reinforcement, not Knowledge, was the actual gap — not glossed over as a clean success.
- › ADKAR Reinforcement dominates. Function Heads can pass every earlier checkpoint and still revert to old decision-making under real operational pressure — this archetype is built specifically to show that failure mode, not initial adoption, is the real test.
- › Built to run past its first sustainment checkpoint with High regression risk — the clearest real-data proof in the library that training completion alone does not guarantee reinforcement.



Operating Model Redesign

Regional Operating Model Redesign
