



Compliance-Driven Change

Loi 09-08 Data Protection Compliance Program

Bringing data handling into compliance with a fixed external deadline — the case where a Phase Gate closing as anything but Go has zero schedule slack to absorb it.

7

PHASES

64

WEEKS

6

EXCEPTIONS

3

TRAINING TIERS

PART 0 — PURPOSE

What This Guide Is, and How to Use It

WHAT THIS GUIDE IS

This deck follows the Loi 09-08 Data Protection Compliance Program — journi's Compliance-Driven Change archetype case — from tenant setup through ongoing compliance handover, bringing Bouregreg Group's data handling into compliance with a fixed CNDP audit deadline.

HOW TO USE IT

This program runs inside the same Bouregreg Group tenant as every other archetype in this series, from the very start of the tenant's life given the fixed external deadline. A reader with the tenant already set up skips straight to CM Project creation.

Verified Against journi's Real Source

Every journi module, field, and role named here is verified against journi's real source. This is journi's own stated case where ALT-009 (Phase Gate No-Go/Conditional) matters most precisely because it does not fire — every Phase Gate in this program's real record closes Go, on schedule.

RACSI CODES USED THROUGHOUT

ES = Executive Sponsor · CM = Change Manager · PM = Program/Project Manager · FPO = Functional Process Owner · ITL = IT/Technical Lead · SUP = Supervisor · EU = End User

Why This Case Matters

Every other program in this series can, in principle, slip a phase gate by a few weeks without an external consequence. This one cannot — the CNDP's own audit schedule is fixed and external, and there is no schedule buffer to absorb a Conditional or No-Go decision without missing a regulatory deadline.

The Case, in Brief

310 staff, HR, Sales, Customer Service

64 weeks (guide numbering, org-calendar aligned)

Bouregreg Group brings customer and employee personal-data handling into compliance with Loi 09-08, under CNDP oversight, for HR, Sales, and Customer Service (310 staff), closing every phase gate on schedule with controls live weeks ahead of the ERP program's own Deploy week.

What This Guide Proves, Concretely

Seven consecutive clean Phase Gate decisions, a controls-go-live date sequenced deliberately ahead of a sibling program's own critical week, and a first monitoring cycle confirming the controls hold under real operating conditions, not just at go-live.

Weighting for This Archetype

Awareness and Ability dominate; Desire matters least of any archetype. Staff do not need to want to comply — they need to know the rule and be able to follow it correctly. The Phase Gate itself is the framework that matters most, since the real risk here is schedule risk, not adoption risk.

The Composite Readiness Index, Read for This Case

The Composite Readiness Index reads high and stable throughout — Knowledge and Ability both clear quickly against specific, checkable rules, and there is no real emotional undercurrent for Bridges or Kübler-Ross to track. Benchmarking reads "In Line" or "Ahead" for the program's whole life.

The Existing Tenant, and Reading Paths by Role

THE EXISTING TENANT

This program runs inside the same tenant journi's Master User Guide builds, under the existing Bouregreg Manufacturing Maroc Organization — no new Organization needed.

READING PATHS, BY ROLE

- › A Change Manager running this program day to day: Part 2 once, then Part 4 in full.
- › A Program/Project Manager: Part 4's PM Track column and the Master WBS & Gantt.
- › An Executive Sponsor: Part 1, then Part 4's phase-opening narratives.
- › A Super Admin or Org Admin: Part 3.

The RACSI Team for This Program

Name	RACSI Code	Role
Karim Idrissi	ES	Sponsor — General Counsel/Chief Compliance Officer
Sanaa Bouzoubaa	CM	Change Manager
Hamza Alaoui	PM	Compliance Program Lead
Nadia Squalli	FPO	HR Data Privacy Lead
Reda Fassi	ITL	Data systems and access-control lead
Amine Tazi	SUP	Sales Operations Manager

Creating the CM Project

- 1** On Module 1 — Hierarchy, create the Loi 09-08 Data Protection Compliance Program CM Project under the existing Bouregreg Manufacturing Maroc Organization.
- 2** Set Change type: Compliance. Target population: "Any function touching personal data — HR, Sales, Customer Service (310)."
Business driver: "A scheduled CNDP audit against Loi 09-08 carries a fixed external deadline, not a discretionary program timeline."
- 3** Save. Lewin opens at Unfreeze, justified: "Opening Unfreeze at program start, Week 1, run from the very start of the tenant's life given the fixed external deadline."
- 4** On Module 17 — WBS & Gantt, load the TPL-COMP-7 phase template: Regulatory Requirement & Gap Analysis, Control Design, Control Implementation, Internal Audit/Independent Testing, Controls Go Live, First Monitoring Cycle, Ongoing Compliance Handover.

Charters for This Program

Charter	Accountable	Review Cadence
CHTR-01 Sponsorship / Leadership Charter	Karim Idrissi (ES)	Per Phase Gate
CHTR-03 Communication Charter	Sanaa Bouzoubaa (CM)	Per communication wave
CHTR-04 Organizational Impact Charter	Sanaa Bouzoubaa (CM)	On scope change
CHTR-08 Pulse / Interview Charter	Sanaa Bouzoubaa (CM)	Per phase gate + ad hoc

Setup Checklist

- ☒ Base tenant confirmed (Bouregreg Group, existing Organization)
- ☒ Compliance team accounts created
- ☒ CM Project created, Lewin opened at Unfreeze
- ☒ TPL-COMP-7 phase template loaded on M17
- ☒ Applicable Charters reviewed and accountable owners confirmed

PART 4 — WEEK-BY-WEEK TIMELINE

7 Phases, In Order



Total program length: 64 weeks (guide numbering, org-calendar aligned). Every phase below is walked in detail across the next slides — normal flow first, then six exceptions in full operational detail.

Regulatory Requirement & Gap Analysis

Weeks 1-14


NARRATIVE

Establishes exactly what Loi 09-08 requires and where current data-handling practice falls short, across HR, Sales, and Customer Service.

Key Moments in This Phase

Week	What Happens
Week 1	Kickoff; Lewin opens at Unfreeze.
Week 5	Gap analysis begins across all three functions.
Week 14	Phase Gate: clean Go.

Framework Snapshot

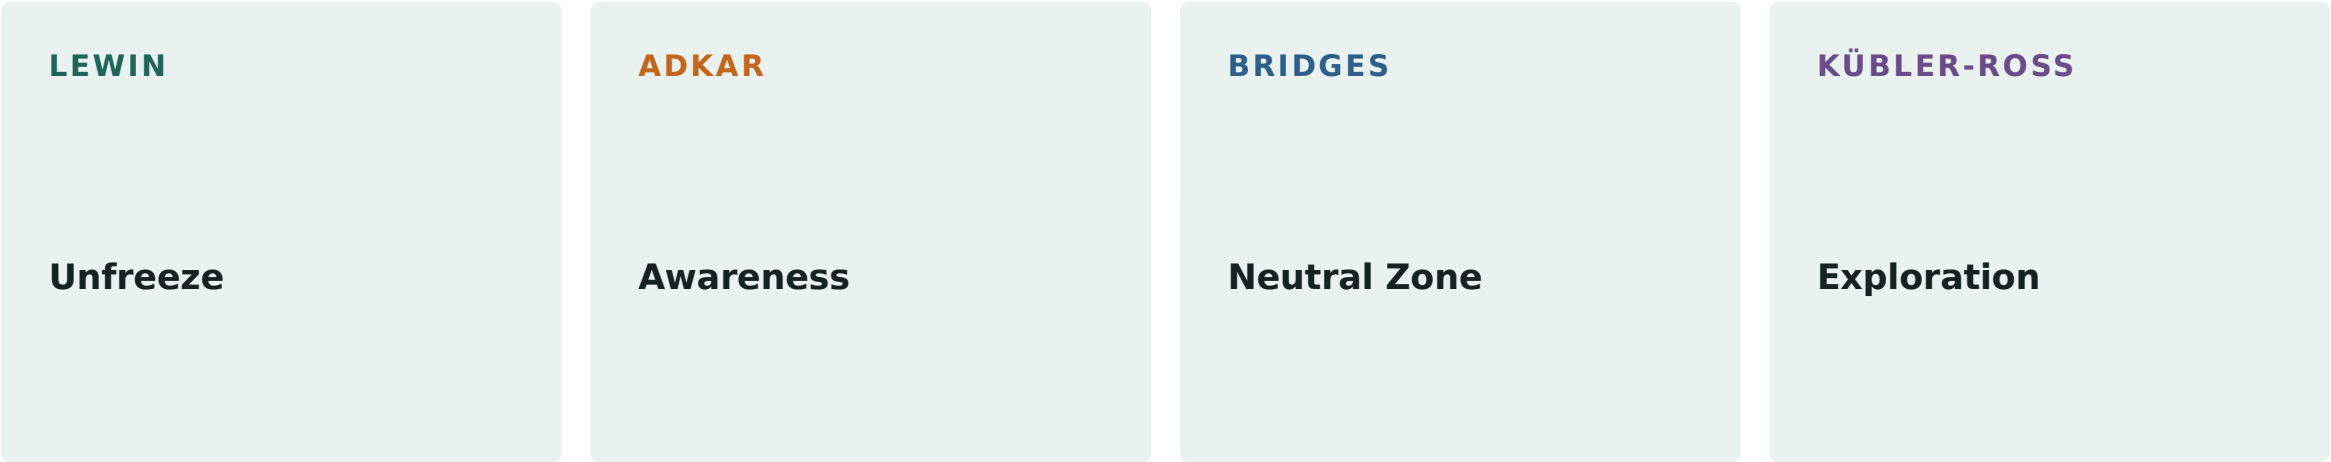

KEY TECHNIQUE THIS PHASE

Statutory clause mapping: Map every Loi 09-08 article to a specific business process it governs.

Control Design

Weeks 12-28

NARRATIVE


Designs the specific controls — retention rules, access restrictions, subject-access-request processes — that close the gaps found.

Key Moments in This Phase

Week	What Happens
Week 15	Retention controls designed for HR personnel records.
Week 19	Subject-access-request process designed.
Week 28	Phase Gate: clean Go.

PHASE 2 · CONTROL DESIGN

Framework Snapshot

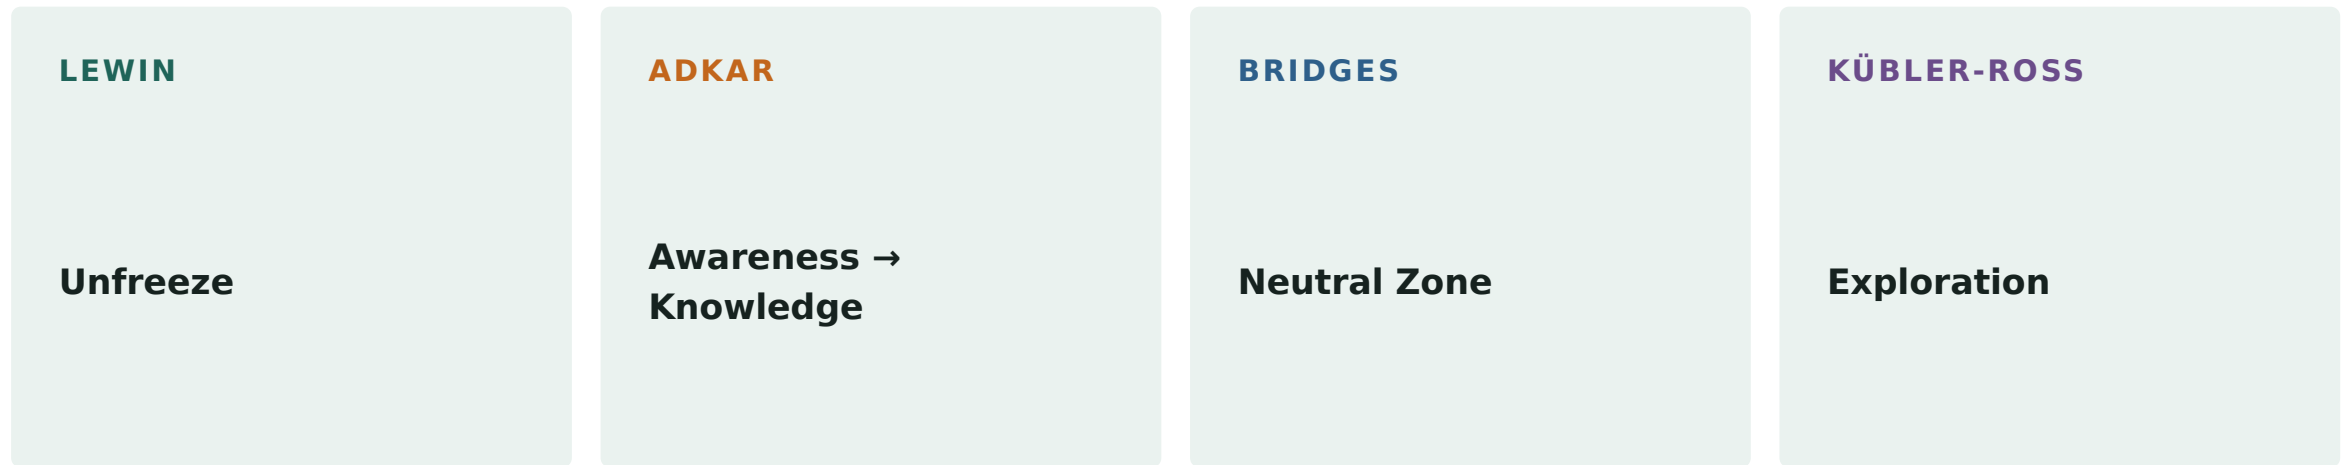

KEY TECHNIQUE THIS PHASE

Control catalogue design: Design specific, checkable controls closing each identified gap.

Control Implementation

Weeks 26–40

NARRATIVE

Implements the designed controls plant-wide across all three functions.

PHASE 3 · CONTROL IMPLEMENTATION

Key Moments in This Phase

Week	What Happens
Week 30	Access-restriction controls implemented across HR, Sales, CS.
Week 36	Retention schedules operational.
Week 40	Phase Gate: clean Go.

PHASE 3 · CONTROL IMPLEMENTATION

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Function-by-function rollout: Implement controls across HR, Sales, and Customer Service without disrupting daily operations.

Internal Audit / Independent Testing

Weeks 38–48


NARRATIVE

Independently tests the implemented controls before go-live — journi's own independence discipline is the point.

Key Moments in This Phase

Week	What Happens
Week 42	Independent testing team confirmed genuinely independent of implementation.
Week 46	Testing findings closed.
Week 48	Phase Gate: clean Go.

Framework Snapshot

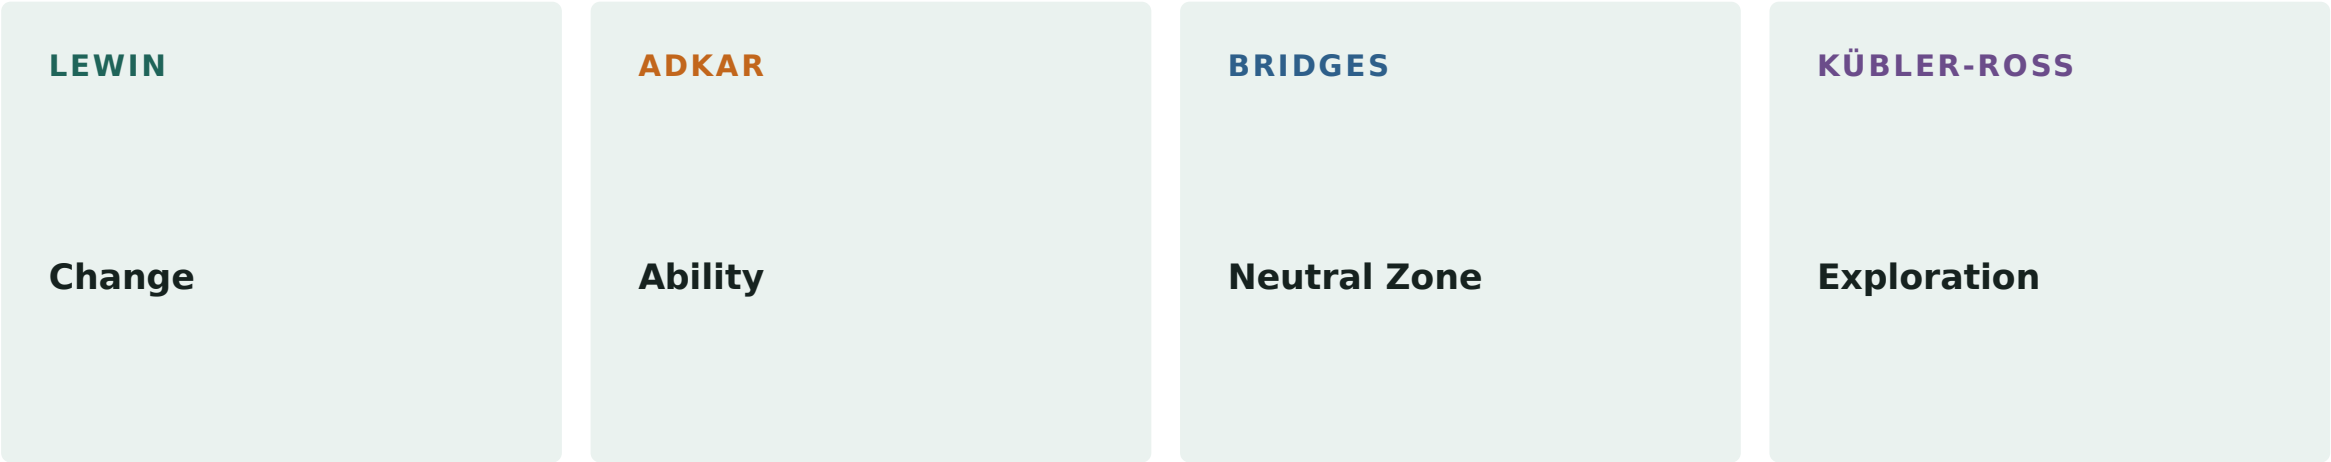

KEY TECHNIQUE THIS PHASE

Independence-verified testing: Confirm controls work, tested by a team genuinely independent of implementation.

Controls Go Live

Weeks 46-52


NARRATIVE

Goes live with the tested controls, timed deliberately ahead of the ERP program's own Deploy week so the two never compete for the same Legal/Compliance attention.

Key Moments in This Phase

Week	What Happens
Week 48	Controls go live across all three functions.
Week 52	Phase Gate: clean Go.

Framework Snapshot

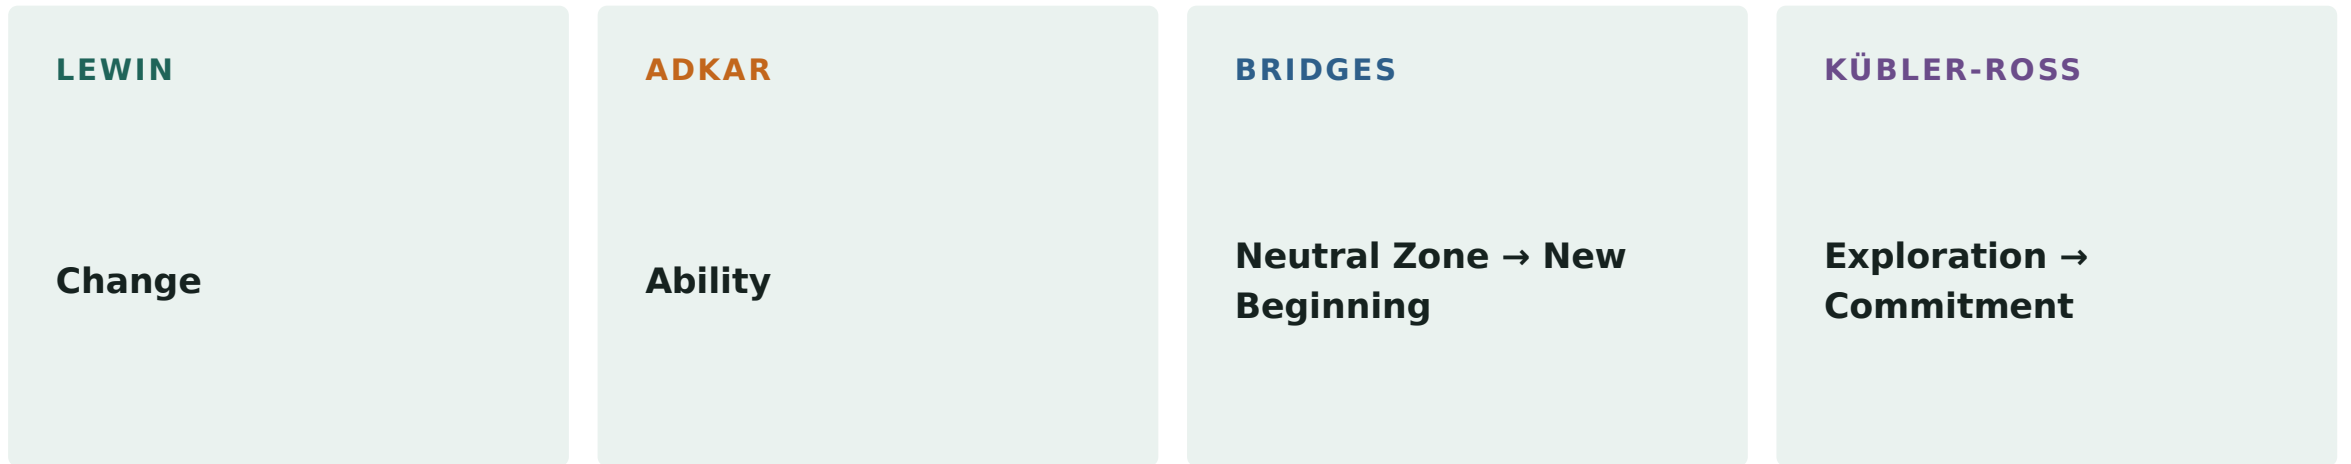

KEY TECHNIQUE THIS PHASE

Deliberately sequenced go-live: Time go-live ahead of the ERP program's own Deploy week to avoid competing for Legal/Compliance attention.

First Monitoring Cycle

Weeks 50-58

NARRATIVE

Confirms the controls hold under real operating conditions, not just at the moment of go-live.


PHASE 6 · FIRST MONITORING CYCLE

Key Moments in This Phase

Week	What Happens
Week 52	First monitoring cycle begins.
Week 58	Phase Gate: clean Go — seventh consecutive clean gate.

PHASE 6 · FIRST MONITORING CYCLE

Framework Snapshot

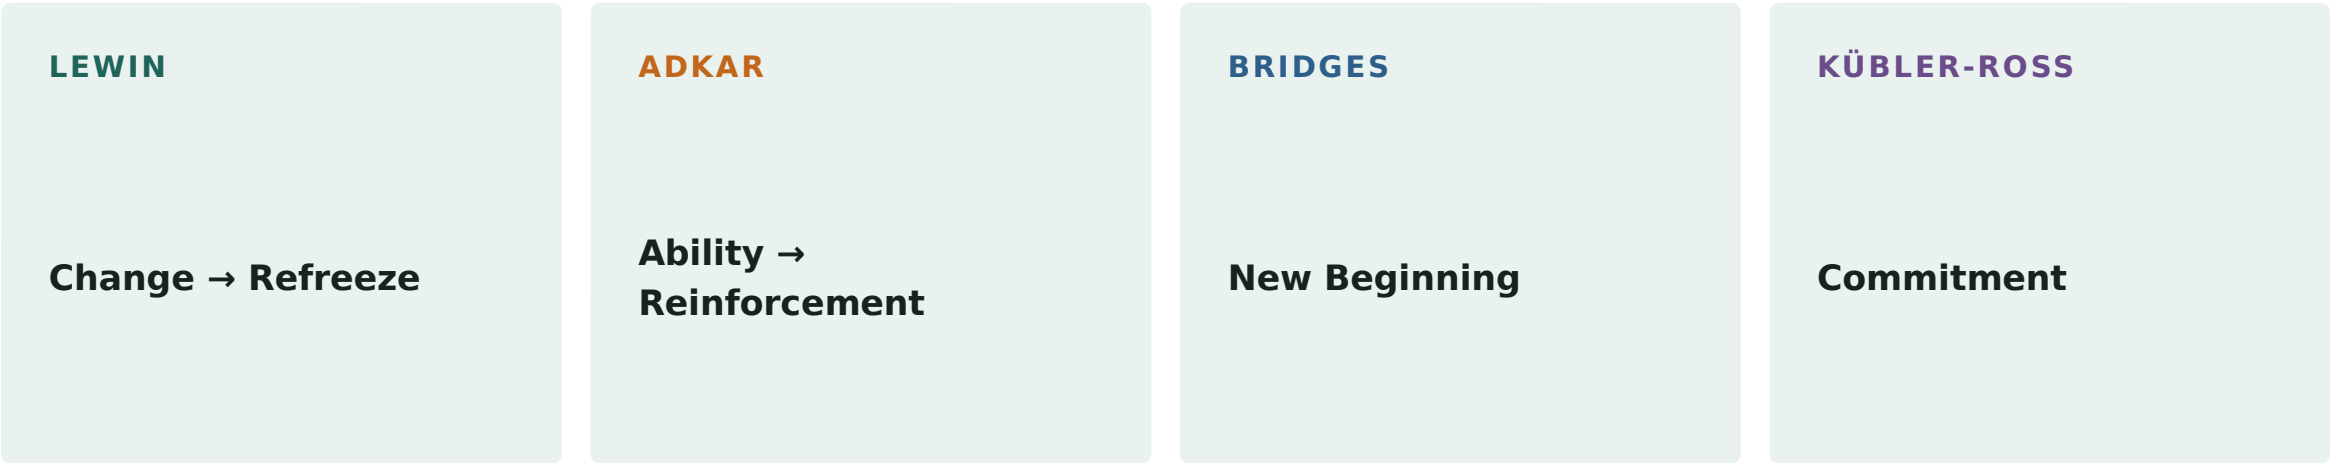

KEY TECHNIQUE THIS PHASE

Real-condition control monitoring: Confirm controls hold under real operating conditions, not just at go-live.

Ongoing Compliance Handover

Weeks 56–64, open-ended beyond


NARRATIVE

Hands ongoing compliance monitoring to standing operations — continuing beyond Week 64 since a regulatory obligation has no project end date.

Key Moments in This Phase

Week	What Happens
Week 60	Ongoing handover package delivered.
Week 64	Program formally closes; compliance monitoring continues beyond, by design.

Framework Snapshot

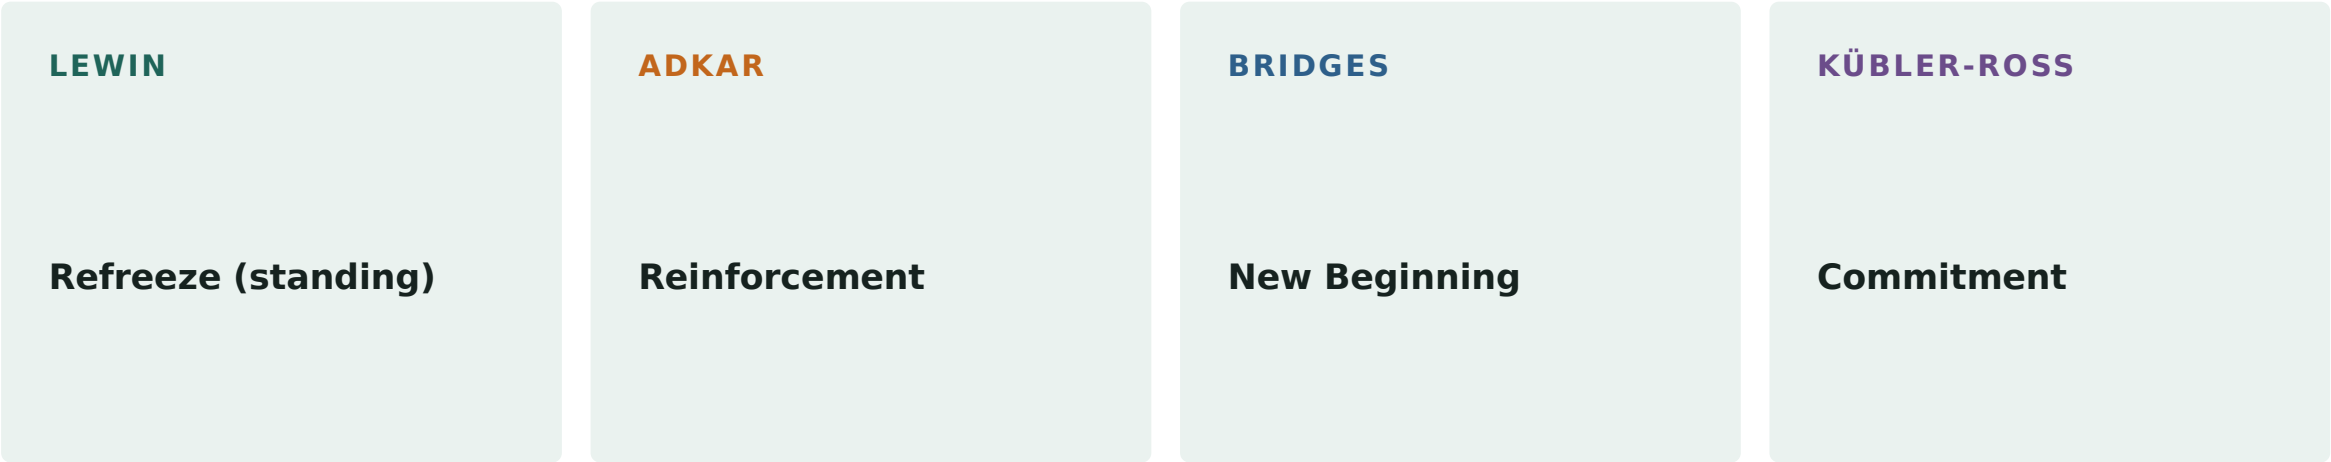

KEY TECHNIQUE THIS PHASE

Standing compliance monitoring handoff: Transfer ongoing monitoring to standing operations, since the obligation has no end date.

Every Phase, Across the Four Frameworks

Phase	Week(s)	Lewin	ADKAR	Bridges	Kübler-Ross
Regulatory Requirement & Gap Analysis	Weeks 1-14	Unfreeze	Awareness	Neutral Zone	Exploration
Control Design	Weeks 12-28	Unfreeze	Awareness → Knowledge	Neutral Zone	Exploration
Control Implementation	Weeks 26-40	Change	Knowledge → Ability	Neutral Zone	Exploration
Internal Audit / Independent Testing	Weeks 38-48	Change	Ability	Neutral Zone	Exploration
Controls Go Live	Weeks 46-52	Change	Ability	Neutral Zone → New Beginning	Exploration → Commitment
First Monitoring Cycle	Weeks 50-58	Change → Refreeze	Ability → Reinforcement	New Beginning	Commitment
Ongoing Compliance Handover	Weeks 56-64+	Refreeze (standing)	Reinforcement	New Beginning	Commitment

Every Phase, Techniques and Tools

Phase	Week(s)	Technique	Goal	Tool
Regulatory Requirement & Gap Analysis	Weeks 1-14	Statutory clause mapping	Map every Loi 09-08 article to a specific business process it governs.	LibreOffice Calc
Control Design	Weeks 12-28	Control catalogue design	Design specific, checkable controls closing each identified gap.	M21 (Field Notes)
Control Implementation	Weeks 26-40	Function-by-function rollout	Implement controls across HR, Sales, and Customer Service without disrupting daily operations.	M17 (WBS & Gantt)
Internal Audit / Independent Testing	Weeks 38-48	Independence-verified testing	Confirm controls work, tested by a team genuinely independent of implementation.	M19 (Charter Registry)
Controls Go Live	Weeks 46-52	Deliberately sequenced go-live	Time go-live ahead of the ERP program's own Deploy week to avoid competing for Legal/Compliance attention.	M3 (Initiative Registry)
First Monitoring Cycle	Weeks 50-58	Real-condition control monitoring	Confirm controls hold under real operating conditions, not just at go-live.	M12 (Sustainment)
Ongoing Compliance Handover	Weeks 56-64+	Standing compliance monitoring handoff	Transfer ongoing monitoring to standing operations, since the obligation has no end date.	M12 (Sustainment)

PART 4 — SIX EXCEPTIONS, IN DETAIL

**Six Realistic Contingencies — None of Which Actually
Occurred**

A Regulatory Clause Misread During Gap Analysis

DESCRIPTION

The gap analysis initially reads a Loi 09-08 retention-period clause more leniently than the CNDP's own published guidance actually requires — a misreading that would only surface when Legal's own independent review catches it late in Phase 1. This did not occur.

TRIGGER

Legal's independent review of the gap analysis catching a clause misreading.

TIMELINE IMPACT

Would extend Phase 1 by one to two weeks while the retention-period control is redesigned against the correct reading.

RECOVERY TASKS

Legal independently re-verifies every retention-period clause reading before Phase 1 closes.

OUTPUTS: A corrected, Legal-verified gap analysis. **RACSI:** R = CM, ES · A = ES · C = FPO · S = PM · I = ITL, SUP, EU

Control Design Insufficient for a Specific Data Type

DESCRIPTION

The general control catalogue, designed for standard HR and customer data, turns out insufficient for health-related data HR holds for occupational-medicine purposes — which Loi 09-08 treats more strictly. This did not occur.

TRIGGER

A specific data category found to need stricter controls than the general catalogue provides.

TIMELINE IMPACT

Would add a targeted control-design cycle for the specific data type, roughly one to two weeks.

RECOVERY TASKS

Design a stricter, data-type-specific control layer on top of the general catalogue.

OUTPUTS: A data-type-specific control addendum. **RACSI:** R = FPO, ITL · A = CM · C = ES · S = PM · I = SUP, EU

A Third-Party Data Processor Missed From Scope

DESCRIPTION

A payroll vendor processing HR personal data on Bouregreg's behalf is missed from the original scope, discovered only when the control catalogue's access-restriction design realizes it has no way to govern a third party's own systems. This did not occur.

TRIGGER

A scope review discovering a third-party processor with no governing control.

TIMELINE IMPACT

Would require a vendor-compliance addendum, adding two to three weeks.

RECOVERY TASKS

Extend the control catalogue to cover third-party processor governance via contractual and technical controls.

OUTPUTS: A vendor-compliance control addendum. **RACSI:** R = ES, ITL · A = ES · C = CM · S = PM · I = FPO, SUP, EU

The Independent Testing Team Isn't Genuinely Independent

DESCRIPTION

A staff member assigned to the "independent" testing team turns out to have also done configuration work on one of the controls being tested — a genuine independence failure. This did not occur.

TRIGGER

A conflict-of-interest review finding testing-team overlap with implementation.

OUTPUTS: A verified, genuinely independent test result. **RACSI:** R = CM · A = CM · C = ES · S = PM · I = FPO, ITL, SUP, EU

TIMELINE IMPACT

Would require reassigning the affected control's testing, adding roughly one week.

RECOVERY TASKS

Reassign the specific control's testing to a genuinely independent reviewer.

A Data Incident During Implementation, Before Controls Are Live

DESCRIPTION

A data-handling incident occurs while implementation is still in progress and the new controls aren't live yet, forcing an unplanned test of whether the incident-response process works before it was scheduled to be tested. This did not occur.

TRIGGER

A reportable data-handling incident during Control Implementation.

TIMELINE IMPACT

Would not delay the schedule directly, but would force an immediate, out-of-cycle incident response.

RECOVERY TASKS

Run the incident response using whatever process exists at that point; accelerate the specific control that would have prevented the incident.

OUTPUTS: A documented incident response; an accelerated control fix. **RACSI:** R = ITL, FPO · A = ES · C = CM · S = PM · I = SUP, EU

CNDP Shifts the Audit Date or Scope Mid-Program

DESCRIPTION

The CNDP itself moves the audit date earlier, or expands its stated scope, partway through the program — an external schedule shock this program's own design has no control over. This did not occur.

TRIGGER

A formal CNDP notice changing the audit date or scope.

TIMELINE IMPACT

Would force compressing every remaining phase proportionally — the single hardest scenario in the contingency list.

RECOVERY TASKS

Immediately re-baseline the WBS against the new date; escalate to the Sponsor and Steering Committee for an explicit prioritization decision.

OUTPUTS: A re-baselined schedule; a documented prioritization decision if full scope cannot be met. **RACSI:** R = PM, CM · A = ES · C = FPO, ITL · S = SUP · I = EU

What This Training Covers

Per the E2E-COMP chain, MP-05 is present — but unlike the Cultural archetype's persuasion-heavy curriculum, this training is built entirely around specific, checkable compliance behaviors, verifiable against the same control checklist independent testers use.

Strategic Management

Cohort: Karim Idrissi (Sponsor), function heads · Weeks 1-16

Curriculum Entry	Content Focus
Sponsoring a Fixed-Deadline Compliance Program	Why a CNDP-facing program cannot treat its own schedule as negotiable.
Reading a Phase Gate Decision Record	How to read Go/Conditional/No-Go as accountable evidence.

Operational Management

Cohort: Nadia Squalli (FPO), Amine Tazi (SUP), CS data-privacy coordinator · Weeks 14-52

Curriculum Entry	Content Focus
Operating the Control Design Checklist	Consent capture, data minimization, and retention limits as specific, checkable steps.
Preparing a Function for Independent Testing	What testers actually check, and how to have evidence ready.
Running the First Monitoring Cycle	Keeping the checklist live after go-live, not just at the moment of testing.

Operations (Frontline)

Cohort: All 310 HR, Sales, and Customer Service staff · Weeks 40-52

Curriculum Entry	Content Focus
Handling a Data Subject Access Request	The specific, checkable steps for responding within the legally required window.
Data Minimization in Daily Sales and CRM Entry	Exactly what personal-data fields are and are not to be captured.
Recognizing and Reporting a Suspected Data Incident	A specific action sequence, rehearsed, not a general "be careful" message.
Retention Schedule Compliance	Specific retention periods and deletion triggers per data category.

Why This Curriculum Is Shaped This Way

Training completion here is a direct, auditable input to the same evidence package CNDP itself may review — unlike every other guide in this series, this program carries no coaching or reinforcement track of its own, because a compliance behavior either happened correctly or it did not.

Which journi Modules Dominate This Archetype

M17 (WBS & Gantt)	The TPL-COMP-7 template — every phase gate dated against a fixed external deadline.
M5 (ADKAR Engine)	Awareness and Ability scored against specific, checkable rules — not general sentiment.
M19 (Charter Registry)	Formal charters matter more here given the external regulator relationship.
M9 (Training)	Checkable-behavior training — data handling, retention, access requests — not persuasion.
M12 (Sustainment)	The First Monitoring Cycle — the direct mechanism behind seven consecutive clean gates.
M3 (Initiative Registry)	A deliberately sequenced go-live date, timed against a sibling program's own critical week.

What This Case Proves By Not Firing

NO LIVE ALERT FIRES IN THIS PROGRAM'S REAL RECORD

Stated plainly, not manufactured — a clean record reported as a clean record.

WHY

None fire in this program's real record — every Phase Gate closes Go, on schedule, which is the entire point: ALT-009 (Phase Gate No-Go/Conditional) matters most here precisely because it does not fire.

KEY TAKEAWAYS

What to Remember About This Archetype

- › Seven consecutive clean Phase Gate decisions, a controls-go-live date sequenced deliberately ahead of a sibling program's own critical week, and a first monitoring cycle confirming the controls hold under real operating conditions, not just at go-live.
- › Awareness and Ability dominate; Desire matters least of any archetype. Staff do not need to want to comply — they need to know the rule and be able to follow it correctly. The Phase Gate itself is the framework that matters most, since the real risk here is schedule risk, not adoption risk.
- › None fire in this program's real record — every Phase Gate closes Go, on schedule, which is the entire point: ALT-009 (Phase Gate No-Go/Conditional) matters most here precisely because it does not fire.



Compliance-Driven Change

Loi 09-08 Data Protection Compliance Program
