



Cultural / Values Transformation

One Bouregreg: Post-Acquisition Culture Integration

Aligning two distinct ways of working under one set of values after an acquisition — not a system or process change at all.

7

PHASES

78

WEEKS

6

EXCEPTIONS

3

TRAINING TIERS

PART 0 — PURPOSE

What This Guide Is, and How to Use It

WHAT THIS GUIDE IS

This deck follows One Bouregreg: Post-Acquisition Culture Integration — journi's Cultural/Values Transformation archetype case — from tenant setup through institutionalization, aligning two distinct ways of working under one set of values after an acquisition.

HOW TO USE IT

This program runs inside the same Bouregreg Group tenant as every other archetype in this series, six months into the ERP program's own life. A reader with the tenant already set up skips straight to CM Project creation.

Verified Against journi's Real Source

Every journi module, field, and role named here is verified against journi's real source. This is journi's own stated case for ALT-003 (Sponsor Coverage Gap) — this deck shows exactly how a newly appointed Sponsor's slow start fires the alert and is corrected.

RACSI CODES USED THROUGHOUT

ES = Executive Sponsor · CM = Change Manager · PM = Program/Project Manager · FPO = Functional Process Owner · ITL = IT/Technical Lead · SUP = Supervisor · EU = End User

Why This Case Matters

A newly appointed Sponsor with zero logged actions damages Bridges and Kübler-Ross — this archetype's dominant frameworks — faster than any other, because a cultural program's central evidence is leadership visibility, not a training-completion metric.

The Case, in Brief

260 staff (acquired Tangier team) + Bouregreg counterparts

78 weeks (guide numbering, 18-month horizon)

Six months into the ERP program, Bouregreg Group acquires a smaller regional competitor's Tangier distribution operation; this project aligns two distinct ways of working under one set of values within an 18-month horizon, targeting the acquired Tangier team plus their new Bouregreg counterparts.

What This Guide Proves, Concretely

A real Sponsor Coverage Gap that fires and is corrected, a real Desire stall traced to a named, acquisition-specific fear, and a Refreeze signed only once the evidence — not the acquisition's own press-release timeline — supports it.

Weighting for This Archetype

Bridges and Kübler-Ross dominate. Identity and emotional integration matter more than any specific skill here — a newly appointed Sponsor with zero logged actions damages exactly these two frameworks fastest, which is why this archetype is built to fire ALT-003 early rather than later.

The Composite Readiness Index, Read for This Case

The Composite Readiness Index's training-completion term rises well ahead of its Bridges/Kübler-Ross-driven cultural terms from Week 35 onward — a deliberate, predicted gap: a high training-completion reading confirms staff can use shared systems, not that the four target values have taken hold.

PART 3 — TENANT AND ADMIN SETUP

The Existing Tenant, and Reading Paths by Role

THE EXISTING TENANT

This program runs inside the same tenant journi's Master User Guide builds, under the existing Bouregreg Manufacturing Maroc Organization — no new Organization needed.

READING PATHS, BY ROLE

- › A Change Manager running this program day to day: Part 2 once, then Part 4 in full.
- › A Program/Project Manager: Part 4's PM Track column and the Master WBS & Gantt.
- › An Executive Sponsor: Part 1, then Part 4's phase-opening narratives.
- › A Super Admin or Org Admin: Part 3.

The RACSI Team for This Program

Name	RACSI Code	Role
Karim Fassi	ES	Sponsor — newly appointed integration Sponsor
Nadia Chraibi	CM	Change Manager
Youssef Idrissi	PM	Integration Program Manager
Amal Ziani	FPO	HR Business Partner for the integration
Hicham Bennani	ITL	Systems/tooling lead
Fatima-Zahra Idrissi	SUP	Tangier Distribution Center site lead
Rachid Amrani	SUP	Casablanca supply chain/logistics lead

Creating the CM Project

- 1** On Module 1 — Hierarchy, create the One Bouregreg: Culture Integration CM Project under the existing Bouregreg Manufacturing Maroc Organization — no new tenant needed, despite the acquisition.
- 2** Set Change type: Cultural / Values Transformation. Target population: "Acquired Tangier team (260) plus Bouregreg counterparts." Business driver: "The acquisition's stated synergies depend on the two workforces actually operating as one company within 18 months."
- 3** Save. Lewin opens at Unfreeze, justified against the acquisition's own closing date, six months into the ERP program's own life.
- 4** On Module 17 — WBS & Gantt, load the TPL-CULT-7 phase template: Diagnosis, Target Values Design, Leadership Modeling & Reinforcement Build, Pilot Cohort, Organization-Wide Rollout, Reinforcement Through Skepticism, Institutionalization.

Charters for This Program

Charter	Accountable	Review Cadence
CHTR-01 Sponsorship / Leadership Charter	Karim Fassi (ES)	Per Phase Gate
CHTR-03 Communication Charter	Nadia Chraibi (CM)	Per communication wave
CHTR-04 Organizational Impact Charter	Nadia Chraibi (CM)	On scope change
CHTR-08 Pulse / Interview Charter	Nadia Chraibi (CM)	Per phase gate + ad hoc

Setup Checklist

- ☒ Base tenant confirmed (Bouregreg Group, existing Organization)
- ☒ Integration program team accounts created across both legacy workforces
- ☒ CM Project created, Lewin opened at Unfreeze
- ☒ TPL-CULT-7 phase template loaded on M17
- ☒ Applicable Charters reviewed and accountable owners confirmed

PART 4 — WEEK-BY-WEEK TIMELINE

7 Phases, In Order



Total program length: 78 weeks (guide numbering, 18-month horizon). Every phase below is walked in detail across the next slides — normal flow first, then six exceptions in full operational detail.

Diagnosis

Weeks 1-10

NARRATIVE

Characterizes two starting cultures, not one — Bouregreg's plant-floor culture and Tangier's distribution-operation culture — before any values are proposed.


PHASE 1 · DIAGNOSIS

Key Moments in This Phase

Week	What Happens
Week 1	Kickoff; Lewin opens at Unfreeze.
Week 1-6	Karim Fassi logs zero visible actions on M7 — Exception E1 opens.
Week 10	Diagnosis gate closes; dual-culture baseline complete.

PHASE 1 · DIAGNOSIS

Framework Snapshot

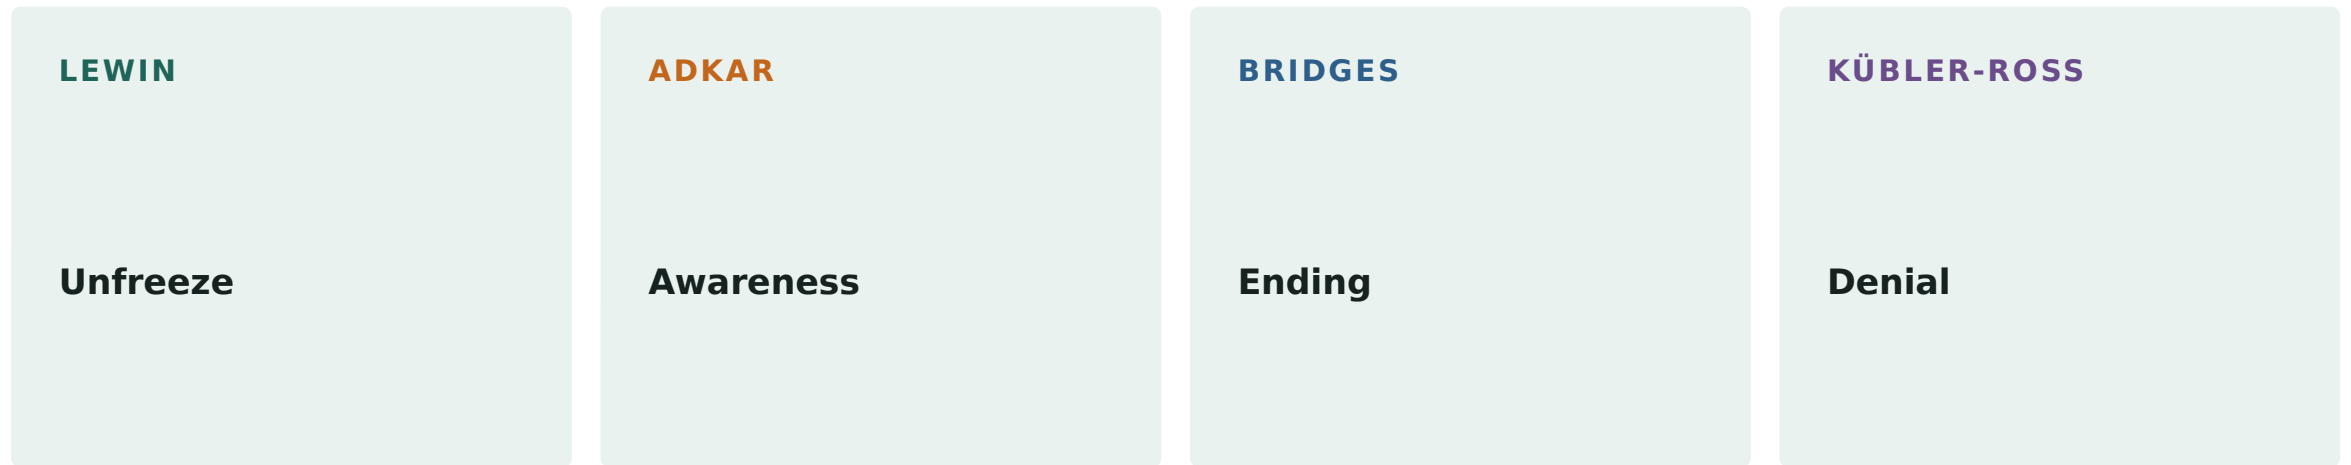

KEY TECHNIQUE THIS PHASE

Dual-culture baseline mapping: Characterize two starting cultures side by side before proposing any values.

Target Values Design

Weeks 4-16


NARRATIVE

Designs the four target values with locked, bilingual-tested behavior anchors — not aspirational language alone.

Key Moments in This Phase

Week	What Happens
Week 6	Sponsor Coverage Gap resolved via a direct, visible town hall.
Week 10	Steering Committee formally seated.
Week 16	All four values carry locked, bilingual-tested behavior anchors.

Framework Snapshot

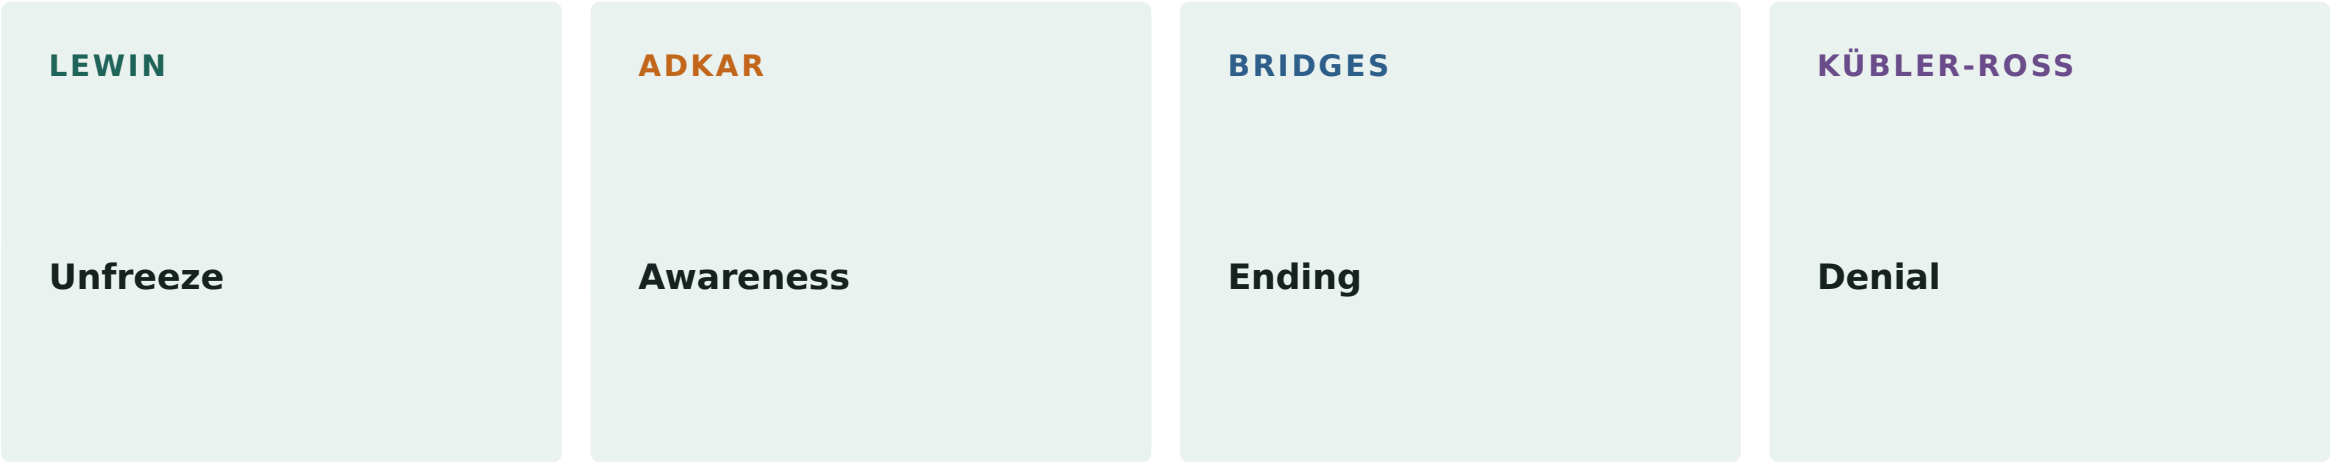

KEY TECHNIQUE THIS PHASE

Bilingual behavior-anchor design: Lock each value to a specific, testable behavior in both languages, not aspirational text.

Leadership Modeling & Reinforcement Build

Weeks 12-26


NARRATIVE

Builds the recognition and escalation reinforcement system while leaders model the target values directly.

Key Moments in This Phase

Week	What Happens
Week 19	Recognition system pilot-tested with a small mixed Tangier/Casablanca group.
Week 22	Manager coaching circles begin.
Week 26	All 8 leaders (4 per side) have logged specific commitments.

Framework Snapshot

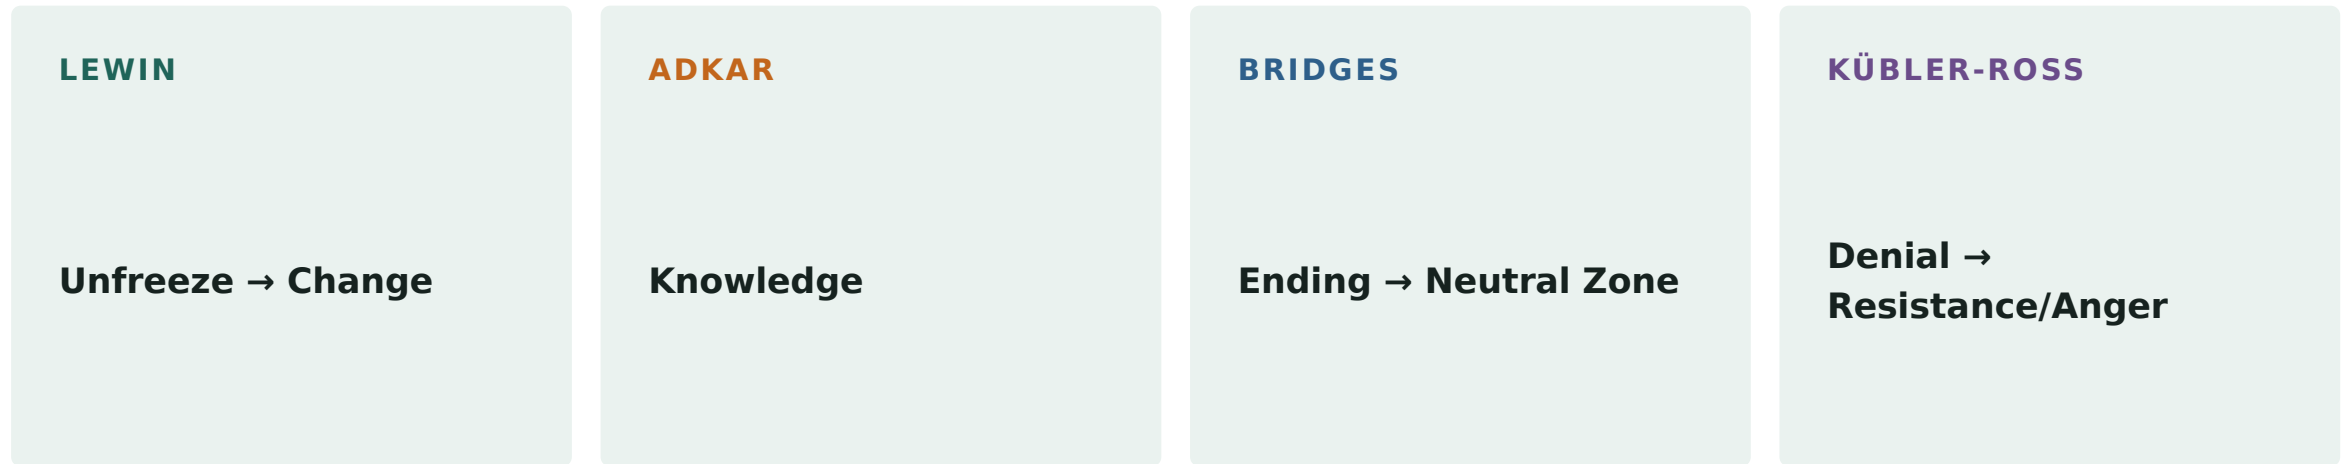

KEY TECHNIQUE THIS PHASE

Paired-leader modeling: Have leaders from both legacy organizations model values jointly, not separately.

Pilot Cohort

Weeks 20-34

NARRATIVE

Pairs one Tangier team with one legacy Bouregreg team as a genuine working pair, not two isolated pilots.

PHASE 4 · PILOT COHORT

Key Moments in This Phase

Week	What Happens
Week 20	Pilot pair selected: Tangier Dispatch and Casablanca Supply Chain Liaison.
Week 25	Tangier Dispatch's Desire drops to 2 over an unconfirmed consolidation rumor — Exception E2 opens.
Week 34	Pilot cohort gate closes.

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Genuine cross-site pairing: Pair one Tangier team with one Bouregreg team as a real working relationship, not two isolated pilots.

Organization-Wide Rollout

Weeks 32-50

NARRATIVE

Rolls the values program out in two waves — where a Divergence Pattern can surface in a cohort with less direct Tangier contact.

Key Moments in This Phase

Week	What Happens
Week 42	A Wave 2 Casablanca cohort fires ALT-001 (Divergence Pattern Detected) — Exception E3 opens.
Week 47	Divergence resolved through a real cross-site paired exposure.
Week 50	Rollout gate closes.

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Two-wave staged rollout: Roll out in waves so later cohorts benefit from earlier lessons.

Reinforcement Through Skepticism

Weeks 45-68

NARRATIVE

Holds the values program's reinforcement work steady against real skepticism — including a Board announcement racing ahead of the program's own evidence.


PHASE 6 · REINFORCEMENT THROUGH SKEPTICISM

Key Moments in This Phase

Week	What Happens
Week 56	A public "Integration Complete" statement outpaces journi's own Lewin reading — Exception E4 opens.
Week 65	A promotion decision regresses Tangier sentiment sharply — Exception E5 opens.
Week 68	Reinforcement phase gate closes.

PHASE 6 · REINFORCEMENT THROUGH SKEPTICISM

Framework Snapshot

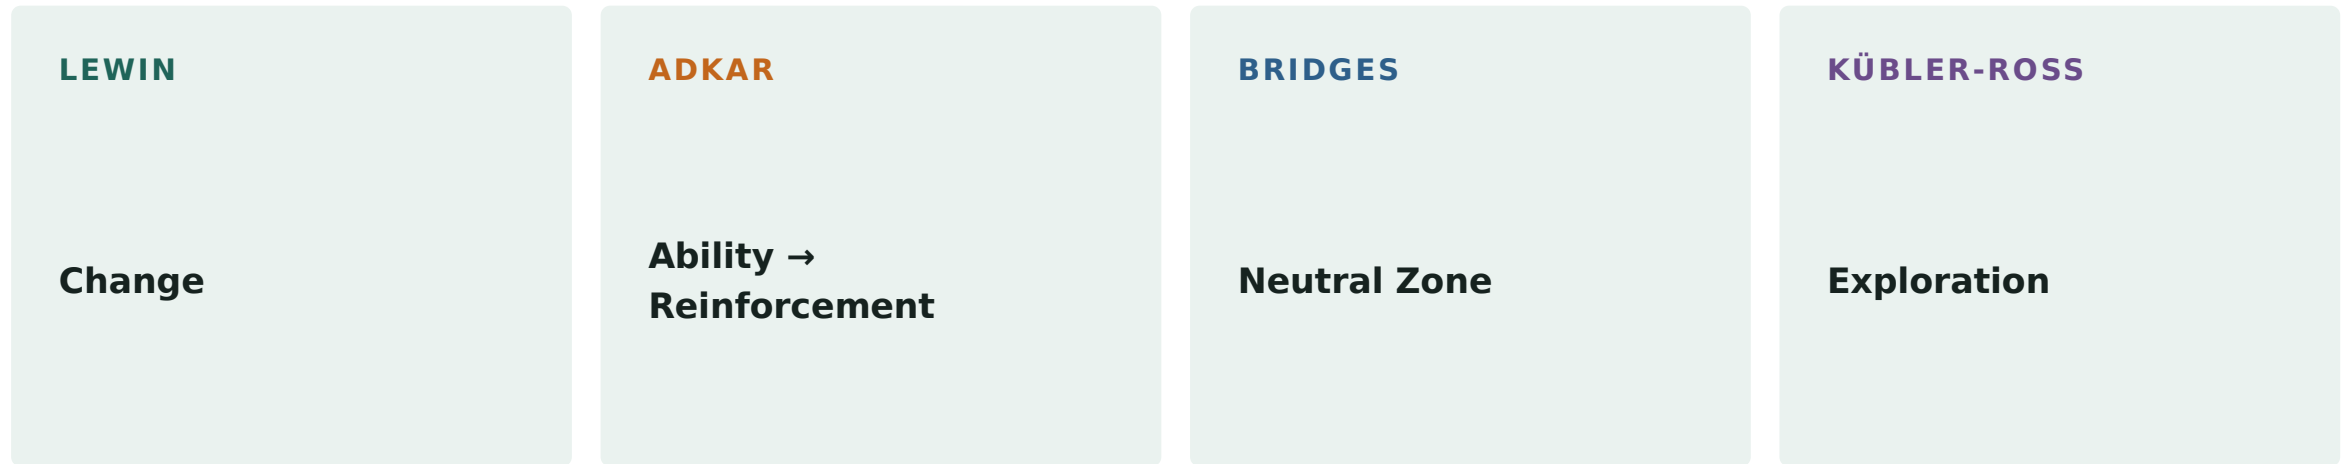

KEY TECHNIQUE THIS PHASE

Two-clock discipline against a public announcement: Separate a corporate/brand milestone from journi's own evidence-based Refreeze call.

Institutionalization

Weeks 62–78, open-ended beyond


NARRATIVE

Confirms the four values are genuinely the new normal — closing Refreeze from evidence, not the acquisition's own press-release timeline.

Key Moments in This Phase

Week	What Happens
Week 70	Cross-site cohort divergence (Exception E6) still being tracked as this phase closes.
Week 78	Refreeze called from evidence; reinforcement continues well past the ERP program's own close.

Framework Snapshot

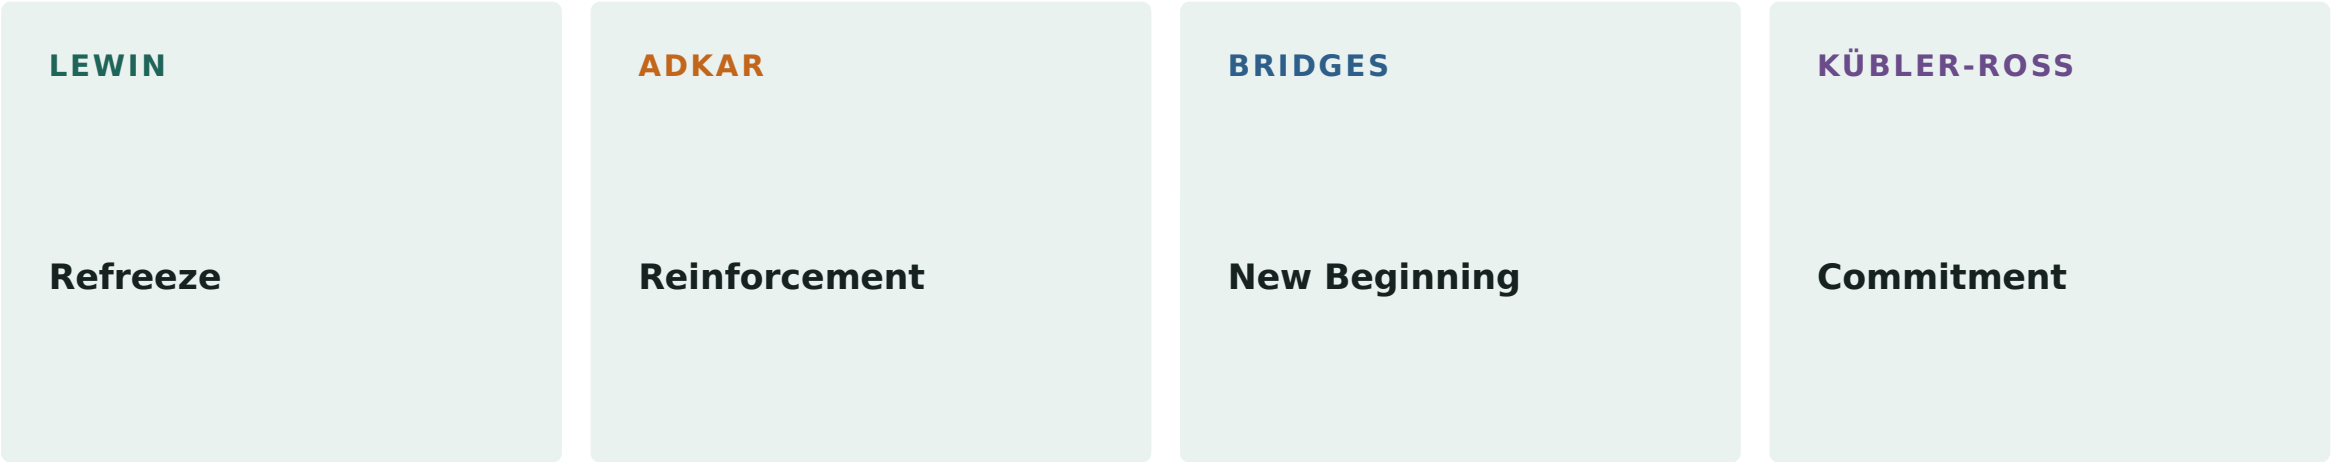

KEY TECHNIQUE THIS PHASE

Cross-site CRI divergence tracking: Track a structural, slow-moving cohort gap rather than treat it as a single-week trigger.

Every Phase, Across the Four Frameworks

Phase	Week(s)	Lewin	ADKAR	Bridges	Kübler-Ross
Diagnosis	Weeks 1-10	Unfreeze	Awareness	Ending	Denial
Target Values Design	Weeks 4-16	Unfreeze	Awareness	Ending	Denial
Leadership Modeling & Reinforcement Build	Weeks 12-26	Unfreeze → Change	Knowledge	Ending → Neutral Zone	Denial → Resistance/Anger
Pilot Cohort	Weeks 20-34	Change	Knowledge → Desire	Neutral Zone	Resistance/Anger
Organization-Wide Rollout	Weeks 32-50	Change	Knowledge → Ability	Neutral Zone	Resistance/Anger → Exploration
Reinforcement Through Skepticism	Weeks 45-68	Change	Ability → Reinforcement	Neutral Zone	Exploration
Institutionalization	Weeks 62-78+	Refreeze	Reinforcement	New Beginning	Commitment

Every Phase, Techniques and Tools

Phase	Week(s)	Technique	Goal	Tool
Diagnosis	Weeks 1-10	Dual-culture baseline mapping	Characterize two starting cultures side by side before proposing any values.	M4 (Stakeholder Mapping)
Target Values Design	Weeks 4-16	Bilingual behavior-anchor design	Lock each value to a specific, testable behavior in both languages, not aspirational text.	M21 (Field Notes)
Leadership Modeling & Reinforcement Build	Weeks 12-26	Paired-leader modeling	Have leaders from both legacy organizations model values jointly, not separately.	M8 (Communications)
Pilot Cohort	Weeks 20-34	Genuine cross-site pairing	Pair one Tangier team with one Bouregreg team as a real working relationship, not two isolated pilots.	M6 (Emotional & Transition Layer)
Organization-Wide Rollout	Weeks 32-50	Two-wave staged rollout	Roll out in waves so later cohorts benefit from earlier lessons.	M5 (ADKAR Engine)
Reinforcement Through Skepticism	Weeks 45-68	Two-clock discipline against a public announcement	Separate a corporate/brand milestone from journi's own evidence-based Refreeze call.	M3 (Initiative Registry)
Institutionalization	Weeks 62-78+	Cross-site CRI divergence tracking	Track a structural, slow-moving cohort gap rather than treat it as a single-week trigger.	M14 (Analytics)

PART 4 — SIX EXCEPTIONS, IN DETAIL

Six Realistic Ways This Program Could Have Gone Differently

E1 · DIAGNOSIS, WEEKS 1-6

Sponsor Coverage Gap

DESCRIPTION

Karim Fassi, newly appointed as this program's integration Sponsor, logged zero visible actions on M7 through the program's first four weeks — exactly ALT-003's condition.

TRIGGER

Sponsor visibility on M7 logged as "weak."

TIMELINE IMPACT

No formal gate delay, but risks damaging Bridges/Kübler-Ross evidence if left unaddressed.

RECOVERY TASKS

A direct, visible town hall and a documented sponsorship action plan.

OUTPUTS: A corrected Sponsor visibility reading; a rebuilt trust baseline. **RACSI:** R = CM, PM · A = ES · C = FPO · S = SUP · I = EU

Desire Stall at Tangier Pilot

DESCRIPTION

Tangier Dispatch's ADKAR Desire score dropped to 2, triggering a mandatory barrier-reason note. The root cause was an unconfirmed rumor that Tangier's dispatch function would be consolidated into Casablanca within a year.

TRIGGER

Desire logged at 2 or below, auto-escalating.

TIMELINE IMPACT

No gate delay — resolved through direct, honest communication within the pilot phase.

RECOVERY TASKS

Confirm or deny the rumor directly and honestly; address the underlying fear rather than the surface symptom.

OUTPUTS: A resolved rumor; a recovered Desire score. **RACSI:** $R = CM \cdot A = CM \cdot C = ES, SUP \cdot S = PM \cdot I = FPO, EU$

Divergence Pattern at Rollout

DESCRIPTION

A Wave 2 Casablanca cohort with markedly less direct Tangier contact showed Knowledge and Ability both at 4 or above while Bridges still read "Ending" — ALT-001's exact condition. The cohort understood the values intellectually but had never had them tested against a real cross-site relationship.

TRIGGER

ALT-001 (Divergence Pattern Detected) fires on M6.

TIMELINE IMPACT

No gate delay — resolved through a targeted cross-site exposure within the rollout window.

RECOVERY TASKS

Create a real, not simulated, cross-site working relationship for the affected cohort.

OUTPUTS: A resolved divergence; a genuine cross-site relationship in place of an intellectual-only understanding. **RACSI:** $R = CM \cdot A = CM \cdot C = SUP, FPO \cdot S = ITL \cdot I = ES, EU$

Premature "Integration Complete" Declaration

DESCRIPTION

Bouregreg Group's Board issued a public "One Bouregreg — Integration Complete" statement timed to fiscal year-end, while journi's own Lewin reading remained "Change," not Refreeze — this program's own two-clock problem.

TRIGGER

A corporate/brand milestone announced ahead of journi's own evidence-based Refreeze call.

TIMELINE IMPACT

No gate delay, but risks staff reading the announcement as premature spin or license to stop reinforcement work.

RECOVERY TASKS

Communicate the distinction between the corporate milestone and the ongoing reinforcement work directly, not silently.

OUTPUTS: A clarified internal message; continued reinforcement work despite the public announcement. **RACSI:** R = CM · A = ES · C = PM · S = FPO · I = SUP, EU

Sentiment Regression

DESCRIPTION

A newly created "combined regional" role passed over a tenured Tangier candidate for a less-tenured Bouregreg-side candidate; Tangier's Kübler-Ross sentiment regressed sharply toward Resistance/Anger — read as evidence that "Equal Standing" was not real in practice.

TRIGGER

A cohort's Kübler-Ross reading moves backward following a specific triggering event.

TIMELINE IMPACT

No gate delay — resolved through a transparent review within the same phase.

RECOVERY TASKS

A transparent review of the decision; correction of the genuine procedural gap found (the role was never posted at Tangier).

OUTPUTS: A documented procedural fix; a rebuilt trust baseline at Tangier. **RACSI:** $R = \text{FPO}, ES \cdot A = ES \cdot C = CM \cdot S = SUP \cdot I = EU$

Cross-Site Cohort Divergence

DESCRIPTION

Across three consecutive Composite Readiness Index readings, Tangier's cohort score consistently trailed the Casablanca-counterpart cohort by a real margin — a slower-moving, structural pattern tracing to Tangier's later program-relative start and deeper trust deficit.

TRIGGER

A persistent, non-noise CRI gap between cohorts across multiple readings.

TIMELINE IMPACT

No single gate delay — tracked continuously from Pilot through Institutionalization.

RECOVERY TASKS

Track the gap explicitly rather than average it away; direct additional reinforcement resources toward the lagging cohort.

OUTPUTS: A standing, disaggregated cross-site tracking practice, still active as Institutionalization closes. **RACSI:** R = CM, SUP · A = CM · C = FPO, PM · S = ITL · I = ES, EU

What This Training Covers

MP-05 does not appear in journi's E2E-CULT chain — nothing here trains anyone into believing the four values. What this program trains is real, values-independent capability: Tangier staff don't yet know Bouregreg's shared systems, and Bouregreg's own People Managers have never supervised a newly-merged team.

Strategic Management

Cohort: The Steering Committee: Karim Fassi, Nadia Chraibi, Youssef Idrissi, Meryem Sabri, Laila Mernissi · Weeks 10–14

Curriculum Entry	Content Focus
Leading a Two-Culture Organization	Governing an integration where neither culture is the default — reading Bridges/Kübler-Ross as leadership signals.
journi Governance for Multi-Organization Programs	Reading a Stakeholder Map and CRI that span two Organizations under one Group.
Communicating Through an Acquisition	Media, investor, and internal-communication discipline, delivered ahead of the Week 56 Two-Clock Problem.

Operational Management

Cohort: People Managers across both Organizations (12 total) · Weeks 18-24

Curriculum Entry	Content Focus
Managing a Newly-Merged Team	Supervisory skills specific to managing staff from the other company's original workforce.
Unified Operating Procedures — Distribution & Logistics	Harmonized SOPs so managers supervise a mixed team on one shared procedure.
Coaching Fundamentals for People Managers	Feeds directly into M11 (Manager as Coach)'s team-scoped heatmap.

Operations (Frontline)

Cohort: All 400 target staff, split by rollout wave · Weeks 35–47

Curriculum Entry	Content Focus
Bouregreg Shared Systems & Tools Orientation	Practical onboarding to shared order-tracking and dispatch tooling.
Unified Safety & Quality Procedures	Harmonized standards across both sites' operations.
Customer Commitment Standards — One Bouregreg	Unified customer-facing service standards.

Why This Curriculum Is Shaped This Way

A high training-completion reading confirms Tangier and Casablanca staff can use the shared systems — it does not, on its own, confirm the four values have taken hold. That evidence still comes from Bridges, Kübler-Ross, and Part 4's own mechanisms, and this program's training term is expected to rise well ahead of its cultural terms, by design.

Which journi Modules Dominate This Archetype

M6 (Emotional & Transition Layer)	The heaviest use of Bridges and Kübler-Ross of any archetype — two starting cultures tracked side by side.
M7 (Sponsor & Coalition)	A newly appointed Sponsor starts with zero logged actions — the direct ALT-003 trigger.
M5 (ADKAR Engine)	Desire is the block most exposed here — a named, specific fear (job security) stalls it.
M8 (Communications)	Joint briefings for paired cohorts, not separate messaging for each legacy culture.
M9 (Training)	A parallel track for real capability gaps, deliberately kept separate from the values curriculum itself.
M14 (Analytics)	Tracks the training-completion term rising well ahead of the cultural CRI terms — a predicted, not alarming, gap.

What This Case Fires

ALERTS THIS CASE EXERCISES

ALT-003 (Sponsor Coverage Gap)

WHY

Built deliberately around a newly appointed Sponsor's slow start — the archetype most exposed to sponsorship visibility risk.

KEY TAKEAWAYS

What to Remember About This Archetype

- › A real Sponsor Coverage Gap that fires and is corrected, a real Desire stall traced to a named, acquisition-specific fear, and a Refreeze signed only once the evidence — not the acquisition's own press-release timeline — supports it.
- › Bridges and Kübler-Ross dominate. Identity and emotional integration matter more than any specific skill here — a newly appointed Sponsor with zero logged actions damages exactly these two frameworks fastest, which is why this archetype is built to fire ALT-003 early rather than later.
- › Built deliberately around a newly appointed Sponsor's slow start — the archetype most exposed to sponsorship visibility risk.



Cultural / Values Transformation

One Bouregreg: Post-Acquisition Culture Integration
