



Integrated Management System

ISO 9001/14001 Integrated Management System

Pursuing ISO 9001/14001 certification on one management system rather than two — sponsored alone, without a guiding coalition.

7

PHASES

60

WEEKS

6

EXCEPTIONS

3

TRAINING TIERS

PART 0 — PURPOSE

What This Guide Is, and How to Use It

WHAT THIS GUIDE IS

This deck follows the ISO 9001/14001 Integrated Management System program — journi's QMS archetype case — from tenant setup through ongoing surveillance, the guide in this series with the longest single-phase tail, since certification surveillance never formally closes.

HOW TO USE IT

This program runs inside the same Bouregreg Group tenant as every other archetype in this series. A reader with the tenant already set up skips straight to CM Project creation.

Verified Against journi's Real Source

Every journi module, field, and role named here is verified against journi's real source. This is journi's own stated case for ALT-010 (Guiding Coalition Gap) — this deck shows exactly how a single-Sponsor structural gap fires the alert and is resolved through genuine coalition-building, not a wider distribution list.

RACSI CODES USED THROUGHOUT

ES = Executive Sponsor · CM = Change Manager · PM = Program/Project Manager · FPO = Functional Process Owner · ITL = IT/Technical Lead · SUP = Supervisor · EU = End User

Why This Case Matters

A Quality Manager sponsoring a certification program alone, without a broader guiding coalition, is a realistic single-sponsor failure mode journey is specifically built to catch — the Sponsor & Coalition record, not any single ADKAR score, is this archetype's central risk signal.

The Case, in Brief

410 staff, Settat plant operations + quality

60 weeks (guide numbering)

Settat plant pursues integrated ISO 9001 (quality) and ISO 14001 (environmental) certification on one management system rather than two, driven by a customer contract now requiring certified quality management, across 410 staff over 60 weeks.

What This Guide Proves, Concretely

A real ALT-010 firing at Week 26-31, resolved by recruiting a genuine Procurement Director and HR Business Partner as coalition members — plus five further exceptions showing exactly how a certification program can drift even after the headline coalition gap is closed.

Weighting for This Archetype

Lewin never fully closes. Ongoing Surveillance is the longest single-phase tail in the library by design — certification surveillance never formally ends, so Refreeze is the one Lewin stage this archetype treats as a standing state, not a destination, unlike every other case in this series.

The Composite Readiness Index, Read for This Case

The Composite Readiness Index climbs steadily through Design and Implementation, dips briefly around the coalition-gap discovery, then recovers once the coalition is genuinely rebuilt — Benchmarking reads "Behind" only in that narrow window, "In Line" everywhere else.

The Existing Tenant, and Reading Paths by Role

THE EXISTING TENANT

This program runs inside the same tenant journi's Master User Guide builds, under the existing Bouregreg Manufacturing Maroc Organization — no new Organization needed.

READING PATHS, BY ROLE

- › A Change Manager running this program day to day: Part 2 once, then Part 4 in full.
- › A Program/Project Manager: Part 4's PM Track column and the Master WBS & Gantt.
- › An Executive Sponsor: Part 1, then Part 4's phase-opening narratives.
- › A Super Admin or Org Admin: Part 3.

The RACSI Team for This Program

Name	RACSI Code	Role
Nadia Fassi	ES	Sponsor — Quality Manager
Rania Bensouda	CM	Change Manager
Samir Chraibi	PM	Program Manager
Mehdi Ouahbi	FPO	Functional Process Owner
Yasmine Kadiri	ITL	IT/Technical Lead
Aziz Berrada	SUP	Supervisor

Creating the CM Project

- 1** On Module 1 — Hierarchy, create the ISO 9001/14001 Integrated Management System CM Project under the existing Bouregreg Manufacturing Maroc Organization.
- 2** Set Change type: Integrated Management System. Target population: "Settat plant operations and quality, 410 staff." Business driver: "A customer contract now requires certified quality management; a parallel environmental certification is bundled in for efficiency."
- 3** Save. Lewin opens at Unfreeze, started alongside the ERP program's own kickoff.
- 4** On Module 17 — WBS & Gantt, load the TPL-IMS-7 phase template: Intake & Diagnosis, Design, Implementation, Mock-up Audit, Certifying Audit, Surveillance Prep, Ongoing Surveillance.

Charters for This Program

Charter	Accountable	Review Cadence
CHTR-01 Sponsorship / Leadership Charter	Nadia Fassi (ES)	Per Phase Gate
CHTR-04 Organizational Impact Charter	Rania Bensouda (CM)	On scope change
CHTR-08 Pulse / Interview Charter	Rania Bensouda (CM)	Per phase gate + ad hoc

Setup Checklist

- ☒ Base tenant confirmed (Bouregreg Group, existing Organization)
- ☒ QMS program team accounts created
- ☒ CM Project created, Lewin opened at Unfreeze
- ☒ TPL-IMS-7 phase template loaded on M17
- ☒ Applicable Charters reviewed and accountable owners confirmed

PART 4 — WEEK-BY-WEEK TIMELINE

7 Phases, In Order



Total program length: 60 weeks (guide numbering). Every phase below is walked in detail across the next slides — normal flow first, then six exceptions in full operational detail.

Intake & Diagnosis

Weeks 1-12

NARRATIVE

Establishes the gap between current practice and both ISO 9001 and ISO 14001 requirements, started alongside the ERP program's own kickoff.


PHASE 1 · INTAKE & DIAGNOSIS

Key Moments in This Phase

Week	What Happens
Week 1	Kickoff; Lewin opens at Unfreeze.
Week 8	Gap analysis against both standards, run as one integrated exercise.
Week 12	Diagnosis gate closes.

PHASE 1 · INTAKE & DIAGNOSIS

Framework Snapshot

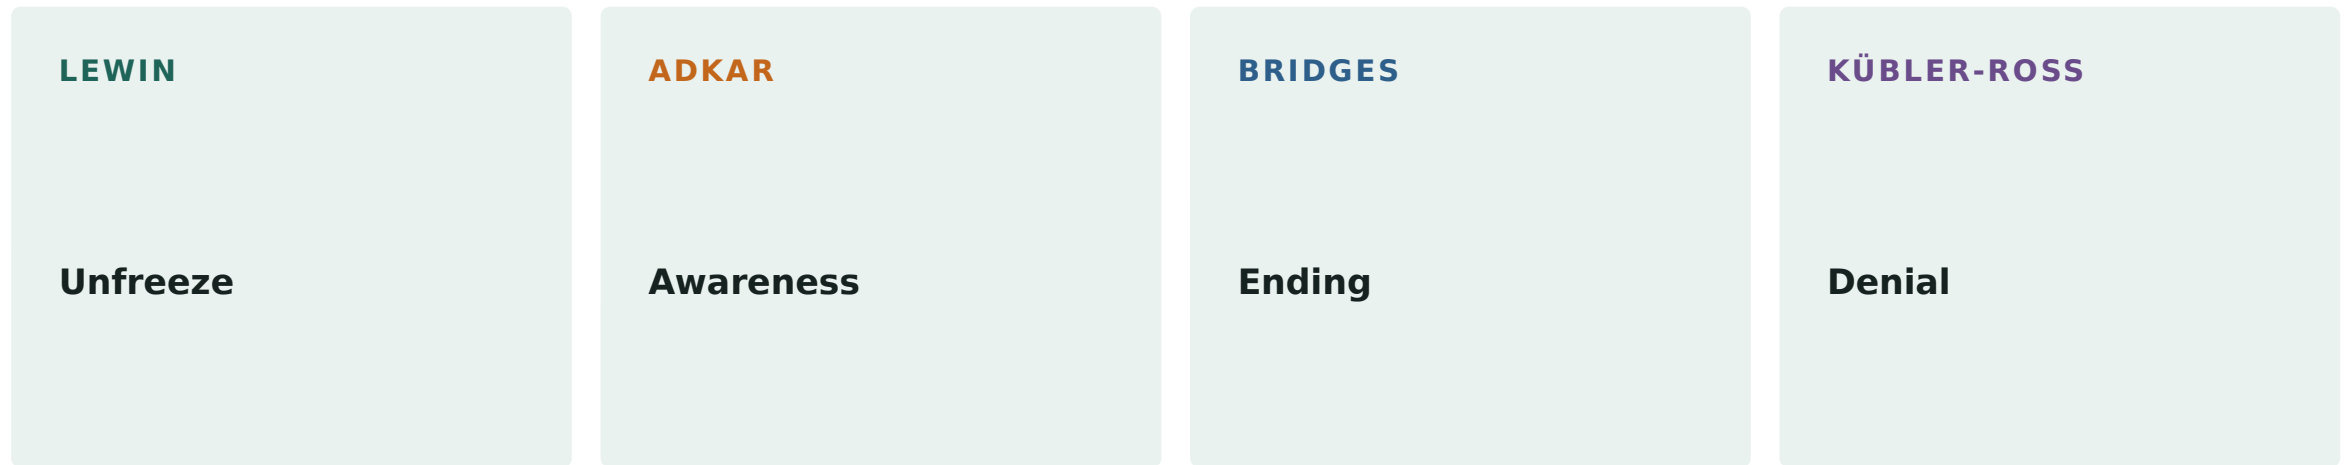

KEY TECHNIQUE THIS PHASE

Dual-standard integrated gap analysis: Assess ISO 9001 and ISO 14001 as one exercise, not two parallel ones.

Design

Weeks 10-26


NARRATIVE

Designs the integrated procedure set covering both quality and environmental requirements — where Exception E5's standards conflict surfaces.

Key Moments in This Phase

Week	What Happens
Week 18	An ISO 14001 waste-handling requirement conflicts with existing operations practice — Exception E5 opens.
Week 26	Design gate closes; five weeks into Implementation the coalition gap is discovered.

Framework Snapshot

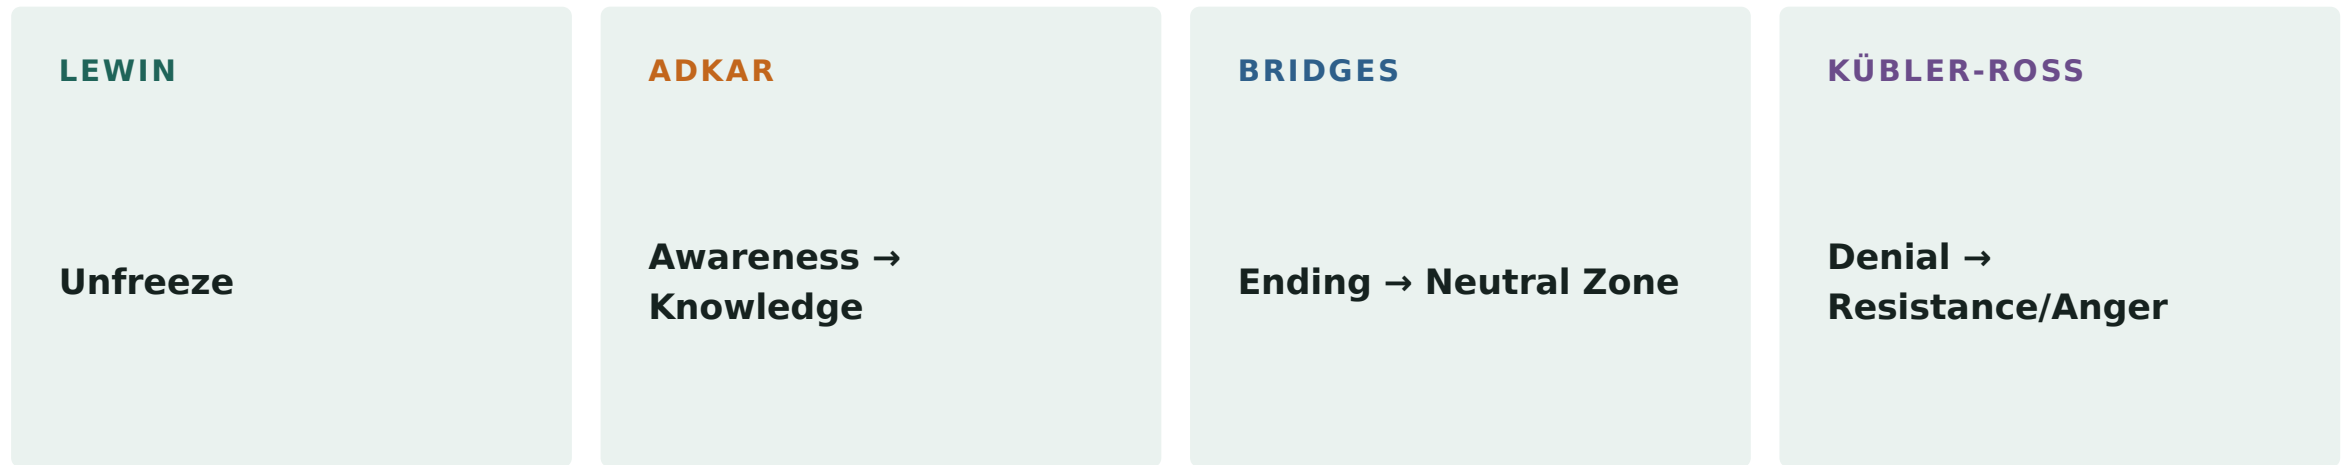

KEY TECHNIQUE THIS PHASE

Integrated procedure-set design: Design one procedure set covering both quality and environmental requirements.

Implementation

Weeks 24-38

NARRATIVE

Implements the designed procedures plant-wide — the phase where Nadia Fassi's solo sponsorship becomes visible as a structural gap.

Key Moments in This Phase

Week	What Happens
Week 26	Sponsor & Coalition record still shows zero named members — Exception E1 opens, firing ALT-010.
Week 31	A Procurement Director and HR Business Partner recruited as genuine coalition members.
Week 38	Implementation gate closes.

PHASE 3 · IMPLEMENTATION

Framework Snapshot



KEY TECHNIQUE THIS PHASE

Genuine coalition recruitment: Move beyond solo sponsorship to a real guiding coalition with named, active members.

Mock-up Audit

Weeks 36–46


NARRATIVE

Runs an internal mock-up audit before the real certifying body ever sees the system — where a systemic documentation gap can still be caught.

Key Moments in This Phase

Week	What Happens
Week 40	Mock-up audit finds a systemic documentation gap in ISO 14001's waste-handling clause — Exception E2 opens.
Week 43	Documentation gap closed across the environmental half of the system.
Week 46	Mock-up audit gate closes clean.

Framework Snapshot

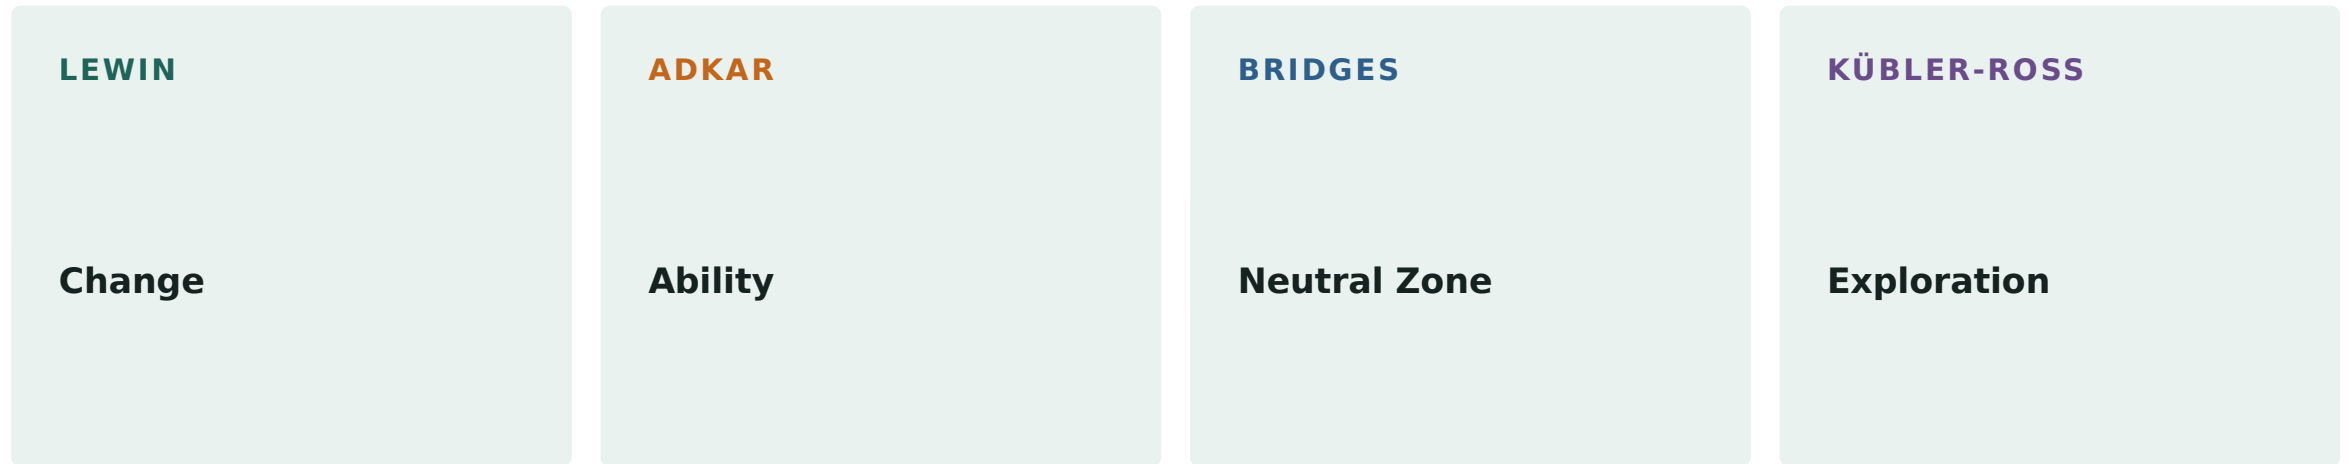

KEY TECHNIQUE THIS PHASE

Internal mock-up audit: Catch systemic documentation gaps before the real certifying body does.

Certifying Audit

Weeks 44-50


NARRATIVE

The real, external certifying audit — the moment this program's preparation is actually tested.

Key Moments in This Phase

Week	What Happens
Week 47	The certifying body's auditor flags a minor nonconformity — Exception E3 opens.
Week 49	Nonconformity corrected and closed with the auditor.
Week 50	Certification passes clean.

Framework Snapshot

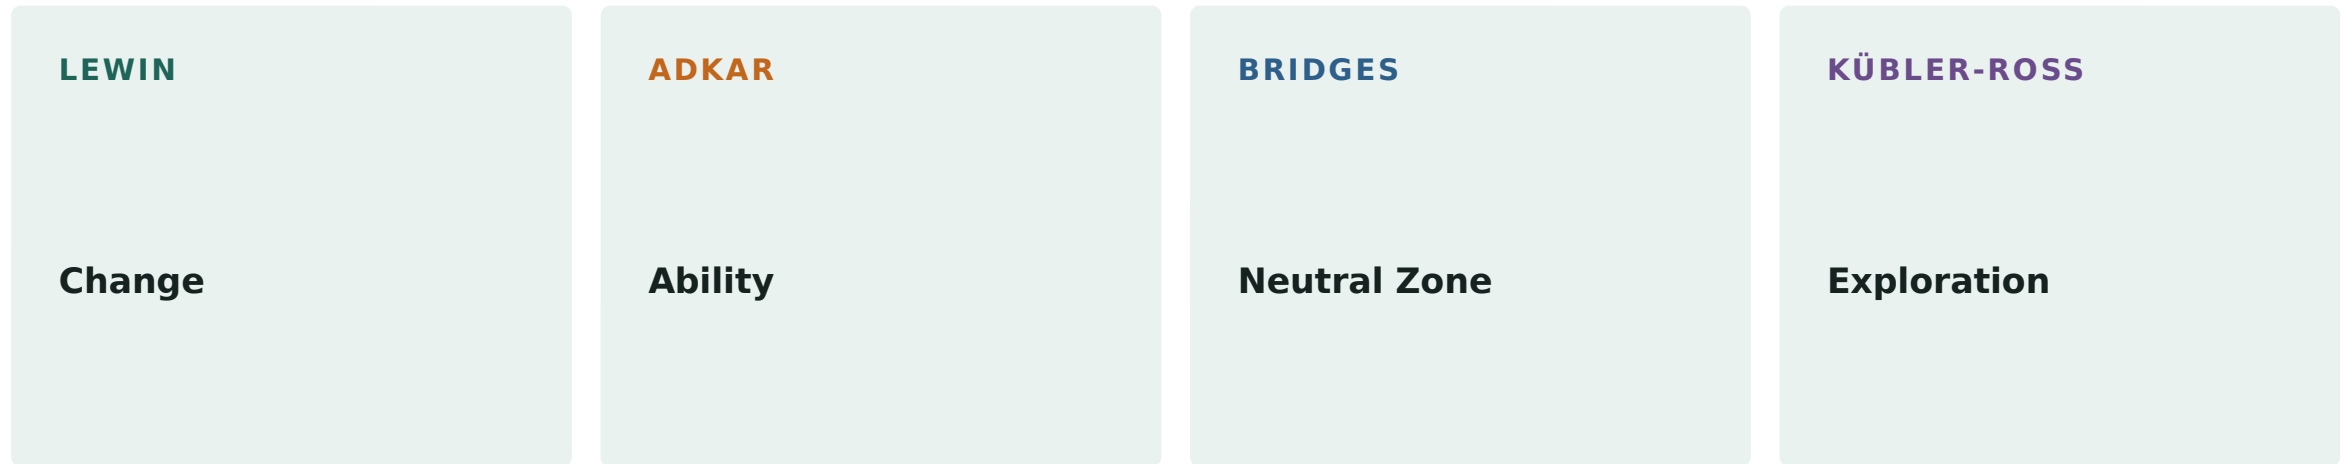

KEY TECHNIQUE THIS PHASE

External certifying audit: Confirm certification against the certifying body's own independent standard.

Surveillance Prep

Weeks 48-52


NARRATIVE

Prepares the standing surveillance rhythm that will run indefinitely past this program's own formal close.

Key Moments in This Phase

Week	What Happens
Week 50	Surveillance schedule and spot-check cadence confirmed.
Week 52	Surveillance prep gate closes.

Framework Snapshot

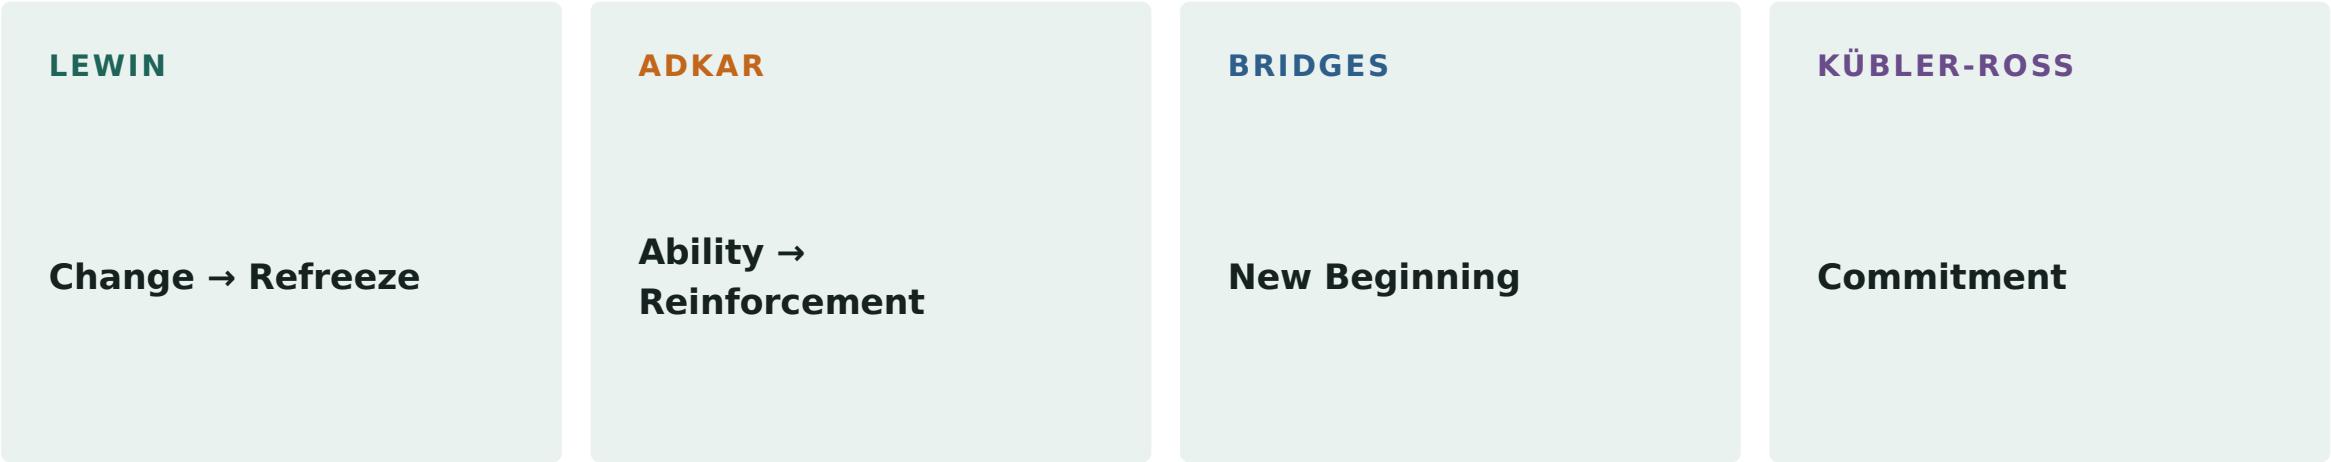

KEY TECHNIQUE THIS PHASE

Standing surveillance-rhythm design: Design a spot-check cadence that will run indefinitely without a dedicated program team.

Ongoing Surveillance

Weeks 52 onward, open-ended


NARRATIVE

The longest single-phase tail in the library — certification surveillance never formally closes, by design.

Key Moments in This Phase

Week	What Happens
Week 56	A function quietly reverts to a pre-certification shortcut once audit pressure passes — Exception E4 opens.
Week 58+	The recruited HR Business Partner departs, risking a quiet reversion to the original coalition gap — Exception E6 opens.

Framework Snapshot

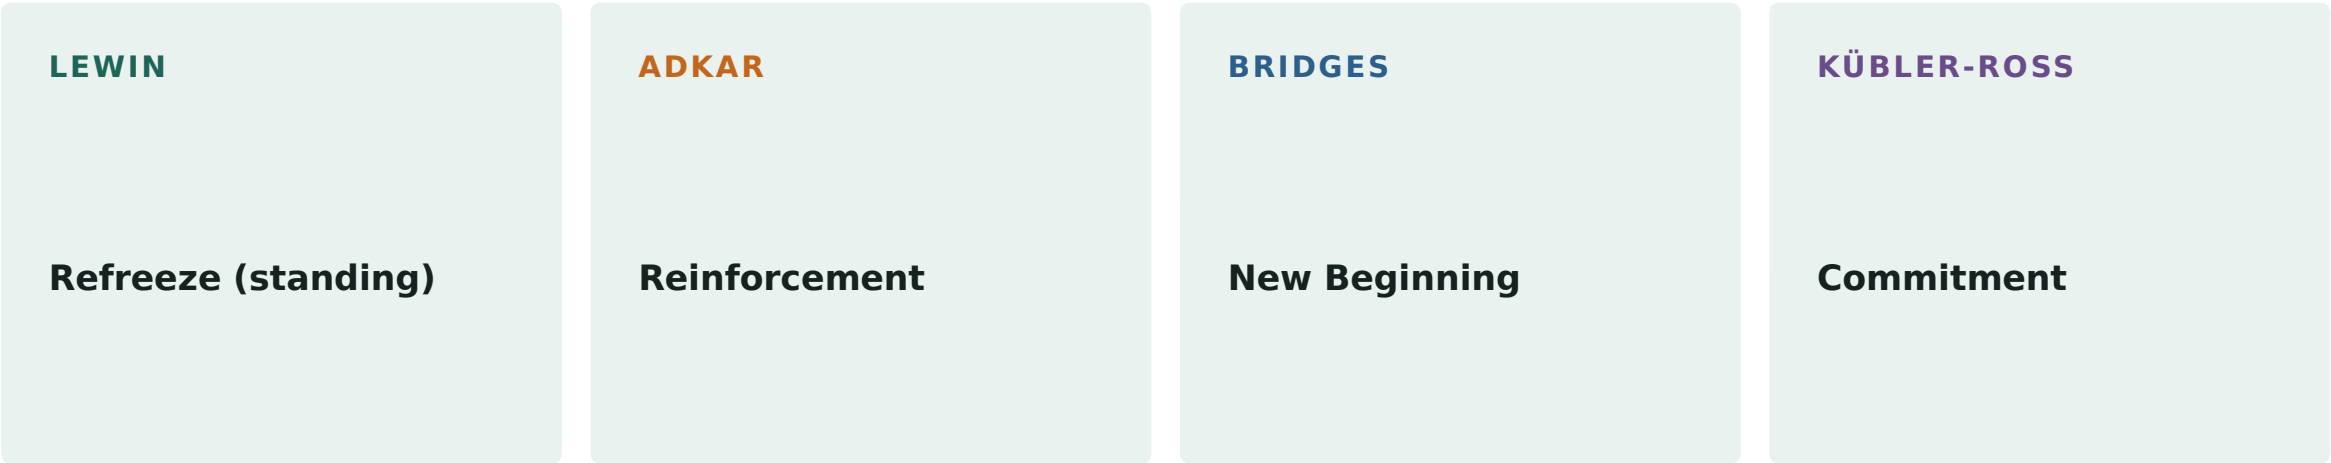

KEY TECHNIQUE THIS PHASE

Surveillance spot-checks: Catch "audit theater" reversion before it becomes the new normal.

Every Phase, Across the Four Frameworks

Phase	Week(s)	Lewin	ADKAR	Bridges	Kübler-Ross
Intake & Diagnosis	Weeks 1-12	Unfreeze	Awareness	Ending	Denial
Design	Weeks 10-26	Unfreeze	Awareness → Knowledge	Ending → Neutral Zone	Denial → Resistance/Anger
Implementation	Weeks 24-38	Change	Knowledge → Ability	Neutral Zone	Resistance/Anger
Mock-up Audit	Weeks 36-46	Change	Ability	Neutral Zone	Exploration
Certifying Audit	Weeks 44-50	Change	Ability	Neutral Zone	Exploration
Surveillance Prep	Weeks 48-52	Change → Refreeze	Ability → Reinforcement	New Beginning	Commitment
Ongoing Surveillance	Weeks 52+	Refreeze (standing)	Reinforcement	New Beginning	Commitment

Every Phase, Techniques and Tools

Phase	Week(s)	Technique	Goal	Tool
Intake & Diagnosis	Weeks 1-12	Dual-standard integrated gap analysis	Assess ISO 9001 and ISO 14001 as one exercise, not two parallel ones.	M4 (Stakeholder Mapping)
Design	Weeks 10-26	Integrated procedure-set design	Design one procedure set covering both quality and environmental requirements.	M17 (WBS & Gantt)
Implementation	Weeks 24-38	Genuine coalition recruitment	Move beyond solo sponsorship to a real guiding coalition with named, active members.	M7 (Sponsor & Coalition)
Mock-up Audit	Weeks 36-46	Internal mock-up audit	Catch systemic documentation gaps before the real certifying body does.	M21 (Field Notes)
Certifying Audit	Weeks 44-50	External certifying audit	Confirm certification against the certifying body's own independent standard.	M17 (WBS & Gantt)
Surveillance Prep	Weeks 48-52	Standing surveillance-rhythm design	Design a spot-check cadence that will run indefinitely without a dedicated program team.	M12 (Sustainment)
Ongoing Surveillance	Weeks 52+	Surveillance spot-checks	Catch "audit theater" reversion before it becomes the new normal.	M12 (Sustainment)

PART 4 — SIX EXCEPTIONS, IN DETAIL

Six Realistic Ways This Program Could Have Gone Differently

Guiding Coalition Gap

DESCRIPTION

Five weeks into Implementation, Nadia Fassi's Sponsor & Coalition record still showed zero named coalition members, and procurement/HR rollout had stalled outside her direct authority — ALT-010's exact condition.

TRIGGER

The Sponsor & Coalition record on M7 names fewer than 2 coalition members.

TIMELINE IMPACT

No formal gate delay, but procurement/HR rollout stalls until the coalition is rebuilt.

RECOVERY TASKS

Recruit a genuine Procurement Director and HR Business Partner as coalition members, not just a wider distribution list.

OUTPUTS: A rebuilt Sponsor & Coalition record with two genuine, active members. **RACSI:** R = CM, ES · A = ES · C = PM · S = FPO · I = SUP, EU

Mock-up Audit Finds a Systemic Documentation Gap

DESCRIPTION

The mock-up audit finds that Design's procedure set never fully addressed ISO 14001's waste-handling documentation clause — a systemic gap across the whole environmental half of the integrated system.

TRIGGER

An internal mock-up audit finding spanning multiple procedures, not a single missed document.

TIMELINE IMPACT

Extends Mock-up Audit by two to three weeks while the environmental documentation set is rebuilt.

RECOVERY TASKS

Rebuild the waste-handling documentation set specifically, cross-checked against ISO 14001's actual clause text.

OUTPUTS: A corrected, complete environmental documentation set. **RACSI:** R = FPO, ITL · A = CM · C = PM · S = SUP · I = ES, EU

External Auditor Flags a Nonconformity During Certification

DESCRIPTION

The certifying body's own auditor, independent of the mock-up audit, flags a minor nonconformity during the real certifying audit — a procedure followed correctly on paper but not consistently in observed plant-floor practice.

TRIGGER

An independent certifying-body finding during the real audit.

TIMELINE IMPACT

A short correction window before the audit's own close-out, typically days not weeks.

RECOVERY TASKS

Correct the specific practice gap and demonstrate the correction to the auditor before close-out.

OUTPUTS: A closed nonconformity; certification passes clean. **RACSI:** R = FPO, SUP · A = CM · C = ES · S = PM · I = ITL, EU

A Function Reverts to Old Practice Once the Auditor Leaves

DESCRIPTION

A surveillance spot-check finds that one function has quietly reverted to a pre-certification shortcut once audit pressure passed — the classic "audit theater" risk every certification program has to guard against.

TRIGGER

A surveillance spot-check finding a reverted practice.

TIMELINE IMPACT

No formal gate — this phase runs open-ended — but requires an immediate corrective conversation.

RECOVERY TASKS

Address the reversion directly with the function; reinforce why the practice matters beyond audit optics.

OUTPUTS: A corrected practice; a reinforced surveillance spot-check cadence. **RACSI:** R = FPO, SUP · A = CM · C = ES · S = PM · I = ITL, EU

Environmental Requirements Conflict With an Existing Operations Practice

DESCRIPTION

A specific ISO 14001 waste-handling requirement conflicts directly with an existing, longstanding operations practice that was never a problem for ISO 9001 alone — the specific complication a genuinely integrated certification introduces.

TRIGGER

A direct conflict identified during Design between the two standards' requirements.

TIMELINE IMPACT

Adds one to two weeks to Design while the conflict is resolved before Implementation begins.

RECOVERY TASKS

Resolve the conflict explicitly, documenting why the resolution satisfies both standards rather than favoring one.

OUTPUTS: A documented, dual-compliant resolution. **RACSI:** R = FPO, SUP · A = CM · C = ITL · S = PM · I = ES, EU

A Coalition Member Departs During Surveillance

DESCRIPTION

The HR Business Partner recruited as a coalition member during Exception E1's recovery leaves the organization during Ongoing Surveillance, risking a quiet reversion to the exact structural gap the program worked to close.

TRIGGER

A confirmed departure of a named coalition member during Ongoing Surveillance.

TIMELINE IMPACT

No formal delay, but requires prompt coalition-seat succession.

RECOVERY TASKS

Identify and onboard a successor coalition member promptly, rather than let the coalition quietly shrink back toward solo sponsorship.

OUTPUTS: A maintained, genuine coalition membership. **RACSI:** R = CM, ES · A = ES · C = FPO · S = PM · I = SUP, ITL, EU

What This Training Covers

Per the E2E-IMS chain, MP-05 is present — training here covers both ISO 9001 and ISO 14001 procedures as one integrated curriculum, not two separate tracks.

Strategic Management

Cohort: Nadia Fassi (Sponsor), plant leadership · Weeks 1-10

Curriculum Entry	Content Focus
Sponsoring a Certification Program	Why solo sponsorship is a structural risk journi is specifically built to catch.
Reading a Guiding Coalition Gap	How to read fewer than 2 coalition members as a real, actionable signal.

Operational Management

Cohort: Mehdi Ouahbi (FPO), Aziz Berrada (SUP) · Weeks 10–36

Curriculum Entry	Content Focus
Operating the Integrated Procedure Set	Quality and environmental procedures as one system, not two.
Preparing for a Mock-up and Certifying Audit	What auditors actually check, and how to have evidence ready.

Operations (Frontline)

Cohort: All 410 Settlat plant operations and quality staff · Weeks 20-46

Curriculum Entry	Content Focus
Following the New Integrated Procedures	Day-to-day quality and environmental practice under the new certified system.
Sustaining Practice Beyond the Audit Window	Specifically addressing the "audit theater" risk Exception E4 shows happening.

Why This Curriculum Is Shaped This Way

Training completion here is necessary but not the finish line — Ongoing Surveillance's indefinite spot-check cadence is what actually verifies the certified practice holds, long after the certifying audit itself passes.

Which journi Modules Dominate This Archetype

M7 (Sponsor & Coalition)	The archetype's central risk — fewer than 2 coalition members fires ALT-010.
M17 (WBS & Gantt)	The TPL-IMS-7 template — Mock-up and Certifying Audit are external-facing gates.
M12 (Sustainment)	Ongoing Surveillance checkpoints, run indefinitely past program close.
M19 (Charter Registry)	Formal charters carry unusual weight given the external audit stakes.
M21 (Field Notes)	Documentation-gap and nonconformity findings, logged with their corrections.
M4 (Stakeholder Mapping)	Both quality and environmental impact dimensions tracked in one integrated map.

What This Case Fires

ALERTS THIS CASE EXERCISES

ALT-010 (Guiding Coalition Gap)

WHY

Built specifically because a Quality Manager sponsoring alone, without a broader coalition, is a realistic single-sponsor failure mode.

KEY TAKEAWAYS

What to Remember About This Archetype

- › A real ALT-010 firing at Week 26–31, resolved by recruiting a genuine Procurement Director and HR Business Partner as coalition members — plus five further exceptions showing exactly how a certification program can drift even after the headline coalition gap is closed.
- › Lewin never fully closes. Ongoing Surveillance is the longest single-phase tail in the library by design — certification surveillance never formally ends, so Refreeze is the one Lewin stage this archetype treats as a standing state, not a destination, unlike every other case in this series.
- › Built specifically because a Quality Manager sponsoring alone, without a broader coalition, is a realistic single-sponsor failure mode.



Integrated Management System

ISO 9001/14001 Integrated Management System
