

POWERACT

CONSULTING

USER GUIDE

CortexPLM

Run innovation projects from idea to launch, relaunch or retirement

Version 1.0 · September 2026

Table of Contents

1. About This Guide.....	5
1.1 Conventions.....	5
2. Getting Started.....	6
2.1 Sign in.....	6
2.2 The dashboard.....	6
2.3 The navigation bar: pin, slide and position.....	7
2.4 Language.....	8
2.5 Organizations and groups.....	9
2.6 Alerts, notifications and the assistant.....	9
3. How a Project Moves Through CortexPLM.....	11
3.1 Who does what in the runs.....	11
3.2 Create a project.....	11
3.3 Complete a task.....	12
3.4 Complete the gate checklist.....	13
3.5 Submit the gate and record the decision.....	14
4. Common Values Used in the Runs.....	17
5. Run 1: Fast Track in the Public Sector.....	18
Step 1. Create the project.....	18
Step 2. E2E-01 Idea-to-Business Plan.....	18
Step 3. E2E-02 Idea-to-Business Proposal.....	19
Step 4. E2E-05 Development-to-Launch.....	20
Result of the run.....	21
6. Run 2: Fast Track in Transportation, with a skipped task and a Recycle decision.....	22
Step 1. Create the project.....	22
Step 2. E2E-01 Idea-to-Business Plan.....	22
Step 3. E2E-02 Idea-to-Business Proposal.....	23
Step 4. E2E-02 Idea-to-Business Proposal.....	24
Step 5. E2E-05 Development-to-Launch.....	25
Result of the run.....	26
7. Run 3: Light Track in Agro-Business (Dairy), from idea to relaunch.....	27
Step 1. Prepare the Light Track observation period.....	27
Step 2. Create the project.....	27

Step 3. E2E-01 Idea-to-Business Plan.....	28
Step 4. E2E-02 Idea-to-Business Proposal.....	29
Step 5. E2E-03 Business Proposal-to-Design.....	30
Step 6. E2E-04 Design-to-Development.....	30
Step 7. E2E-05 Development-to-Launch.....	31
Step 8. E2E-07 After-Sales-to-Performance.....	32
Step 9. E2E-09 Market Strategy-to-Campaign.....	33
Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch A.....	34
Step 11. E2E-05 Development-to-Launch (run 2).....	34
Result of the run.....	35
8. Run 4: Full Track in Healthcare, from idea to retirement.....	36
Step 1. Create the project.....	36
Step 2. E2E-01 Idea-to-Business Plan.....	36
Step 3. E2E-02 Idea-to-Business Proposal.....	37
Step 4. E2E-03 Business Proposal-to-Design.....	39
Step 5. E2E-04 Design-to-Development.....	40
Step 6. E2E-05 Development-to-Launch.....	41
Step 7. E2E-06 Launch-to-After-Sales.....	42
Step 8. E2E-09 Market Strategy-to-Campaign.....	42
Step 9. E2E-07 After-Sales-to-Performance.....	43
Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch B.....	44
Result of the run.....	45
9. Run 5: Full Track in Oil, Gas & Energy, relaunching a live product.....	46
Step 1. Open the project.....	46
Step 2. E2E-09 Market Strategy-to-Campaign.....	46
Step 3. E2E-07 After-Sales-to-Performance.....	46
Step 4. E2E-08 Assessment-to-Relaunch or Retirement · Branch A.....	47
Step 5. E2E-04 Design-to-Development (run 2).....	48
Step 6. E2E-05 Development-to-Launch (run 2).....	49
Result of the run.....	50
10. Run 6: Benchmarking in Construction, within the organization and across the group.....	51
Step 1. Compare project types.....	51
Step 2. Compare tracks and filter.....	52

Step 3. Compare with the organizations of the group.....	53
Step 4. Stop or resume sharing with the group.....	54
Step 5. An independent organization.....	54
11. Everyday Scenarios by Module.....	56
11.1 Record a business rule.....	56
11.2 Add a control, change it and compare versions.....	56
11.3 Log a risk and read the heat map.....	56
11.4 See the governance of one process.....	56
11.5 Build a RACSI activity.....	57
11.6 Track a custom KPI.....	57
11.7 Edit and exchange a BPMN diagram.....	57
11.8 Ask for an AI suggestion on a task.....	57
11.9 Search the knowledge base in your language.....	57
11.10 Create a project template and use it.....	58
11.11 Plan with a WBS and a Gantt chart.....	58
11.12 Record a lesson learned.....	58
11.13 Export a report.....	58
11.14 Choose how you are notified.....	58
11.15 Add a user within the licence limit.....	59
11.16 Give a project its own team tree (OBS).....	59
11.17 Back up the database.....	59
11.18 Check the audit trail.....	59
12. Messages You May Meet.....	60

1. About This Guide

This guide shows how to use CortexPLM through complete, worked examples. Five runs take real projects through their whole lifecycle, in five industries and all three tracks. Every value you type is given in **bold**, exactly as you enter it. The runs were replayed on a freshly installed demonstration database, so the codes and results match what you will see.

Run	Industry	Track	From	To	Gate decisions
1	Public Sector	Fast	New idea	Launched	T-1, T0, T3
2	Transportation	Fast	New idea	Launched	T-1, T0 (Recycle, then Go), T3
3	Agro-Business – Dairy	Light	New idea	Relaunched	T-1, T0, T1, T2, T3, T5, T3
4	Healthcare	Full	New idea	Retired	T-1, T0, T1, T2, T3, T4, T5, T6
5	Oil, Gas & Energy	Full	Live product	Relaunched	T5, T2, T3
6	Construction	All	Portfolio	Benchmarked	Within the organization and across its group

Chapter 11 adds short scenarios for every other module: governance registers, RACSI, KPIs, BPMN, AI, knowledge, templates, WBS, lessons learned, reports, notifications and administration.

Before you start Start from a fresh demonstration database (Installation Guide, "Reset the demonstration data") so the project codes match: PUB-022, TRN-022, DAI-022 and HLT-022. If you already created projects, your codes will simply have a higher number.

1.1 Conventions

You see	Meaning
Bold text	A value to type, or a button, tab or menu item to select.
Menu > Item	Open the menu group, then the item, in the navigation bar.
UFT-01-02	The identifier of a user-facing task from the process reference.
T-1 ... T6	The eight decision gates of the phase-gate process.

2. Getting Started

2.1 Sign in

1. Open **http://localhost:5173** in your browser.
2. Type your e-mail and password (demonstration users: password **Demo#2026**).
3. Select **Sign in**.

CortexPLM

PRODUCT-SERVICE LIFECYCLE MANAGEMENT

69 macro processes. 9 end-to-end processes. 8 gates.

Run innovation projects from idea to relaunch or retirement, with the rigor of the Full, Light or Fast Track.

81 user-facing tasks with RACSI

3 innovation tracks

11 solution packs

Sign in English

E-mail *

Password *

→ Sign in

Demo accounts

Platform administrator: admin@cortexplm.example / Admin#2026. Other demo users: password Demo#2026.


Public Sector

Product Manager pm1@metrocity.example	Gate Review Board Member board1@metrocity.example
Quality Manager quality@metrocity.example	Executive Sponsor exec@metrocity.example
Process Owner / Track Administrator process@metrocity.example	Platform Administrator admin@metrocity.example

The sign-in page lists the demonstration accounts.

2.2 The dashboard

The dashboard leads with four figures: active projects, gates waiting for a decision, overdue tasks and checklist compliance. Charts below show E2E instances and gate decisions.

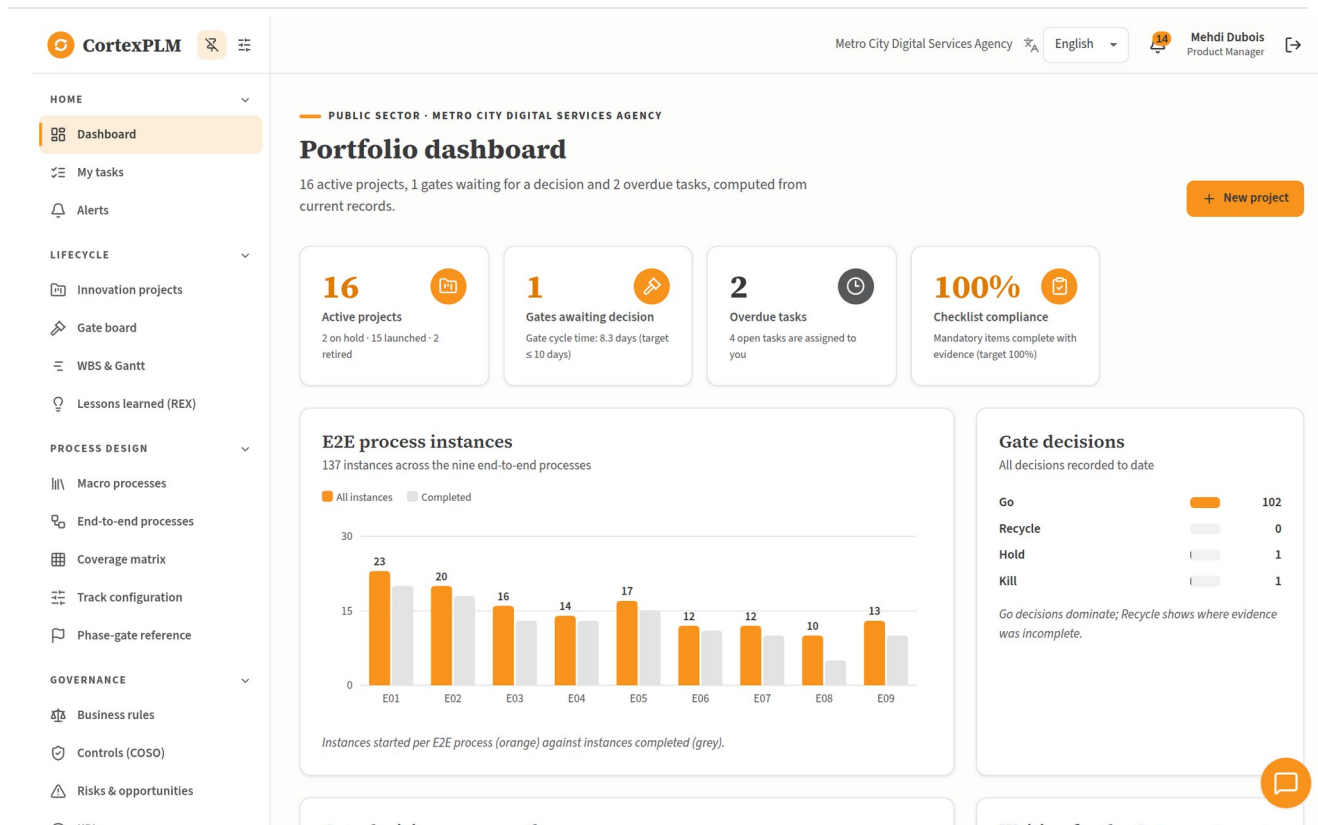

Dashboard of Metro City Digital Services Agency for a Product Manager.

2.3 The navigation bar: pin, slide and position

1. Select the **sliders** icon at the top of the navigation bar to open **Menu position**.
2. Choose **Left**, **Right**, **Top** or **Bottom**. The menu moves at once and the choice is saved for your account.
3. Clear **Keep the menu pinned open** to let the menu slide away. It slides back when you point at the edge of the screen. The pin icon next to the sliders does the same.
4. Select the star next to any item to add it to **Pinned** favourites at the top of the menu. Select a group title to fold or unfold it.

Menu position

☒ Left
 ☐ Right
 ☐ Top
 ☐ Bottom

☒ Keep the menu pinned open

When unpinned, the menu slides away and slides back when you point at the screen edge.

Due	Task	Project	E2E	My role	Status
2025-11-16 · Overdue	Gather Customer Experience Data UFT-09-01	PUB-013 · Library E-Lending Service	E2E-09	Evaluator	Evaluation pending
2025-11-23 · Overdue	Gather Product Delivery Feedback UFT-09-02	PUB-013 · Library E-Lending Service	E2E-09	Evaluator	Evaluation pending
2025-11-30 · Overdue	Establish Market Segments UFT-09-03	PUB-013 · Library E-Lending Service	E2E-09	Evaluator	Evaluation pending
2025-12-07 · Overdue	Link Segments & Products UFT-09-04	PUB-013 · Library E-Lending Service	E2E-09	Evaluator	Evaluation pending
2025-12-14 · Overdue	Establish Market Strategy UFT-09-05	PUB-013 · Library E-Lending Service	E2E-09	Evaluator	Evaluation pending
2025-12-21 · Overdue	Plan & Develop Campaign UFT-09-06	PUB-013 · Library E-Lending Service	E2E-09	Evaluator	Evaluation pending
2026-07-21 · Overdue	Gather Customer Experience Data UFT-09-01	PUB-011 · Street Lighting Fault Reporting	E2E-09	Evaluator	Evaluation pending
2026-07-27 · Overdue	Define High-Level Functional Specs UFT-02-03	PUB-015 · Senior Citizen Transport Card	E2E-02	Evaluator	Evaluation pending
2026-07-28 · Overdue	Gather Product Delivery Feedback	PUB-011 · Street Lighting Fault Reporting	E2E-09	Evaluator	Evaluation pending

Menu position settings: four positions and the pin option.

2.4 Language

Choose **English**, **Français** or العربية in the language list of the top bar. Arabic switches the whole layout to right-to-left, and the navigation bar moves to the right. Your choice is saved; the organization default applies otherwise.



The dashboard in Arabic, laid out right to left.

2.5 Organizations and groups

The demonstration has seven organizations, one per sector. An organization may belong to a group; its members can compare themselves with each other (Run 6). The others are independent.

Organization	Sector	Domain	Group
Metro City Digital Services Agency	Public Sector	metrocity.example	No (independent)
Cedarline Precast Systems	Manufacturing in Construction	cedarline.example	Atlas Infrastructure Holding
Meridale Health Network	Healthcare	meridale.example	No (independent)
Valdora Dairy Cooperative	Agro-Business – Dairy Products	valdora.example	Crescent Agro-Energy Group
Orvane Transit Group	Transportation	orvane.example	Atlas Infrastructure Holding
Kestrel Energy & Utilities	Oil, Gas & Energy	kestrel.example	Crescent Agro-Energy Group
Ridgeway Construction Contractors	Construction	ridgeway.example	Atlas Infrastructure Holding

2.6 Alerts, notifications and the assistant

- The **bell** in the top bar shows unread alerts, such as overdue tasks or a gate waiting too long. Open **Alerts** for the full list.
- Notifications** holds your inbox and lets you choose, per category, the channels you want (in-app, e-mail, webhook, SMS, push).
- The round **assistant** button at the bottom of the screen answers questions about your data within your permissions, for example **How many active projects?**, and explains how to use each screen.

CortexPLM Metro City Digital Services Agency English Mehdi Dubois Product Manager

HOME

- Dashboard
- My tasks
- Alerts

LIFECYCLE

- Innovation projects
- Gate board
- WBS & Gantt
- Lessons learned (REX)

PROCESS DESIGN

- Macro processes
- End-to-end processes
- Coverage matrix
- Track configuration
- Phase-gate reference

GOVERNANCE

- Business rules
- Controls (COSO)
- Risks & opportunities

INTELLIGENCE

AI Assistant

Answers questions about your organization within your permissions, and explains how to use the application. It runs offline on the built-in engine.

Ask about your data, for example "How many active projects?" or "Which gates are pending?", or ask how to use the application.

How many active projects?

Data answer - Computed from your organization data
16 active projects: 2 Fast, 11 Full, 3 Light.

- Fast - 2
- Full - 11
- Light - 3

What it can answer

- Active projects by track
- Gates waiting for a decision
- Your open tasks
- Overdue tasks
- Top open risks
- Any built-in KPI, for example "time to market"
- Unread alerts
- Projects by current E2E process
- How-to questions about any screen

Each data question needs a specific permission.
When your roles do not include it, the assistant says so instead of answering.

How many active projects? Which gates are pending a decision? Show my tasks What are the top risks?

How do I submit a gate?

Type a question **Ask**

The assistant answers from live organization data and says which permission it used.

3. How a Project Moves Through CortexPLM

Every project follows the end-to-end (E2E) processes of its track. Each E2E process is a list of tasks and ends with a gate. At the gate, the Executive Sponsor records one of four decisions.

Track	Total score	E2E processes	Gates	Checklist items per gate
Fast	7 to 14	E2E-01, E2E-02, E2E-05	T-1, T0, T3	6
Light	15 to 24	E2E-01 to E2E-05, E2E-07, E2E-08 (relaunch only), E2E-09	T-1, T0, T1, T2, T3, T5	15
Full	25 to 35, or any safety-critical product	All nine	All eight	30

Decision	What happens
Go	The gate is passed and the next E2E process starts automatically.
Kill	The project stops. You are invited to record a lesson learned.
Hold	The project pauses until a re-review date. Resume project reopens the gate.
Recycle	Named tasks go back to To do; the gate is reviewed again afterwards.

3.1 Who does what in the runs

- The **Product Manager** creates the project, completes the tasks, completes the gate checklist and submits the gate. Each task shows its own owner (for example Finance or Marketing). In daily use each owner completes their task; in these runs the Product Manager completes them on the owners' behalf, which the role allows.
- The **Executive Sponsor** records the gate decision. The project owner can never decide their own gate (control CTL-01).
- The **evaluator** of a task (Accountable in the RACSI matrix) rates it Effective or Not effective after completion. Evaluations do not block the process.

3.2 Create a project

Open **Innovation projects > New project**. Step 1 describes the project, Step 2 scores seven complexity criteria from 1 to 5, Step 3 confirms the recommended track, and Step 4 adds optional macro processes. Select **Create project**; E2E-01 starts.

UFS-28 CONFIGURE TRACK & MACRO PROCESSES

New innovation project

Describe the idea, score its complexity, confirm the track, then create it. E2E-01 Idea-to-Business Plan starts automatically.

Step 1. Describe the project

Start from a template

No template

Optional. A template pre-fills scores and optional macro processes.

Project name *

Online Parking Permit Renewal

Description

Residents renew their parking permit online in under five minutes, without visiting a counter.

Offer type

Service

Region

Metro City

Product Manager (owner)

Mehdi Dubois

Executive Sponsor

Amina Benali

Owning department (OBS)

Choose

Complexity profile

This project Medium (3)

Scores per criterion against the medium reference line.

Track rules

7 - 14 → Fast Track. Not allowed if any criterion scores 5.

15 - 24 → Light Track. Minimum track if regulatory and safety exposure scores 4 or more.

25 - 35 → Full Track. Mandatory for any safety-critical product, whatever the total.

Full	T-1, T0, T1, T2, T3, T4, T5, T6	30-50
Fast	T-1, T0, T3	5-10

Fast Track

Step 2. Score the complexity

Score each criterion from 1 (low) to 5 (high). Use 2 or 4 between the descriptions.

Strategic impact

1 = Incremental change to an existing offer - 3 = New segment or product-line extension - 5 = New platform or business model

1 2 3 4 5

Technical novelty

1 = Known technology, configuration change - 3 = Adaptation of existing technology - 5 = New technology or architecture

1 2 3 4 5

Regulatory and safety exposure

1 = No new certification needed - 3 = Standard certifications or declarations - 5 = Regulated or safety-critical product

1 2 3 4 5

Market scope

1 = One market, existing channel - 3 = Several markets or a new channel - 5 = Multi-market or global launch

1 2 3 4 5

Cross-functional reach

1 = 1 to 2 functions - 3 = 3 to 5 functions - 5 = More than 5 functions or external partners

1 2 3 4 5

Product-service integration

1 = Product-only or service-only change - 3 = Change to an existing bundle - 5 = New integrated or outcome-based offer

1 2 3 4 5

☐ Safety-critical product (Full Track is then mandatory)

Step 3. Confirm the track

Total score 11 of 35. Recommended: Fast Track.

☒ Fast Track - recommended ☐ Light Track ☐ Full Track

Step 4. Select optional macro processes

Mandatory processes are activated automatically. Select the optional ones this project needs.

☐ MP-03 Requirements & Systems Engineering	☐ MP-04 Engineering & Design Management
☐ MP-12 Lifecycle Governance & Analytics	☐ MP-15 AI & Machine Learning Core Services
☐ MP-20 Knowledge & Content Management	☐ MP-23 Incident, Problem, Request & Change Management
☐ MP-27 Data Governance & Master Data Management	☐ MP-28 Integration & API Management
☐ MP-35 Cost & Profitability Management	☐ MP-38 Training & Enablement Management
☐ MP-40 Mobile & Offline Access Management	

Cancel Create project

The New project wizard with the scores of Run 1 and the Fast Track selected.

3.3 Complete a task

Open the task from the project page or from **My tasks**. Fill in the fields, type the **Result / output** and select **Complete task**. A window proposes to record a lesson learned: fill it in, or select **Skip**. You may select **Start task** first to show that work has begun; it is optional.

UFT-01-02 · E2E-01 IDEA-TO-BUSINESS PLAN

Assess Market Opportunity

Analyze market trends, customer needs, and competitive landscape · [PUB-023 UI](#)

[Check Permit Kiosk](#)

[To do](#) [Assign](#)

Record the result

Fill in the fields, write the result, then select Complete task.

[▶ Start task](#)

Target segment *

Residents with an on-street parking permit

Addressable market (MUSD)

2

Strategic-fit score (0-100) *

78

Below 50 parks the idea (BR-001).

Result / output *

Assess Market Opportunity done for PUB-022. Summary filed as PUB-022-01-02.

Describe what was done and the outcome. This text goes into the gate evidence.

[Complete task](#) [Skip \(Rule R2\)](#) [Attach evidence file](#)

Accountability (RACSI)

Owner	Youssef Blanc
Evaluator	Mehdi Dubois
Due date	2026-10-07
Responsible	Marketing
Accountable	Product Manager
Consulted	Sales
Supportive	Customers
Informed	Finance
Macro processes	MP-01 Portfolio MP-17 CX
Module	Market Intelligence
Chain link	Feeds E2E-02

AI assistance

Use a suggestion as a starting point for the result.

Task UFT-01-02 Assess Market Opportunity with its fields filled in.

3.4 Complete the gate checklist

The last task before each gate is **Complete Gate Checklist**. Every **Mandatory** item needs an evidence reference (or an attached file) before **Mark complete** works (BR-005). When all mandatory items are complete or waived, select **Complete checklist task** (BR-004).

CortexPLM Metro City Digital Services Agency English Mehdi Dubois Product Manager

HOME

- Dashboard
- My tasks
- Alerts

LIFECYCLE

- Innovation projects
- Gate board
- WBS & Gantt
- Lessons learned (REX)

PROCESS DESIGN

- Macro processes
- End-to-end processes
- Coverage matrix
- Track configuration
- Phase-gate reference

GOVERNANCE

- Business rules
- Controls (COSO)
- Risks & opportunities

UFT-01-07 · E2E-01 IDEA-TO-BUSINESS PLAN

Complete Gate Checklist (T-1)

Complete mandatory T-1 checklist · [PUB-023 UI Check Permit Kiosk](#)

Gate T-1 checklist
2 of 5 mandatory items complete or waived · 6 items in total (Fast Track)

Decision question: Is the idea strategically aligned and worth a funded opportunity study?

1. Captured idea **Mandatory**
Source: Gate T-1 minimum evidence (Part 8) · Completed by Mehdi Dubois
Evidence: PUB-023-T-1-01 **Complete**
[Reopen](#)

2. Market opportunity assessment **Mandatory**
Source: Gate T-1 minimum evidence (Part 8) · Completed by Mehdi Dubois
Evidence: PUB-023-T-1-02 **Complete**
[Reopen](#)

3. Preliminary business case (NPV, ROI, risk) **Mandatory**
Source: Gate T-1 minimum evidence (Part 8) **Open**
PUB-023-T-1-03 [Mark complete](#) [Attach file](#) [Request waiver](#)

4. Initial risk and compliance register **Mandatory**
Source: Gate T-1 minimum evidence (Part 8) **Open**
Evidence reference (required) [Mark complete](#) [Attach file](#) [Request waiver](#)

5. Portfolio fit **Mandatory**
Source: Gate T-1 minimum evidence (Part 8) **Open**
Evidence reference (required) [Mark complete](#) [Attach file](#) [Request waiver](#)

6. Evidence: Define strategic product themes, goals, and investment horizons **Optional** **Open**
Source: MP-01.1
Evidence reference [Mark complete](#) [Attach file](#) [Request waiver](#)

When every mandatory item is complete or waived, close the checklist task (BR-004).
[Complete checklist task](#)

Accountability (RACSI)

Owner	Chloe Bennani
Evaluator	Mehdi Dubois
Due date	2026-11-08
Responsible	Quality Assurance
Accountable	Product Manager
Consulted	Compliance
Supportive	R&D
Informed	Executive
Macro processes	MP-122 Checklist MP-121 Phase-Gate
Module	Checklist Module
Chain link	Gate for E2E-02

The T-1 checklist: mandatory items need an evidence reference.

3.5 Submit the gate and record the decision

When all tasks are done, the project page shows **Submit gate for decision** on the gate card. The Executive Sponsor then opens **Gate board**, opens the gate, chooses the decision, types a rationale and selects **Record decision**.

Metro City Digital Services Agency
English
Mehdi Dubois
Product Manager

HOME
Dashboard
My tasks
Alerts
LIFECYCLE
Innovation projects
Gate board
WBS & Gantt
Lessons learned (REX)
PROCESS DESIGN
Macro processes
End-to-end processes
Coverage matrix
Track configuration
Phase-gate reference
GOVERNANCE
Business rules
Controls (COSO)
Risks & opportunities

PUB-023 · FAST TRACK · SERVICE

UI Check Permit Kiosk

Checks the wizard.
Active Edit Add lesson learned Delete

E2E-01
1 run(s)
E2E-02
Not started
E2E-03
Not in track
E2E-04
Not in track
E2E-05
Not started
E2E-06
Not in track
E2E-07
Not in track
E2E-08
Not in track
E2E-09
Not in track

Lifecycle & tasks
Business case & risks
Tailoring
AI assistance
Lessons learned
History

E2E-01

Idea-to-Business Plan

Project created (UFS-28 Configure Track & Macro Processes).
In progress 7/8

UFT-01-01 · Capture Strategic Idea
Owner: Mehdi Dubois · Evaluator: Amina Benali · Due 2026-09-30
Done

UFT-01-02 · Assess Market Opportunity
Owner: Youssef Blanc · Evaluator: Mehdi Dubois · Due 2026-10-07
Done

UFT-01-03 · Build Preliminary Business Case
Owner: Marc Martin · Evaluator: Mehdi Dubois · Due 2026-10-14
Done

UFT-01-04 · Assess Risks & Compliance
Owner: Omar Roche · Evaluator: Julie Saidi · Due 2026-10-21
Done

UFT-01-05 · Describe High-Level Capability
Owner: Emma Alaoui · Evaluator: Mehdi Dubois · Due 2026-10-28
Done

Project page: E2E-01 tasks done and the gate ready to submit.

Metro City Digital Services Agency
English
Amina Benali
Executive Sponsor

HOME
Dashboard
My tasks
Alerts
LIFECYCLE
Innovation projects
Gate board
WBS & Gantt
Lessons learned (REX)
PROCESS DESIGN
Macro processes
End-to-end processes
Coverage matrix
Track configuration
Phase-gate reference
GOVERNANCE
Business rules
Controls (COSO)
Risks & opportunities

MP-121 INNOVATION PHASE-GATE MANAGEMENT

Gate board

2 gate packs wait for a Go, Kill, Hold or Recycle decision. Decisions pending more than 10 working days are escalated (BR-008).

Awaiting decision
Open
On hold
Decided

Filter rows
2 rows CSV

Gate	Project	Decision question	Checklist	Submitted	Decision	Status
T-1	PUB-023 · UI Check Permit Kiosk Fast Track	Is the idea strategically aligned and worth a funded opportunity study?	5/6	2026-09-23 1 working days	—	Submitted
T0	PUB-015 · Senior Citizen Transport Card Light Track	Should we commit investment to design and development?	14/15	2026-08-13 30 working days	—	Submitted

Gate board: gates waiting for a decision, with the working days elapsed.

Metro City Digital Services Agency
English
Amina Benali
Executive Sponsor

HOME
Dashboard
My tasks
Alerts
LIFECYCLE
Innovation projects
Gate board
WBS & Gantt
Lessons learned (REX)
PROCESS DESIGN
Macro processes
End-to-end processes
Coverage matrix
Track configuration
Phase-gate reference
GOVERNANCE
Business rules
Controls (COSO)
Risks & opportunities
KPIs

GATE T-1 · E2E-01 IDEA-TO-BUSINESS PLAN

Is the idea strategically aligned and worth a funded opportunity study?

PUB-023 UI Check Permit Kiosk - Fast Track
Submitted Gate review pack (PDF)

5/5
Mandatory items complete or waived
120
NPV (kUSD)
150%
ROI
6/6
Work tasks closed

Minimum evidence for T-1

Captured idea; market opportunity assessment; preliminary business case (NPV, ROI, risk); initial risk and compliance register; portfolio fit.

#	Checklist Item	Evidence	Status
1	Captured idea Mandatory	PUB-023-T-1-01	Complete
2	Market opportunity assessment Mandatory	PUB-023-T-1-02	Complete
3	Preliminary business case (NPV, ROI, risk) Mandatory	PUB-023-T-1-03	Complete
4	Initial risk and compliance register Mandatory	PUB-023-T-1-04	Complete
5	Portfolio fit Mandatory	PUB-023-T-1-05	Complete
6	Evidence: Define strategic product themes, goals, and investment horizons	—	Open

Task results

- UFT-01-01 - Capture Strategic Idea
Capture Strategic Idea done. **Done**
- UFT-01-02 - Assess Market Opportunity
Assess Market Opportunity done. **Done**
- UFT-01-03 - Build Preliminary Business Case
Build Preliminary Business Case done. **Done**
- UFT-01-04 - Assess Risks & Compliance
Assess Risks & Compliance done. **Done**
- UFT-01-05 - Describe High-Level Capability
Describe High-Level Capability done. **Done**
- UFT-01-06 - Establish Product Portfolio Strategy
Establish Product Portfolio Strategy done. **Done**
- UFT-01-07 - Complete Gate Checklist (T-1) **Done**
- UFT-01-08 - Approve T-1 Gate (Go/No-Go) **In progress**

Record the gate decision

Performed by the Executive Sponsor, owned by the Gate Review Board. The project owner cannot decide (CTL-01).

Go Kill Hold Recycle

The project proceeds; the next E2E process starts.

Rationale *

Aligned with strategy; fund the opportunity study.

Recorded with the decision (MP-121 task 11).

Board votes for Board votes against

A vote that is not unanimous is escalated (BR-008).

Record decision

Gate readiness (advisory)

AIUC-12. The board decides; the assessment only summarizes the evidence.

AI use case Context (optional)

AIUC-12 Gate reac Add details for the su

Get suggestion

Gate decision page: evidence summary on the left, decision form on the right.

4. Common Values Used in the Runs

The runs use the same patterns so you can type quickly:

- Result / output of a task: "<task name> done for <project code>. Summary filed as <project code>-<task number>." The exact text is given in every table.
- Evidence reference of a checklist item: <project code>-<gate>-<item number>, for example **PUB-022-T-1-01**.
- Dates: any future date works; the tables show the dates used in the example runs.
- Fields not listed in a table can stay empty.

5. Run 1: Fast Track in the Public Sector

A low-complexity citizen service goes from idea to launch in the Fast Track: E2E-01, E2E-02 and E2E-05 with gates T-1, T0 and T3.

Item	Value
Organization	Metro City Digital Services Agency (Public Sector)
Product Manager	Mehdi Dubois · pm1@metrocity.example
Executive Sponsor	Amina Benali · exec@metrocity.example
Project	PUB-022 Online Parking Permit Renewal
Track	Fast (total score 11 of 35)
End state	Launched · NPV 120 kUSD, ROI 132.1%

Step 1. Create the project

Sign in as **pm1@metrocity.example** (password **Demo#2026**), the Product Manager.

Open **Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Project name	Online Parking Permit Renewal
Description	Residents renew their parking permit online in under five minutes, without visiting a counter.
Offer type	Service
Region	Metro City
Product Manager (owner)	keep Mehdi Dubois
Executive Sponsor	Amina Benali
Strategic impact	select 2
Investment level	select 1
Technical novelty	select 2
Regulatory and safety exposure	select 2
Market scope	select 1
Cross-functional reach	select 2
Product-service integration	select 1
Step 3. Confirm the track	Total score 11 of 35: select Fast Track · recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project PUB-022 created. E2E-01 has started." and the project page opens.

Step 2. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Customer request One-sentence idea statement: Let residents renew parking permits online.	Capture Strategic Idea done for PUB-022. Summary filed as PUB-022-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Residents with an on-street parking permit Addressable market (MUSD): 2 Strategic-fit score (0-100): 78	Assess Market Opportunity done for PUB-022. Summary filed as PUB-022-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 120 Expected net cash flow per year (kUSD): 60 Evaluation horizon (years): 5	Build Preliminary Business Case done for PUB-022. Summary filed as PUB-022-01-03.

#	Task	Fields to fill	Result / output to type
4	UFT-01-04 Assess Risks & Compliance	Discount rate (%): 8 Main risk identified: Payment data exposure Likelihood (1-5): 2 Impact (1-5): 3 Regulated product?: No	Assess Risks & Compliance done for PUB-022. Summary filed as PUB-022-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Online forms, payment gateway, permit database link	Describe High-Level Capability done for PUB-022. Summary filed as PUB-022-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Core Roadmap slot (e.g. 2027-Q2): 2027-Q1	Establish Product Portfolio Strategy done for PUB-022. Summary filed as PUB-022-01-06.

What you will see NPV 120 kUSD, ROI 150%, payback 2 years. Risk added to the risk register.

Evaluation example: Amina Benali is the evaluator of **Capture Strategic Idea**. Sign in as **exec@metrocity.example**, open **My tasks**, filter **To evaluate**, open the task, choose Verdict **Effective**, type Notes **Clear and complete**. and select **Record evaluation**. Then sign in again as **pm1@metrocity.example**.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 6 items; 5 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	PUB-022-T-1-01
2	Market opportunity assessment	PUB-022-T-1-02
3	Preliminary business case (NPV, ROI, risk)	PUB-022-T-1-03
4	Initial risk and compliance register	PUB-022-T-1-04
5	Portfolio fit	PUB-022-T-1-05

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@metrocity.example** (Amina Benali, Executive Sponsor) and open **Gate board**.
2. Open the T-1 line of **PUB-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@metrocity.example** to continue.

Step 3. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for PUB-022. Summary filed as PUB-022-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 140 Expected net cash flow per year (kUSD): 65 Evaluation horizon (years): 5	Develop Detailed Business Case done for PUB-022. Summary filed as PUB-022-02-02.

#	Task	Fields to fill	Result / output to type
3	UFT-02-03 Define High-Level Functional Specs	Discount rate (%): 8 —	Define High-Level Functional Specs done for PUB-022. Summary filed as PUB-022-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	—	Map Preliminary Customer Journey done for PUB-022. Summary filed as PUB-022-02-04.
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 35	Conduct Detailed Profitability Analysis done for PUB-022. Summary filed as PUB-022-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: GDPR, PCI DSS for card payments	Validate Regulatory Aspects done for PUB-022. Summary filed as PUB-022-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: High	Assess Technical Feasibility done for PUB-022. Summary filed as PUB-022-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for PUB-022. Summary filed as PUB-022-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for PUB-022. Summary filed as PUB-022-02-09.

What you will see NPV 120 kUSD, ROI 132.1%, payback 2.2 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 6 items; 6 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	PUB-022-T0-01
2	Detailed business case and profitability analysis	PUB-022-T0-02
3	High-level functional specifications	PUB-022-T0-03
4	Preliminary customer journey	PUB-022-T0-04
5	Regulatory validation	PUB-022-T0-05
6	Technical feasibility	PUB-022-T0-06

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@metrocity.example** (Amina Benali, Executive Sponsor) and open **Gate board**.
2. Open the T0 line of **PUB-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@metrocity.example** to continue.

Step 4. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for PUB-022. Summary filed as PUB-022-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-11-22 (any future date)	Develop Detailed Launch Plan done for PUB-022. Summary filed as PUB-022-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for PUB-022. Summary filed as PUB-022-05-03.
4	UFT-05-04 Develop Marketing	—	Develop Marketing & Sales Materials done

#	Task	Fields to fill	Result / output to type
	& Sales Materials		for PUB-022. Summary filed as PUB-022-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for PUB-022. Summary filed as PUB-022-05-05.
6	UFT-05-06 Train Teams	People trained: 14	Train Teams done for PUB-022. Summary filed as PUB-022-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for PUB-022. Summary filed as PUB-022-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for PUB-022. Summary filed as PUB-022-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 6 items; 5 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	PUB-022-T3-01
2	Marketing and sales materials	PUB-022-T3-02
3	Trained teams	PUB-022-T3-03
4	Validated customer journey	PUB-022-T3-04
5	Final regulatory validation	PUB-022-T3-05

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@metrocity.example** (Amina Benali, Executive Sponsor) and open **Gate board**.
2. Open the T3 line of **PUB-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: no further process starts; see the result of the run below. Sign in again as **pm1@metrocity.example** to continue.

Result of the run

The project status is **Launched**. The Fast Track ends at T3; performance and retirement follow the parent product (Rule R3).

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

6. Run 2: Fast Track in Transportation, with a skipped task and a Recycle decision

A Fast Track feature for bus passengers. One task is skipped under Rule R2, and the board sends the T0 gate back once (Recycle) before approving it.

Item	Value
Organization	Orvane Transit Group (Transportation)
Product Manager	Rachid Nguyen · pm1@orvane.example
Executive Sponsor	Laura Mansouri · exec@orvane.example
Project	TRN-022 Real-time Bus Crowding Indicator
Track	Fast (total score 13 of 35)
End state	Launched · NPV 140 kUSD, ROI 106.5%

Step 1. Create the project

Sign in as **pm1@orvane.example** (password **Demo#2026**), the Product Manager.

Open **Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Project name	Real-time Bus Crowding Indicator
Description	Shows how full the next bus is in the passenger app, using existing automatic passenger counters.
Offer type	Product-Service
Region	Orvane network
Product Manager (owner)	keep Rachid Nguyen
Executive Sponsor	Laura Mansouri
Strategic impact	select 2
Investment level	select 2
Technical novelty	select 2
Regulatory and safety exposure	select 1
Market scope	select 2
Cross-functional reach	select 2
Product-service integration	select 2
Step 3. Confirm the track	Total score 13 of 35: select Fast Track · recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project TRN-022 created. E2E-01 has started." and the project page opens.

Step 2. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Market trend One-sentence idea statement: Show bus occupancy in real time in the passenger app.	Capture Strategic Idea done for TRN-022. Summary filed as TRN-022-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Daily commuters on the ten busiest lines Addressable market (MUSD): 5 Strategic-fit score (0-100): 71	Assess Market Opportunity done for TRN-022. Summary filed as TRN-022-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 210 Expected net cash flow per year	Build Preliminary Business Case done for TRN-022. Summary filed as TRN-022-01-

#	Task	Fields to fill	Result / output to type
		(kUSD): 90 Evaluation horizon (years): 5 Discount rate (%): 9	03.
4	UFT-01-04 Assess Risks & Compliance	Main risk identified: Counter data latency above 2 minutes Likelihood (1-5): 3 Impact (1-5): 2 Regulated product?: No	Assess Risks & Compliance done for TRN-022. Summary filed as TRN-022-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Passenger counter feed, mobile app update, data pipeline	Describe High-Level Capability done for TRN-022. Summary filed as TRN-022-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Adjacent Roadmap slot (e.g. 2027-Q2): 2027-Q2	Establish Product Portfolio Strategy done for TRN-022. Summary filed as TRN-022-01-06.

What you will see NPV 140 kUSD, ROI 114.3%, payback 2.3 years. Risk added to the risk register.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 6 items; 5 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	TRN-022-T-1-01
2	Market opportunity assessment	TRN-022-T-1-02
3	Preliminary business case (NPV, ROI, risk)	TRN-022-T-1-03
4	Initial risk and compliance register	TRN-022-T-1-04
5	Portfolio fit	TRN-022-T-1-05

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@orvane.example** (Laura Mansouri, Executive Sponsor) and open **Gate board**.
2. Open the T-1 line of **TRN-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@orvane.example** to continue.

Step 3. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for TRN-022. Summary filed as TRN-022-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 230 Expected net cash flow per year (kUSD): 95 Evaluation horizon (years): 5 Discount rate (%): 9	Develop Detailed Business Case done for TRN-022. Summary filed as TRN-022-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for TRN-022. Summary filed as TRN-022-02-03.
4	UFT-02-04 Map Preliminary	Select Skip (Rule R2) . Reason: The	Select Skip task .

#	Task	Fields to fill	Result / output to type
	Customer Journey	dependent macro process is not activated in the Fast Track.	
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 28	Conduct Detailed Profitability Analysis done for TRN-022. Summary filed as TRN-022-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: GDPR (location data), accessibility of the app	Validate Regulatory Aspects done for TRN-022. Summary filed as TRN-022-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: Medium	Assess Technical Feasibility done for TRN-022. Summary filed as TRN-022-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for TRN-022. Summary filed as TRN-022-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for TRN-022. Summary filed as TRN-022-02-09.

What you will see NPV 140 kUSD, ROI 106.5%, payback 2.4 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 6 items; 6 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	TRN-022-T0-01
2	Detailed business case and profitability analysis	TRN-022-T0-02
3	High-level functional specifications	TRN-022-T0-03
4	Preliminary customer journey	TRN-022-T0-04
5	Regulatory validation	TRN-022-T0-05
6	Technical feasibility	TRN-022-T0-06

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@orvane.example** (Laura Mansouri, Executive Sponsor) and open **Gate board**.
2. Open the T0 line of **TRN-022**.
3. Under **Decision**, select **Recycle**. Under **Tasks to rework**, tick **UFT-02-02 Develop Detailed Business Case**.
4. In **Rationale**, type **The business case needs a sensitivity analysis before we commit.**, then select **Record decision**.
5. Sign in again as **pm1@orvane.example**. The reworked task is back to **To do**, and so are the checklist and gate tasks. Complete the task again with the same values, complete the checklist task again (items already complete stay complete), then submit the gate again.

Step 4. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 230 Expected net cash flow per year (kUSD): 95 Evaluation horizon (years): 5 Discount rate (%): 9	Develop Detailed Business Case done for TRN-022. Summary filed as TRN-022-02-02.

What you will see NPV 140 kUSD, ROI 106.5%, payback 2.4 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 6 items; 6 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	TRN-022-T0-01
2	Detailed business case and profitability analysis	TRN-022-T0-02
3	High-level functional specifications	TRN-022-T0-03
4	Preliminary customer journey	TRN-022-T0-04
5	Regulatory validation	TRN-022-T0-05
6	Technical feasibility	TRN-022-T0-06

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@orvane.example** (Laura Mansouri, Executive Sponsor) and open **Gate board**.
2. Open the T0 line of **TRN-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@orvane.example** to continue.

Step 5. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for TRN-022. Summary filed as TRN-022-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-12-07 (any future date)	Develop Detailed Launch Plan done for TRN-022. Summary filed as TRN-022-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for TRN-022. Summary filed as TRN-022-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for TRN-022. Summary filed as TRN-022-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for TRN-022. Summary filed as TRN-022-05-05.
6	UFT-05-06 Train Teams	People trained: 40	Train Teams done for TRN-022. Summary filed as TRN-022-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for TRN-022. Summary filed as TRN-022-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for TRN-022. Summary filed as TRN-022-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 6 items; 5 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	TRN-022-T3-01
2	Marketing and sales materials	TRN-022-T3-02
3	Trained teams	TRN-022-T3-03
4	Validated customer journey	TRN-022-T3-04
5	Final regulatory validation	TRN-022-T3-05

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@orvane.example** (Laura Mansouri, Executive Sponsor) and open **Gate board**.
2. Open the T3 line of **TRN-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: no further process starts; see the result of the run below. Sign in again as **pm1@orvane.example** to continue.

Result of the run

The project status is **Launched**. The Fast Track ends at T3; performance and retirement follow the parent product (Rule R3).

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

7. Run 3: Light Track in Agro-Business (Dairy), from idea to relaunch

A new dairy product runs the whole Light Track: six gate decisions, the E2E-09 market campaign, the performance review (E2E-07) with Rule R1, and a relaunch through E2E-08 Branch A that loops back to launch (E2E-05).

Item	Value
Organization	Valdora Dairy Cooperative (Agro-Business - Dairy Products)
Product Manager	Leila Mansouri · pm1@valdora.example
Executive Sponsor	Daniel Roche · exec@valdora.example
Project	DAI-022 Lactose-free Greek Yogurt 500 g
Track	Light (total score 19 of 35)
End state	Active · NPV 389 kUSD, ROI 114.3%

Step 1. Prepare the Light Track observation period

1. Sign in as **process@valdora.example** (Mehdi Carpentier, Process Owner / Track Administrator).
2. Open **Process design > Track configuration**.
3. In the card **Light Track observation period (Rule R1)**, type **0** in **Observation period (days)** and select **Save**.
4. Sign out. With 0 days, the performance review (E2E-07) starts right after the T3 Go-Live decision, so you can finish the whole run today. The default is 182 days.

Step 2. Create the project

Sign in as **pm1@valdora.example** (password **Demo#2026**), the Product Manager.

Open **Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Project name	Lactose-free Greek Yogurt 500 g
Description	A lactose-free strained yogurt for the national retail chains, made on the existing cup line.
Offer type	Product
Region	National retail
Product Manager (owner)	keep Leila Mansouri
Executive Sponsor	Daniel Roche
Strategic impact	select 3
Investment level	select 3
Technical novelty	select 2
Regulatory and safety exposure	select 3
Market scope	select 3
Cross-functional reach	select 3
Product-service integration	select 2
Step 3. Confirm the track	Total score 19 of 35: select Light Track · recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project DAI-022 created. E2E-01 has started." and the project page opens.

Step 3. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Market trend One-sentence idea statement: Launch a lactose-free Greek yogurt in 500 g cups.	Capture Strategic Idea done for DAI-022. Summary filed as DAI-022-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Lactose-intolerant households Addressable market (MUSD): 18 Strategic-fit score (0-100): 74	Assess Market Opportunity done for DAI-022. Summary filed as DAI-022-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 650 Expected net cash flow per year (kUSD): 240 Evaluation horizon (years): 6 Discount rate (%): 10	Build Preliminary Business Case done for DAI-022. Summary filed as DAI-022-01-03.
4	UFT-01-04 Assess Risks & Compliance	Main risk identified: Lactase enzyme supply shortage Likelihood (1-5): 3 Impact (1-5): 3 Regulated product?: Yes	Assess Risks & Compliance done for DAI-022. Summary filed as DAI-022-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Lactase treatment, straining, cup filling	Describe High-Level Capability done for DAI-022. Summary filed as DAI-022-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Adjacent Roadmap slot (e.g. 2027-Q2): 2027-Q3	Establish Product Portfolio Strategy done for DAI-022. Summary filed as DAI-022-01-06.

What you will see NPV 395 kUSD, ROI 121.5%, payback 2.7 years. Risk added to the risk register.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	DAI-022-T-1-01
2	Market opportunity assessment	DAI-022-T-1-02
3	Preliminary business case (NPV, ROI, risk)	DAI-022-T-1-03
4	Initial risk and compliance register	DAI-022-T-1-04
5	Portfolio fit	DAI-022-T-1-05
7	Evidence: Elicit and capture requirements from all sources	DAI-022-T-1-07
10	Evidence: Monitor regulatory intelligence	DAI-022-T-1-10
13	Evidence: Define and manage lifecycle workflows	DAI-022-T-1-13

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@valdora.example** (Daniel Roche, Executive Sponsor) and open **Gate board**.
2. Open the T-1 line of **DAI-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@valdora.example** to continue.

Step 4. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for DAI-022. Summary filed as DAI-022-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 700 Expected net cash flow per year (kUSD): 250 Evaluation horizon (years): 6 Discount rate (%): 10	Develop Detailed Business Case done for DAI-022. Summary filed as DAI-022-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for DAI-022. Summary filed as DAI-022-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	—	Map Preliminary Customer Journey done for DAI-022. Summary filed as DAI-022-02-04.
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 32	Conduct Detailed Profitability Analysis done for DAI-022. Summary filed as DAI-022-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: Food labelling rules, lactose-free claim threshold	Validate Regulatory Aspects done for DAI-022. Summary filed as DAI-022-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: High	Assess Technical Feasibility done for DAI-022. Summary filed as DAI-022-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for DAI-022. Summary filed as DAI-022-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for DAI-022. Summary filed as DAI-022-02-09.

What you will see NPV 389 kUSD, ROI 114.3%, payback 2.8 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 15 items; 9 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	DAI-022-T0-01
2	Detailed business case and profitability analysis	DAI-022-T0-02
3	High-level functional specifications	DAI-022-T0-03
4	Preliminary customer journey	DAI-022-T0-04
5	Regulatory validation	DAI-022-T0-05
6	Technical feasibility	DAI-022-T0-06
7	Development plan	DAI-022-T0-07
10	Evidence: Perform should-cost and target costing	DAI-022-T0-10
13	Evidence: Monitor regulatory intelligence	DAI-022-T0-13

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@valdora.example** (Daniel Roche, Executive Sponsor) and open **Gate board**.
2. Open the T0 line of **DAI-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.

5. Result: **E2E-03** starts automatically. Sign in again as **pm1@valdora.example** to continue.

Step 5. E2E-03 Business Proposal-to-Design

Open the project, tab **Lifecycle & tasks**, card **E2E-03**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-03-01 Develop Detailed Specifications	—	Develop Detailed Specifications done for DAI-022. Summary filed as DAI-022-03-01.
2	UFT-03-02 Validate Marketing Specifications	—	Validate Marketing Specifications done for DAI-022. Summary filed as DAI-022-03-02.
3	UFT-03-03 Validate Customer Journey	—	Validate Customer Journey done for DAI-022. Summary filed as DAI-022-03-03.
4	UFT-03-04 Model Detailed Processes	—	Model Detailed Processes done for DAI-022. Summary filed as DAI-022-03-04.
5	UFT-03-05 Develop Detailed Design	—	Develop Detailed Design done for DAI-022. Summary filed as DAI-022-03-05.
6	UFT-03-06 Build Functional Prototype	—	Build Functional Prototype done for DAI-022. Summary filed as DAI-022-03-06.
7	UFT-03-07 Validate Architectures	—	Validate Architectures done for DAI-022. Summary filed as DAI-022-03-07.
8	UFT-03-08 Develop Development Plan	—	Develop Development Plan done for DAI-022. Summary filed as DAI-022-03-08.

Open the task **Complete Gate Checklist (T1)**. The gate T1 checklist has 15 items; 9 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed specifications	DAI-022-T1-01
2	Validated marketing specifications and customer journey	DAI-022-T1-02
3	Process models	DAI-022-T1-03
4	Detailed design	DAI-022-T1-04
5	Functional prototype	DAI-022-T1-05
6	Architecture validation	DAI-022-T1-06
7	Detailed development plan	DAI-022-T1-07
10	Evidence: Define personas and segments	DAI-022-T1-10
13	Evidence: Train generative AI models	DAI-022-T1-13

Submit the gate: on the project page, card **Gate T1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@valdora.example** (Daniel Roche, Executive Sponsor) and open **Gate board**.
2. Open the T1 line of **DAI-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Design validated; start development.**, then select **Record decision**.
5. Result: **E2E-04** starts automatically. Sign in again as **pm1@valdora.example** to continue.

Step 6. E2E-04 Design-to-Development

Open the project, tab **Lifecycle & tasks**, card **E2E-04**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-04-01 Support Operational Introduction	—	Support Operational Introduction done for DAI-022. Summary filed as DAI-022-04-01.
2	UFT-04-02 Conduct Operational Readiness Testing	—	Conduct Operational Readiness Testing done for DAI-022. Summary filed as DAI-022-04-02.
3	UFT-04-03 Manage Product Configuration	—	Manage Product Configuration done for DAI-022. Summary filed as DAI-022-04-03.
4	UFT-04-04 Develop Product Offering Procedures	—	Develop Product Offering Procedures done for DAI-022. Summary filed as DAI-022-04-04.
5	UFT-04-05 Manage Acceptance Testing	Acceptance tests passed (%): 97	Manage Acceptance Testing done for DAI-022. Summary filed as DAI-022-04-05.
6	UFT-04-06 Develop Preliminary Launch Plan	—	Develop Preliminary Launch Plan done for DAI-022. Summary filed as DAI-022-04-06.
7	UFT-04-07 Complete Functionalities	—	Complete Functionalities done for DAI-022. Summary filed as DAI-022-04-07.

Open the task **Complete Gate Checklist (T2)**. The gate T2 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Completed functionalities	DAI-022-T2-01
2	Operational readiness and acceptance test results	DAI-022-T2-02
3	Configuration baseline	DAI-022-T2-03
4	Offering procedures	DAI-022-T2-04
5	Preliminary launch plan	DAI-022-T2-05
7	Evidence: Define manufacturing process plans and routings	DAI-022-T2-07
10	Evidence: Initiate and submit change requests (ECR)	DAI-022-T2-10
13	Evidence: Develop go-to-market plans	DAI-022-T2-13

Submit the gate: on the project page, card **Gate T2**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@valdora.example** (Daniel Roche, Executive Sponsor) and open **Gate board**.
2. Open the T2 line of **DAI-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Product complete and tested; prepare launch.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@valdora.example** to continue.

Step 7. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for DAI-022. Summary filed as DAI-022-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-12-22 (any future date)	Develop Detailed Launch Plan done for DAI-022. Summary filed as DAI-022-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for DAI-022. Summary filed as DAI-022-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for DAI-022. Summary filed as DAI-022-05-04.

#	Task	Fields to fill	Result / output to type
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for DAI-022. Summary filed as DAI-022-05-05.
6	UFT-05-06 Train Teams	People trained: 60	Train Teams done for DAI-022. Summary filed as DAI-022-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for DAI-022. Summary filed as DAI-022-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for DAI-022. Summary filed as DAI-022-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	DAI-022-T3-01
2	Marketing and sales materials	DAI-022-T3-02
3	Trained teams	DAI-022-T3-03
4	Validated customer journey	DAI-022-T3-04
5	Final regulatory validation	DAI-022-T3-05
7	Evidence: Define personas and segments	DAI-022-T3-07
10	Evidence: Define and manage quality plans (APQP, PPAP)	DAI-022-T3-10
13	Evidence: Onboard and certify partners	DAI-022-T3-13

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@valdora.example** (Daniel Roche, Executive Sponsor) and open **Gate board**.
2. Open the T3 line of **DAI-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-07, E2E-09** start automatically. Sign in again as **pm1@valdora.example** to continue.

Step 8. E2E-07 After-Sales-to-Performance

Open the project, tab **Lifecycle & tasks**, card **E2E-07**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-06-04 Track Customer Satisfaction (light form, Rule R1)	CSAT (1-5): 4.3 Net Promoter Score (-100 to 100): 38	Track Customer Satisfaction done for DAI-022. Summary filed as DAI-022-06-04.
2	UFT-06-05 Track Product Performance (light form, Rule R1)	—	Track Product Performance done for DAI-022. Summary filed as DAI-022-06-05.
3	UFT-07-01 Evaluate Overall Performance	—	Evaluate Overall Performance done for DAI-022. Summary filed as DAI-022-07-01.
4	UFT-07-02 Analyze Profitability	Revenue to date (kUSD): 1450 Cost of goods sold (kUSD): 960	Analyze Profitability done for DAI-022. Summary filed as DAI-022-07-02.
5	UFT-07-03 Gather Customer Experience Feedback	CSAT (1-5): 4.2 Net Promoter Score (-100 to 100): 35	Gather Customer Experience Feedback done for DAI-022. Summary filed as DAI-022-07-03.
6	UFT-07-04 Develop Improvement	Recommendation to the T5 gate: Relaunch	Develop Improvement Recommendations done for DAI-022. Summary filed as DAI-

#	Task	Fields to fill	Result / output to type
	Recommendations		022-07-04.

Open the task **Complete Gate Checklist (T5)**. The gate T5 checklist has 15 items; 7 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Overall performance evaluation	DAI-022-T5-01
2	Profitability analysis	DAI-022-T5-02
3	Customer experience feedback	DAI-022-T5-03
4	Improvement recommendations	DAI-022-T5-04
7	Evidence: Define personas and segments	DAI-022-T5-07
10	Evidence: Provide generative design	DAI-022-T5-10
13	Evidence: Manage lifecycle costing	DAI-022-T5-13

Step 9. E2E-09 Market Strategy-to-Campaign

Open the project, tab **Lifecycle & tasks**, card **E2E-09**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-09-01 Gather Customer Experience Data	—	Gather Customer Experience Data done for DAI-022. Summary filed as DAI-022-09-01.
2	UFT-09-02 Gather Product Delivery Feedback	—	Gather Product Delivery Feedback done for DAI-022. Summary filed as DAI-022-09-02.
3	UFT-09-03 Establish Market Segments	—	Establish Market Segments done for DAI-022. Summary filed as DAI-022-09-03.
4	UFT-09-04 Link Segments & Products	—	Link Segments & Products done for DAI-022. Summary filed as DAI-022-09-04.
5	UFT-09-05 Establish Market Strategy	—	Establish Market Strategy done for DAI-022. Summary filed as DAI-022-09-05.
6	UFT-09-06 Plan & Develop Campaign	—	Plan & Develop Campaign done for DAI-022. Summary filed as DAI-022-09-06.
7	UFT-09-07 Launch & Monitor Campaign	—	Launch & Monitor Campaign done for DAI-022. Summary filed as DAI-022-09-07.
8	UFT-09-08 Complete Campaign & Report	Qualified leads generated: 420 Conversion rate (%): 12	Complete Campaign & Report done for DAI-022. Summary filed as DAI-022-09-08.

Submit the gate: on the project page, card **Gate T5**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@valdora.example** (Daniel Roche, Executive Sponsor) and open **Gate board**.
2. Open the T5 line of **DAI-022**.
3. Under **Decision**, keep **Go**.
4. Under **Next path (E2E-08)**, select **Relaunch (Branch A)**.
5. In **Rationale**, type **Performance is below target but fixable; relaunch.**, then select **Record decision**.
6. Result: **E2E-08** starts automatically. Sign in again as **pm1@valdora.example** to continue.

Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch A

Open the project, tab **Lifecycle & tasks**, card **E2E-08**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-08-01 Update Product Specifications	—	Update Product Specifications done for DAI-022. Summary filed as DAI-022-08-01.
2	UFT-08-02 Support Operational Re-introduction	—	Support Operational Re-introduction done for DAI-022. Summary filed as DAI-022-08-02.
3	UFT-08-03 Manage Product Improvements	—	Manage Product Improvements done for DAI-022. Summary filed as DAI-022-08-03.
4	UFT-08-04 Approve for Relaunch	Relaunch re-entry point: E2E-05	Approve for Relaunch done for DAI-022. Summary filed as DAI-022-08-04.

Step 11. E2E-05 Development-to-Launch (run 2)

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for DAI-022. Summary filed as DAI-022-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-12-22 (any future date)	Develop Detailed Launch Plan done for DAI-022. Summary filed as DAI-022-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for DAI-022. Summary filed as DAI-022-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for DAI-022. Summary filed as DAI-022-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for DAI-022. Summary filed as DAI-022-05-05.
6	UFT-05-06 Train Teams	People trained: 60	Train Teams done for DAI-022. Summary filed as DAI-022-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for DAI-022. Summary filed as DAI-022-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for DAI-022. Summary filed as DAI-022-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	DAI-022-T3-01
2	Marketing and sales materials	DAI-022-T3-02
3	Trained teams	DAI-022-T3-03
4	Validated customer journey	DAI-022-T3-04
5	Final regulatory validation	DAI-022-T3-05
7	Evidence: Define personas and segments	DAI-022-T3-07
10	Evidence: Define and manage quality plans (APQP, PPAP)	DAI-022-T3-10
13	Evidence: Onboard and certify partners	DAI-022-T3-13

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@valdora.example** (Daniel Roche, Executive Sponsor) and open **Gate board**.
2. Open the T3 line of **DAI-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-07, E2E-09** start automatically. Sign in again as **pm1@valdora.example** to continue.

Result of the run

The project stays **Active**, now in E2E-07 after gate T3. Active · open runs: E2E-07, E2E-09

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

8. Run 4: Full Track in Healthcare, from idea to retirement

A safety-critical medical device runs the complete Full Track: all nine E2E processes and all eight gates, ending with retirement through E2E-08 Branch B.

Item	Value
Organization	Meridale Health Network (Healthcare)
Product Manager	Youssef Roche · pm1@meridale.example
Executive Sponsor	Julie Alaoui · exec@meridale.example
Project	HLT-022 Remote Cardiac Monitoring Patch
Track	Full (total score 29 of 35)
End state	Retired · NPV 1527 kUSD, ROI 120.8%

Step 1. Create the project

Sign in as **pm1@meridale.example** (password **Demo#2026**), the Product Manager.

Open **Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Project name	Remote Cardiac Monitoring Patch
Description	A wearable ECG patch that sends arrhythmia alerts to the cardiology team.
Offer type	Product-Service
Region	Meridale hospitals
Product Manager (owner)	keep Youssef Roche
Executive Sponsor	Julie Alaoui
Strategic impact	select 5
Investment level	select 4
Technical novelty	select 4
Regulatory and safety exposure	select 5
Market scope	select 3
Cross-functional reach	select 4
Product-service integration	select 4
Safety-critical product	tick the box
Step 3. Confirm the track	Total score 29 of 35: select Full Track · recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project HLT-022 created. E2E-01 has started." and the project page opens.

Step 2. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Internal - strategy One-sentence idea statement: Monitor cardiac patients at home with a wearable ECG patch.	Capture Strategic Idea done for HLT-022. Summary filed as HLT-022-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Post-discharge cardiac patients Addressable market (MUSD): 40 Strategic-fit score (0-100): 86	Assess Market Opportunity done for HLT-022. Summary filed as HLT-022-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 2400 Expected net cash flow per year (kUSD): 780 Evaluation horizon (years): 7	Build Preliminary Business Case done for HLT-022. Summary filed as HLT-022-01-03.

#	Task	Fields to fill	Result / output to type
4	UFT-01-04 Assess Risks & Compliance	Discount rate (%): 9 Main risk identified: Missed arrhythmia alert Likelihood (1-5): 2 Impact (1-5): 5 Regulated product?: Yes	Assess Risks & Compliance done for HLT-022. Summary filed as HLT-022-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Biosensor design, secure telemetry, clinical dashboard	Describe High-Level Capability done for HLT-022. Summary filed as HLT-022-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Transformational Roadmap slot (e.g. 2027-Q2): 2028-Q1	Establish Product Portfolio Strategy done for HLT-022. Summary filed as HLT-022-01-06.

What you will see NPV 1526 kUSD, ROI 127.5%, payback 3.1 years. Risk added to the risk register.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	HLT-022-T-1-01
2	Market opportunity assessment	HLT-022-T-1-02
3	Preliminary business case (NPV, ROI, risk)	HLT-022-T-1-03
4	Initial risk and compliance register	HLT-022-T-1-04
5	Portfolio fit	HLT-022-T-1-05
7	Evidence: Elicit and capture requirements from all sources	HLT-022-T-1-07
9	Evidence: Perform should-cost and target costing	HLT-022-T-1-09
11	Evidence: Manage invention disclosures and patent filings	HLT-022-T-1-11
13	Evidence: Define and manage lifecycle workflows	HLT-022-T-1-13
15	Evidence: Provide generative design	HLT-022-T-1-15
17	Evidence: Structure and categorize requirements	HLT-022-T-1-17
19	Evidence: Manage lifecycle costing	HLT-022-T-1-19
21	Evidence: Manage trademark and copyright registrations	HLT-022-T-1-21
23	Evidence: Enforce GRC policies	HLT-022-T-1-23
25	Evidence: Automate data classification	HLT-022-T-1-25
27	Evidence: Analyze and validate requirements	HLT-022-T-1-27
29	Evidence: Analyze profitability	HLT-022-T-1-29

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@meridale.example** (Julie Alaoui, Executive Sponsor) and open **Gate board**.
2. Open the T-1 line of **HLT-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@meridale.example** to continue.

Step 3. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for HLT-022. Summary filed as HLT-022-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 2600 Expected net cash flow per year (kUSD): 820 Evaluation horizon (years): 7 Discount rate (%): 9	Develop Detailed Business Case done for HLT-022. Summary filed as HLT-022-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for HLT-022. Summary filed as HLT-022-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	—	Map Preliminary Customer Journey done for HLT-022. Summary filed as HLT-022-02-04.
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 41	Conduct Detailed Profitability Analysis done for HLT-022. Summary filed as HLT-022-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: EU MDR class IIa, IEC 60601, ISO 13485, GDPR	Validate Regulatory Aspects done for HLT-022. Summary filed as HLT-022-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: Medium	Assess Technical Feasibility done for HLT-022. Summary filed as HLT-022-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for HLT-022. Summary filed as HLT-022-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for HLT-022. Summary filed as HLT-022-02-09.

What you will see NPV 1527 kUSD, ROI 120.8%, payback 3.2 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 30 items; 18 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	HLT-022-T0-01
2	Detailed business case and profitability analysis	HLT-022-T0-02
3	High-level functional specifications	HLT-022-T0-03
4	Preliminary customer journey	HLT-022-T0-04
5	Regulatory validation	HLT-022-T0-05
6	Technical feasibility	HLT-022-T0-06
7	Development plan	HLT-022-T0-07
9	Evidence: Elicit and capture requirements from all sources	HLT-022-T0-09
11	Evidence: Manage design process (conceptual, detailed, validation)	HLT-022-T0-11
13	Evidence: Monitor regulatory intelligence	HLT-022-T0-13
15	Evidence: Define and manage lifecycle workflows	HLT-022-T0-15
17	Evidence: Manage invention disclosures and patent filings	HLT-022-T0-17
19	Evidence: Structure and categorize requirements	HLT-022-T0-19
21	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	HLT-022-T0-21
23	Evidence: Prepare and submit filings	HLT-022-T0-23
25	Evidence: Enforce GRC policies	HLT-022-T0-25
27	Evidence: Manage trademark and copyright registrations	HLT-022-T0-27
29	Evidence: Analyze and validate requirements	HLT-022-T0-29

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@meridale.example** (Julie Alaoui, Executive Sponsor) and open **Gate board**.
2. Open the T0 line of **HLT-022**.
3. Under **Decision**, keep **Go**.

4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-03** starts automatically. Sign in again as **pm1@meridale.example** to continue.

Step 4. E2E-03 Business Proposal-to-Design

Open the project, tab **Lifecycle & tasks**, card **E2E-03**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-03-01 Develop Detailed Specifications	—	Develop Detailed Specifications done for HLT-022. Summary filed as HLT-022-03-01.
2	UFT-03-02 Validate Marketing Specifications	—	Validate Marketing Specifications done for HLT-022. Summary filed as HLT-022-03-02.
3	UFT-03-03 Validate Customer Journey	—	Validate Customer Journey done for HLT-022. Summary filed as HLT-022-03-03.
4	UFT-03-04 Model Detailed Processes	—	Model Detailed Processes done for HLT-022. Summary filed as HLT-022-03-04.
5	UFT-03-05 Develop Detailed Design	—	Develop Detailed Design done for HLT-022. Summary filed as HLT-022-03-05.
6	UFT-03-06 Build Functional Prototype	—	Build Functional Prototype done for HLT-022. Summary filed as HLT-022-03-06.
7	UFT-03-07 Validate Architectures	—	Validate Architectures done for HLT-022. Summary filed as HLT-022-03-07.
8	UFT-03-08 Develop Development Plan	—	Develop Development Plan done for HLT-022. Summary filed as HLT-022-03-08.

Open the task **Complete Gate Checklist (T1)**. The gate T1 checklist has 30 items; 18 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed specifications	HLT-022-T1-01
2	Validated marketing specifications and customer journey	HLT-022-T1-02
3	Process models	HLT-022-T1-03
4	Detailed design	HLT-022-T1-04
5	Functional prototype	HLT-022-T1-05
6	Architecture validation	HLT-022-T1-06
7	Detailed development plan	HLT-022-T1-07
9	Evidence: Manage design process (conceptual, detailed, validation)	HLT-022-T1-09
11	Evidence: Develop go-to-market plans	HLT-022-T1-11
13	Evidence: Train generative AI models	HLT-022-T1-13
15	Evidence: Initiate and submit change requests (ECR)	HLT-022-T1-15
17	Evidence: Define and manage lifecycle workflows	HLT-022-T1-17
19	Evidence: Monitor regulatory intelligence	HLT-022-T1-19
21	Evidence: Perform should-cost and target costing	HLT-022-T1-21
23	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	HLT-022-T1-23
25	Evidence: Prepare collateral	HLT-022-T1-25
27	Evidence: Generate design alternatives	HLT-022-T1-27
29	Evidence: Assess change impact (cost, schedule, quality, compliance)	HLT-022-T1-29

Submit the gate: on the project page, card **Gate T1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@meridale.example** (Julie Alaoui, Executive Sponsor) and open **Gate board**.
2. Open the T1 line of **HLT-022**.

3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Design validated; start development.**, then select **Record decision**.
5. Result: **E2E-04** starts automatically. Sign in again as **pm1@meridale.example** to continue.

Step 5. E2E-04 Design-to-Development

Open the project, tab **Lifecycle & tasks**, card **E2E-04**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-04-01 Support Operational Introduction	—	Support Operational Introduction done for HLT-022. Summary filed as HLT-022-04-01.
2	UFT-04-02 Conduct Operational Readiness Testing	—	Conduct Operational Readiness Testing done for HLT-022. Summary filed as HLT-022-04-02.
3	UFT-04-03 Manage Product Configuration	—	Manage Product Configuration done for HLT-022. Summary filed as HLT-022-04-03.
4	UFT-04-04 Develop Product Offering Procedures	—	Develop Product Offering Procedures done for HLT-022. Summary filed as HLT-022-04-04.
5	UFT-04-05 Manage Acceptance Testing	Acceptance tests passed (%): 99	Manage Acceptance Testing done for HLT-022. Summary filed as HLT-022-04-05.
6	UFT-04-06 Develop Preliminary Launch Plan	—	Develop Preliminary Launch Plan done for HLT-022. Summary filed as HLT-022-04-06.
7	UFT-04-07 Complete Functionalities	—	Complete Functionalities done for HLT-022. Summary filed as HLT-022-04-07.

Open the task **Complete Gate Checklist (T2)**. The gate T2 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Completed functionalities	HLT-022-T2-01
2	Operational readiness and acceptance test results	HLT-022-T2-02
3	Configuration baseline	HLT-022-T2-03
4	Offering procedures	HLT-022-T2-04
5	Preliminary launch plan	HLT-022-T2-05
7	Evidence: Define manufacturing process plans and routings	HLT-022-T2-07
9	Evidence: Create and manage Engineering BOM (eBOM)	HLT-022-T2-09
11	Evidence: Design and model processes (BPMN)	HLT-022-T2-11
13	Evidence: Develop go-to-market plans	HLT-022-T2-13
15	Evidence: Provide generative design	HLT-022-T2-15
17	Evidence: Monitor regulatory intelligence	HLT-022-T2-17
19	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	HLT-022-T2-19
21	Evidence: Manage non-conformance reports (NCR)	HLT-022-T2-21
23	Evidence: Assess change impact (cost, schedule, quality, compliance)	HLT-022-T2-23
25	Evidence: Review and approve	HLT-022-T2-25
27	Evidence: Enforce GRC policies	HLT-022-T2-27
29	Evidence: Map journeys and touchpoints	HLT-022-T2-29

Submit the gate: on the project page, card **Gate T2**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@meridale.example** (Julie Alaoui, Executive Sponsor) and open **Gate board**.
2. Open the T2 line of **HLT-022**.

3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Product complete and tested; prepare launch.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@meridale.example** to continue.

Step 6. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for HLT-022. Summary filed as HLT-022-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2027-01-21 (any future date)	Develop Detailed Launch Plan done for HLT-022. Summary filed as HLT-022-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for HLT-022. Summary filed as HLT-022-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for HLT-022. Summary filed as HLT-022-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for HLT-022. Summary filed as HLT-022-05-05.
6	UFT-05-06 Train Teams	People trained: 85	Train Teams done for HLT-022. Summary filed as HLT-022-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for HLT-022. Summary filed as HLT-022-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for HLT-022. Summary filed as HLT-022-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	HLT-022-T3-01
2	Marketing and sales materials	HLT-022-T3-02
3	Trained teams	HLT-022-T3-03
4	Validated customer journey	HLT-022-T3-04
5	Final regulatory validation	HLT-022-T3-05
7	Evidence: Define personas and segments	HLT-022-T3-07
9	Evidence: Monitor regulatory intelligence	HLT-022-T3-09
11	Evidence: Define and manage lifecycle workflows	HLT-022-T3-11
13	Evidence: Onboard and certify partners	HLT-022-T3-13
15	Evidence: Manage invention disclosures and patent filings	HLT-022-T3-15
17	Evidence: Develop and manage mobile apps	HLT-022-T3-17
19	Evidence: Map journeys and touchpoints	HLT-022-T3-19
21	Evidence: Prepare and submit filings	HLT-022-T3-21
23	Evidence: Enforce GRC policies	HLT-022-T3-23
25	Evidence: Manage partner agreements and contracts	HLT-022-T3-25
27	Evidence: Manage trademark and copyright registrations	HLT-022-T3-27
29	Evidence: Enable offline access and synchronization	HLT-022-T3-29

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@meridale.example** (Julie Alaoui, Executive Sponsor) and open **Gate board**.

2. Open the T3 line of **HLT-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-06**, **E2E-09** start automatically. Sign in again as **pm1@meridale.example** to continue.

Step 7. E2E-06 Launch-to-After-Sales

Open the project, tab **Lifecycle & tasks**, card **E2E-06**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-06-01 Identify Product Issues	Open product issues: 3	Identify Product Issues done for HLT-022. Summary filed as HLT-022-06-01.
2	UFT-06-02 Assess Product Performance	—	Assess Product Performance done for HLT-022. Summary filed as HLT-022-06-02.
3	UFT-06-03 Analyze Campaign Results	—	Analyze Campaign Results done for HLT-022. Summary filed as HLT-022-06-03.
4	UFT-06-04 Track Customer Satisfaction	CSAT (1-5): 4.4 Net Promoter Score (-100 to 100): 41	Track Customer Satisfaction done for HLT-022. Summary filed as HLT-022-06-04.
5	UFT-06-05 Track Product Performance	Field MTBF (hours): 5200	Track Product Performance done for HLT-022. Summary filed as HLT-022-06-05.

Open the task **Complete Gate Checklist (T4)**. The gate T4 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Issue log	HLT-022-T4-01
2	Performance assessment	HLT-022-T4-02
3	Campaign results	HLT-022-T4-03
4	CSAT and NPS	HLT-022-T4-04
5	Field performance data	HLT-022-T4-05
7	Evidence: Log and categorize incidents and requests	HLT-022-T4-07
9	Evidence: Collect field failure data	HLT-022-T4-09
11	Evidence: Define personas and segments	HLT-022-T4-11
13	Evidence: Manage service parts and inventory	HLT-022-T4-13
15	Evidence: Perform should-cost and target costing	HLT-022-T4-15
17	Evidence: Prioritize and escalate	HLT-022-T4-17
19	Evidence: Analyze failure modes	HLT-022-T4-19
21	Evidence: Map journeys and touchpoints	HLT-022-T4-21
23	Evidence: Create and manage maintenance plans (preventive, predictive)	HLT-022-T4-23
25	Evidence: Manage lifecycle costing	HLT-022-T4-25
27	Evidence: Diagnose and resolve	HLT-022-T4-27
29	Evidence: Model reliability (Weibull, MTBF)	HLT-022-T4-29

Step 8. E2E-09 Market Strategy-to-Campaign

Open the project, tab **Lifecycle & tasks**, card **E2E-09**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-09-01 Gather Customer	—	Gather Customer Experience Data done for

#	Task	Fields to fill	Result / output to type
	Experience Data		HLT-022. Summary filed as HLT-022-09-01.
2	UFT-09-02 Gather Product Delivery Feedback	—	Gather Product Delivery Feedback done for HLT-022. Summary filed as HLT-022-09-02.
3	UFT-09-03 Establish Market Segments	—	Establish Market Segments done for HLT-022. Summary filed as HLT-022-09-03.
4	UFT-09-04 Link Segments & Products	—	Link Segments & Products done for HLT-022. Summary filed as HLT-022-09-04.
5	UFT-09-05 Establish Market Strategy	—	Establish Market Strategy done for HLT-022. Summary filed as HLT-022-09-05.
6	UFT-09-06 Plan & Develop Campaign	—	Plan & Develop Campaign done for HLT-022. Summary filed as HLT-022-09-06.
7	UFT-09-07 Launch & Monitor Campaign	—	Launch & Monitor Campaign done for HLT-022. Summary filed as HLT-022-09-07.
8	UFT-09-08 Complete Campaign & Report	Qualified leads generated: 260 Conversion rate (%): 18	Complete Campaign & Report done for HLT-022. Summary filed as HLT-022-09-08.

Submit the gate: on the project page, card **Gate T4**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@meridale.example** (Julie Alaoui, Executive Sponsor) and open **Gate board**.
2. Open the T4 line of **HLT-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Post-launch performance is stable; move to steady-state review.**, then select **Record decision**.
5. Result: **E2E-07** starts automatically. Sign in again as **pm1@meridale.example** to continue.

Step 9. E2E-07 After-Sales-to-Performance

Open the project, tab **Lifecycle & tasks**, card **E2E-07**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-07-01 Evaluate Overall Performance	—	Evaluate Overall Performance done for HLT-022. Summary filed as HLT-022-07-01.
2	UFT-07-02 Analyze Profitability	Revenue to date (kUSD): 3100 Cost of goods sold (kUSD): 1850	Analyze Profitability done for HLT-022. Summary filed as HLT-022-07-02.
3	UFT-07-03 Gather Customer Experience Feedback	CSAT (1-5): 3.6 Net Promoter Score (-100 to 100): 12	Gather Customer Experience Feedback done for HLT-022. Summary filed as HLT-022-07-03.
4	UFT-07-04 Develop Improvement Recommendations	Recommendation to the T5 gate: Retire	Develop Improvement Recommendations done for HLT-022. Summary filed as HLT-022-07-04.

Open the task **Complete Gate Checklist (T5)**. The gate T5 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Overall performance evaluation	HLT-022-T5-01
2	Profitability analysis	HLT-022-T5-02
3	Customer experience feedback	HLT-022-T5-03

Item	Checklist item (mandatory)	Evidence reference to type
4	Improvement recommendations	HLT-022-T5-04
5	Evidence: Define and manage lifecycle workflows	HLT-022-T5-05
7	Evidence: Define personas and segments	HLT-022-T5-07
9	Evidence: Define strategic product themes, goals, and investment horizons	HLT-022-T5-09
11	Evidence: Collect field failure data	HLT-022-T5-11
13	Evidence: Manage lifecycle costing	HLT-022-T5-13
15	Evidence: Collect and analyze feedback	HLT-022-T5-15
17	Evidence: Automate data classification	HLT-022-T5-17
19	Evidence: Define and track KPIs	HLT-022-T5-19
21	Evidence: Identify pain points and moments of truth	HLT-022-T5-21
23	Evidence: Evaluate and score product ideas against strategic fit	HLT-022-T5-23
25	Evidence: Model reliability (Weibull, MTBF)	HLT-022-T5-25
27	Evidence: Optimize cost structures	HLT-022-T5-27
29	Evidence: Conduct quality audits	HLT-022-T5-29

Submit the gate: on the project page, card **Gate T5**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@meridale.example** (Julie Alaoui, Executive Sponsor) and open **Gate board**.
2. Open the T5 line of **HLT-022**.
3. Under **Decision**, keep **Go**.
4. Under **Next path (E2E-08)**, select **Retire (Branch B)**.
5. In **Rationale**, type **Demand has fallen and a successor exists; retire the product.**, then select **Record decision**.
6. Result: **E2E-08** starts automatically. Sign in again as **pm1@meridale.example** to continue.

Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch B

Open the project, tab **Lifecycle & tasks**, card **E2E-08**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-08-05 Assess Exit Impact	—	Assess Exit Impact done for HLT-022. Summary filed as HLT-022-08-05.
2	UFT-08-06 Develop Exit Strategy	—	Develop Exit Strategy done for HLT-022. Summary filed as HLT-022-08-06.
3	UFT-08-07 Execute Product Exit	—	Execute Product Exit done for HLT-022. Summary filed as HLT-022-08-07.
4	UFT-08-08 Communicate End-of-Life	—	Communicate End-of-Life done for HLT-022. Summary filed as HLT-022-08-08.
5	UFT-08-09 Support Customer Migration	Customers affected: 1200 Customers migrated: 1200	Support Customer Migration done for HLT-022. Summary filed as HLT-022-08-09.
6	UFT-08-10 Financial Closure	Closure cost (kUSD): 180	Financial Closure done for HLT-022. Summary filed as HLT-022-08-10.

Open the task **Complete Gate Checklist (T6)**. The gate T6 checklist has 30 items; 18 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Exit impact assessment	HLT-022-T6-01
2	Exit strategy	HLT-022-T6-02
3	Executed market exit	HLT-022-T6-03
4	End-of-life communication	HLT-022-T6-04

Item	Checklist item (mandatory)	Evidence reference to type
5	Customer migration	HLT-022-T6-05
6	Financial closure	HLT-022-T6-06
7	Evidence: Elicit and capture requirements from all sources	HLT-022-T6-07
9	Evidence: Manage design process (conceptual, detailed, validation)	HLT-022-T6-09
11	Evidence: Define and manage quality plans (APQP, PPAP)	HLT-022-T6-11
13	Evidence: Define and manage lifecycle workflows	HLT-022-T6-13
15	Evidence: Monitor obsolescence	HLT-022-T6-15
17	Evidence: Define personas and segments	HLT-022-T6-17
19	Evidence: Perform should-cost and target costing	HLT-022-T6-19
21	Evidence: Create and manage Engineering BOM (eBOM)	HLT-022-T6-21
23	Evidence: Provide generative design	HLT-022-T6-23
25	Evidence: Manage invention disclosures and patent filings	HLT-022-T6-25
27	Evidence: Structure and categorize requirements	HLT-022-T6-27
29	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	HLT-022-T6-29

Submit the gate: on the project page, card **Gate T6**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@meridale.example** (Julie Alaoui, Executive Sponsor) and open **Gate board**.
2. Open the T6 line of **HLT-022**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Customers migrated and costs closed; end of life confirmed.**, then select **Record decision**.
5. Result: no further process starts; see the result of the run below. Sign in again as **pm1@meridale.example** to continue.

Result of the run

The project status is **Retired**. The whole Full Track, from idea to end of life, is recorded in the tab **History**.

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

9. Run 5: Full Track in Oil, Gas & Energy, relaunching a live product

The seeded project ENR-012 is live and waiting in its performance review. You finish its open market campaign (E2E-09) and review (E2E-07); the T5 board chooses a relaunch; E2E-08 Branch A loops back to development (E2E-04), and the improved product goes live again at T3.

Item	Value
Organization	Kestrel Energy & Utilities (Oil, Gas & Energy)
Product Manager	Salma Amrani · pm1@kestrel.example
Executive Sponsor	Adam Nguyen · exec@kestrel.example
Project	ENR-012 Green Hydrogen Electrolyser Pilot
End state	Active · NPV 3743 kUSD, ROI 160.9%

Step 1. Open the project

Sign in as **pm1@kestrel.example** (password **Demo#2026**), the Product Manager.

Open **Innovation projects**, type **ENR-012** in **Filter rows** and open the project. It belongs to another product manager; as Product Manager you can complete its tasks on the owners' behalf.

Step 2. E2E-09 Market Strategy-to-Campaign

Open the project, tab **Lifecycle & tasks**, card **E2E-09**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-09-07 Launch & Monitor Campaign	—	Launch & Monitor Campaign done for ENR-012. Summary filed as ENR-012-09-07.
2	UFT-09-08 Complete Campaign & Report	—	Complete Campaign & Report done for ENR-012. Summary filed as ENR-012-09-08.

Step 3. E2E-07 After-Sales-to-Performance

Open the project, tab **Lifecycle & tasks**, card **E2E-07**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-07-01 Evaluate Overall Performance	—	Evaluate Overall Performance done for ENR-012. Summary filed as ENR-012-07-01.
2	UFT-07-02 Analyze Profitability	Revenue to date (kUSD): 5200 Cost of goods sold (kUSD): 4300	Analyze Profitability done for ENR-012. Summary filed as ENR-012-07-02.
3	UFT-07-03 Gather Customer Experience Feedback	CSAT (1-5): 3.9 Net Promoter Score (-100 to 100): 22	Gather Customer Experience Feedback done for ENR-012. Summary filed as ENR-012-07-03.
4	UFT-07-04 Develop Improvement Recommendations	Recommendation to the T5 gate: Relaunch	Develop Improvement Recommendations done for ENR-012. Summary filed as ENR-012-07-04.

Open the task **Complete Gate Checklist (T5)**. The gate T5 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Overall performance evaluation	ENR-012-T5-01
2	Profitability analysis	ENR-012-T5-02
3	Customer experience feedback	ENR-012-T5-03
4	Improvement recommendations	ENR-012-T5-04
5	Evidence: Define and manage lifecycle workflows	ENR-012-T5-05
7	Evidence: Define personas and segments	ENR-012-T5-07
9	Evidence: Define strategic product themes, goals, and investment horizons	ENR-012-T5-09
11	Evidence: Collect field failure data	ENR-012-T5-11
13	Evidence: Manage lifecycle costing	ENR-012-T5-13
15	Evidence: Collect and analyze feedback	ENR-012-T5-15
17	Evidence: Automate data classification	ENR-012-T5-17
19	Evidence: Define and track KPIs	ENR-012-T5-19
21	Evidence: Identify pain points and moments of truth	ENR-012-T5-21
23	Evidence: Evaluate and score product ideas against strategic fit	ENR-012-T5-23
25	Evidence: Model reliability (Weibull, MTBF)	ENR-012-T5-25
27	Evidence: Optimize cost structures	ENR-012-T5-27
29	Evidence: Conduct quality audits	ENR-012-T5-29

Submit the gate: on the project page, card **Gate T5**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@kestrel.example** (Adam Nguyen, Executive Sponsor) and open **Gate board**.
2. Open the T5 line of **ENR-012**.
3. Under **Decision**, keep **Go**.
4. Under **Next path (E2E-08)**, select **Relaunch (Branch A)**.
5. In **Rationale**, type **Performance is below target but fixable; relaunch.**, then select **Record decision**.
6. Result: **E2E-08** starts automatically. Sign in again as **pm1@kestrel.example** to continue.

Step 4. E2E-08 Assessment-to-Relaunch or Retirement · Branch A

Open the project, tab **Lifecycle & tasks**, card **E2E-08**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-08-01 Update Product Specifications	—	Update Product Specifications done for ENR-012. Summary filed as ENR-012-08-01.
2	UFT-08-02 Support Operational Re-introduction	—	Support Operational Re-introduction done for ENR-012. Summary filed as ENR-012-08-02.
3	UFT-08-03 Manage Product Improvements	—	Manage Product Improvements done for ENR-012. Summary filed as ENR-012-08-03.
4	UFT-08-04 Approve for Relaunch	Relaunch re-entry point: E2E-04	Approve for Relaunch done for ENR-012. Summary filed as ENR-012-08-04.

Step 5. E2E-04 Design-to-Development (run 2)

Open the project, tab **Lifecycle & tasks**, card **E2E-04**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-04-01 Support Operational Introduction	—	Support Operational Introduction done for ENR-012. Summary filed as ENR-012-04-01.
2	UFT-04-02 Conduct Operational Readiness Testing	—	Conduct Operational Readiness Testing done for ENR-012. Summary filed as ENR-012-04-02.
3	UFT-04-03 Manage Product Configuration	—	Manage Product Configuration done for ENR-012. Summary filed as ENR-012-04-03.
4	UFT-04-04 Develop Product Offering Procedures	—	Develop Product Offering Procedures done for ENR-012. Summary filed as ENR-012-04-04.
5	UFT-04-05 Manage Acceptance Testing	Acceptance tests passed (%): 98	Manage Acceptance Testing done for ENR-012. Summary filed as ENR-012-04-05.
6	UFT-04-06 Develop Preliminary Launch Plan	—	Develop Preliminary Launch Plan done for ENR-012. Summary filed as ENR-012-04-06.
7	UFT-04-07 Complete Functionalities	—	Complete Functionalities done for ENR-012. Summary filed as ENR-012-04-07.

Open the task **Complete Gate Checklist (T2)**. The gate T2 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Completed functionalities	ENR-012-T2-01
2	Operational readiness and acceptance test results	ENR-012-T2-02
3	Configuration baseline	ENR-012-T2-03
4	Offering procedures	ENR-012-T2-04
5	Preliminary launch plan	ENR-012-T2-05
7	Evidence: Define manufacturing process plans and routings	ENR-012-T2-07
9	Evidence: Create and manage Engineering BOM (eBOM)	ENR-012-T2-09
11	Evidence: Design and model processes (BPMN)	ENR-012-T2-11
13	Evidence: Develop go-to-market plans	ENR-012-T2-13
15	Evidence: Provide generative design	ENR-012-T2-15
17	Evidence: Monitor regulatory intelligence	ENR-012-T2-17
19	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	ENR-012-T2-19
21	Evidence: Manage non-conformance reports (NCR)	ENR-012-T2-21
23	Evidence: Assess change impact (cost, schedule, quality, compliance)	ENR-012-T2-23
25	Evidence: Review and approve	ENR-012-T2-25
27	Evidence: Enforce GRC policies	ENR-012-T2-27
29	Evidence: Map journeys and touchpoints	ENR-012-T2-29

Submit the gate: on the project page, card **Gate T2**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@kestrel.example** (Adam Nguyen, Executive Sponsor) and open **Gate board**.
2. Open the T2 line of **ENR-012**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Product complete and tested; prepare launch.**, then select **Record decision**.

5. Result: **E2E-05** starts automatically. Sign in again as **pm1@kestrel.example** to continue.

Step 6. E2E-05 Development-to-Launch (run 2)

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for ENR-012. Summary filed as ENR-012-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-11-07 (any future date)	Develop Detailed Launch Plan done for ENR-012. Summary filed as ENR-012-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for ENR-012. Summary filed as ENR-012-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for ENR-012. Summary filed as ENR-012-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for ENR-012. Summary filed as ENR-012-05-05.
6	UFT-05-06 Train Teams	People trained: 25	Train Teams done for ENR-012. Summary filed as ENR-012-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for ENR-012. Summary filed as ENR-012-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for ENR-012. Summary filed as ENR-012-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	ENR-012-T3-01
2	Marketing and sales materials	ENR-012-T3-02
3	Trained teams	ENR-012-T3-03
4	Validated customer journey	ENR-012-T3-04
5	Final regulatory validation	ENR-012-T3-05
7	Evidence: Define personas and segments	ENR-012-T3-07
9	Evidence: Monitor regulatory intelligence	ENR-012-T3-09
11	Evidence: Define and manage lifecycle workflows	ENR-012-T3-11
13	Evidence: Onboard and certify partners	ENR-012-T3-13
15	Evidence: Manage invention disclosures and patent filings	ENR-012-T3-15
17	Evidence: Develop and manage mobile apps	ENR-012-T3-17
19	Evidence: Map journeys and touchpoints	ENR-012-T3-19
21	Evidence: Prepare and submit filings	ENR-012-T3-21
23	Evidence: Enforce GRC policies	ENR-012-T3-23
25	Evidence: Manage partner agreements and contracts	ENR-012-T3-25
27	Evidence: Manage trademark and copyright registrations	ENR-012-T3-27
29	Evidence: Enable offline access and synchronization	ENR-012-T3-29

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@kestrel.example** (Adam Nguyen, Executive Sponsor) and open **Gate board**.
2. Open the T3 line of **ENR-012**.
3. Under **Decision**, keep **Go**.

4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-06, E2E-09** start automatically. Sign in again as **pm1@kestrel.example** to continue.

Result of the run

The project stays **Active**, now in E2E-06 after gate T3. Active · open runs: E2E-06, E2E-09

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

10. Run 6: Benchmarking in Construction, within the organization and across the group

Ridgeway Construction Contractors (Construction) belongs to Atlas Infrastructure Holding with Cedarline Precast Systems and Orvane Transit Group. Its Executive Sponsor compares the organization's own project types and tracks, then compares the organization with its two sister companies. Comparisons outside the group are not possible: external benchmarking is out of scope.


Item	Value
Organization	Ridgeway Construction Contractors (Construction), group Atlas Infrastructure Holding
Sign in	exec@ridgeway.example / Demo#2026 (Executive Sponsor)
Screen	Reports > Benchmarking

Step 1. Compare project types

1. Sign in as **exec@ridgeway.example** and open **Reports > Benchmarking**. The tab **Within the organization** opens, with **Compare by** set to **Project type**.
2. Read the four figures at the top: projects compared, first-time Go rate, time to market and checklist compliance for the whole organization.
3. In the chart, open the **Indicator** list and choose **Time to market**, then **Average NPV**. The bars compare Product, Product-Service and Service projects.
4. Read the **Scorecard by project type**. Green marks the best segment and red the weakest for each indicator.

Project type	Projects	First-time Go	Time to market	Average NPV
Product	7	90.3%	246 days	89 kUSD
Product-Service	4	77.8%	245 days	186 kUSD
Service	10	86.5%	237 days	433 kUSD

What it tells you: Service projects reach the market fastest and carry the best business cases, while Product-Service projects are sent back most often (lowest first-time Go rate).

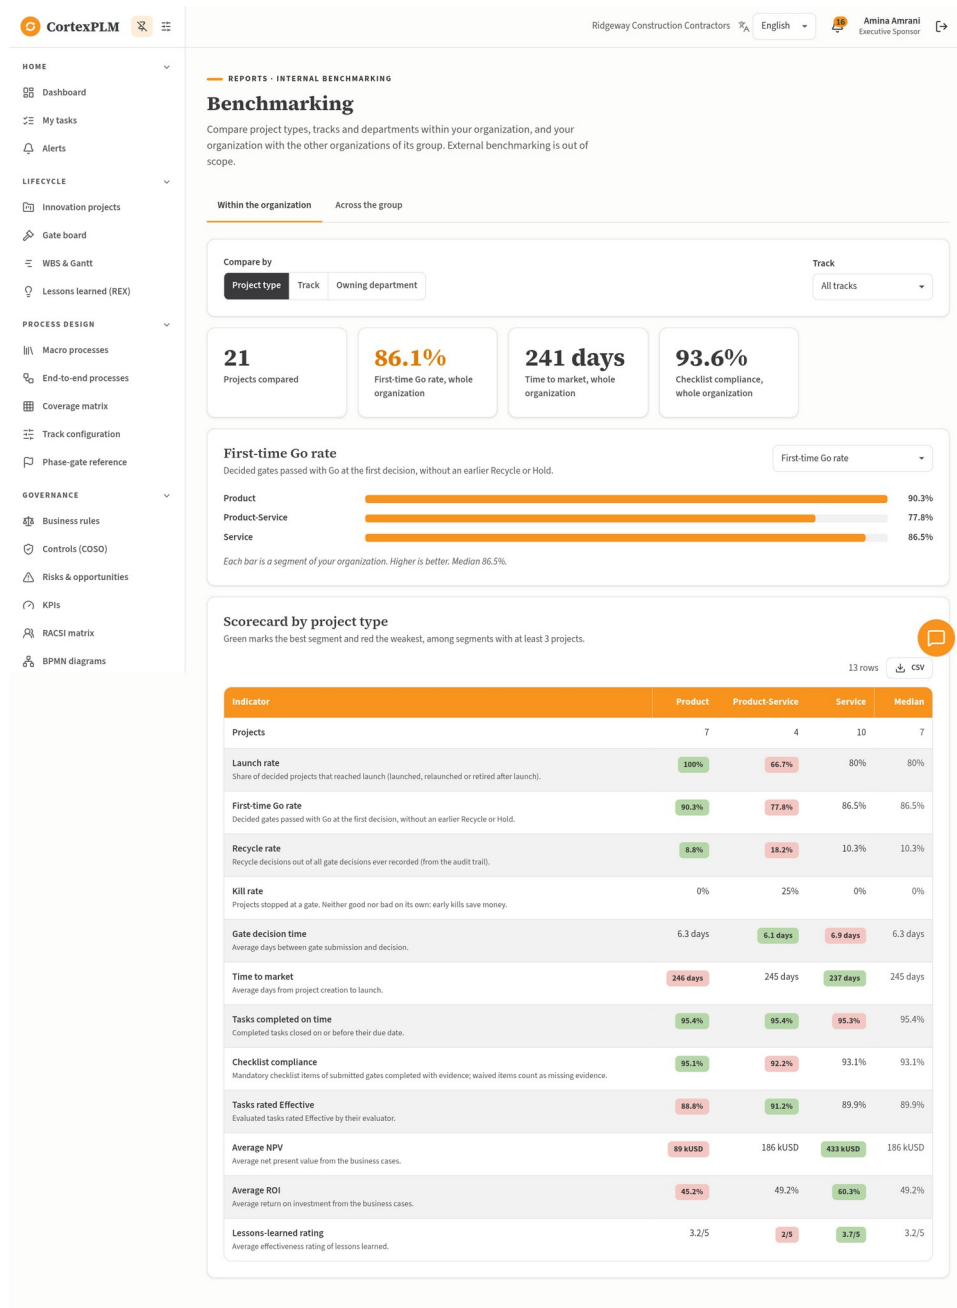

Benchmarking within the organization, compared by project type.

Step 2. Compare tracks and filter

1. Under **Compare by**, select **Track**. The scorecard now compares the Full, Light and Fast tracks.
2. In **Project type**, choose **Service** to compare tracks for Service projects only. Choose **All project types** to reset.
3. Select **CSV** above the scorecard to download the figures.

Track	Projects	First-time Go	Time to market	Average NPV
Fast	3	100%	121 days	957 kUSD
Full	15	86.4%	250 days	190 kUSD
Light	3	75%	254 days	201 kUSD

Step 3. Compare with the organizations of the group

1. Select the tab **Across the group**. The card shows **Atlas Infrastructure Holding** and its three organizations.
2. Read the note: only aggregated indicators are exchanged. No project, person or document of Cedarline or Orvane is visible.
3. In the chart, choose **First-time Go rate**, then **Gate decision time**. Your organization is marked **(you)**.
4. Read the **Scorecard by organization** and the **Median** column.

Organization	First-time Go	Recycle	Decision time	Time to market
Cedarline Precast Systems	95%	2.9%	4.2 days	174 days
Orvane Transit Group	86.5%	11.1%	7.7 days	212 days
Ridgeway Construction Contractors (you)	86.1%	11.4%	6.6 days	241 days

What it tells you: Cedarline passes gates first time most often and decides fastest; Ridgeway can learn from its gate preparation.

CortexPLM Ridgeway Construction Contractors English Amina Amrani Executive Sponsor

HOME

- Dashboard
- My tasks
- Alerts

LIFECYCLE

- Innovation projects
- Gate board
- WBS & Gantt
- Lessons learned (REX)

PROCESS DESIGN

- Macro processes
- End-to-end processes
- Coverage matrix
- Track configuration
- Phase-gate reference

GOVERNANCE

- Business rules
- Controls (COSO)
- Risks & opportunities
- KPIs
- RACSI matrix
- BPMN diagrams

REPORTS - INTERNAL BENCHMARKING

Benchmarking

Compare project types, tracks and departments within your organization, and your organization with the other organizations of its group. External benchmarking is out of scope.

Within the organization **Across the group**

Atlas Infrastructure Holding
3 organizations in the group

Track: All tracks Project type: All project types

☐ Only aggregated indicators are exchanged between organizations of the group. No project, person or document of another organization is visible.

☒ Share our aggregated indicators with the organizations of our group

First-time Go rate

Decided gates passed with Go at the first decision, without an earlier Recycle or Hold.

First-time Go rate

Cedarline Precast Systems	95%
Orvane Transit Group	86.5%
Ridgeway Construction Contra...	86.1%

Each bar is an organization of your group. Higher is better. Median 86.5%

Scorecard by organization

Green marks the best organization and red the weakest. Organizations that do not share their indicators are shown as not shared.

13 rows

Indicator	Cedarline Precast Systems	Orvane Transit Group	Ridgeway Construction Contractors (you)	Median
Projects	21	22	21	21
Launch rate Share of decided projects that reached launch (launched, relaunched or retired after launch).	82.4%	83.3%	82.4%	82.4%
First-time Go rate Decided gates passed with Go at the first decision, without an earlier Recycle or Hold.	95%	86.5%	86.1%	86.5%
Recycle rate Recycle decisions out of all gate decisions ever recorded (from the audit trail).	2.9%	11.1%	11.4%	11.1%
Kill rate Projects stopped at a gate. Neither good nor bad on its own: early kills save money.	4.8%	4.5%	4.8%	4.8%
Gate decision time Average days between gate submission and decision.	4.2 days	7.7 days	6.6 days	6.6 days
Time to market Average days from project creation to launch.	174 days	212 days	241 days	212 days
Tasks completed on time Completed tasks closed on or before their due date.	98.1%	97.1%	95.4%	97.1%
Checklist compliance Mandatory checklist items of submitted gates completed with evidence; waived items count as missing evidence.	96.6%	96%	93.6%	96%
Tasks rated Effective Evaluated tasks rated Effective by their evaluator.	93.9%	86.1%	89.8%	89.8%
Average NPV Average net present value from the business cases.	805 kUSD	662 kUSD	272 kUSD	662 kUSD
Average ROI Average return on investment from the business cases.	93.1%	82.4%	53.2%	82.4%
Lessons-learned rating Average effectiveness rating of lessons learned.	3.8/5	2.7/5	3.2/5	3.2/5

Benchmarking across Atlas Infrastructure Holding, as seen by Ridgeway.


Step 4. Stop or resume sharing with the group

1. Still on **Across the group**, clear **Share our aggregated indicators with the organizations of our group**. A message confirms **Saved**.
2. Sign in as **exec@cedarline.example**, open **Benchmarking > Across the group**: Ridgeway now shows **Not shared** in every row.
3. Sign in again as **exec@ridgeway.example** and tick the box again to resume sharing.

Step 5. An independent organization

1. Sign in as **exec@meridale.example** (Meridale Health Network, no group) and open **Reports > Benchmarking**.

2. The tab **Within the organization** works as in Step 1. The tab **Across the group** explains that the organization belongs to no group, so there is no comparison.

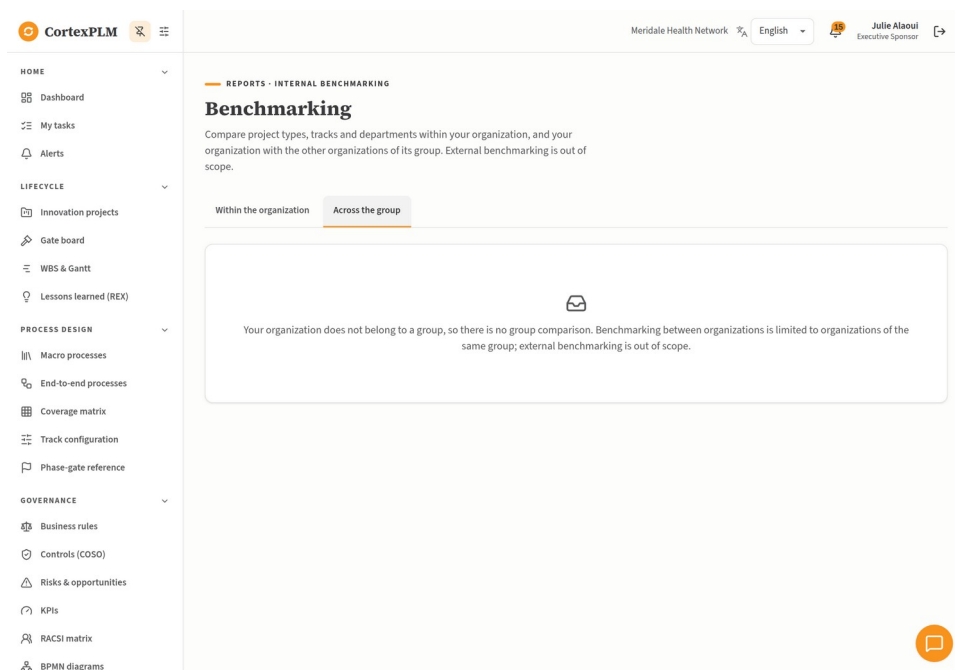

An independent organization has no group comparison.

11. Everyday Scenarios by Module

Short scenarios for the modules not used in the runs. All take place in Metro City Digital Services Agency unless stated; the password is **Demo#2026**. Where a justification is requested, type the text given or your own reason.

11.1 Record a business rule

Sign in as **process@metrocity.example**.

1. Open **Governance > Business rules** and select **Add rule**.
2. Type Rule ID **BR-PUB-101**, Triggering step **MP-33.2**, Condition **A service goes live without an accessibility audit**, Action **Block the T3 submission and notify the Quality Manager**.
3. Choose Rule type **Validation**, Severity **High**, type Owner **Quality Manager** and Process tag **MP-121**.
4. Select **Save**. In the justification window type **New accessibility policy 2026** and select **Save change**.

11.2 Add a control, change it and compare versions

Sign in as **process@metrocity.example**.

1. Open **Governance > Controls (COSO)** and select **Add control**.
2. Type Name **Accessibility audit before go-live**; choose COSO component **Control Activities**, Control type **Preventive**, Testing frequency **Per change**; type Owner **Quality Manager**; choose Effectiveness **Not tested**; type Process tag **MP-121**. Select **Save**, justification **New control for the accessibility policy**.
3. Open the new control, change Effectiveness to **Effective**, select **Save**, justification **Tested on PUB-022**.
4. Open it again, select the tab **Version history**. Under **Compare two versions** choose From **Version 1** and To **Version 2**: the row **effectiveness** is marked **Changed**.

11.3 Log a risk and read the heat map

Sign in as **process@metrocity.example**.

1. Open **Governance > Risks & opportunities** and select **Add**.
2. Choose Type **Risk**; type Name **Payment provider outage**, Category **Operational**, Likelihood **3**, Impact **4**, Owner **Finance Controller**; choose Status **Open**; type Process tag **MP-121**. Save with the justification **Identified during PUB-022 launch**.
3. In the heat map, select the cell likelihood 3 × impact 4: the list shows the risks scored 12.

11.4 See the governance of one process

Sign in as **process@metrocity.example**.

1. Open **Process design > Macro processes** and open **MP-121**.
2. Scroll to **Governance tagged to this process**: the rule BR-PUB-101, the new control and the new risk appear with the organization's other MP-121 records.

11.5 Build a RACSI activity

Sign in as **process@metrocity.example**.

1. Open **Governance > RACSI matrix** and select **Add activity**. Type Activity **Accessibility audit**, Process tag **MP-121**, then **Save**.
2. In the row, select + under **R** and type **Quality Manager**; select + under **A** and type **Product Manager**.
3. Select + under **A** again and type **Executive Sponsor**: the application refuses a second Accountable.

11.6 Track a custom KPI

Sign in as **process@metrocity.example**.

1. Open **Governance > KPIs**, tab **Custom KPIs**, and select **Add custom KPI**.
2. Type Name **Online completion rate**, Formula (plain language) **Requests completed online divided by all requests**, Target **85**, Unit **%**, Current value **81**, Owner **Product Manager**, Process tag **MP-12**. **Save**.
3. Open the tab **Built-in KPIs** and select **KPI-07 Design review first-pass yield**. Select **Record measurement**, type Period (YYYY-MM) **2026-09** and Value **88**, then **Save**. The trend line shows the measurement against the dashed target.

11.7 Edit and exchange a BPMN diagram

Sign in as **process@metrocity.example**.

1. Open **Governance > BPMN diagrams** and open the E2E-01 diagram.
2. Drag a task from the palette on the left onto the canvas and name it **Accessibility audit**. Select **Save diagram**.
3. Select **Export .bpmn** to download the file; **Import .bpmn** loads a file from any BPMN 2.0 tool.

11.8 Ask for an AI suggestion on a task

Sign in as **pm1@metrocity.example**.

1. Open **My tasks** and open a task in progress.
2. In the card **AI assistance**, keep the proposed use case, type **Focus on accessibility** in **Add details for the suggestion**, then select **Get suggestion**.
3. The suggestion is labelled AI-generated with its tier, source and references. Select **Accept**, **Edit** or **Reject**; the decision goes to the usage log (**Intelligence > AI use cases > Usage log**).

11.9 Search the knowledge base in your language

Sign in as **pm2@metrocity.example** (French interface).

1. Open **Intelligence > Base de connaissances** (tab **Rechercher**).
2. In the search box type **preuves checklist jalon**: the French reference articles are ranked first, followed by matching records of your organization.

3. Open the tab **Articles**: the list shows French articles by default; use the language filter to show **English** or العربية articles.

11.10 Create a project template and use it

Sign in as **process@metrocity.example**.

1. Open **Intelligence > Templates** and select **Add template**. Type Name **Citizen e-service (Fast)**, Kind **Project**.
2. In **Default values (JSON)** type `{"offer_type":"Service","scores":{"strategic":2,"investment":1,"novelty":2,"regulatory":2,"market":1,"reach":2,"integration":1}}`. Save.
3. Sign in as **pm1@metrocity.example**, open **New project** and choose the template in **Start from a template**: type and scores are pre-filled and remain editable.

11.11 Plan with a WBS and a Gantt chart

Sign in as **pm1@metrocity.example**.

1. Open **Lifecycle > WBS & Gantt** and select **New WBS**. Type Name **PUB-022 launch plan**, choose Project **PUB-022**, tick **Fill it with all tasks of this project, grouped by E2E run**, then **Create**.
2. Open the Gantt: bars show planned, in-progress, completed and overdue tasks with dependency lines.
3. Select **Export PDF** to download the chart.

11.12 Record a lesson learned

Sign in as **pm1@metrocity.example**.

1. Open **Lifecycle > Lessons learned (REX)** and select **Add lesson**.
2. Type Title **Accessibility audit booked too late**, What went well **The audit found no blocking issue**, What did not go well **The audit slot was booked two weeks before go-live**, Root cause **No audit step in the launch plan**, Recommendation **Add the audit to UFT-05-02 Develop Detailed Launch Plan**; choose Category **Governance**; type Effectiveness rating 3. Save.
3. The register view groups lessons by category and shows the average rating by month.

11.13 Export a report

Sign in as **exec@metrocity.example**.

1. Open **Reports & cockpits** and open **RPT-01**.
2. Select **PDF**, **Excel** or **Word**: the file is named with the report key and today's date.

11.14 Choose how you are notified

Sign in as **pm1@metrocity.example**.

1. Open **Notifications**, tab **Preferences**, and tick **E-mail** for **Gate submissions and decisions**.
2. Open the tab **Delivery log** to see each delivery with its status and attempts.

11.15 Add a user within the licence limit

Sign in as **admin@metrocity.example**.

1. Open **Administration > Users & roles** and select **Add user**.
2. Type Name **Nora Idrissi**, E-mail **nora.idrissi@metrocity.example**, choose Roles **Quality Manager**, Language **Français**, and type Password **Welcome#2026**. Save.
3. The seat counter increases by one. When all seats are used, the application refuses new users.

11.16 Give a project its own team tree (OBS)

Sign in as **admin@metrocity.example**.

1. Open **Administration > Organizations & OBS**, tab **OBS of Metro City Digital Services Agency**.
2. In **Tree**, choose **PUB-022 Online Parking Permit Renewal**, then **Add node**. Type Name **Permit delivery team**, Type **Team**, and Save.
3. Choose **Organization tree** in **Tree** to return to the organization's own structure.

11.17 Back up the database

Sign in as **admin@cortexplm.example / Admin#2026 (platform administrator)**.

1. Open **Administration > Configuration** and scroll to **Backups**.
2. Select **Back up now**. The new file appears in the list; one automatic backup is also made every day.

11.18 Check the audit trail

Sign in as **auditor@metrocity.example**.

1. Open **Administration > Audit trail**, type **accessibility** in the search box and select **Search**.
2. Each line shows who changed what, when, the old and new values and the justification. The trail is read-only.

12. Messages You May Meet

Message	Why	What to do
Evidence is required before this item can be marked complete (BR-005).	A mandatory checklist item has no evidence.	Type an evidence reference or attach a file, then select Mark complete .
Gate submission blocked: ... mandatory checklist item(s) are open (BR-004).	The checklist is not finished.	Complete or waive the mandatory items, then complete the checklist task.
The person accountable for the project cannot record its gate decision (CTL-01).	You own the project.	Ask the Executive Sponsor or a Gate Review Board member to decide.
Go-live is blocked: final regulatory validation reports incomplete approvals (BR-030).	UFT-05-08 answered No .	Once the approvals are obtained, open Final Regulatory Validation , select Reopen task , type the reason, answer Yes , complete the task and submit the gate again.
Strategic-fit score below 50: the idea is parked (BR-001).	UFT-01-02 scored below 50.	The project goes On Hold for 90 days. Select Resume project after re-review.
Only the task owner or a process manager can update this task.	You are not the owner and lack project edit rights.	Ask the owner, or sign in as the Product Manager.
This E2E run has not started yet (observation period, Rule R1).	Light Track performance review is scheduled after launch.	Wait for the start date, or ask the Track Administrator to shorten the observation period.
