

POWERACT

CONSULTING

USER GUIDE

CortexPLM

Run innovation projects from group and organization set-up to launch, relaunch or retirement

Version 2.0 · September 2026

Table of Contents

1. About This Guide.....	6
1.1 Conventions.....	6
2. Getting Started.....	7
2.1 Sign in.....	7
2.2 The menu, organized by what you do.....	7
2.3 The navigation bar: pin, slide and position.....	8
2.4 Language.....	9
2.5 Groups, organizations and projects.....	10
2.6 Portfolio overview.....	11
2.7 Alerts, notifications and the assistant.....	12
3. How a Project Moves Through CortexPLM.....	14
3.1 Who does what in the runs.....	14
3.2 Create the organization.....	14
3.3 Create a project.....	15
3.4 Complete a task and attach documents.....	17
3.5 Complete the gate checklist.....	18
3.6 Submit the gate and record the decision.....	19
4. Decision Matrix: How to Fill In the Fields.....	22
4.1 Group, organization and project.....	22
4.2 Complexity scores (Step 2 of New project).....	22
4.3 From total score to track.....	22
4.4 Task fields.....	23
4.5 Gates, checklists, evaluations, lessons and AI.....	23
5. Common Values Used in the Runs.....	24
6. Run 1: Fast Track in the Public Sector.....	25
Step 0. Create the tenancy: Group (Yes / No), then the organization.....	25
Step 1. Create the project.....	25
Step 2. E2E-01 Idea-to-Business Plan.....	26
Step 3. E2E-02 Idea-to-Business Proposal.....	27
Step 4. E2E-05 Development-to-Launch.....	28
Result of the run.....	29
7. Run 2: Fast Track in Transportation, with a skipped task and a Recycle decision.....	30

Step 0. Create the tenancy: Group (Yes / No), then the organization.....	30
Step 1. Create the project.....	30
Step 2. E2E-01 Idea-to-Business Plan.....	31
Step 3. E2E-02 Idea-to-Business Proposal.....	32
Step 4. E2E-02 Idea-to-Business Proposal.....	33
Step 5. E2E-05 Development-to-Launch.....	34
Result of the run.....	35
8. Run 3: Light Track in Agro-Business (Dairy), from idea to relaunch.....	36
Step 0. Create the tenancy: Group (Yes / No), then the organization.....	36
Step 1. Prepare the Light Track observation period.....	36
Step 2. Create the project.....	37
Step 3. E2E-01 Idea-to-Business Plan.....	37
Step 4. E2E-02 Idea-to-Business Proposal.....	38
Step 5. E2E-03 Business Proposal-to-Design.....	39
Step 6. E2E-04 Design-to-Development.....	40
Step 7. E2E-05 Development-to-Launch.....	41
Step 8. E2E-07 After-Sales-to-Performance.....	42
Step 9. E2E-09 Market Strategy-to-Campaign.....	42
Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch A.....	43
Step 11. E2E-05 Development-to-Launch (run 2).....	43
Result of the run.....	44
9. Run 4: Full Track in Healthcare, from idea to retirement.....	45
Step 0. Create the tenancy: Group (Yes / No), then the organization.....	45
Step 1. Create the project.....	45
Step 2. E2E-01 Idea-to-Business Plan.....	46
Step 3. E2E-02 Idea-to-Business Proposal.....	47
Step 4. E2E-03 Business Proposal-to-Design.....	48
Step 5. E2E-04 Design-to-Development.....	49
Step 6. E2E-05 Development-to-Launch.....	50
Step 7. E2E-06 Launch-to-After-Sales.....	51
Step 8. E2E-09 Market Strategy-to-Campaign.....	52
Step 9. E2E-07 After-Sales-to-Performance.....	53
Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch B.....	54

Result of the run.....	55
10. Run 5: Full Track in Oil, Gas & Energy, from idea to a relaunch.....	56
Step 0. Create the tenancy: Group (Yes / No), then the organization.....	56
Step 1. Create the project.....	56
Step 2. E2E-01 Idea-to-Business Plan.....	57
Step 3. E2E-02 Idea-to-Business Proposal.....	58
Step 4. E2E-03 Business Proposal-to-Design.....	59
Step 5. E2E-04 Design-to-Development.....	60
Step 6. E2E-05 Development-to-Launch.....	61
Step 7. E2E-06 Launch-to-After-Sales.....	62
Step 8. E2E-09 Market Strategy-to-Campaign.....	63
Step 9. E2E-07 After-Sales-to-Performance.....	64
Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch A.....	65
Step 11. E2E-04 Design-to-Development (run 2).....	65
Step 12. E2E-05 Development-to-Launch (run 2).....	66
Result of the run.....	67
11. Run 6: Light Track in Real Estate Development, from idea to launch.....	68
Step 0. Create the tenancy: Group (Yes / No), then the organization.....	68
Step 1. Create the project.....	68
Step 2. E2E-01 Idea-to-Business Plan.....	69
Step 3. E2E-02 Idea-to-Business Proposal.....	70
Step 4. E2E-03 Business Proposal-to-Design.....	71
Step 5. E2E-04 Design-to-Development.....	72
Step 6. E2E-05 Development-to-Launch.....	73
Result of the run.....	74
12. Run 7: Benchmarking in Real Estate Development, within the organization and across the group	75
Step 1. Compare project types.....	75
Step 2. Compare tracks and filter.....	76
Step 3. Compare with the organizations of the group.....	76
Step 4. Stop or resume sharing with the group.....	77
Step 5. An independent organization.....	77
13. Everyday Scenarios by Module.....	78
13.1 Record a business rule.....	78

13.2 Add a control, change it and compare versions.....	78
13.3 Log a risk and read the heat map.....	78
13.4 See the governance of one process.....	78
13.5 Build a RACSI activity.....	79
13.6 Track a custom KPI.....	79
13.7 Edit and exchange a BPMN diagram.....	79
13.8 Ask for an AI suggestion on a task.....	79
13.9 Search the knowledge base in your language.....	79
13.10 Create a project template and use it.....	80
13.11 Plan with a WBS and a Gantt chart.....	80
13.12 Record a lesson learned.....	80
13.13 Export a report.....	80
13.14 Choose how you are notified.....	80
13.15 Add a user within the licence limit.....	81
13.16 Place people in a project team with their roles (OBS).....	81
13.17 Back up the database.....	81
13.18 Check the audit trail.....	81
13.19 Create a second project in the same organization.....	81
13.20 Attach documents to a task.....	82
13.21 Add checklist items at a gate, from a template or by hand.....	82
13.22 Build a checklist template and link it to a gate.....	82
13.23 See where AI helps in the process design and run a use case.....	83
13.24 Create, change and delete an AI use case.....	83
13.25 Choose the live AI model.....	83
13.26 Look at a group portfolio.....	83
13.27 Work on a BPMN diagram in full screen.....	84
14. Messages You May Meet.....	88

1. About This Guide

This guide shows how to use CortexPLM through complete, worked examples. Every run starts the same way: create the **group** (or decide there is none: Group Yes / No), create the **organization** with its team, then create the **project(s)**. Six runs then take real projects through their whole lifecycle, in six sectors and all three tracks. Every value you type is given in **bold**, exactly as you enter it. The runs were replayed on a freshly installed demonstration database, so the codes and results match what you will see.

Run	Group (Yes / No)	Organization (sector)	Track	To	Gate decisions
1	No	Harbourview City Services (Public Sector)	Fast	Launched	T-1, T0, T3
2	Yes, new: Meridian Mobility Holding	Northline Regional Transit (Transportation)	Fast	Launched	T-1, T0 (Recycle, then Go), T3
3	Yes: Crescent Agro-Energy Group	Oasis Fresh Dairies (Agro-Business – Dairy)	Light	Relaunched	T-1, T0, T1, T2, T3, T5, T3
4	No	Clearwater Medical Devices (Healthcare)	Full	Retired	T-1 to T6
5	Yes: Crescent Agro-Energy Group	Sahara Hydrogen Energy (Oil, Gas & Energy)	Full	Relaunched	T-1 to T5, then T2, T3
6	Yes: Atlas Infrastructure Holding	Palmgrove Residential Developers (Real Estate Development)	Light	Launched	T-1, T0, T1, T2, T3
7	Yes: Atlas Infrastructure Holding	Ridgeway Real Estate Development (seeded)	All	Benchmarked	Within the organization and across the group

Chapter 4 is the **decision matrix**: which value to choose in each field. Chapter 13 adds short scenarios for every other module, continuing in the organization created in Run 1.

Before you start Start from a fresh demonstration database (Installation Guide, "Reset the demonstration data") and follow the runs in order: Run 2 creates the group that Run 1 does not need, and the module scenarios use the organization of Run 1.

1.1 Conventions

You see	Meaning
Bold text	A value to type, or a button, tab or menu item to select.
Menu > Item	Open the menu group, then the item, in the navigation bar.
UFT-01-02	The identifier of a user-facing task from the process reference.
T-1 ... T6	The eight decision gates of the phase-gate process.
Group: Yes / No	Whether an organization belongs to a group of organizations.

2. Getting Started

2.1 Sign in


1. Open **http://localhost:5173** in your browser.
2. Type your e-mail and password (seeded demonstration users: **Demo#2026**; teams created in the runs: **Start#2026**; platform administrator: **admin@cortexplm.example** / **Admin#2026**).
3. Select **Sign in**.

The sign-in page lists the demonstration accounts.

2.2 The menu, organized by what you do

Menu group	What you find there
Home	Dashboard, My tasks, Alerts, Notifications.
Portfolio	Groups, organizations & projects (tenancy), Portfolio overview, Innovation projects, Gate board, WBS & Gantt, Benchmarking.
Process design	End-to-end processes (with Tasks and AI), Macro processes (with the Part legend), BPMN diagrams, Checklist templates, Track configuration, Phase-gate reference, Coverage matrix.
Governance & risk	Business rules, Controls (COSO), Risks & opportunities, KPIs, RACSI matrix.
AI & knowledge	AI use cases, AI Assistant, Knowledge base, Lessons learned (REX), Project templates.
Reports	Reports & cockpits, Data model, Role menus.
Administration	Organizations, OBS & teams, Users & roles, Permission matrix, Configuration & AI model, Commercial catalog, Integrations, Licensing, Audit trail, Requirements traceability.
Me	Settings (language, menu, password, live AI model) and Help.

You only see the items your roles allow. The dashboard leads with four figures: active projects, gates waiting for a decision, overdue tasks and checklist compliance.

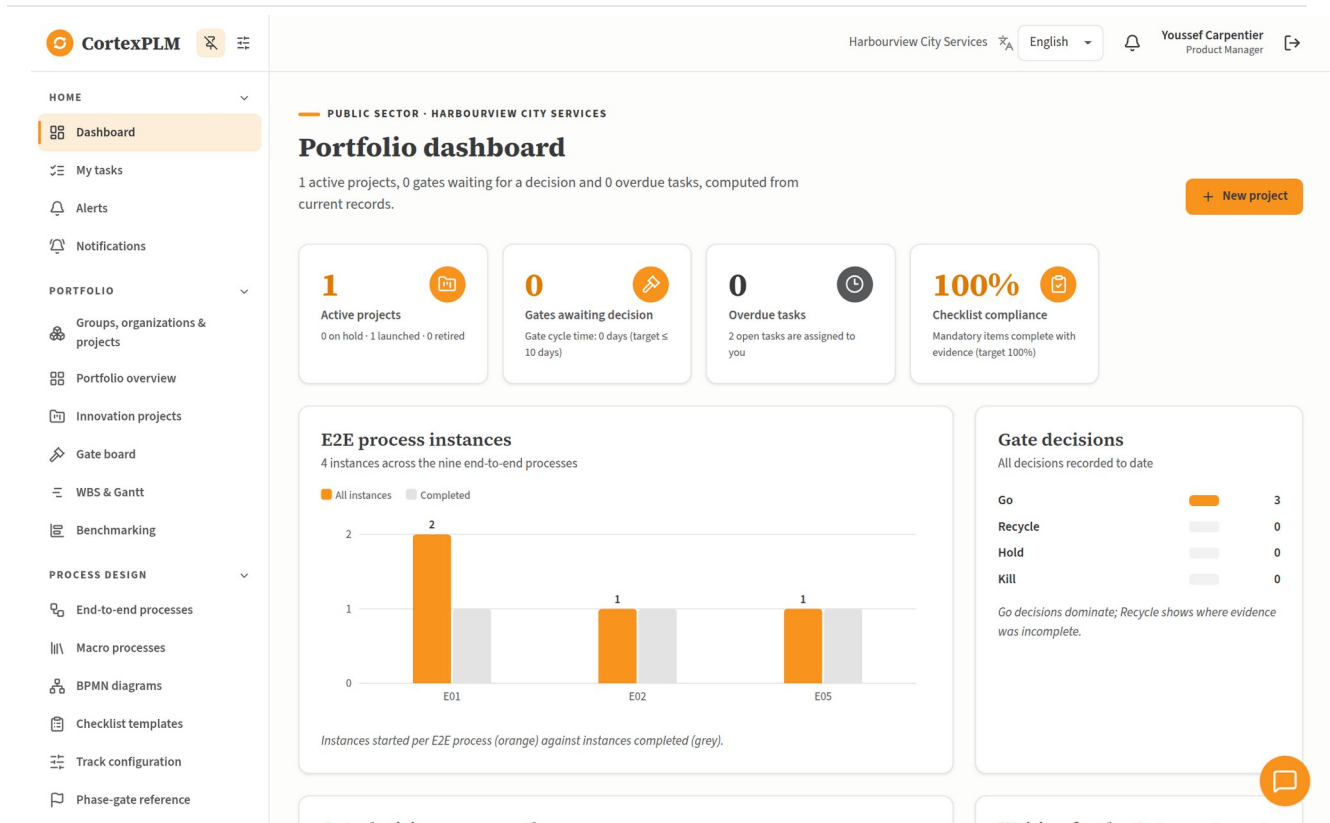

Dashboard of Harbourview City Services for its Product Manager, after Run 1.

2.3 The navigation bar: pin, slide and position

1. Select the **sliders** icon at the top of the navigation bar to open **Menu position**.
2. Choose **Left**, **Right**, **Top** or **Bottom**. The menu moves at once and the choice is saved for your account.
3. Clear **Keep the menu pinned open** to let the menu slide away. It slides back when you point at the edge of the screen. The pin icon next to the sliders does the same.
4. Select the star next to any item to add it to the favourites at the top of the menu. Select a group title to fold or unfold it.

Menu position

Left Right Top Bottom

☒ Keep the menu pinned open

When unpinned, the menu slides away and slides back when you point at the screen edge.

Dashboard

Waiting for a decision and 0 overdue tasks, computed from

Active projects
0 on hold · 1 launched · 0 retired

Gates awaiting decision
Gate cycle time: 0 days (target ≤ 10 days)

Overdue tasks
2 open tasks are assigned to you

Checklist compliance
Mandatory items complete with evidence (target 100%)

E2E process instances
4 instances across the nine end-to-end processes

Legend: All instances (orange), Completed (grey)

E2E Process	All instances	Completed
E01	2	1
E02	1	1
E05	1	1

Instances started per E2E process (orange) against instances completed (grey).

Gate decisions
All decisions recorded to date

Decision	Count
Go	3
Recycle	0
Hold	0
Kill	0

Go decisions dominate; Recycle shows where evidence was incomplete.

Menu position settings: four positions and the pin option.

2.4 Language

Choose **English**, **Français** or العربية in the language list of the top bar. Arabic switches the whole layout to right-to-left, and the navigation bar moves to the right. Your choice is saved; the organization default applies otherwise.



The dashboard in Arabic, laid out right to left.

2.5 Groups, organizations and projects

Open **Portfolio > Groups, organizations & projects**. The tree reads **Group (Yes / No) > Organization > Projects**. Open an organization to list its projects; the **Table** view lists Group (Yes / No), Group, Organization, Sector and Projects in one grid. A platform administrator sees every organization; an executive or portfolio manager sees the organizations of their group (read-only outside their own); everyone else sees their own organization.

Group (Yes / No)	Group	Organization	Sector	E-mail domain	Projects
No	—	Metro City Digital Services Agency	Public Sector	metrocity.example	PUB-001 ... PUB-021
Yes	Atlas Infrastructure Holding	Cedarline Precast Systems	Manufacturing	cedarline.example	MFG-001 ... MFG-021
No	—	Meridale Health Network	Healthcare	meridale.example	HLT-001 ... HLT-021
Yes	Crescent Agro-Energy Group	Valdora Dairy Cooperative	Agro-Business – Dairy Products	valdora.example	DAI-001 ... DAI-021
Yes	Atlas Infrastructure Holding	Orvane Transit Group	Transportation	orvane.example	TRN-001 ... TRN-021
Yes	Crescent Agro-Energy Group	Kestrel Energy & Utilities	Oil, Gas & Energy	kestrel.example	ENR-001 ... ENR-021
Yes	Atlas Infrastructure Holding	Ridgeway Real Estate Development	Real Estate Development	ridgeway.example	RED-001 ... RED-021

Every seeded project also has its own team tree (OBS) with the role of each person: steering committee, project management and delivery teams.

CortexPLM Metro City Digital Services Agency · Publi English Platform Administrator

HOME

- Dashboard
- My tasks
- Alerts
- Notifications

PORTFOLIO

- Groups, organizations & projects**
- Portfolio overview
- Innovation projects
- Gate board
- WBS & Gantt
- Benchmarking

PROCESS DESIGN

- End-to-end processes
- Macro processes
- BPMN diagrams
- Checklist templates
- Track configuration
- Phase-gate reference

PORTFOLIO

Groups, organizations & projects

Group (Yes / No) > Organization > Projects. An organization belongs to at most one group; every project belongs to exactly one organization.

+ Add group + Add organization + New project

3 Groups

13 Organizations
9 in a group, 4 independent

154 Projects

All organizations
What you can see

Tenancy
Open an organization to list its projects. Projects of other organizations are read-only.

Find an organization or Tree Table

Group (Yes / No) > Organization	Sector	Country	Users	Projects	
Group: Yes Atlas Infrastructure Holding Real estate development, precast manufacturing and transport operations under one holding.					
> Cedarline Precast Systems	Manufacturing	United Arab Emirates	24	21	Switch to + Project
> Orvane Transit Group	Transportation	Canada	24	21	Switch to + Project
> Ridgeway Real Estate Development	Real Estate Development	Saudi Arabia	24	21	Switch to + Project
> Palmgrove Residential Developers	Real Estate Development	Saudi Arabia	24	1	Switch to + Project
Group: Yes Crescent Agro-Energy Group Dairy cooperative and energy utility owned by the same regional investment group.					

Groups, organizations & projects: the tree Group (Yes / No) > Organization > Projects.

2.6 Portfolio overview

Open **Portfolio** > **Portfolio overview** and choose a scope: a group, one organization, or a set of projects. Each row is a project and each column an end-to-end process; the cell shows the status of that process for the project. The legend explains the colours: **Completed**, **In progress**, **At gate** (waiting for the board), **On hold**, **Stopped**, **Not started** and **Not in track**. **Export CSV** downloads the grid.

Portfolio overview

Rows are projects, columns are the end-to-end processes; each cell shows where the project stands in that process.

Scope
Choose a group, one organization, or a set of projects. Only what your permissions allow is listed.

All groups | All organizations | Add a project to the set | All tracks

64 Projects in scope | **4** Organizations | **3** Waiting for a gate decision | **6** On hold or stopped

Projects × end-to-end processes Export CSV


☒ Completed
 ☒ In progress
 ☒ At gate
 ☒ On hold
 ☒ Stopped
 ☐ Not started
 ☐ Not in track

Project	E2E-01 Idea-to-Business Plan Gate T-1	E2E-02 Idea-to-Business Proposal Gate T0	E2E-03 Business Proposal-to-Design Gate T1	E2E-04 Design-to-Development Gate T2	E2E-05 Development-to-Launch Gate T3	E2E-06 Launch-to-After-Sales Gate T4	E2E-07 After-Sales-to-Performance Gate T5	E2E-08 Assessment-to-Relaunch or Retirement Gate T6	E2E-09 Market Strategy-to-Campaign
MFG-001 Precast Hollow-Core Floor Slab Line Cedarline Precast Systems - Full Track - Retired	☒	☒	☒	☒	☒	☒	☒	☒	☒

Portfolio overview of Atlas Infrastructure Holding, seen by the Executive Sponsor of Ridgeway.

2.7 Alerts, notifications and the assistant

- The **bell** in the top bar shows unread alerts, such as overdue tasks or a gate waiting too long. Open **Alerts** for the full list.
- Notifications** holds your inbox and lets you choose, per category, the channels you want (in-app, e-mail, webhook, SMS, push).
- The round **assistant** button at the bottom of the screen answers questions about your data within your permissions, for example **How many active projects?**, and explains how to use each screen.

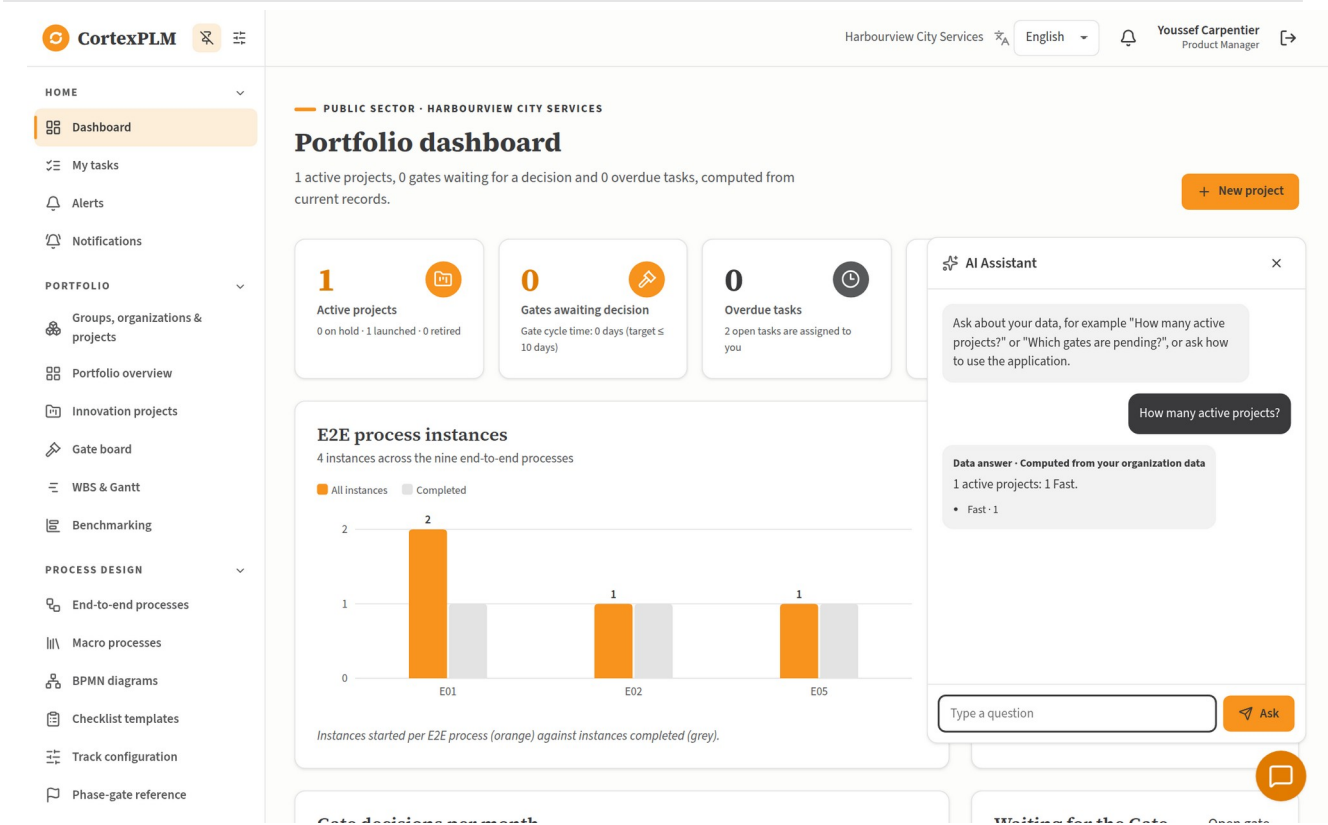

The assistant answers from live organization data.

3. How a Project Moves Through CortexPLM

Every project belongs to one organization and follows the end-to-end (E2E) processes of its track. Each E2E process is a list of tasks and ends with a gate. At the gate, the Executive Sponsor records one of four decisions.

Track	Total score	E2E processes	Gates	Standard checklist items per gate
Fast	7 to 14	E2E-01, E2E-02, E2E-05	T-1, T0, T3	6
Light	15 to 24	E2E-01 to E2E-05, E2E-07, E2E-08 (relaunch only), E2E-09	T-1, T0, T1, T2, T3, T5	15
Full	25 to 35, or any safety-critical product	All nine	All eight	30

Decision	What happens
Go	The gate is passed and the next E2E process starts automatically.
Kill	The project stops. You are invited to record a lesson learned.
Hold	The project pauses until a re-review date. Resume project reopens the gate.
Recycle	Named tasks go back to To do; the gate is reviewed again afterwards.

3.1 Who does what in the runs

- The **platform administrator** creates the group (if any) and the organization with its starting team.
- The **Product Manager** creates the project, completes the tasks, completes the gate checklist and submits the gate. Each task shows its own owner (for example Finance or Marketing). In daily use each owner completes their task; in these runs the Product Manager completes them on the owners' behalf, which the role allows.
- The **Executive Sponsor** records the gate decision. The project owner can never decide their own gate (control CTL-01).
- The **evaluator** of a task (Accountable in the RACSI matrix) rates it Effective or Not effective after completion. Evaluations do not block the process.

3.2 Create the organization

In **Groups, organizations & projects**, **Add organization** asks whether the organization belongs to a group (Yes / No), its name, sector, country and subscription. Tick **Create the starting team** and type the e-mail domain and an initial password to create one account per role.

Add organization: Group Yes, the group, and the starting team.

3.3 Create a project

Open **Innovation projects** > **New project**. **Step 0** shows the organization the project belongs to and whether it is in a group. Step 1 describes the project, Step 2 scores seven complexity criteria from 1 to 5 (the **Decision matrix** button explains each level), Step 3 confirms the recommended track, and Step 4 adds optional macro processes. Select **Create project**; E2E-01 starts.

Decision matrix: how to score a new project

Pick, for each criterion, the description closest to the project. The total decides the recommended track.

Criterion	Score 1	Score 2	Score 3	Score 4	Score 5
Strategic impact	Incremental change to an existing offer	Improvement customers notice, same segment	New segment or product-line extension	Major extension that changes the competitive position	New platform or business model
Investment level	Within the business unit's delegated authority	Up to twice the delegated authority, one budget line	Requires portfolio-level approval	Funding over several years or a large share of the portfolio budget	Requires executive or board approval
Technical novelty	Known technology; configuration change	Known technologies in a new combination	Adaptation of existing technology	Technology new to the organization but proven elsewhere	New technology or architecture
Regulatory and safety exposure	No new certification needed	Update of an existing declaration or file	Standard certifications or declarations	New approval by an authority or a notified body	Regulated or safety-critical product
Market scope	One market, existing channel	One market, new segment or adapted channel	Several markets or a new channel	Several regions with local adaptations	Multi-market or global launch
Cross-functional reach	1 to 2 functions	2 to 3 functions with light coordination	3 to 5 functions	More than 5 functions	More than 5 functions or external partners
Product-service integration	Product-only or service-only change	Service sold separately around a product	Change to an existing bundle	New bundle of existing products and services	New integrated or outcome-based offer

From total score to track

Total score	Recommended track	Rule
7 - 14	Fast Track	Not allowed if any criterion scores 5.
15 - 24	Light Track	Light is the minimum when regulatory and safety exposure scores 4 or more.
25 - 35	Full Track	Mandatory for any safety-critical product, whatever the total.

The decision matrix opened from Step 2.

3.4 Complete a task and attach documents

Open the task from the project page or from **My tasks**. Fill in the fields, type the **Result / output** and select **Complete task**. A window proposes to record a lesson learned: fill it in, or select **Skip**. In **Attachments**, add several files at once (documents, spreadsheets, presentations, images, drawings and CAD, data, archives, audio and video, e-mails). The **AI for this task** line shows the AI use cases you can run on the task.

CortexPLM Harbourview City Services English Youssef Carpentier Product Manager

HOME

- Dashboard
- My tasks
- Alerts
- Notifications

PORTFOLIO

- Groups, organizations & projects
- Portfolio overview
- Innovation projects
- Gate board
- WBS & Gantt
- Benchmarking

PROCESS DESIGN

- End-to-end processes
- Macro processes
- BPMN diagrams
- Checklist templates
- Track configuration
- Phase-gate reference

UFT-01-01 - E2E-01 IDEA-TO-BUSINESS PLAN

Capture Strategic Idea

Capture new product/service idea from an internal or external source - [HAR-002 Street Lighting Fault Reporting](#)

Record the result
Fill in the fields, write the result, then select Complete task.

Idea source *
Choose

One-sentence idea statement *

Result / output *

Describe what was done and the outcome. This text goes into the gate evidence.

Attachments (3)
Documents, drawings, pictures and data that support this task.

Add files or drop them here
Up to 10 files of 25 MB each: documents, spreadsheets, presentations, images, drawings and CAD, data, archives, audio and video, e-mails.
Accepted file types

photo-report.pdf
PDF - 1 KB - Youssef Carpentier - 2026-09-23

fault-list.xlsx
XLSX - 1 KB - Youssef Carpentier - 2026-09-23

site.jpg
JPG - 1 KB - Youssef Carpentier - 2026-09-23

Accountability (RACSI)

Owner	Youssef Carpentier
Evaluator	Julie Zahiri
Due date	2026-09-30
Responsible	Product Manager
Accountable	Executive Sponsor
Consulted	Marketing
Supportive	R&D
Informed	Finance
Macro processes	MP-01 Portfolio MP-03 Requirements
Module	Ideation Module
Chain link	Feeds E2E-02
AI for this task	AIUC-01 - Assistive AI AIUC-02 - Assistive AI AIUC-03 - Assistive AI

AI assistance
Use a suggestion as a starting point for the result.

AI use case
AIUC-02 Business

Context (optional)
Add details for the su

Get suggestion

Task UFT-01-01 with its attachments and the AI available for the task.

3.5 Complete the gate checklist

The last task before each gate is **Complete Gate Checklist**. Its items come from the checklist templates linked to that gate and track. Every **Mandatory** item needs an evidence reference (or an attached file) before **Mark complete** works (BR-005). On the gate screen, **Add to this checklist** adds items from any template of the library, or typed by hand; **Save as template** keeps the checklist for later projects.

Is the idea strategically aligned and worth a funded opportunity study?
 HAR-002 Street Lighting Fault Reporting - Fast Track

Open Gate review pack (PDF)

0/6 Mandatory items complete or waived

NPV (kUSD)

ROI

0/6 Work tasks closed

Minimum evidence for T-1
 Captured idea; market opportunity assessment; preliminary business case (NPV, ROI, risk); initial risk and compliance register; portfolio fit.

#	Checklist item	Evidence	Source	Status
1	Captured idea Mandatory	—	Gate T-1 minimum evidence (Part 8)	Open
2	Market opportunity assessment Mandatory	—	Gate T-1 minimum evidence (Part 8)	Open
3	Preliminary business case (NPV, ROI, risk) Mandatory	—	Gate T-1 minimum evidence (Part 8)	Open
5	Portfolio fit Mandatory	—	Gate T-1 minimum evidence (Part 8)	Open
6	Evidence: Define strategic product themes, goals, and investment horizons	—	MP-01.1	Open
7	Photo of the fault location is mandatory in the form Mandatory	—	Added by Youssef Carpenterier	Open

Gate not yet submitted
 Complete the work tasks and the checklist, then submit the gate.
 Submit gate for decision

Gate readiness (advisory)
 AIUC-12. The board decides; the assessment only summarizes the evidence.

AI use case: AIUC-12 Gate reac
 Context (optional): Add details for the su

Youssef Carpenterier Product Manager

Add to this checklist
 From the checklist template library, or item by item. Items already in the checklist are not added twice.
 Save as template

From a template Manually

#	Checklist item	Mandatory	Evidence required
1		☐	☐

+ Add item

Add to checklist

Task results

- UFT-01-01 - Capture Strategic Idea To do
- UFT-01-02 - Assess Market Opportunity To do
- UFT-01-03 - Build Preliminary Business Case To do
- UFT-01-04 - Assess Risks & Compliance To do
- UFT-01-05 - Describe High-Level Capability To do
- UFT-01-06 - Establish Product Portfolio Strategy To do
- UFT-01-07 - Complete Gate Checklist (T-1) To do
- UFT-01-08 - Approve T-1 Gate (Go/No-Go) To do

Gate T-1 of HAR-002: the checklist and the Add to this checklist card.

3.6 Submit the gate and record the decision

When all tasks are done, the project page shows **Submit gate for decision** on the gate card. The Executive Sponsor then opens **Gate board**, opens the gate, chooses the decision, types a rationale and selects **Record decision**.

Harbourview City Services

English

Youssef Carpentier
Product Manager

HOME

Dashboard

My tasks

Alerts

Notifications

PORTFOLIO

Groups, organizations & projects

Portfolio overview

Innovation projects

Gate board

WBS & Gantt

Benchmarking

PROCESS DESIGN

End-to-end processes

Macro processes

BPMN diagrams

Checklist templates

Track configuration

Phase-gate reference

HAR-002 · FAST TRACK · SERVICE

Street Lighting Fault Reporting

Residents report broken street lights with a photo; crews receive work orders.

Active Edit Add lesson learned Delete

E2E-01
1 run(s)

E2E-02
Not started

E2E-03
Not in track

E2E-04
Not in track

E2E-05
Not started

E2E-06
Not in track

E2E-07
Not in track

E2E-08
Not in track

E2E-09
Not in track

Lifecycle & tasksBusiness case & risksTailoringAI assistanceLessons learnedHistory

E2E-01

Idea-to-Business Plan

Project created (UFS-28 Configure Track & Macro Processes).

In progress 0/8

UFT-01-01 · Capture Strategic Idea

Owner: Youssef Carpentier · Evaluator: Julie Zahiri · Due 2026-09-30

To do

UFT-01-02 · Assess Market Opportunity

Owner: Rachid Leroy · Evaluator: Youssef Carpentier · Due 2026-10-07

Skippable (R2) To do

UFT-01-03 · Build Preliminary Business Case

Owner: Tariq Mercier · Evaluator: Youssef Carpentier · Due 2026-10-14

To do

UFT-01-04 · Assess Risks & Compliance

Owner: Samir Dubois · Evaluator: Laura Berrada · Due 2026-10-21

Skippable (R2) To do

UFT-01-05 · Describe High-Level Capability

Owner: Sara Benali · Evaluator: Youssef Carpentier · Due 2026-10-28

To do

Project page: the lifecycle and the tasks of the current process.

Ridgeway Real Estate Development

English

Amina Amrani
Executive Sponsor

HOME

Dashboard

My tasks

Alerts

Notifications

PORTFOLIO

Groups, organizations & projects

Portfolio overview

Innovation projects

Gate board

WBS & Gantt

Benchmarking

PROCESS DESIGN

End-to-end processes

Macro processes

BPMN diagrams

Checklist templates

Track configuration

Phase-gate reference

MP-121 INNOVATION PHASE-GATE MANAGEMENT

Gate board

1 gate packs wait for a Go, Kill, Hold or Recycle decision. Decisions pending more than 10 working days are escalated (BR-008).

Awaiting decisionOpenOn holdDecided

Filter rows

1 rows

CSV

Gate	Project	Decision question	Checklist	Submitted	Decision	Status
T0	RED-015 · Solar Rooftop Offer for Buyers Light Track	Should we commit investment to design and development?	15/15	2026-07-25 44 working days	—	Submitted

Gate board: gates waiting for a decision, with the working days elapsed.

POWERACT Consulting · Page 20 of 88

CortexPLM

HOME

Dashboard

My tasks

Alerts

Notifications

PORTFOLIO

Groups, organizations & projects

Portfolio overview

Innovation projects

Gate board

WBS & Gantt

Benchmarking

PROCESS DESIGN

End-to-end processes

Macro processes

BPMN diagrams

Checklist templates

Track configuration

Phase-gate reference

GATE T0 - E2E-02 IDEA-TO-BUSINESS PROPOSAL

Should we commit investment to design and development?

RED-015 Solar Rooftop Offer for Buyers - Light Track

SubmittedGate review pack (PDF)

9/9

Mandatory items complete or waived

901

NPV (KUSD)

97%

ROI

9/9

Work tasks closed

Minimum evidence for T0

Opportunity study; detailed business case and profitability analysis; high-level functional specifications; preliminary customer journey; regulatory validation; technical feasibility; development plan.

#	Checklist Item	Evidence	Source	Status
1	Opportunity studyMandatory	Evidence pack RED-015/T0/01 - document stored in the project folder	Gate T0 minimum evidence (Part 8)	Complete
2	Detailed business case and profitability analysisMandatory	Evidence pack RED-015/T0/02 - document stored in the project folder	Gate T0 minimum evidence (Part 8)	Complete
3	High-level functional specificationsMandatory	Evidence pack RED-015/T0/03 - document stored in the project folder	Gate T0 minimum evidence (Part 8)	Complete

Record the gate decision

Performed by the Executive Sponsor, owned by the Gate Review Board. The project owner cannot decide (CTL-01).

GoKillHoldRecycle

The project proceeds; the next E2E process starts.

Rationale *

Recorded with the decision (MP-121 task 11).

Board votes forBoard votes against

Gate decision page: evidence summary on the left, decision form on the right.

POWERACT Consulting · Page 21 of 88

4. Decision Matrix: How to Fill In the Fields

Use these tables whenever you are unsure which value to choose. The same scoring matrix opens in the application with the **Decision matrix** button of the New project screen.

4.1 Group, organization and project

Field	Choose	When
Belongs to a group?	Yes	The organization is owned by, or reports to, a holding that also owns other organizations using CortexPLM, and they want to compare performance (benchmarking, group portfolio).
	No (independent)	The organization stands alone. Its data is never compared with anyone else.
Create the starting team	Ticked	A new organization that needs its people now; one account per role is created and can be renamed later.
	Not ticked	Accounts will be added one by one in Users & roles , or come from an identity provider.
Organization of a project	The organization that funds and runs the project	A project belongs to exactly one organization; other organizations of the group only see it read-only.
Offer type	Product	The customer buys a physical or digital product.
	Service	The customer buys a service or an outcome delivered over time.
	Product-Service	Product and service are sold and supported together.
Safety-critical product	Ticked	A failure could injure people or damage property (medical device, pressure equipment, vehicle safety function). The Full Track becomes mandatory.

4.2 Complexity scores (Step 2 of New project)

Score each criterion from 1 to 5 with the description closest to the project. When the project sits between two descriptions, take the lower score unless the evidence clearly supports the higher one.

Criterion	1	2	3	4	5
Strategic impact	Incremental change to an existing offer	Improvement customers notice, same segment	New segment or product-line extension	Major extension that changes the competitive position	New platform or business model
Investment level	Within the business unit's delegated authority	Up to twice the delegated authority, one budget line	Requires portfolio-level approval	Funding over several years or a large share of the portfolio budget	Requires executive or board approval
Technical novelty	Known technology; configuration change	Known technologies in a new combination	Adaptation of existing technology	Technology new to the organization but proven elsewhere	New technology or architecture
Regulatory and safety exposure	No new certification needed	Update of an existing declaration or file	Standard certifications or declarations	New approval by an authority or a notified body	Regulated or safety-critical product
Market scope	One market, existing channel	One market, new segment or adapted channel	Several markets or a new channel	Several regions with local adaptations	Multi-market or global launch
Cross-functional reach	1 to 2 functions	2 to 3 functions with light coordination	3 to 5 functions	More than 5 functions	More than 5 functions or external partners
Product-service integration	Product-only or service-only change	Service sold separately around a product	Change to an existing bundle	New bundle of existing products and services	New integrated or outcome-based offer

4.3 From total score to track

Total score	Recommended track	Rule
7 – 14	Fast Track	Not allowed if any criterion scores 5.
15 – 24	Light Track	Light is the minimum when regulatory and safety exposure scores 4

Total score	Recommended track	Rule
		or more.
25 – 35	Full Track	Mandatory for any safety-critical product, whatever the total.

Choose another allowed track only with a reason (for example a group standard for the product family); the reason is recorded as a track override.

4.4 Task fields

Field (task)	Value	When
Idea source (UFT-01-01)	Internal - employee / Internal - strategy / Customer request / Market trend / Partner / Regulation	Where the idea first came from; choose Regulation when a new rule forces the change.
Strategic-fit score (UFT-01-02)	0 – 100	80 or more: core to the strategy; 50 – 79: supports it; below 50: the idea is parked for 90 days (BR-001).
Likelihood (UFT-01-04)	1 – 5	1 rare (less than once in 10 years) · 2 unlikely · 3 possible (once in the project) · 4 likely · 5 almost certain.
Impact (UFT-01-04)	1 – 5	1 negligible · 2 minor delay or cost · 3 visible to customers or 10% budget · 4 regulatory breach or 25% budget · 5 safety, legal or reputational crisis.
Regulated (UFT-01-04)	Yes / No	Yes when an authority must approve, certify or be notified before launch.
Portfolio position (UFT-01-06)	Core / Adjacent / Transformational	Core: current customers and offers; Adjacent: new segment or channel; Transformational: new business model or market.
Technical feasibility (UFT-02-07)	High / Medium / Low	High: done before; Medium: prototypes needed; Low: key technology not yet proven.
All regulatory approvals obtained? (UFT-05-08)	Yes / No	Answer No while any approval is missing; go-live is then blocked (BR-030).
Recommendation to the T5 gate (UFT-07-04)	Continue / Relaunch / Retire	Continue: on target; Relaunch: below target but fixable; Retire: demand gone or a successor exists.
Relaunch re-entry point (UFT-08-04)	E2E-03 / E2E-04 / E2E-05	E2E-03 when the design changes, E2E-04 when only development changes, E2E-05 when only the launch is repeated.

4.5 Gates, checklists, evaluations, lessons and AI

Decision	Choose	When
Gate decision	Go	The evidence answers the gate question and the business case holds.
	Recycle	The direction is right but named evidence is missing or weak; name the tasks to redo.
	Hold	An outside event must happen first (budget cycle, regulator, partner); set a re-review date.
	Kill	The case no longer holds or the risk is unacceptable; record a lesson learned.
Checklist item	Mandatory + Evidence required	The gate cannot be passed without it and a document or reference proves it.
	Waive	The item does not apply to this project; a board member must approve the waiver and its reason.
Checklist template	Link to the gate	Every project of that track needs the items at that gate.
	Not linked	Only some projects need the items; add them from the gate screen when needed.
Task evaluation	Effective / Not effective	Effective when the result meets its purpose without rework.
Lesson rating	1 – 5	1 serious problem · 3 acceptable · 5 exemplary; use the rating for the whole experience.
AI use case tier	Assistive / Augmented	Assistive when the AI only suggests; Augmented when it drafts a result a person approves. Never autonomous.
AI suggestion	Accept / Modify / Reject	Accept when correct as is, Modify when useful but imperfect, Reject when wrong or unhelpful.

5. Common Values Used in the Runs

The runs use the same patterns so you can type quickly:

- Passwords: the platform administrator uses **Admin#2026**; every team created in the runs uses **Start#2026**.
- Result / output of a task: "<task name> done for <project code>. Summary filed as <project code>-<task number>." The exact text is given in every table.
- Evidence reference of a checklist item: <project code>-<gate>-<item number>, for example **HAR-001-T-1-01**.
- Dates: any future date works; the tables show the dates used in the example runs.
- Fields not listed in a table can stay empty.

6. Run 1: Fast Track in the Public Sector

A new independent organization (Group: No) launches a low-complexity citizen service on the Fast Track: E2E-01, E2E-02 and E2E-05 with gates T-1, T0 and T3.

Item	Value
Tenancy	Group: No > Harbourview City Services > project HAR-001
Organization	Harbourview City Services (Public Sector), e-mail domain harbourview.example
Product Manager	Youssef Carpentier · pm1@harbourview.example
Executive Sponsor	Julie Zahiri · exec@harbourview.example
Project	HAR-001 Online Parking Permit Renewal
Track	Fast (total score 11 of 35)
End state	Launched · NPV 120 kUSD, ROI 132.1%

Step 0. Create the tenancy: Group (Yes / No), then the organization

Sign in as **admin@cortexplm.example** (password **Admin#2026**), the platform administrator.

Open **Portfolio > Groups, organizations & projects**.

1. This organization belongs to no group: it will appear under **Group: No · Independent organizations**.
2. Select **Add organization** and fill in the window:

Field	What to type or select
Belongs to a group?	select No (independent)
Name	Harbourview City Services
Sector	select Public Sector
Country	Morocco
Default language	keep English
Initial subscription	select PACK-11 CortexPLM Enterprise
Create the starting team	keep the box ticked
E-mail domain	harbourview.example
Initial password	Start#2026

Select **Save**. The message reads "Organization created with 24 accounts." The organization receives its OBS departments, the governance catalog, the AI use case library and the checklist templates, and one account per role, for example **pm1@harbourview.example** (Product Manager) and **exec@harbourview.example** (Executive Sponsor). Sign out.

Step 1. Create the project

Sign in as **pm1@harbourview.example** (password **Start#2026**), the Product Manager.

Open **Portfolio > Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Step 0. Organization	shows Harbourview City Services ; Belongs to a group? No
Project name	Online Parking Permit Renewal
Description	Residents renew their parking permit online in under five minutes, without visiting a counter.
Offer type	Service
Region	Metro City
Product Manager (owner)	keep Youssef Carpentier
Executive Sponsor	Julie Zahiri
Strategic impact	select 2
Investment level	select 1

Field	What to type or select
Technical novelty	select 2
Regulatory and safety exposure	select 2
Market scope	select 1
Cross-functional reach	select 2
Product-service integration	select 1
Step 3. Confirm the track	Total score 11 of 35: select Fast Track • recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project HAR-001 created. E2E-01 has started." and the project page opens.

Step 2. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Customer request One-sentence idea statement: Let residents renew parking permits online.	Capture Strategic Idea done for HAR-001. Summary filed as HAR-001-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Residents with an on-street parking permit Addressable market (MUSD): 2 Strategic-fit score (0-100): 78	Assess Market Opportunity done for HAR-001. Summary filed as HAR-001-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 120 Expected net cash flow per year (kUSD): 60 Evaluation horizon (years): 5 Discount rate (%): 8	Build Preliminary Business Case done for HAR-001. Summary filed as HAR-001-01-03.
4	UFT-01-04 Assess Risks & Compliance	Main risk identified: Payment data exposure Likelihood (1-5): 2 Impact (1-5): 3 Regulated product?: No	Assess Risks & Compliance done for HAR-001. Summary filed as HAR-001-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Online forms, payment gateway, permit database link	Describe High-Level Capability done for HAR-001. Summary filed as HAR-001-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Core Roadmap slot (e.g. 2027-Q2): 2027-Q1	Establish Product Portfolio Strategy done for HAR-001. Summary filed as HAR-001-01-06.

What you will see NPV 120 kUSD, ROI 150%, payback 2 years. Risk added to the risk register.

Evaluation example: Julie Zahiri is the evaluator of **Capture Strategic Idea**. Sign in as **exec@harbourview.example**, open **My tasks**, filter **To evaluate**, open the task, choose Verdict **Effective**, type Notes **Clear and complete.** and select **Record evaluation**. Then sign in again as **pm1@harbourview.example**.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 6 items; 5 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	HAR-001-T-1-01

Item	Checklist item (mandatory)	Evidence reference to type
2	Market opportunity assessment	HAR-001-T-1-02
3	Preliminary business case (NPV, ROI, risk)	HAR-001-T-1-03
4	Initial risk and compliance register	HAR-001-T-1-04
5	Portfolio fit	HAR-001-T-1-05

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@harbourview.example** (Julie Zahiri, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T-1 line of **HAR-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@harbourview.example** to continue.

Step 3. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for HAR-001. Summary filed as HAR-001-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 140 Expected net cash flow per year (kUSD): 65 Evaluation horizon (years): 5 Discount rate (%): 8	Develop Detailed Business Case done for HAR-001. Summary filed as HAR-001-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for HAR-001. Summary filed as HAR-001-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	—	Map Preliminary Customer Journey done for HAR-001. Summary filed as HAR-001-02-04.
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 35	Conduct Detailed Profitability Analysis done for HAR-001. Summary filed as HAR-001-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: GDPR, PCI DSS for card payments	Validate Regulatory Aspects done for HAR-001. Summary filed as HAR-001-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: High	Assess Technical Feasibility done for HAR-001. Summary filed as HAR-001-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for HAR-001. Summary filed as HAR-001-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for HAR-001. Summary filed as HAR-001-02-09.

What you will see NPV 120 kUSD, ROI 132.1%, payback 2.2 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 6 items; 6 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	HAR-001-T0-01
2	Detailed business case and profitability analysis	HAR-001-T0-02

Item	Checklist item (mandatory)	Evidence reference to type
3	High-level functional specifications	HAR-001-T0-03
4	Preliminary customer journey	HAR-001-T0-04
5	Regulatory validation	HAR-001-T0-05
6	Technical feasibility	HAR-001-T0-06

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@harbourview.example** (Julie Zahiri, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T0 line of **HAR-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@harbourview.example** to continue.

Step 4. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for HAR-001. Summary filed as HAR-001-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-11-22 (any future date)	Develop Detailed Launch Plan done for HAR-001. Summary filed as HAR-001-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for HAR-001. Summary filed as HAR-001-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for HAR-001. Summary filed as HAR-001-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for HAR-001. Summary filed as HAR-001-05-05.
6	UFT-05-06 Train Teams	People trained: 14	Train Teams done for HAR-001. Summary filed as HAR-001-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for HAR-001. Summary filed as HAR-001-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for HAR-001. Summary filed as HAR-001-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 6 items; 5 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	HAR-001-T3-01
2	Marketing and sales materials	HAR-001-T3-02
3	Trained teams	HAR-001-T3-03
4	Validated customer journey	HAR-001-T3-04
5	Final regulatory validation	HAR-001-T3-05

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@harbourview.example** (Julie Zahiri, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T3 line of **HAR-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: no further process starts; see the result of the run below. Sign in again as **pm1@harbourview.example** to continue.

Result of the run

The project status is **Launched**. The Fast Track ends at T3; performance and retirement follow the parent product (Rule R3).

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Portfolio > Portfolio overview**: the project row shows the status of each E2E process.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

7. Run 2: Fast Track in Transportation, with a skipped task and a Recycle decision

A new group and a new organization inside it (Group: Yes). A Fast Track feature for bus passengers: one task is skipped under Rule R2, and the board sends the T0 gate back once (Recycle) before approving it.

Item	Value
Tenancy	Group: Yes (Meridian Mobility Holding) > Northline Regional Transit > project NOR-001
Organization	Northline Regional Transit (Transportation), e-mail domain northline.example
Product Manager	Leila Benali · pm1@northline.example
Executive Sponsor	Daniel Carpentier · exec@northline.example
Project	NOR-001 Real-time Bus Crowding Indicator
Track	Fast (total score 13 of 35)
End state	Launched · NPV 140 kUSD, ROI 106.5%

Step 0. Create the tenancy: Group (Yes / No), then the organization

Sign in as **admin@cortexplm.example** (password **Admin#2026**), the platform administrator.

Open **Portfolio > Groups, organizations & projects**.

1. Select **Add group**. Type Name **Meridian Mobility Holding** and Description **Regional transport operators owned by one holding.**, then **Save**. The group appears in the tree as **Group: Yes**.

2. Select **Add organization** and fill in the window:

Field	What to type or select
Belongs to a group?	select Yes
Group	select Meridian Mobility Holding
Name	Northline Regional Transit
Sector	select Transportation
Country	Canada
Default language	keep English
Initial subscription	select BND-05 Innovation Bundle
Create the starting team	keep the box ticked
E-mail domain	northline.example
Initial password	Start#2026

Select **Save**. The message reads "Organization created with 24 accounts." The organization receives its OBS departments, the governance catalog, the AI use case library and the checklist templates, and one account per role, for example **pm1@northline.example** (Product Manager) and **exec@northline.example** (Executive Sponsor). Sign out.

Step 1. Create the project

Sign in as **pm1@northline.example** (password **Start#2026**), the Product Manager.

Open **Portfolio > Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Step 0. Organization	shows Northline Regional Transit ; Belongs to a group? Yes
Project name	Real-time Bus Crowding Indicator
Description	Shows how full the next bus is in the passenger app, using existing automatic passenger counters.

Field	What to type or select
Offer type	Product-Service
Region	Orvane network
Product Manager (owner)	keep Leila Benali
Executive Sponsor	Daniel Carpentier
Strategic impact	select 2
Investment level	select 2
Technical novelty	select 2
Regulatory and safety exposure	select 1
Market scope	select 2
Cross-functional reach	select 2
Product-service integration	select 2
Step 3. Confirm the track	Total score 13 of 35: select Fast Track · recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project NOR-001 created. E2E-01 has started." and the project page opens.

Step 2. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Market trend One-sentence idea statement: Show bus occupancy in real time in the passenger app.	Capture Strategic Idea done for NOR-001. Summary filed as NOR-001-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Daily commuters on the ten busiest lines Addressable market (MUSD): 5 Strategic-fit score (0-100): 71	Assess Market Opportunity done for NOR-001. Summary filed as NOR-001-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 210 Expected net cash flow per year (kUSD): 90 Evaluation horizon (years): 5 Discount rate (%): 9	Build Preliminary Business Case done for NOR-001. Summary filed as NOR-001-01-03.
4	UFT-01-04 Assess Risks & Compliance	Main risk identified: Counter data latency above 2 minutes Likelihood (1-5): 3 Impact (1-5): 2 Regulated product?: No	Assess Risks & Compliance done for NOR-001. Summary filed as NOR-001-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Passenger counter feed, mobile app update, data pipeline	Describe High-Level Capability done for NOR-001. Summary filed as NOR-001-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Adjacent Roadmap slot (e.g. 2027-Q2): 2027-Q2	Establish Product Portfolio Strategy done for NOR-001. Summary filed as NOR-001-01-06.

What you will see NPV 140 kUSD, ROI 114.3%, payback 2.3 years. Risk added to the risk register.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 6 items; 5 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	NOR-001-T-1-01

Item	Checklist item (mandatory)	Evidence reference to type
2	Market opportunity assessment	NOR-001-T-1-02
3	Preliminary business case (NPV, ROI, risk)	NOR-001-T-1-03
4	Initial risk and compliance register	NOR-001-T-1-04
5	Portfolio fit	NOR-001-T-1-05

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@northline.example** (Daniel Carpentier, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T-1 line of **NOR-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@northline.example** to continue.

Step 3. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for NOR-001. Summary filed as NOR-001-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 230 Expected net cash flow per year (kUSD): 95 Evaluation horizon (years): 5 Discount rate (%): 9	Develop Detailed Business Case done for NOR-001. Summary filed as NOR-001-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for NOR-001. Summary filed as NOR-001-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	Select Skip (Rule R2) . Reason: The dependent macro process is not activated in the Fast Track.	Select Skip task .
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 28	Conduct Detailed Profitability Analysis done for NOR-001. Summary filed as NOR-001-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: GDPR (location data), accessibility of the app	Validate Regulatory Aspects done for NOR-001. Summary filed as NOR-001-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: Medium	Assess Technical Feasibility done for NOR-001. Summary filed as NOR-001-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for NOR-001. Summary filed as NOR-001-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for NOR-001. Summary filed as NOR-001-02-09.

What you will see NPV 140 kUSD, ROI 106.5%, payback 2.4 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 6 items; 6 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	NOR-001-T0-01

Item	Checklist item (mandatory)	Evidence reference to type
2	Detailed business case and profitability analysis	NOR-001-T0-02
3	High-level functional specifications	NOR-001-T0-03
4	Preliminary customer journey	NOR-001-T0-04
5	Regulatory validation	NOR-001-T0-05
6	Technical feasibility	NOR-001-T0-06

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@northline.example** (Daniel Carpentier, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T0 line of **NOR-001**.
3. Under **Decision**, select **Recycle**. Under **Tasks to rework**, tick **UFT-02-02 Develop Detailed Business Case**.
4. In **Rationale**, type **The business case needs a sensitivity analysis before we commit.**, then select **Record decision**.
5. Sign in again as **pm1@northline.example**. The reworked task is back to **To do**, and so are the checklist and gate tasks. Complete the task again with the same values, complete the checklist task again (items already complete stay complete), then submit the gate again.

Step 4. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 230 Expected net cash flow per year (kUSD): 95 Evaluation horizon (years): 5 Discount rate (%): 9	Develop Detailed Business Case done for NOR-001. Summary filed as NOR-001-02-02.

What you will see NPV 140 kUSD, ROI 106.5%, payback 2.4 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 6 items; 6 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	NOR-001-T0-01
2	Detailed business case and profitability analysis	NOR-001-T0-02
3	High-level functional specifications	NOR-001-T0-03
4	Preliminary customer journey	NOR-001-T0-04
5	Regulatory validation	NOR-001-T0-05
6	Technical feasibility	NOR-001-T0-06

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@northline.example** (Daniel Carpentier, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T0 line of **NOR-001**.

3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@northline.example** to continue.

Step 5. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for NOR-001. Summary filed as NOR-001-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-12-07 (any future date)	Develop Detailed Launch Plan done for NOR-001. Summary filed as NOR-001-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for NOR-001. Summary filed as NOR-001-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for NOR-001. Summary filed as NOR-001-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for NOR-001. Summary filed as NOR-001-05-05.
6	UFT-05-06 Train Teams	People trained: 40	Train Teams done for NOR-001. Summary filed as NOR-001-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for NOR-001. Summary filed as NOR-001-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for NOR-001. Summary filed as NOR-001-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 6 items; 5 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	NOR-001-T3-01
2	Marketing and sales materials	NOR-001-T3-02
3	Trained teams	NOR-001-T3-03
4	Validated customer journey	NOR-001-T3-04
5	Final regulatory validation	NOR-001-T3-05

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@northline.example** (Daniel Carpentier, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T3 line of **NOR-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: no further process starts; see the result of the run below. Sign in again as **pm1@northline.example** to continue.

Result of the run

The project status is **Launched**. The Fast Track ends at T3; performance and retirement follow the parent product (Rule R3).

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Portfolio > Portfolio overview**: the project row shows the status of each E2E process.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

8. Run 3: Light Track in Agro-Business (Dairy), from idea to relaunch

A new organization joins an existing group (Group: Yes). A new dairy product runs the whole Light Track: six gate decisions, the E2E-09 market campaign, the performance review (E2E-07) with Rule R1, and a relaunch through E2E-08 Branch A.

Item	Value
Tenancy	Group: Yes (Crescent Agro-Energy Group) > Oasis Fresh Dairies > project OAS-001
Organization	Oasis Fresh Dairies (Agro-Business - Dairy Products), e-mail domain oasisdairy.example
Product Manager	Rachid Dubois · pm1@oasisdairy.example
Executive Sponsor	Laura Benali · exec@oasisdairy.example
Project	OAS-001 Lactose-free Greek Yogurt 500 g
Track	Light (total score 19 of 35)
End state	Active · NPV 389 kUSD, ROI 114.3%

Step 0. Create the tenancy: Group (Yes / No), then the organization

Sign in as **admin@cortexplm.example** (password **Admin#2026**), the platform administrator.

Open **Portfolio > Groups, organizations & projects**.

1. The group **Crescent Agro-Energy Group** already exists (Group: Yes). You will attach the new organization to it.
2. Select **Add organization** and fill in the window:

Field	What to type or select
Belongs to a group?	select Yes
Group	select Crescent Agro-Energy Group
Name	Oasis Fresh Dairies
Sector	select Agro-Business - Dairy Products
Country	Morocco
Default language	keep English
Initial subscription	select BND-05 Innovation Bundle
Create the starting team	keep the box ticked
E-mail domain	oasisdairy.example
Initial password	Start#2026

Select **Save**. The message reads "Organization created with 24 accounts." The organization receives its OBS departments, the governance catalog, the AI use case library and the checklist templates, and one account per role, for example **pm1@oasisdairy.example** (Product Manager) and **exec@oasisdairy.example** (Executive Sponsor). Sign out.

Step 1. Prepare the Light Track observation period

1. Sign in as **process@oasisdairy.example** (password **Start#2026**), Chloe Amrani, Process Owner / Track Administrator.
2. Open **Process design > Track configuration**.
3. In the card **Light Track observation period (Rule R1)**, type **0** in **Observation period (days)** and select **Save**.
4. Sign out. With 0 days, the performance review (E2E-07) starts right after the T3 Go-Live decision, so you can finish the whole run today. The default is 182 days.

Step 2. Create the project

Sign in as **pm1@oasisdairy.example** (password **Start#2026**), the Product Manager.

Open **Portfolio > Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Step 0. Organization	shows Oasis Fresh Dairies ; Belongs to a group? Yes
Project name	Lactose-free Greek Yogurt 500 g
Description	A lactose-free strained yogurt for the national retail chains, made on the existing cup line.
Offer type	Product
Region	National retail
Product Manager (owner)	keep Rachid Dubois
Executive Sponsor	Laura Benali
Strategic impact	select 3
Investment level	select 3
Technical novelty	select 2
Regulatory and safety exposure	select 3
Market scope	select 3
Cross-functional reach	select 3
Product-service integration	select 2
Step 3. Confirm the track	Total score 19 of 35: select Light Track · recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project OAS-001 created. E2E-01 has started." and the project page opens.

Step 3. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Market trend One-sentence idea statement: Launch a lactose-free Greek yogurt in 500 g cups.	Capture Strategic Idea done for OAS-001. Summary filed as OAS-001-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Lactose-intolerant households Addressable market (MUSD): 18 Strategic-fit score (0-100): 74	Assess Market Opportunity done for OAS-001. Summary filed as OAS-001-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 650 Expected net cash flow per year (kUSD): 240 Evaluation horizon (years): 6 Discount rate (%): 10	Build Preliminary Business Case done for OAS-001. Summary filed as OAS-001-01-03.
4	UFT-01-04 Assess Risks & Compliance	Main risk identified: Lactase enzyme supply shortage Likelihood (1-5): 3 Impact (1-5): 3 Regulated product?: Yes	Assess Risks & Compliance done for OAS-001. Summary filed as OAS-001-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Lactase treatment, straining, cup filling	Describe High-Level Capability done for OAS-001. Summary filed as OAS-001-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Adjacent Roadmap slot (e.g. 2027-Q2): 2027-Q3	Establish Product Portfolio Strategy done for OAS-001. Summary filed as OAS-001-01-06.

What you will see NPV 395 kUSD, ROI 121.5%, payback 2.7 years. Risk added to the risk register.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	OAS-001-T-1-01
2	Market opportunity assessment	OAS-001-T-1-02
3	Preliminary business case (NPV, ROI, risk)	OAS-001-T-1-03
4	Initial risk and compliance register	OAS-001-T-1-04
5	Portfolio fit	OAS-001-T-1-05
7	Evidence: Elicit and capture requirements from all sources	OAS-001-T-1-07
10	Evidence: Monitor regulatory intelligence	OAS-001-T-1-10
13	Evidence: Define and manage lifecycle workflows	OAS-001-T-1-13

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@oasisdairy.example** (Laura Benali, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T-1 line of **OAS-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@oasisdairy.example** to continue.

Step 4. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for OAS-001. Summary filed as OAS-001-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 700 Expected net cash flow per year (kUSD): 250 Evaluation horizon (years): 6 Discount rate (%): 10	Develop Detailed Business Case done for OAS-001. Summary filed as OAS-001-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for OAS-001. Summary filed as OAS-001-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	—	Map Preliminary Customer Journey done for OAS-001. Summary filed as OAS-001-02-04.
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 32	Conduct Detailed Profitability Analysis done for OAS-001. Summary filed as OAS-001-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: Food labelling rules, lactose-free claim threshold	Validate Regulatory Aspects done for OAS-001. Summary filed as OAS-001-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: High	Assess Technical Feasibility done for OAS-001. Summary filed as OAS-001-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for OAS-001. Summary filed as OAS-001-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for OAS-001. Summary filed as OAS-001-02-09.

What you will see NPV 389 kUSD, ROI 114.3%, payback 2.8 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 15 items; 9 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	OAS-001-T0-01
2	Detailed business case and profitability analysis	OAS-001-T0-02
3	High-level functional specifications	OAS-001-T0-03
4	Preliminary customer journey	OAS-001-T0-04
5	Regulatory validation	OAS-001-T0-05
6	Technical feasibility	OAS-001-T0-06
7	Development plan	OAS-001-T0-07
10	Evidence: Perform should-cost and target costing	OAS-001-T0-10
13	Evidence: Monitor regulatory intelligence	OAS-001-T0-13

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@oasisdairy.example** (Laura Benali, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T0 line of **OAS-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-03** starts automatically. Sign in again as **pm1@oasisdairy.example** to continue.

Step 5. E2E-03 Business Proposal-to-Design

Open the project, tab **Lifecycle & tasks**, card **E2E-03**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-03-01 Develop Detailed Specifications	—	Develop Detailed Specifications done for OAS-001. Summary filed as OAS-001-03-01.
2	UFT-03-02 Validate Marketing Specifications	—	Validate Marketing Specifications done for OAS-001. Summary filed as OAS-001-03-02.
3	UFT-03-03 Validate Customer Journey	—	Validate Customer Journey done for OAS-001. Summary filed as OAS-001-03-03.
4	UFT-03-04 Model Detailed Processes	—	Model Detailed Processes done for OAS-001. Summary filed as OAS-001-03-04.
5	UFT-03-05 Develop Detailed Design	—	Develop Detailed Design done for OAS-001. Summary filed as OAS-001-03-05.
6	UFT-03-06 Build Functional Prototype	—	Build Functional Prototype done for OAS-001. Summary filed as OAS-001-03-06.
7	UFT-03-07 Validate Architectures	—	Validate Architectures done for OAS-001. Summary filed as OAS-001-03-07.
8	UFT-03-08 Develop Development Plan	—	Develop Development Plan done for OAS-001. Summary filed as OAS-001-03-08.

Open the task **Complete Gate Checklist (T1)**. The gate T1 checklist has 15 items; 9 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select

Mark complete. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed specifications	OAS-001-T1-01
2	Validated marketing specifications and customer journey	OAS-001-T1-02
3	Process models	OAS-001-T1-03
4	Detailed design	OAS-001-T1-04
5	Functional prototype	OAS-001-T1-05
6	Architecture validation	OAS-001-T1-06
7	Detailed development plan	OAS-001-T1-07
10	Evidence: Define personas and segments	OAS-001-T1-10
13	Evidence: Train generative AI models	OAS-001-T1-13

Submit the gate: on the project page, card **Gate T1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@oasisdairy.example** (Laura Benali, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T1 line of **OAS-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Design validated; start development.**, then select **Record decision**.
5. Result: **E2E-04** starts automatically. Sign in again as **pm1@oasisdairy.example** to continue.

Step 6. E2E-04 Design-to-Development

Open the project, tab **Lifecycle & tasks**, card **E2E-04**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-04-01 Support Operational Introduction	—	Support Operational Introduction done for OAS-001. Summary filed as OAS-001-04-01.
2	UFT-04-02 Conduct Operational Readiness Testing	—	Conduct Operational Readiness Testing done for OAS-001. Summary filed as OAS-001-04-02.
3	UFT-04-03 Manage Product Configuration	—	Manage Product Configuration done for OAS-001. Summary filed as OAS-001-04-03.
4	UFT-04-04 Develop Product Offering Procedures	—	Develop Product Offering Procedures done for OAS-001. Summary filed as OAS-001-04-04.
5	UFT-04-05 Manage Acceptance Testing	Acceptance tests passed (%): 97	Manage Acceptance Testing done for OAS-001. Summary filed as OAS-001-04-05.
6	UFT-04-06 Develop Preliminary Launch Plan	—	Develop Preliminary Launch Plan done for OAS-001. Summary filed as OAS-001-04-06.
7	UFT-04-07 Complete Functionalities	—	Complete Functionalities done for OAS-001. Summary filed as OAS-001-04-07.

Open the task **Complete Gate Checklist (T2)**. The gate T2 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Completed functionalities	OAS-001-T2-01
2	Operational readiness and acceptance test results	OAS-001-T2-02
3	Configuration baseline	OAS-001-T2-03
4	Offering procedures	OAS-001-T2-04

Item	Checklist item (mandatory)	Evidence reference to type
5	Preliminary launch plan	OAS-001-T2-05
7	Evidence: Define manufacturing process plans and routings	OAS-001-T2-07
10	Evidence: Initiate and submit change requests (ECR)	OAS-001-T2-10
13	Evidence: Develop go-to-market plans	OAS-001-T2-13

Submit the gate: on the project page, card **Gate T2**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@oasisdairy.example** (Laura Benali, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T2 line of **OAS-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Product complete and tested; prepare launch.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@oasisdairy.example** to continue.

Step 7. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for OAS-001. Summary filed as OAS-001-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-12-22 (any future date)	Develop Detailed Launch Plan done for OAS-001. Summary filed as OAS-001-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for OAS-001. Summary filed as OAS-001-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for OAS-001. Summary filed as OAS-001-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for OAS-001. Summary filed as OAS-001-05-05.
6	UFT-05-06 Train Teams	People trained: 60	Train Teams done for OAS-001. Summary filed as OAS-001-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for OAS-001. Summary filed as OAS-001-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for OAS-001. Summary filed as OAS-001-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	OAS-001-T3-01
2	Marketing and sales materials	OAS-001-T3-02
3	Trained teams	OAS-001-T3-03
4	Validated customer journey	OAS-001-T3-04
5	Final regulatory validation	OAS-001-T3-05
7	Evidence: Define personas and segments	OAS-001-T3-07
10	Evidence: Define and manage quality plans (APQP, PPAP)	OAS-001-T3-10
13	Evidence: Onboard and certify partners	OAS-001-T3-13

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@oasisdairy.example** (Laura Benali, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T3 line of **OAS-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-07, E2E-09** start automatically. Sign in again as **pm1@oasisdairy.example** to continue.

Step 8. E2E-07 After-Sales-to-Performance

Open the project, tab **Lifecycle & tasks**, card **E2E-07**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-06-04 Track Customer Satisfaction (light form, Rule R1)	CSAT (1-5): 4.3 Net Promoter Score (-100 to 100): 38	Track Customer Satisfaction done for OAS-001. Summary filed as OAS-001-06-04.
2	UFT-06-05 Track Product Performance (light form, Rule R1)	—	Track Product Performance done for OAS-001. Summary filed as OAS-001-06-05.
3	UFT-07-01 Evaluate Overall Performance	—	Evaluate Overall Performance done for OAS-001. Summary filed as OAS-001-07-01.
4	UFT-07-02 Analyze Profitability	Revenue to date (kUSD): 1450 Cost of goods sold (kUSD): 960	Analyze Profitability done for OAS-001. Summary filed as OAS-001-07-02.
5	UFT-07-03 Gather Customer Experience Feedback	CSAT (1-5): 4.2 Net Promoter Score (-100 to 100): 35	Gather Customer Experience Feedback done for OAS-001. Summary filed as OAS-001-07-03.
6	UFT-07-04 Develop Improvement Recommendations	Recommendation to the T5 gate: Relaunch	Develop Improvement Recommendations done for OAS-001. Summary filed as OAS-001-07-04.

Open the task **Complete Gate Checklist (T5)**. The gate T5 checklist has 15 items; 7 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Overall performance evaluation	OAS-001-T5-01
2	Profitability analysis	OAS-001-T5-02
3	Customer experience feedback	OAS-001-T5-03
4	Improvement recommendations	OAS-001-T5-04
7	Evidence: Define personas and segments	OAS-001-T5-07
10	Evidence: Provide generative design	OAS-001-T5-10
13	Evidence: Manage lifecycle costing	OAS-001-T5-13

Step 9. E2E-09 Market Strategy-to-Campaign

Open the project, tab **Lifecycle & tasks**, card **E2E-09**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-09-01 Gather Customer Experience Data	—	Gather Customer Experience Data done for OAS-001. Summary filed as OAS-001-09-01.
2	UFT-09-02 Gather Product Delivery Feedback	—	Gather Product Delivery Feedback done for OAS-001. Summary filed as OAS-001-09-02.
3	UFT-09-03 Establish Market Segments	—	Establish Market Segments done for OAS-001. Summary filed as OAS-001-09-03.
4	UFT-09-04 Link Segments & Products	—	Link Segments & Products done for OAS-001. Summary filed as OAS-001-09-04.
5	UFT-09-05 Establish Market Strategy	—	Establish Market Strategy done for OAS-001. Summary filed as OAS-001-09-05.
6	UFT-09-06 Plan & Develop Campaign	—	Plan & Develop Campaign done for OAS-001. Summary filed as OAS-001-09-06.
7	UFT-09-07 Launch & Monitor Campaign	—	Launch & Monitor Campaign done for OAS-001. Summary filed as OAS-001-09-07.
8	UFT-09-08 Complete Campaign & Report	Qualified leads generated: 420 Conversion rate (%): 12	Complete Campaign & Report done for OAS-001. Summary filed as OAS-001-09-08.

Submit the gate: on the project page, card **Gate T5**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@oasisdairy.example** (Laura Benali, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T5 line of **OAS-001**.
3. Under **Decision**, keep **Go**.
4. Under **Next path (E2E-08)**, select **Relaunch (Branch A)**.
5. In **Rationale**, type **Performance is below target but fixable; relaunch.**, then select **Record decision**.
6. Result: **E2E-08** starts automatically. Sign in again as **pm1@oasisdairy.example** to continue.

Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch A

Open the project, tab **Lifecycle & tasks**, card **E2E-08**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-08-01 Update Product Specifications	—	Update Product Specifications done for OAS-001. Summary filed as OAS-001-08-01.
2	UFT-08-02 Support Operational Re-introduction	—	Support Operational Re-introduction done for OAS-001. Summary filed as OAS-001-08-02.
3	UFT-08-03 Manage Product Improvements	—	Manage Product Improvements done for OAS-001. Summary filed as OAS-001-08-03.
4	UFT-08-04 Approve for Relaunch	Relaunch re-entry point: E2E-05	Approve for Relaunch done for OAS-001. Summary filed as OAS-001-08-04.

Step 11. E2E-05 Development-to-Launch (run 2)

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for OAS-001. Summary filed as OAS-001-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-12-22 (any future date)	Develop Detailed Launch Plan done for OAS-001. Summary filed as OAS-001-05-02.

#	Task	Fields to fill	Result / output to type
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for OAS-001. Summary filed as OAS-001-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for OAS-001. Summary filed as OAS-001-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for OAS-001. Summary filed as OAS-001-05-05.
6	UFT-05-06 Train Teams	People trained: 60	Train Teams done for OAS-001. Summary filed as OAS-001-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for OAS-001. Summary filed as OAS-001-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for OAS-001. Summary filed as OAS-001-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	OAS-001-T3-01
2	Marketing and sales materials	OAS-001-T3-02
3	Trained teams	OAS-001-T3-03
4	Validated customer journey	OAS-001-T3-04
5	Final regulatory validation	OAS-001-T3-05
7	Evidence: Define personas and segments	OAS-001-T3-07
10	Evidence: Define and manage quality plans (APQP, PPAP)	OAS-001-T3-10
13	Evidence: Onboard and certify partners	OAS-001-T3-13

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@oasisdairy.example** (Laura Benali, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T3 line of **OAS-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-07, E2E-09** start automatically. Sign in again as **pm1@oasisdairy.example** to continue.

Result of the run

The project stays **Active**, now in E2E-07 after gate T3. Active · open runs: E2E-07, E2E-09

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Portfolio > Portfolio overview**: the project row shows the status of each E2E process.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

9. Run 4: Full Track in Healthcare, from idea to retirement

A new independent organization (Group: No). A safety-critical medical device runs the complete Full Track: all nine E2E processes and all eight gates, ending with retirement through E2E-08 Branch B.

Item	Value
Tenancy	Group: No > Clearwater Medical Devices > project CLE-001
Organization	Clearwater Medical Devices (Healthcare), e-mail domain clearwater.example
Product Manager	Salma Alaoui · pm1@clearwater.example
Executive Sponsor	Adam Dubois · exec@clearwater.example
Project	CLE-001 Remote Cardiac Monitoring Patch
Track	Full (total score 29 of 35)
End state	Retired · NPV 1527 kUSD, ROI 120.8%

Step 0. Create the tenancy: Group (Yes / No), then the organization

Sign in as **admin@cortexplm.example** (password **Admin#2026**), the platform administrator.

Open **Portfolio > Groups, organizations & projects**.

1. This organization belongs to no group: it will appear under **Group: No · Independent organizations**.
2. Select **Add organization** and fill in the window:

Field	What to type or select
Belongs to a group?	select No (independent)
Name	Clearwater Medical Devices
Sector	select Healthcare
Country	France
Default language	keep English
Initial subscription	select BND-06 Regulated Bundle
Create the starting team	keep the box ticked
E-mail domain	clearwater.example
Initial password	Start#2026

Select **Save**. The message reads "Organization created with 24 accounts." The organization receives its OBS departments, the governance catalog, the AI use case library and the checklist templates, and one account per role, for example **pm1@clearwater.example** (Product Manager) and **exec@clearwater.example** (Executive Sponsor). Sign out.

Step 1. Create the project

Sign in as **pm1@clearwater.example** (password **Start#2026**), the Product Manager.

Open **Portfolio > Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Step 0. Organization	shows Clearwater Medical Devices ; Belongs to a group? No
Project name	Remote Cardiac Monitoring Patch
Description	A wearable ECG patch that sends arrhythmia alerts to the cardiology team.
Offer type	Product-Service
Region	Meridale hospitals
Product Manager (owner)	keep Salma Alaoui
Executive Sponsor	Adam Dubois
Strategic impact	select 5
Investment level	select 4

Field	What to type or select
Technical novelty	select 4
Regulatory and safety exposure	select 5
Market scope	select 3
Cross-functional reach	select 4
Product-service integration	select 4
Safety-critical product	tick the box
Step 3. Confirm the track	Total score 29 of 35: select Full Track • recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project CLE-001 created. E2E-01 has started." and the project page opens.

Step 2. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Internal - strategy One-sentence idea statement: Monitor cardiac patients at home with a wearable ECG patch.	Capture Strategic Idea done for CLE-001. Summary filed as CLE-001-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Post-discharge cardiac patients Addressable market (MUSD): 40 Strategic-fit score (0-100): 86	Assess Market Opportunity done for CLE-001. Summary filed as CLE-001-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 2400 Expected net cash flow per year (kUSD): 780 Evaluation horizon (years): 7 Discount rate (%): 9	Build Preliminary Business Case done for CLE-001. Summary filed as CLE-001-01-03.
4	UFT-01-04 Assess Risks & Compliance	Main risk identified: Missed arrhythmia alert Likelihood (1-5): 2 Impact (1-5): 5 Regulated product?: Yes	Assess Risks & Compliance done for CLE-001. Summary filed as CLE-001-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Biosensor design, secure telemetry, clinical dashboard	Describe High-Level Capability done for CLE-001. Summary filed as CLE-001-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Transformational Roadmap slot (e.g. 2027-Q2): 2028-Q1	Establish Product Portfolio Strategy done for CLE-001. Summary filed as CLE-001-01-06.

What you will see NPV 1526 kUSD, ROI 127.5%, payback 3.1 years. Risk added to the risk register.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	CLE-001-T-1-01
2	Market opportunity assessment	CLE-001-T-1-02
3	Preliminary business case (NPV, ROI, risk)	CLE-001-T-1-03
4	Initial risk and compliance register	CLE-001-T-1-04
5	Portfolio fit	CLE-001-T-1-05
7	Evidence: Elicit and capture requirements from all sources	CLE-001-T-1-07

Item	Checklist item (mandatory)	Evidence reference to type
9	Evidence: Perform should-cost and target costing	CLE-001-T-1-09
11	Evidence: Manage invention disclosures and patent filings	CLE-001-T-1-11
13	Evidence: Define and manage lifecycle workflows	CLE-001-T-1-13
15	Evidence: Provide generative design	CLE-001-T-1-15
17	Evidence: Structure and categorize requirements	CLE-001-T-1-17
19	Evidence: Manage lifecycle costing	CLE-001-T-1-19
21	Evidence: Manage trademark and copyright registrations	CLE-001-T-1-21
23	Evidence: Enforce GRC policies	CLE-001-T-1-23
25	Evidence: Automate data classification	CLE-001-T-1-25
27	Evidence: Analyze and validate requirements	CLE-001-T-1-27
29	Evidence: Analyze profitability	CLE-001-T-1-29

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@clearwater.example** (Adam Dubois, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T-1 line of **CLE-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@clearwater.example** to continue.

Step 3. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for CLE-001. Summary filed as CLE-001-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 2600 Expected net cash flow per year (kUSD): 820 Evaluation horizon (years): 7 Discount rate (%): 9	Develop Detailed Business Case done for CLE-001. Summary filed as CLE-001-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for CLE-001. Summary filed as CLE-001-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	—	Map Preliminary Customer Journey done for CLE-001. Summary filed as CLE-001-02-04.
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 41	Conduct Detailed Profitability Analysis done for CLE-001. Summary filed as CLE-001-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: EU MDR class IIa, IEC 60601, ISO 13485, GDPR	Validate Regulatory Aspects done for CLE-001. Summary filed as CLE-001-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: Medium	Assess Technical Feasibility done for CLE-001. Summary filed as CLE-001-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for CLE-001. Summary filed as CLE-001-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for CLE-001. Summary filed as CLE-001-02-09.

What you will see NPV 1527 kUSD, ROI 120.8%, payback 3.2 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 30 items; 18 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	CLE-001-T0-01
2	Detailed business case and profitability analysis	CLE-001-T0-02
3	High-level functional specifications	CLE-001-T0-03
4	Preliminary customer journey	CLE-001-T0-04
5	Regulatory validation	CLE-001-T0-05
6	Technical feasibility	CLE-001-T0-06
7	Development plan	CLE-001-T0-07
9	Evidence: Elicit and capture requirements from all sources	CLE-001-T0-09
11	Evidence: Manage design process (conceptual, detailed, validation)	CLE-001-T0-11
13	Evidence: Monitor regulatory intelligence	CLE-001-T0-13
15	Evidence: Define and manage lifecycle workflows	CLE-001-T0-15
17	Evidence: Manage invention disclosures and patent filings	CLE-001-T0-17
19	Evidence: Structure and categorize requirements	CLE-001-T0-19
21	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	CLE-001-T0-21
23	Evidence: Prepare and submit filings	CLE-001-T0-23
25	Evidence: Enforce GRC policies	CLE-001-T0-25
27	Evidence: Manage trademark and copyright registrations	CLE-001-T0-27
29	Evidence: Analyze and validate requirements	CLE-001-T0-29

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@clearwater.example** (Adam Dubois, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T0 line of **CLE-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-03** starts automatically. Sign in again as **pm1@clearwater.example** to continue.

Step 4. E2E-03 Business Proposal-to-Design

Open the project, tab **Lifecycle & tasks**, card **E2E-03**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-03-01 Develop Detailed Specifications	—	Develop Detailed Specifications done for CLE-001. Summary filed as CLE-001-03-01.
2	UFT-03-02 Validate Marketing Specifications	—	Validate Marketing Specifications done for CLE-001. Summary filed as CLE-001-03-02.
3	UFT-03-03 Validate Customer Journey	—	Validate Customer Journey done for CLE-001. Summary filed as CLE-001-03-03.
4	UFT-03-04 Model Detailed Processes	—	Model Detailed Processes done for CLE-001. Summary filed as CLE-001-03-04.
5	UFT-03-05 Develop Detailed Design	—	Develop Detailed Design done for CLE-001. Summary filed as CLE-001-03-05.
6	UFT-03-06 Build Functional Prototype	—	Build Functional Prototype done for CLE-001. Summary filed as CLE-001-03-06.
7	UFT-03-07 Validate Architectures	—	Validate Architectures done for CLE-001. Summary filed as CLE-001-03-07.
8	UFT-03-08 Develop Development Plan	—	Develop Development Plan done for CLE-001. Summary filed as CLE-001-03-08.

Open the task **Complete Gate Checklist (T1)**. The gate T1 checklist has 30 items; 18 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed specifications	CLE-001-T1-01
2	Validated marketing specifications and customer journey	CLE-001-T1-02
3	Process models	CLE-001-T1-03
4	Detailed design	CLE-001-T1-04
5	Functional prototype	CLE-001-T1-05
6	Architecture validation	CLE-001-T1-06
7	Detailed development plan	CLE-001-T1-07
9	Evidence: Manage design process (conceptual, detailed, validation)	CLE-001-T1-09
11	Evidence: Develop go-to-market plans	CLE-001-T1-11
13	Evidence: Train generative AI models	CLE-001-T1-13
15	Evidence: Initiate and submit change requests (ECR)	CLE-001-T1-15
17	Evidence: Define and manage lifecycle workflows	CLE-001-T1-17
19	Evidence: Monitor regulatory intelligence	CLE-001-T1-19
21	Evidence: Perform should-cost and target costing	CLE-001-T1-21
23	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	CLE-001-T1-23
25	Evidence: Prepare collateral	CLE-001-T1-25
27	Evidence: Generate design alternatives	CLE-001-T1-27
29	Evidence: Assess change impact (cost, schedule, quality, compliance)	CLE-001-T1-29

Submit the gate: on the project page, card **Gate T1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@clearwater.example** (Adam Dubois, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T1 line of **CLE-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Design validated; start development.**, then select **Record decision**.
5. Result: **E2E-04** starts automatically. Sign in again as **pm1@clearwater.example** to continue.

Step 5. E2E-04 Design-to-Development

Open the project, tab **Lifecycle & tasks**, card **E2E-04**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-04-01 Support Operational Introduction	—	Support Operational Introduction done for CLE-001. Summary filed as CLE-001-04-01.
2	UFT-04-02 Conduct Operational Readiness Testing	—	Conduct Operational Readiness Testing done for CLE-001. Summary filed as CLE-001-04-02.
3	UFT-04-03 Manage Product Configuration	—	Manage Product Configuration done for CLE-001. Summary filed as CLE-001-04-03.
4	UFT-04-04 Develop Product Offering Procedures	—	Develop Product Offering Procedures done for CLE-001. Summary filed as CLE-001-04-04.
5	UFT-04-05 Manage Acceptance Testing	Acceptance tests passed (%): 99	Manage Acceptance Testing done for CLE-001. Summary filed as CLE-001-04-05.
6	UFT-04-06 Develop Preliminary Launch Plan	—	Develop Preliminary Launch Plan done for CLE-001. Summary filed as CLE-001-04-06.
7	UFT-04-07 Complete Functionalities	—	Complete Functionalities done for CLE-001. Summary filed as CLE-001-04-07.

Open the task **Complete Gate Checklist (T2)**. The gate T2 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Completed functionalities	CLE-001-T2-01
2	Operational readiness and acceptance test results	CLE-001-T2-02
3	Configuration baseline	CLE-001-T2-03
4	Offering procedures	CLE-001-T2-04
5	Preliminary launch plan	CLE-001-T2-05
7	Evidence: Define manufacturing process plans and routings	CLE-001-T2-07
9	Evidence: Create and manage Engineering BOM (eBOM)	CLE-001-T2-09
11	Evidence: Design and model processes (BPMN)	CLE-001-T2-11
13	Evidence: Develop go-to-market plans	CLE-001-T2-13
15	Evidence: Provide generative design	CLE-001-T2-15
17	Evidence: Monitor regulatory intelligence	CLE-001-T2-17
19	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	CLE-001-T2-19
21	Evidence: Manage non-conformance reports (NCR)	CLE-001-T2-21
23	Evidence: Assess change impact (cost, schedule, quality, compliance)	CLE-001-T2-23
25	Evidence: Review and approve	CLE-001-T2-25
27	Evidence: Enforce GRC policies	CLE-001-T2-27
29	Evidence: Map journeys and touchpoints	CLE-001-T2-29

Submit the gate: on the project page, card **Gate T2**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@clearwater.example** (Adam Dubois, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T2 line of **CLE-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Product complete and tested; prepare launch.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@clearwater.example** to continue.

Step 6. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for CLE-001. Summary filed as CLE-001-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2027-01-21 (any future date)	Develop Detailed Launch Plan done for CLE-001. Summary filed as CLE-001-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for CLE-001. Summary filed as CLE-001-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for CLE-001. Summary filed as CLE-001-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for CLE-001. Summary filed as CLE-001-05-05.
6	UFT-05-06 Train Teams	People trained: 85	Train Teams done for CLE-001. Summary filed as CLE-001-05-06.
7	UFT-05-07 Validate Customer	—	Validate Customer Journey done for CLE-

#	Task	Fields to fill	Result / output to type
8	Journey UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	001. Summary filed as CLE-001-05-07. Final Regulatory Validation done for CLE-001. Summary filed as CLE-001-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	CLE-001-T3-01
2	Marketing and sales materials	CLE-001-T3-02
3	Trained teams	CLE-001-T3-03
4	Validated customer journey	CLE-001-T3-04
5	Final regulatory validation	CLE-001-T3-05
7	Evidence: Define personas and segments	CLE-001-T3-07
9	Evidence: Monitor regulatory intelligence	CLE-001-T3-09
11	Evidence: Define and manage lifecycle workflows	CLE-001-T3-11
13	Evidence: Onboard and certify partners	CLE-001-T3-13
15	Evidence: Manage invention disclosures and patent filings	CLE-001-T3-15
17	Evidence: Develop and manage mobile apps	CLE-001-T3-17
19	Evidence: Map journeys and touchpoints	CLE-001-T3-19
21	Evidence: Prepare and submit filings	CLE-001-T3-21
23	Evidence: Enforce GRC policies	CLE-001-T3-23
25	Evidence: Manage partner agreements and contracts	CLE-001-T3-25
27	Evidence: Manage trademark and copyright registrations	CLE-001-T3-27
29	Evidence: Enable offline access and synchronization	CLE-001-T3-29

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@clearwater.example** (Adam Dubois, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T3 line of **CLE-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-06, E2E-09** start automatically. Sign in again as **pm1@clearwater.example** to continue.

Step 7. E2E-06 Launch-to-After-Sales

Open the project, tab **Lifecycle & tasks**, card **E2E-06**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-06-01 Identify Product Issues	Open product issues: 3	Identify Product Issues done for CLE-001. Summary filed as CLE-001-06-01.
2	UFT-06-02 Assess Product Performance	—	Assess Product Performance done for CLE-001. Summary filed as CLE-001-06-02.
3	UFT-06-03 Analyze Campaign Results	—	Analyze Campaign Results done for CLE-001. Summary filed as CLE-001-06-03.
4	UFT-06-04 Track Customer Satisfaction	CSAT (1-5): 4.4 Net Promoter Score (-100 to 100): 41	Track Customer Satisfaction done for CLE-001. Summary filed as CLE-001-06-04.
5	UFT-06-05 Track Product Performance	Field MTBF (hours): 5200	Track Product Performance done for CLE-001. Summary filed as CLE-001-06-05.

Open the task **Complete Gate Checklist (T4)**. The gate T4 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Issue log	CLE-001-T4-01
2	Performance assessment	CLE-001-T4-02
3	Campaign results	CLE-001-T4-03
4	CSAT and NPS	CLE-001-T4-04
5	Field performance data	CLE-001-T4-05
7	Evidence: Log and categorize incidents and requests	CLE-001-T4-07
9	Evidence: Collect field failure data	CLE-001-T4-09
11	Evidence: Define personas and segments	CLE-001-T4-11
13	Evidence: Manage service parts and inventory	CLE-001-T4-13
15	Evidence: Perform should-cost and target costing	CLE-001-T4-15
17	Evidence: Prioritize and escalate	CLE-001-T4-17
19	Evidence: Analyze failure modes	CLE-001-T4-19
21	Evidence: Map journeys and touchpoints	CLE-001-T4-21
23	Evidence: Create and manage maintenance plans (preventive, predictive)	CLE-001-T4-23
25	Evidence: Manage lifecycle costing	CLE-001-T4-25
27	Evidence: Diagnose and resolve	CLE-001-T4-27
29	Evidence: Model reliability (Weibull, MTBF)	CLE-001-T4-29

Step 8. E2E-09 Market Strategy-to-Campaign

Open the project, tab **Lifecycle & tasks**, card **E2E-09**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-09-01 Gather Customer Experience Data	—	Gather Customer Experience Data done for CLE-001. Summary filed as CLE-001-09-01.
2	UFT-09-02 Gather Product Delivery Feedback	—	Gather Product Delivery Feedback done for CLE-001. Summary filed as CLE-001-09-02.
3	UFT-09-03 Establish Market Segments	—	Establish Market Segments done for CLE-001. Summary filed as CLE-001-09-03.
4	UFT-09-04 Link Segments & Products	—	Link Segments & Products done for CLE-001. Summary filed as CLE-001-09-04.
5	UFT-09-05 Establish Market Strategy	—	Establish Market Strategy done for CLE-001. Summary filed as CLE-001-09-05.
6	UFT-09-06 Plan & Develop Campaign	—	Plan & Develop Campaign done for CLE-001. Summary filed as CLE-001-09-06.
7	UFT-09-07 Launch & Monitor Campaign	—	Launch & Monitor Campaign done for CLE-001. Summary filed as CLE-001-09-07.
8	UFT-09-08 Complete Campaign & Report	Qualified leads generated: 260 Conversion rate (%): 18	Complete Campaign & Report done for CLE-001. Summary filed as CLE-001-09-08.

Submit the gate: on the project page, card **Gate T4**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@clearwater.example** (Adam Dubois, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T4 line of **CLE-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Post-launch performance is stable; move to steady-state review.**, then select **Record decision**.

5. Result: **E2E-07** starts automatically. Sign in again as **pm1@clearwater.example** to continue.

Step 9. E2E-07 After-Sales-to-Performance

Open the project, tab **Lifecycle & tasks**, card **E2E-07**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-07-01 Evaluate Overall Performance	—	Evaluate Overall Performance done for CLE-001. Summary filed as CLE-001-07-01.
2	UFT-07-02 Analyze Profitability	Revenue to date (kUSD): 3100 Cost of goods sold (kUSD): 1850	Analyze Profitability done for CLE-001. Summary filed as CLE-001-07-02.
3	UFT-07-03 Gather Customer Experience Feedback	CSAT (1-5): 3.6 Net Promoter Score (-100 to 100): 12	Gather Customer Experience Feedback done for CLE-001. Summary filed as CLE-001-07-03.
4	UFT-07-04 Develop Improvement Recommendations	Recommendation to the T5 gate: Retire	Develop Improvement Recommendations done for CLE-001. Summary filed as CLE-001-07-04.

Open the task **Complete Gate Checklist (T5)**. The gate T5 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Overall performance evaluation	CLE-001-T5-01
2	Profitability analysis	CLE-001-T5-02
3	Customer experience feedback	CLE-001-T5-03
4	Improvement recommendations	CLE-001-T5-04
5	Evidence: Define and manage lifecycle workflows	CLE-001-T5-05
7	Evidence: Define personas and segments	CLE-001-T5-07
9	Evidence: Define strategic product themes, goals, and investment horizons	CLE-001-T5-09
11	Evidence: Collect field failure data	CLE-001-T5-11
13	Evidence: Manage lifecycle costing	CLE-001-T5-13
15	Evidence: Collect and analyze feedback	CLE-001-T5-15
17	Evidence: Automate data classification	CLE-001-T5-17
19	Evidence: Define and track KPIs	CLE-001-T5-19
21	Evidence: Identify pain points and moments of truth	CLE-001-T5-21
23	Evidence: Evaluate and score product ideas against strategic fit	CLE-001-T5-23
25	Evidence: Model reliability (Weibull, MTBF)	CLE-001-T5-25
27	Evidence: Optimize cost structures	CLE-001-T5-27
29	Evidence: Conduct quality audits	CLE-001-T5-29

Submit the gate: on the project page, card **Gate T5**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@clearwater.example** (Adam Dubois, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T5 line of **CLE-001**.
3. Under **Decision**, keep **Go**.
4. Under **Next path (E2E-08)**, select **Retire (Branch B)**.
5. In **Rationale**, type **Demand has fallen and a successor exists; retire the product.**, then select **Record decision**.
6. Result: **E2E-08** starts automatically. Sign in again as **pm1@clearwater.example** to continue.

Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch B

Open the project, tab **Lifecycle & tasks**, card **E2E-08**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-08-05 Assess Exit Impact	—	Assess Exit Impact done for CLE-001. Summary filed as CLE-001-08-05.
2	UFT-08-06 Develop Exit Strategy	—	Develop Exit Strategy done for CLE-001. Summary filed as CLE-001-08-06.
3	UFT-08-07 Execute Product Exit	—	Execute Product Exit done for CLE-001. Summary filed as CLE-001-08-07.
4	UFT-08-08 Communicate End-of-Life	—	Communicate End-of-Life done for CLE-001. Summary filed as CLE-001-08-08.
5	UFT-08-09 Support Customer Migration	Customers affected: 1200 Customers migrated: 1200	Support Customer Migration done for CLE-001. Summary filed as CLE-001-08-09.
6	UFT-08-10 Financial Closure	Closure cost (kUSD): 180	Financial Closure done for CLE-001. Summary filed as CLE-001-08-10.

Open the task **Complete Gate Checklist (T6)**. The gate T6 checklist has 30 items; 18 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Exit impact assessment	CLE-001-T6-01
2	Exit strategy	CLE-001-T6-02
3	Executed market exit	CLE-001-T6-03
4	End-of-life communication	CLE-001-T6-04
5	Customer migration	CLE-001-T6-05
6	Financial closure	CLE-001-T6-06
7	Evidence: Elicit and capture requirements from all sources	CLE-001-T6-07
9	Evidence: Manage design process (conceptual, detailed, validation)	CLE-001-T6-09
11	Evidence: Define and manage quality plans (APQP, PPAP)	CLE-001-T6-11
13	Evidence: Define and manage lifecycle workflows	CLE-001-T6-13
15	Evidence: Monitor obsolescence	CLE-001-T6-15
17	Evidence: Define personas and segments	CLE-001-T6-17
19	Evidence: Perform should-cost and target costing	CLE-001-T6-19
21	Evidence: Create and manage Engineering BOM (eBOM)	CLE-001-T6-21
23	Evidence: Provide generative design	CLE-001-T6-23
25	Evidence: Manage invention disclosures and patent filings	CLE-001-T6-25
27	Evidence: Structure and categorize requirements	CLE-001-T6-27
29	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	CLE-001-T6-29

Submit the gate: on the project page, card **Gate T6**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@clearwater.example** (Adam Dubois, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T6 line of **CLE-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Customers migrated and costs closed; end of life confirmed.**, then select **Record decision**.
5. Result: no further process starts; see the result of the run below. Sign in again as **pm1@clearwater.example** to continue.

Result of the run

The project status is **Retired**. The whole Full Track, from idea to end of life, is recorded in the tab **History**.

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Portfolio > Portfolio overview**: the project row shows the status of each E2E process.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

10. Run 5: Full Track in Oil, Gas & Energy, from idea to a relaunch

A new organization in an existing group (Group: Yes). A green hydrogen offer runs the Full Track to launch and performance review; the T5 board chooses a relaunch; E2E-08 Branch A loops back to development (E2E-04), and the improved product goes live again at T3.

Item	Value
Tenancy	Group: Yes (Crescent Agro-Energy Group) > Sahara Hydrogen Energy > project SAH-001
Organization	Sahara Hydrogen Energy (Oil, Gas & Energy), e-mail domain saharah2.example
Product Manager	Mehdi Roche · pm1@saharah2.example
Executive Sponsor	Amina Alaoui · exec@saharah2.example
Project	SAH-001 Green Hydrogen Refuelling Kit
Track	Full (total score 28 of 35)
End state	Active · NPV 1668 kUSD, ROI 123.5%

Step 0. Create the tenancy: Group (Yes / No), then the organization

Sign in as **admin@cortexplm.example** (password **Admin#2026**), the platform administrator.

Open **Portfolio > Groups, organizations & projects**.

1. The group **Crescent Agro-Energy Group** already exists (Group: Yes). You will attach the new organization to it.
2. Select **Add organization** and fill in the window:

Field	What to type or select
Belongs to a group?	select Yes
Group	select Crescent Agro-Energy Group
Name	Sahara Hydrogen Energy
Sector	select Oil, Gas & Energy
Country	Oman
Default language	keep English
Initial subscription	select PACK-11 CortexPLM Enterprise
Create the starting team	keep the box ticked
E-mail domain	saharah2.example
Initial password	Start#2026

Select **Save**. The message reads "Organization created with 24 accounts." The organization receives its OBS departments, the governance catalog, the AI use case library and the checklist templates, and one account per role, for example **pm1@saharah2.example** (Product Manager) and **exec@saharah2.example** (Executive Sponsor). Sign out.

Step 1. Create the project

Sign in as **pm1@saharah2.example** (password **Start#2026**), the Product Manager.

Open **Portfolio > Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Step 0. Organization	shows Sahara Hydrogen Energy ; Belongs to a group? Yes
Project name	Green Hydrogen Refuelling Kit
Description	Containerised electrolyser and dispenser that lets fleet depots refuel hydrogen trucks on site.
Offer type	Product-Service

Field	What to type or select
Region	Oman industrial zones
Product Manager (owner)	keep Mehdi Roche
Executive Sponsor	Amina Alaoui
Strategic impact	select 5
Investment level	select 4
Technical novelty	select 4
Regulatory and safety exposure	select 4
Market scope	select 3
Cross-functional reach	select 4
Product-service integration	select 4
Step 3. Confirm the track	Total score 28 of 35: select Full Track · recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project SAH-001 created. E2E-01 has started." and the project page opens.

Step 2. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Market trend One-sentence idea statement: Offer on-site hydrogen refuelling to truck fleets.	Capture Strategic Idea done for SAH-001. Summary filed as SAH-001-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Logistics fleets with 20 trucks or more Addressable market (MUSD): 60 Strategic-fit score (0-100): 82	Assess Market Opportunity done for SAH-001. Summary filed as SAH-001-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 3200 Expected net cash flow per year (kUSD): 900 Evaluation horizon (years): 8 Discount rate (%): 10	Build Preliminary Business Case done for SAH-001. Summary filed as SAH-001-01-03.
4	UFT-01-04 Assess Risks & Compliance	Main risk identified: Hydrogen leak at the dispenser Likelihood (1-5): 2 Impact (1-5): 5 Regulated product?: Yes	Assess Risks & Compliance done for SAH-001. Summary filed as SAH-001-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Electrolyser stack, compression, dispenser, remote monitoring	Describe High-Level Capability done for SAH-001. Summary filed as SAH-001-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Transformational Roadmap slot (e.g. 2027-Q2): 2028-Q2	Establish Product Portfolio Strategy done for SAH-001. Summary filed as SAH-001-01-06.

What you will see NPV 1601 kUSD, ROI 125%, payback 3.6 years. Risk added to the risk register.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	SAH-001-T-1-01
2	Market opportunity assessment	SAH-001-T-1-02

Item	Checklist item (mandatory)	Evidence reference to type
3	Preliminary business case (NPV, ROI, risk)	SAH-001-T-1-03
4	Initial risk and compliance register	SAH-001-T-1-04
5	Portfolio fit	SAH-001-T-1-05
7	Evidence: Elicit and capture requirements from all sources	SAH-001-T-1-07
9	Evidence: Perform should-cost and target costing	SAH-001-T-1-09
11	Evidence: Manage invention disclosures and patent filings	SAH-001-T-1-11
13	Evidence: Define and manage lifecycle workflows	SAH-001-T-1-13
15	Evidence: Provide generative design	SAH-001-T-1-15
17	Evidence: Structure and categorize requirements	SAH-001-T-1-17
19	Evidence: Manage lifecycle costing	SAH-001-T-1-19
21	Evidence: Manage trademark and copyright registrations	SAH-001-T-1-21
23	Evidence: Enforce GRC policies	SAH-001-T-1-23
25	Evidence: Automate data classification	SAH-001-T-1-25
27	Evidence: Analyze and validate requirements	SAH-001-T-1-27
29	Evidence: Analyze profitability	SAH-001-T-1-29

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T-1 line of **SAH-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@saharah2.example** to continue.

Step 3. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for SAH-001. Summary filed as SAH-001-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 3400 Expected net cash flow per year (kUSD): 950 Evaluation horizon (years): 8 Discount rate (%): 10	Develop Detailed Business Case done for SAH-001. Summary filed as SAH-001-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for SAH-001. Summary filed as SAH-001-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	—	Map Preliminary Customer Journey done for SAH-001. Summary filed as SAH-001-02-04.
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 32	Conduct Detailed Profitability Analysis done for SAH-001. Summary filed as SAH-001-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: Pressure equipment directive, ATEX, ISO 19880 hydrogen fuelling	Validate Regulatory Aspects done for SAH-001. Summary filed as SAH-001-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: Medium	Assess Technical Feasibility done for SAH-001. Summary filed as SAH-001-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for SAH-001. Summary filed as SAH-001-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for SAH-001. Summary filed as SAH-001-02-09.

What you will see NPV 1668 kUSD, ROI 123.5%, payback 3.6 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 30 items; 18 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	SAH-001-T0-01
2	Detailed business case and profitability analysis	SAH-001-T0-02
3	High-level functional specifications	SAH-001-T0-03
4	Preliminary customer journey	SAH-001-T0-04
5	Regulatory validation	SAH-001-T0-05
6	Technical feasibility	SAH-001-T0-06
7	Development plan	SAH-001-T0-07
9	Evidence: Elicit and capture requirements from all sources	SAH-001-T0-09
11	Evidence: Manage design process (conceptual, detailed, validation)	SAH-001-T0-11
13	Evidence: Monitor regulatory intelligence	SAH-001-T0-13
15	Evidence: Define and manage lifecycle workflows	SAH-001-T0-15
17	Evidence: Manage invention disclosures and patent filings	SAH-001-T0-17
19	Evidence: Structure and categorize requirements	SAH-001-T0-19
21	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	SAH-001-T0-21
23	Evidence: Prepare and submit filings	SAH-001-T0-23
25	Evidence: Enforce GRC policies	SAH-001-T0-25
27	Evidence: Manage trademark and copyright registrations	SAH-001-T0-27
29	Evidence: Analyze and validate requirements	SAH-001-T0-29

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T0 line of **SAH-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-03** starts automatically. Sign in again as **pm1@saharah2.example** to continue.

Step 4. E2E-03 Business Proposal-to-Design

Open the project, tab **Lifecycle & tasks**, card **E2E-03**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-03-01 Develop Detailed Specifications	—	Develop Detailed Specifications done for SAH-001. Summary filed as SAH-001-03-01.
2	UFT-03-02 Validate Marketing Specifications	—	Validate Marketing Specifications done for SAH-001. Summary filed as SAH-001-03-02.
3	UFT-03-03 Validate Customer Journey	—	Validate Customer Journey done for SAH-001. Summary filed as SAH-001-03-03.
4	UFT-03-04 Model Detailed Processes	—	Model Detailed Processes done for SAH-001. Summary filed as SAH-001-03-04.
5	UFT-03-05 Develop Detailed Design	—	Develop Detailed Design done for SAH-001. Summary filed as SAH-001-03-05.
6	UFT-03-06 Build Functional Prototype	—	Build Functional Prototype done for SAH-001. Summary filed as SAH-001-03-06.

#	Task	Fields to fill	Result / output to type
7	UFT-03-07 Validate Architectures	—	Validate Architectures done for SAH-001. Summary filed as SAH-001-03-07.
8	UFT-03-08 Develop Development Plan	—	Develop Development Plan done for SAH-001. Summary filed as SAH-001-03-08.

Open the task **Complete Gate Checklist (T1)**. The gate T1 checklist has 30 items; 18 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed specifications	SAH-001-T1-01
2	Validated marketing specifications and customer journey	SAH-001-T1-02
3	Process models	SAH-001-T1-03
4	Detailed design	SAH-001-T1-04
5	Functional prototype	SAH-001-T1-05
6	Architecture validation	SAH-001-T1-06
7	Detailed development plan	SAH-001-T1-07
9	Evidence: Manage design process (conceptual, detailed, validation)	SAH-001-T1-09
11	Evidence: Develop go-to-market plans	SAH-001-T1-11
13	Evidence: Train generative AI models	SAH-001-T1-13
15	Evidence: Initiate and submit change requests (ECR)	SAH-001-T1-15
17	Evidence: Define and manage lifecycle workflows	SAH-001-T1-17
19	Evidence: Monitor regulatory intelligence	SAH-001-T1-19
21	Evidence: Perform should-cost and target costing	SAH-001-T1-21
23	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	SAH-001-T1-23
25	Evidence: Prepare collateral	SAH-001-T1-25
27	Evidence: Generate design alternatives	SAH-001-T1-27
29	Evidence: Assess change impact (cost, schedule, quality, compliance)	SAH-001-T1-29

Submit the gate: on the project page, card **Gate T1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T1 line of **SAH-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Design validated; start development.**, then select **Record decision**.
5. Result: **E2E-04** starts automatically. Sign in again as **pm1@saharah2.example** to continue.

Step 5. E2E-04 Design-to-Development

Open the project, tab **Lifecycle & tasks**, card **E2E-04**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-04-01 Support Operational Introduction	—	Support Operational Introduction done for SAH-001. Summary filed as SAH-001-04-01.
2	UFT-04-02 Conduct Operational Readiness Testing	—	Conduct Operational Readiness Testing done for SAH-001. Summary filed as SAH-001-04-02.
3	UFT-04-03 Manage Product Configuration	—	Manage Product Configuration done for SAH-001. Summary filed as SAH-001-04-03.
4	UFT-04-04 Develop Product Offering Procedures	—	Develop Product Offering Procedures done for SAH-001. Summary filed as SAH-001-04-04.

#	Task	Fields to fill	Result / output to type
5	UFT-04-05 Manage Acceptance Testing	Acceptance tests passed (%): 97	Manage Acceptance Testing done for SAH-001. Summary filed as SAH-001-04-05.
6	UFT-04-06 Develop Preliminary Launch Plan	—	Develop Preliminary Launch Plan done for SAH-001. Summary filed as SAH-001-04-06.
7	UFT-04-07 Complete Functionalities	—	Complete Functionalities done for SAH-001. Summary filed as SAH-001-04-07.

Open the task **Complete Gate Checklist (T2)**. The gate T2 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Completed functionalities	SAH-001-T2-01
2	Operational readiness and acceptance test results	SAH-001-T2-02
3	Configuration baseline	SAH-001-T2-03
4	Offering procedures	SAH-001-T2-04
5	Preliminary launch plan	SAH-001-T2-05
7	Evidence: Define manufacturing process plans and routings	SAH-001-T2-07
9	Evidence: Create and manage Engineering BOM (eBOM)	SAH-001-T2-09
11	Evidence: Design and model processes (BPMN)	SAH-001-T2-11
13	Evidence: Develop go-to-market plans	SAH-001-T2-13
15	Evidence: Provide generative design	SAH-001-T2-15
17	Evidence: Monitor regulatory intelligence	SAH-001-T2-17
19	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	SAH-001-T2-19
21	Evidence: Manage non-conformance reports (NCR)	SAH-001-T2-21
23	Evidence: Assess change impact (cost, schedule, quality, compliance)	SAH-001-T2-23
25	Evidence: Review and approve	SAH-001-T2-25
27	Evidence: Enforce GRC policies	SAH-001-T2-27
29	Evidence: Map journeys and touchpoints	SAH-001-T2-29

Submit the gate: on the project page, card **Gate T2**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T2 line of **SAH-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Product complete and tested; prepare launch.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@saharah2.example** to continue.

Step 6. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for SAH-001. Summary filed as SAH-001-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-12-22 (any future date)	Develop Detailed Launch Plan done for SAH-001. Summary filed as SAH-001-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for SAH-001. Summary filed as SAH-001-05-03.
4	UFT-05-04 Develop Marketing	—	Develop Marketing & Sales Materials done

#	Task	Fields to fill	Result / output to type
	& Sales Materials		for SAH-001. Summary filed as SAH-001-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for SAH-001. Summary filed as SAH-001-05-05.
6	UFT-05-06 Train Teams	People trained: 30	Train Teams done for SAH-001. Summary filed as SAH-001-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for SAH-001. Summary filed as SAH-001-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for SAH-001. Summary filed as SAH-001-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	SAH-001-T3-01
2	Marketing and sales materials	SAH-001-T3-02
3	Trained teams	SAH-001-T3-03
4	Validated customer journey	SAH-001-T3-04
5	Final regulatory validation	SAH-001-T3-05
7	Evidence: Define personas and segments	SAH-001-T3-07
9	Evidence: Monitor regulatory intelligence	SAH-001-T3-09
11	Evidence: Define and manage lifecycle workflows	SAH-001-T3-11
13	Evidence: Onboard and certify partners	SAH-001-T3-13
15	Evidence: Manage invention disclosures and patent filings	SAH-001-T3-15
17	Evidence: Develop and manage mobile apps	SAH-001-T3-17
19	Evidence: Map journeys and touchpoints	SAH-001-T3-19
21	Evidence: Prepare and submit filings	SAH-001-T3-21
23	Evidence: Enforce GRC policies	SAH-001-T3-23
25	Evidence: Manage partner agreements and contracts	SAH-001-T3-25
27	Evidence: Manage trademark and copyright registrations	SAH-001-T3-27
29	Evidence: Enable offline access and synchronization	SAH-001-T3-29

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T3 line of **SAH-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-06, E2E-09** start automatically. Sign in again as **pm1@saharah2.example** to continue.

Step 7. E2E-06 Launch-to-After-Sales

Open the project, tab **Lifecycle & tasks**, card **E2E-06**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-06-01 Identify Product Issues	Open product issues: 5	Identify Product Issues done for SAH-001. Summary filed as SAH-001-06-01.

#	Task	Fields to fill	Result / output to type
2	UFT-06-02 Assess Product Performance	—	Assess Product Performance done for SAH-001. Summary filed as SAH-001-06-02.
3	UFT-06-03 Analyze Campaign Results	—	Analyze Campaign Results done for SAH-001. Summary filed as SAH-001-06-03.
4	UFT-06-04 Track Customer Satisfaction	CSAT (1-5): 3.8 Net Promoter Score (-100 to 100): 18	Track Customer Satisfaction done for SAH-001. Summary filed as SAH-001-06-04.
5	UFT-06-05 Track Product Performance	Field MTBF (hours): 3100	Track Product Performance done for SAH-001. Summary filed as SAH-001-06-05.

Open the task **Complete Gate Checklist (T4)**. The gate T4 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Issue log	SAH-001-T4-01
2	Performance assessment	SAH-001-T4-02
3	Campaign results	SAH-001-T4-03
4	CSAT and NPS	SAH-001-T4-04
5	Field performance data	SAH-001-T4-05
7	Evidence: Log and categorize incidents and requests	SAH-001-T4-07
9	Evidence: Collect field failure data	SAH-001-T4-09
11	Evidence: Define personas and segments	SAH-001-T4-11
13	Evidence: Manage service parts and inventory	SAH-001-T4-13
15	Evidence: Perform should-cost and target costing	SAH-001-T4-15
17	Evidence: Prioritize and escalate	SAH-001-T4-17
19	Evidence: Analyze failure modes	SAH-001-T4-19
21	Evidence: Map journeys and touchpoints	SAH-001-T4-21
23	Evidence: Create and manage maintenance plans (preventive, predictive)	SAH-001-T4-23
25	Evidence: Manage lifecycle costing	SAH-001-T4-25
27	Evidence: Diagnose and resolve	SAH-001-T4-27
29	Evidence: Model reliability (Weibull, MTBF)	SAH-001-T4-29

Step 8. E2E-09 Market Strategy-to-Campaign

Open the project, tab **Lifecycle & tasks**, card **E2E-09**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-09-01 Gather Customer Experience Data	—	Gather Customer Experience Data done for SAH-001. Summary filed as SAH-001-09-01.
2	UFT-09-02 Gather Product Delivery Feedback	—	Gather Product Delivery Feedback done for SAH-001. Summary filed as SAH-001-09-02.
3	UFT-09-03 Establish Market Segments	—	Establish Market Segments done for SAH-001. Summary filed as SAH-001-09-03.
4	UFT-09-04 Link Segments & Products	—	Link Segments & Products done for SAH-001. Summary filed as SAH-001-09-04.
5	UFT-09-05 Establish Market Strategy	—	Establish Market Strategy done for SAH-001. Summary filed as SAH-001-09-05.
6	UFT-09-06 Plan & Develop Campaign	—	Plan & Develop Campaign done for SAH-001. Summary filed as SAH-001-09-06.
7	UFT-09-07 Launch & Monitor Campaign	—	Launch & Monitor Campaign done for SAH-001. Summary filed as SAH-001-09-07.
8	UFT-09-08 Complete Campaign & Report	Qualified leads generated: 140 Conversion rate (%): 12	Complete Campaign & Report done for SAH-001. Summary filed as SAH-001-09-08.

Submit the gate: on the project page, card **Gate T4**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T4 line of **SAH-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Post-launch performance is stable; move to steady-state review.**, then select **Record decision**.
5. Result: **E2E-07** starts automatically. Sign in again as **pm1@saharah2.example** to continue.

Step 9. E2E-07 After-Sales-to-Performance

Open the project, tab **Lifecycle & tasks**, card **E2E-07**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-07-01 Evaluate Overall Performance	—	Evaluate Overall Performance done for SAH-001. Summary filed as SAH-001-07-01.
2	UFT-07-02 Analyze Profitability	Revenue to date (kUSD): 5200 Cost of goods sold (kUSD): 4300	Analyze Profitability done for SAH-001. Summary filed as SAH-001-07-02.
3	UFT-07-03 Gather Customer Experience Feedback	CSAT (1-5): 3.9 Net Promoter Score (-100 to 100): 22	Gather Customer Experience Feedback done for SAH-001. Summary filed as SAH-001-07-03.
4	UFT-07-04 Develop Improvement Recommendations	Recommendation to the T5 gate: Relaunch	Develop Improvement Recommendations done for SAH-001. Summary filed as SAH-001-07-04.

Open the task **Complete Gate Checklist (T5)**. The gate T5 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Overall performance evaluation	SAH-001-T5-01
2	Profitability analysis	SAH-001-T5-02
3	Customer experience feedback	SAH-001-T5-03
4	Improvement recommendations	SAH-001-T5-04
5	Evidence: Define and manage lifecycle workflows	SAH-001-T5-05
7	Evidence: Define personas and segments	SAH-001-T5-07
9	Evidence: Define strategic product themes, goals, and investment horizons	SAH-001-T5-09
11	Evidence: Collect field failure data	SAH-001-T5-11
13	Evidence: Manage lifecycle costing	SAH-001-T5-13
15	Evidence: Collect and analyze feedback	SAH-001-T5-15
17	Evidence: Automate data classification	SAH-001-T5-17
19	Evidence: Define and track KPIs	SAH-001-T5-19
21	Evidence: Identify pain points and moments of truth	SAH-001-T5-21
23	Evidence: Evaluate and score product ideas against strategic fit	SAH-001-T5-23
25	Evidence: Model reliability (Weibull, MTBF)	SAH-001-T5-25
27	Evidence: Optimize cost structures	SAH-001-T5-27
29	Evidence: Conduct quality audits	SAH-001-T5-29

Submit the gate: on the project page, card **Gate T5**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T5 line of **SAH-001**.
3. Under **Decision**, keep **Go**.

4. Under **Next path (E2E-08)**, select **Relaunch (Branch A)**.
5. In **Rationale**, type **Performance is below target but fixable; relaunch.**, then select **Record decision**.
6. Result: **E2E-08** starts automatically. Sign in again as **pm1@saharah2.example** to continue.

Step 10. E2E-08 Assessment-to-Relaunch or Retirement · Branch A

Open the project, tab **Lifecycle & tasks**, card **E2E-08**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-08-01 Update Product Specifications	—	Update Product Specifications done for SAH-001. Summary filed as SAH-001-08-01.
2	UFT-08-02 Support Operational Re-introduction	—	Support Operational Re-introduction done for SAH-001. Summary filed as SAH-001-08-02.
3	UFT-08-03 Manage Product Improvements	—	Manage Product Improvements done for SAH-001. Summary filed as SAH-001-08-03.
4	UFT-08-04 Approve for Relaunch	Relaunch re-entry point: E2E-04	Approve for Relaunch done for SAH-001. Summary filed as SAH-001-08-04.

Step 11. E2E-04 Design-to-Development (run 2)

Open the project, tab **Lifecycle & tasks**, card **E2E-04**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-04-01 Support Operational Introduction	—	Support Operational Introduction done for SAH-001. Summary filed as SAH-001-04-01.
2	UFT-04-02 Conduct Operational Readiness Testing	—	Conduct Operational Readiness Testing done for SAH-001. Summary filed as SAH-001-04-02.
3	UFT-04-03 Manage Product Configuration	—	Manage Product Configuration done for SAH-001. Summary filed as SAH-001-04-03.
4	UFT-04-04 Develop Product Offering Procedures	—	Develop Product Offering Procedures done for SAH-001. Summary filed as SAH-001-04-04.
5	UFT-04-05 Manage Acceptance Testing	Acceptance tests passed (%): 97	Manage Acceptance Testing done for SAH-001. Summary filed as SAH-001-04-05.
6	UFT-04-06 Develop Preliminary Launch Plan	—	Develop Preliminary Launch Plan done for SAH-001. Summary filed as SAH-001-04-06.
7	UFT-04-07 Complete Functionalities	—	Complete Functionalities done for SAH-001. Summary filed as SAH-001-04-07.

Open the task **Complete Gate Checklist (T2)**. The gate T2 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Completed functionalities	SAH-001-T2-01
2	Operational readiness and acceptance test results	SAH-001-T2-02
3	Configuration baseline	SAH-001-T2-03
4	Offering procedures	SAH-001-T2-04
5	Preliminary launch plan	SAH-001-T2-05
7	Evidence: Define manufacturing process plans and routings	SAH-001-T2-07

Item	Checklist item (mandatory)	Evidence reference to type
9	Evidence: Create and manage Engineering BOM (eBOM)	SAH-001-T2-09
11	Evidence: Design and model processes (BPMN)	SAH-001-T2-11
13	Evidence: Develop go-to-market plans	SAH-001-T2-13
15	Evidence: Provide generative design	SAH-001-T2-15
17	Evidence: Monitor regulatory intelligence	SAH-001-T2-17
19	Evidence: Integrate with CAD/CAM/CAE tools (Creo, NX, CATIA, SolidWorks, AutoCAD)	SAH-001-T2-19
21	Evidence: Manage non-conformance reports (NCR)	SAH-001-T2-21
23	Evidence: Assess change impact (cost, schedule, quality, compliance)	SAH-001-T2-23
25	Evidence: Review and approve	SAH-001-T2-25
27	Evidence: Enforce GRC policies	SAH-001-T2-27
29	Evidence: Map journeys and touchpoints	SAH-001-T2-29

Submit the gate: on the project page, card **Gate T2**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T2 line of **SAH-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Product complete and tested; prepare launch.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@saharah2.example** to continue.

Step 12. E2E-05 Development-to-Launch (run 2)

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for SAH-001. Summary filed as SAH-001-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-12-22 (any future date)	Develop Detailed Launch Plan done for SAH-001. Summary filed as SAH-001-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for SAH-001. Summary filed as SAH-001-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for SAH-001. Summary filed as SAH-001-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for SAH-001. Summary filed as SAH-001-05-05.
6	UFT-05-06 Train Teams	People trained: 30	Train Teams done for SAH-001. Summary filed as SAH-001-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for SAH-001. Summary filed as SAH-001-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for SAH-001. Summary filed as SAH-001-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 30 items; 17 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	SAH-001-T3-01
2	Marketing and sales materials	SAH-001-T3-02

Item	Checklist item (mandatory)	Evidence reference to type
3	Trained teams	SAH-001-T3-03
4	Validated customer journey	SAH-001-T3-04
5	Final regulatory validation	SAH-001-T3-05
7	Evidence: Define personas and segments	SAH-001-T3-07
9	Evidence: Monitor regulatory intelligence	SAH-001-T3-09
11	Evidence: Define and manage lifecycle workflows	SAH-001-T3-11
13	Evidence: Onboard and certify partners	SAH-001-T3-13
15	Evidence: Manage invention disclosures and patent filings	SAH-001-T3-15
17	Evidence: Develop and manage mobile apps	SAH-001-T3-17
19	Evidence: Map journeys and touchpoints	SAH-001-T3-19
21	Evidence: Prepare and submit filings	SAH-001-T3-21
23	Evidence: Enforce GRC policies	SAH-001-T3-23
25	Evidence: Manage partner agreements and contracts	SAH-001-T3-25
27	Evidence: Manage trademark and copyright registrations	SAH-001-T3-27
29	Evidence: Enable offline access and synchronization	SAH-001-T3-29

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@saharah2.example** (Amina Alaoui, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T3 line of **SAH-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-06, E2E-09** start automatically. Sign in again as **pm1@saharah2.example** to continue.

Result of the run

The project stays **Active**, now in E2E-06 after gate T3. Active · open runs: E2E-06, E2E-09

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Portfolio > Portfolio overview**: the project row shows the status of each E2E process.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

11. Run 6: Light Track in Real Estate Development, from idea to launch

A new organization joins Atlas Infrastructure Holding (Group: Yes). A real estate developer launches a new home offer on the Light Track; at gate T2 the sector checklist template "Off-plan launch readiness" is added from the library.

Item	Value
Tenancy	Group: Yes (Atlas Infrastructure Holding) > Palmgrove Residential Developers > project PAL-001
Organization	Palmgrove Residential Developers (Real Estate Development), e-mail domain palmgrove.example
Product Manager	Chloe Mansouri · pm1@palmgrove.example
Executive Sponsor	Karim Roche · exec@palmgrove.example
Project	PAL-001 Smart Townhouse Collection
Track	Light (total score 22 of 35)
End state	Active · NPV 2312 kUSD, ROI 65.3%

Step 0. Create the tenancy: Group (Yes / No), then the organization

Sign in as **admin@cortexplm.example** (password **Admin#2026**), the platform administrator.

Open **Portfolio > Groups, organizations & projects**.

1. The group **Atlas Infrastructure Holding** already exists (Group: Yes). You will attach the new organization to it.
2. Select **Add organization** and fill in the window:

Field	What to type or select
Belongs to a group?	select Yes
Group	select Atlas Infrastructure Holding
Name	Palmgrove Residential Developers
Sector	select Real Estate Development
Country	Saudi Arabia
Default language	keep English
Initial subscription	select BND-05 Innovation Bundle
Create the starting team	keep the box ticked
E-mail domain	palmgrove.example
Initial password	Start#2026

Select **Save**. The message reads "Organization created with 24 accounts." The organization receives its OBS departments, the governance catalog, the AI use case library and the checklist templates, and one account per role, for example **pm1@palmgrove.example** (Product Manager) and **exec@palmgrove.example** (Executive Sponsor). Sign out.

Step 1. Create the project

Sign in as **pm1@palmgrove.example** (password **Start#2026**), the Product Manager.

Open **Portfolio > Innovation projects** and select **New project**. Fill in the wizard:

Field	What to type or select
Step 0. Organization	shows Palmgrove Residential Developers ; Belongs to a group? Yes
Project name	Smart Townhouse Collection
Description	Townhouses sold off-plan with smart home equipment, solar roof and a resident app.

Field	What to type or select
Offer type	Product-Service
Region	Riyadh region
Product Manager (owner)	keep Chloe Mansouri
Executive Sponsor	Karim Roche
Strategic impact	select 3
Investment level	select 4
Technical novelty	select 3
Regulatory and safety exposure	select 3
Market scope	select 2
Cross-functional reach	select 4
Product-service integration	select 3
Step 3. Confirm the track	Total score 22 of 35: select Light Track · recommended
Step 4. Optional macro processes	leave all unticked

Select **Create project**. The message reads "Project PAL-001 created. E2E-01 has started." and the project page opens.

Step 2. E2E-01 Idea-to-Business Plan

Open the project, tab **Lifecycle & tasks**, card **E2E-01**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-01-01 Capture Strategic Idea	Idea source: Customer request One-sentence idea statement: Offer smart, energy-efficient townhouses for young families.	Capture Strategic Idea done for PAL-001. Summary filed as PAL-001-01-01.
2	UFT-01-02 Assess Market Opportunity	Target segment: Young families buying their first home Addressable market (MUSD): 25 Strategic-fit score (0-100): 76	Assess Market Opportunity done for PAL-001. Summary filed as PAL-001-01-02.
3	UFT-01-03 Build Preliminary Business Case	Investment (kUSD): 9500 Expected net cash flow per year (kUSD): 2600 Evaluation horizon (years): 6 Discount rate (%): 9	Build Preliminary Business Case done for PAL-001. Summary filed as PAL-001-01-03.
4	UFT-01-04 Assess Risks & Compliance	Main risk identified: Slow off-plan sales Likelihood (1-5): 3 Impact (1-5): 4 Regulated product?: Yes	Assess Risks & Compliance done for PAL-001. Summary filed as PAL-001-01-04.
5	UFT-01-05 Describe High-Level Capability	Key capabilities and skills needed: Modular townhouse design, smart home kit, resident app	Describe High-Level Capability done for PAL-001. Summary filed as PAL-001-01-05.
6	UFT-01-06 Establish Product Portfolio Strategy	Portfolio position: Adjacent Roadmap slot (e.g. 2027-Q2): 2027-Q4	Establish Product Portfolio Strategy done for PAL-001. Summary filed as PAL-001-01-06.

What you will see NPV 2163 kUSD, ROI 64.2%, payback 3.7 years. Risk added to the risk register.

Open the task **Complete Gate Checklist (T-1)**. The gate T-1 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Captured idea	PAL-001-T-1-01

Item	Checklist item (mandatory)	Evidence reference to type
2	Market opportunity assessment	PAL-001-T-1-02
3	Preliminary business case (NPV, ROI, risk)	PAL-001-T-1-03
4	Initial risk and compliance register	PAL-001-T-1-04
5	Portfolio fit	PAL-001-T-1-05
7	Evidence: Elicit and capture requirements from all sources	PAL-001-T-1-07
10	Evidence: Monitor regulatory intelligence	PAL-001-T-1-10
13	Evidence: Define and manage lifecycle workflows	PAL-001-T-1-13

Submit the gate: on the project page, card **Gate T-1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@palmgrove.example** (Karim Roche, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T-1 line of **PAL-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Aligned with strategy; fund the opportunity study.**, then select **Record decision**.
5. Result: **E2E-02** starts automatically. Sign in again as **pm1@palmgrove.example** to continue.

Step 3. E2E-02 Idea-to-Business Proposal

Open the project, tab **Lifecycle & tasks**, card **E2E-02**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-02-01 Conduct Opportunity Study	—	Conduct Opportunity Study done for PAL-001. Summary filed as PAL-001-02-01.
2	UFT-02-02 Develop Detailed Business Case	Investment (kUSD): 9800 Expected net cash flow per year (kUSD): 2700 Evaluation horizon (years): 6 Discount rate (%): 9	Develop Detailed Business Case done for PAL-001. Summary filed as PAL-001-02-02.
3	UFT-02-03 Define High-Level Functional Specs	—	Define High-Level Functional Specs done for PAL-001. Summary filed as PAL-001-02-03.
4	UFT-02-04 Map Preliminary Customer Journey	—	Map Preliminary Customer Journey done for PAL-001. Summary filed as PAL-001-02-04.
5	UFT-02-05 Conduct Detailed Profitability Analysis	Expected gross margin (%): 27	Conduct Detailed Profitability Analysis done for PAL-001. Summary filed as PAL-001-02-05.
6	UFT-02-06 Validate Regulatory Aspects	Applicable regulations and standards: Off-plan sales regulation (escrow), building code, green building rating	Validate Regulatory Aspects done for PAL-001. Summary filed as PAL-001-02-06.
7	UFT-02-07 Assess Technical Feasibility	Technical feasibility: High	Assess Technical Feasibility done for PAL-001. Summary filed as PAL-001-02-07.
8	UFT-02-08 Develop Development Plan	—	Develop Development Plan done for PAL-001. Summary filed as PAL-001-02-08.
9	UFT-02-09 Validate Opportunity	—	Validate Opportunity done for PAL-001. Summary filed as PAL-001-02-09.

What you will see NPV 2312 kUSD, ROI 65.3%, payback 3.6 years.

Open the task **Complete Gate Checklist (T0)**. The gate T0 checklist has 15 items; 9 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select

Mark complete. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Opportunity study	PAL-001-T0-01
2	Detailed business case and profitability analysis	PAL-001-T0-02
3	High-level functional specifications	PAL-001-T0-03
4	Preliminary customer journey	PAL-001-T0-04
5	Regulatory validation	PAL-001-T0-05
6	Technical feasibility	PAL-001-T0-06
7	Development plan	PAL-001-T0-07
10	Evidence: Perform should-cost and target costing	PAL-001-T0-10
13	Evidence: Monitor regulatory intelligence	PAL-001-T0-13

Submit the gate: on the project page, card **Gate T0**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@palmgrove.example** (Karim Roche, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T0 line of **PAL-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Business case and feasibility are convincing; commit design investment.**, then select **Record decision**.
5. Result: **E2E-03** starts automatically. Sign in again as **pm1@palmgrove.example** to continue.

Step 4. E2E-03 Business Proposal-to-Design

Open the project, tab **Lifecycle & tasks**, card **E2E-03**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-03-01 Develop Detailed Specifications	—	Develop Detailed Specifications done for PAL-001. Summary filed as PAL-001-03-01.
2	UFT-03-02 Validate Marketing Specifications	—	Validate Marketing Specifications done for PAL-001. Summary filed as PAL-001-03-02.
3	UFT-03-03 Validate Customer Journey	—	Validate Customer Journey done for PAL-001. Summary filed as PAL-001-03-03.
4	UFT-03-04 Model Detailed Processes	—	Model Detailed Processes done for PAL-001. Summary filed as PAL-001-03-04.
5	UFT-03-05 Develop Detailed Design	—	Develop Detailed Design done for PAL-001. Summary filed as PAL-001-03-05.
6	UFT-03-06 Build Functional Prototype	—	Build Functional Prototype done for PAL-001. Summary filed as PAL-001-03-06.
7	UFT-03-07 Validate Architectures	—	Validate Architectures done for PAL-001. Summary filed as PAL-001-03-07.
8	UFT-03-08 Develop Development Plan	—	Develop Development Plan done for PAL-001. Summary filed as PAL-001-03-08.

Open the task **Complete Gate Checklist (T1)**. The gate T1 checklist has 15 items; 9 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed specifications	PAL-001-T1-01
2	Validated marketing specifications and customer journey	PAL-001-T1-02
3	Process models	PAL-001-T1-03

Item	Checklist item (mandatory)	Evidence reference to type
4	Detailed design	PAL-001-T1-04
5	Functional prototype	PAL-001-T1-05
6	Architecture validation	PAL-001-T1-06
7	Detailed development plan	PAL-001-T1-07
10	Evidence: Define personas and segments	PAL-001-T1-10
13	Evidence: Train generative AI models	PAL-001-T1-13

Submit the gate: on the project page, card **Gate T1**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@palmgrove.example** (Karim Roche, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T1 line of **PAL-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Design validated; start development.**, then select **Record decision**.
5. Result: **E2E-04** starts automatically. Sign in again as **pm1@palmgrove.example** to continue.

Step 5. E2E-04 Design-to-Development

Open the project, tab **Lifecycle & tasks**, card **E2E-04**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-04-01 Support Operational Introduction	—	Support Operational Introduction done for PAL-001. Summary filed as PAL-001-04-01.
2	UFT-04-02 Conduct Operational Readiness Testing	—	Conduct Operational Readiness Testing done for PAL-001. Summary filed as PAL-001-04-02.
3	UFT-04-03 Manage Product Configuration	—	Manage Product Configuration done for PAL-001. Summary filed as PAL-001-04-03.
4	UFT-04-04 Develop Product Offering Procedures	—	Develop Product Offering Procedures done for PAL-001. Summary filed as PAL-001-04-04.
5	UFT-04-05 Manage Acceptance Testing	Acceptance tests passed (%): 96	Manage Acceptance Testing done for PAL-001. Summary filed as PAL-001-04-05.
6	UFT-04-06 Develop Preliminary Launch Plan	—	Develop Preliminary Launch Plan done for PAL-001. Summary filed as PAL-001-04-06.
7	UFT-04-07 Complete Functionalities	—	Complete Functionalities done for PAL-001. Summary filed as PAL-001-04-07.

This gate needs the sector items too. Open the gate (**Gate board**, line T2 of **PAL-001**). In **Add to this checklist**, keep **From a template**, choose **T2 · Light Track · Off-plan launch readiness (escrow and permits)** and select **Add to checklist**: 5 items are added, the mandatory ones marked **Mandatory**.

Open the task **Complete Gate Checklist (T2)**. The gate T2 checklist has 20 items; 11 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Completed functionalities	PAL-001-T2-01
2	Operational readiness and acceptance test results	PAL-001-T2-02
3	Configuration baseline	PAL-001-T2-03
4	Offering procedures	PAL-001-T2-04
5	Preliminary launch plan	PAL-001-T2-05

Item	Checklist item (mandatory)	Evidence reference to type
7	Evidence: Define manufacturing process plans and routings	PAL-001-T2-07
10	Evidence: Initiate and submit change requests (ECR)	PAL-001-T2-10
13	Evidence: Develop go-to-market plans	PAL-001-T2-13
16	Building permit issued	PAL-001-T2-16
17	Off-plan sales licence issued	PAL-001-T2-17
18	Escrow account opened with the bank	PAL-001-T2-18

Submit the gate: on the project page, card **Gate T2**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@palmgrove.example** (Karim Roche, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T2 line of **PAL-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Product complete and tested; prepare launch.**, then select **Record decision**.
5. Result: **E2E-05** starts automatically. Sign in again as **pm1@palmgrove.example** to continue.

Step 6. E2E-05 Development-to-Launch

Open the project, tab **Lifecycle & tasks**, card **E2E-05**. Open each task in turn, fill in the fields shown, type the **Result / output**, then select **Complete task**. In the **Record a lesson learned** window that follows, select **Skip**.

#	Task	Fields to fill	Result / output to type
1	UFT-05-01 Approve for Launch/Rollout	—	Approve for Launch/Rollout done for PAL-001. Summary filed as PAL-001-05-01.
2	UFT-05-02 Develop Detailed Launch Plan	Planned launch date: 2026-11-22 (any future date)	Develop Detailed Launch Plan done for PAL-001. Summary filed as PAL-001-05-02.
3	UFT-05-03 Develop Communication Plan	—	Develop Communication Plan done for PAL-001. Summary filed as PAL-001-05-03.
4	UFT-05-04 Develop Marketing & Sales Materials	—	Develop Marketing & Sales Materials done for PAL-001. Summary filed as PAL-001-05-04.
5	UFT-05-05 Execute Communication Campaign	—	Execute Communication Campaign done for PAL-001. Summary filed as PAL-001-05-05.
6	UFT-05-06 Train Teams	People trained: 18	Train Teams done for PAL-001. Summary filed as PAL-001-05-06.
7	UFT-05-07 Validate Customer Journey	—	Validate Customer Journey done for PAL-001. Summary filed as PAL-001-05-07.
8	UFT-05-08 Final Regulatory Validation	All regulatory approvals obtained?: Yes	Final Regulatory Validation done for PAL-001. Summary filed as PAL-001-05-08.

Open the task **Complete Gate Checklist (T3)**. The gate T3 checklist has 15 items; 8 are **Mandatory**. For each mandatory item, type the evidence reference below in its field and select **Mark complete**. Optional items can stay open. Then select **Complete checklist task** (and **Skip** in the lesson window).

Item	Checklist item (mandatory)	Evidence reference to type
1	Detailed launch and communication plans	PAL-001-T3-01
2	Marketing and sales materials	PAL-001-T3-02
3	Trained teams	PAL-001-T3-03
4	Validated customer journey	PAL-001-T3-04
5	Final regulatory validation	PAL-001-T3-05
7	Evidence: Define personas and segments	PAL-001-T3-07
10	Evidence: Define and manage quality plans (APQP, PPAP)	PAL-001-T3-10
13	Evidence: Onboard and certify partners	PAL-001-T3-13

Submit the gate: on the project page, card **Gate T3**, select **Submit gate for decision**. Sign out.

1. Sign in as **exec@palmgrove.example** (Karim Roche, Executive Sponsor, password **Start#2026**) and open **Portfolio > Gate board**.
2. Open the T3 line of **PAL-001**.
3. Under **Decision**, keep **Go**.
4. In **Rationale**, type **Approvals in place and teams trained; go live.**, then select **Record decision**.
5. Result: **E2E-07, E2E-09** start automatically. Sign in again as **pm1@palmgrove.example** to continue.

Result of the run

The project stays **Active**, now in E2E-07 after gate T3. Active · open runs: E2E-07, E2E-09

- Open the tab **Business case & risks** to see NPV, ROI and payback calculated from your entries (BR-002), and the risk created by "Assess Risks & Compliance".
- Open the tab **History** to read every change with its author and time.
- Open **Portfolio > Portfolio overview**: the project row shows the status of each E2E process.
- Open **Reports & cockpits** to see the project counted in the portfolio figures.

12. Run 7: Benchmarking in Real Estate Development, within the organization and across the group

Tenancy of this run: **Group: Yes** (Atlas Infrastructure Holding) > **Ridgeway Real Estate Development** > its 21 projects. Ridgeway belongs to Atlas with Cedarline Precast Systems, Orvane Transit Group and, after Run 6, Palmgrove Residential Developers. Its Executive Sponsor compares the organization's own project types and tracks, then compares the organization with its two sister companies. Comparisons outside the group are not possible: external benchmarking is out of scope.


Item	Value
Organization	Ridgeway Real Estate Development (Real Estate Development), group Atlas Infrastructure Holding
Sign in	exec@ridgeway.example / Demo#2026 (Executive Sponsor)
Screen	Portfolio > Benchmarking

Step 1. Compare project types

1. Sign in as **exec@ridgeway.example** and open **Portfolio > Benchmarking**. The tab **Within the organization** opens, with **Compare by** set to **Project type**.
2. Read the four figures at the top: projects compared, first-time Go rate, time to market and checklist compliance for the whole organization.
3. In the chart, open the **Indicator** list and choose **Time to market**, then **Average NPV**. The bars compare Product, Product-Service and Service projects.
4. Read the **Scorecard by project type**. Green marks the best segment and red the weakest for each indicator.

Project type	Projects	First-time Go	Time to market	Average NPV
Product	8	88.6%	228 days	271 kUSD
Product-Service	4	90%	249 days	-20 kUSD
Service	9	82.6%	247 days	420 kUSD

What it tells you: Service projects reach the market fastest and carry the best business cases, while Product-Service projects are sent back most often (lowest first-time Go rate).

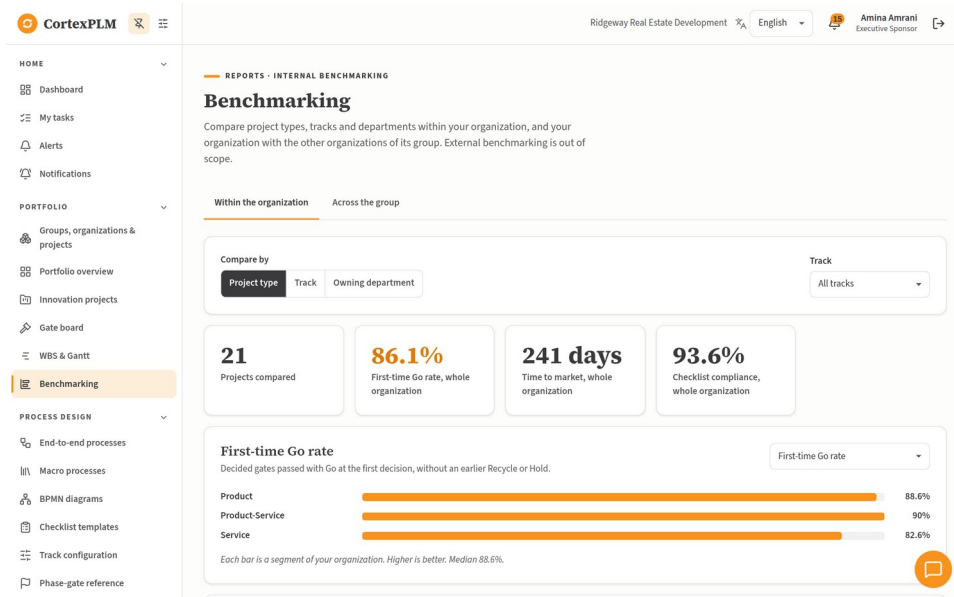

Benchmarking within the organization, compared by project type.

Step 2. Compare tracks and filter

1. Under **Compare by**, select **Track**. The scorecard now compares the Full, Light and Fast tracks.
2. In **Project type**, choose **Service** to compare tracks for Service projects only. Choose **All project types** to reset.
3. Select **CSV** above the scorecard to download the figures.

Track	Projects	First-time Go	Time to market	Average NPV
Fast	3	100%	121 days	957 kUSD
Full	15	86.4%	250 days	190 kUSD
Light	3	75%	254 days	201 kUSD

Step 3. Compare with the organizations of the group

1. Select the tab **Across the group**. The card shows **Atlas Infrastructure Holding** and its organizations. An organization with fewer than 3 projects, such as Palmgrove after Run 6, is marked not comparable.
2. Read the note: only aggregated indicators are exchanged. No project, person or document of Cedarline or Orvane is visible.
3. In the chart, choose **First-time Go rate**, then **Gate decision time**. Your organization is marked **(you)**.
4. Read the **Scorecard by organization** and the **Median** column.

Organization	First-time Go	Recycle	Decision time	Time to market
Cedarline Precast Systems	95%	2.9%	4.2 days	174 days
Orvane Transit Group	87.1%	10.6%	7.9 days	227 days
Palmgrove Residential Developers	100%	0%	0 days	-1 days
Ridgeway Real Estate Development (you)	86.1%	11.4%	6.6 days	241 days

What it tells you: Cedarline passes gates first time most often and decides fastest; Ridgeway can learn from its gate preparation.

The screenshot shows the CortexPLM interface with the 'Benchmarking' section selected. The 'Across the group' tab is active, displaying a comparison for 'Atlas Infrastructure Holding' (4 organizations in the group). The interface includes filters for 'Track' (All tracks) and 'Project type' (All project types). A message states: 'Only aggregated indicators are exchanged between organizations of the group. No project, person or document of another organization is visible.' A checkbox 'Share our aggregated indicators with the organizations of our group' is checked. Below, a 'First-time Go rate' chart shows performance for four organizations: Cedarline Precast Systems (95%), Orvane Transit Group (87.1%), Palmgrove Residential Devel... (100%), and Ridgeway Real Estate Develop... (86.1%). A note indicates the median is 87.1%.

Organization	First-time Go rate
Cedarline Precast Systems	95%
Orvane Transit Group	87.1%
Palmgrove Residential Devel...	100%
Ridgeway Real Estate Develop...	86.1%

Each bar is an organization of your group. Higher is better. Median 87.1%.

Benchmarking across Atlas Infrastructure Holding, as seen by Ridgeway.

Step 4. Stop or resume sharing with the group

1. Still on **Across the group**, clear **Share our aggregated indicators with the organizations of our group**. A message confirms **Saved**.
2. Sign in as **exec@cedarline.example**, open **Benchmarking > Across the group**: Ridgeway now shows **Not shared** in every row.
3. Sign in again as **exec@ridgeway.example** and tick the box again to resume sharing.

Step 5. An independent organization

1. Sign in as **exec@meridale.example** (Meridale Health Network, **Group: No**) and open **Portfolio > Benchmarking**.
2. The tab **Within the organization** works as in Step 1. The tab **Across the group** explains that the organization belongs to no group, so there is no comparison.

The screenshot shows the CortexPLM interface with the 'Benchmarking' section selected. The 'Across the group' tab is active, displaying a message: 'Your organization does not belong to a group, so there is no group comparison. Benchmarking between organizations is limited to organizations of the same group; external benchmarking is out of scope.'

An independent organization has no group comparison.

13. Everyday Scenarios by Module

Short scenarios for the modules not used in the runs. Their tenancy is the one created in Run 1: **Group: No > Harbourview City Services > projects HAR-001 and HAR-002**; the password of its team is **Start#2026**. Where a justification is requested, type the text given or your own reason.

13.1 Record a business rule

Sign in as **process@harbourview.example**.

1. Open **Governance > Business rules** and select **Add rule**.
2. Type Rule ID **BR-PUB-101**, Triggering step **MP-33.2**, Condition **A service goes live without an accessibility audit**, Action **Block the T3 submission and notify the Quality Manager**.
3. Choose Rule type **Validation**, Severity **High**, type Owner **Quality Manager** and Process tag **MP-121**.
4. Select **Save**. In the justification window type **New accessibility policy 2026** and select **Save change**.

13.2 Add a control, change it and compare versions

Sign in as **process@harbourview.example**.

1. Open **Governance > Controls (COSO)** and select **Add control**.
2. Type Name **Accessibility audit before go-live**; choose COSO component **Control Activities**, Control type **Preventive**, Testing frequency **Per change**; type Owner **Quality Manager**; choose Effectiveness **Not tested**; type Process tag **MP-121**. Select **Save**, justification **New control for the accessibility policy**.
3. Open the new control, change Effectiveness to **Effective**, select **Save**, justification **Tested on HAR-001**.
4. Open it again, select the tab **Version history**. Under **Compare two versions** choose From **Version 1** and To **Version 2**: the row **effectiveness** is marked **Changed**.

13.3 Log a risk and read the heat map

Sign in as **process@harbourview.example**.

1. Open **Governance > Risks & opportunities** and select **Add**.
2. Choose Type **Risk**; type Name **Payment provider outage**, Category **Operational**, Likelihood **3**, Impact **4**, Owner **Finance Controller**; choose Status **Open**; type Process tag **MP-121**. Save with the justification **Identified during HAR-001 launch**.
3. In the heat map, select the cell likelihood 3 × impact 4: the list shows the risks scored 12.

13.4 See the governance of one process

Sign in as **process@harbourview.example**.

1. Open **Process design > Macro processes** and open **MP-121**.
2. Scroll to **Governance tagged to this process**: the rule BR-PUB-101, the new control and the new risk appear with the organization's other MP-121 records.

13.5 Build a RACSI activity

Sign in as **process@harbourview.example**.

1. Open **Governance > RACSI matrix** and select **Add activity**. Type Activity **Accessibility audit**, Process tag **MP-121**, then **Save**.
2. In the row, select + under **R** and type **Quality Manager**; select + under **A** and type **Product Manager**.
3. Select + under **A** again and type **Executive Sponsor**: the application refuses a second Accountable.

13.6 Track a custom KPI

Sign in as **process@harbourview.example**.

1. Open **Governance > KPIs**, tab **Custom KPIs**, and select **Add custom KPI**.
2. Type Name **Online completion rate**, Formula (plain language) **Requests completed online divided by all requests**, Target **85**, Unit **%**, Current value **81**, Owner **Product Manager**, Process tag **MP-12**. **Save**.
3. Open the tab **Built-in KPIs** and select **KPI-07 Design review first-pass yield**. Select **Record measurement**, type Period (YYYY-MM) **2026-09** and Value **88**, then **Save**. The trend line shows the measurement against the dashed target.

13.7 Edit and exchange a BPMN diagram

Sign in as **process@harbourview.example**.

1. Open **Process design > BPMN diagrams** and open the E2E-01 diagram.
2. In the **Shapes** palette on the left, drag **User task** onto the canvas and name it **Accessibility audit**. Select **Save diagram**.
3. Select **Export .bpmn** to download the file; **Import .bpmn** loads a file from any BPMN 2.0 tool.

13.8 Ask for an AI suggestion on a task

Sign in as **pm1@harbourview.example**.

1. Open **My tasks** and open a task in progress.
2. In the card **AI assistance**, keep the proposed use case, type **Focus on accessibility** in **Add details for the suggestion**, then select **Get suggestion**.
3. The suggestion is labelled AI-generated with its tier, source and references. Select **Accept**, **Modify** or **Reject**; the decision goes to the usage log (**AI & knowledge > AI use cases > Usage log**).

13.9 Search the knowledge base in your language

Sign in as **pm2@harbourview.example**.

1. In the language list of the top bar choose **Français**. Open **IA et connaissances > Base de connaissances** (tab **Rechercher**).

2. In the search box type **preuves checklist jalon**: the French reference articles are ranked first, followed by matching records of your organization.
3. Open the tab **Articles**: the list shows French articles by default; use the language filter to show **English** or العربية articles.

13.10 Create a project template and use it

Sign in as **process@harbourview.example**.

1. Open **AI & knowledge > Project templates** and select **Add template**. Type Name **Citizen e-service (Fast)**, Kind **Project**.
2. In **Default values (JSON)** type `{"offer_type":"Service","scores":{"strategic":2,"investment":1,"novelty":2,"regulatory":2,"market":1,"reach":2,"integration":1}}`. Save.
3. Sign in as **pm1@harbourview.example**, open **New project** and choose the template in **Start from a template**: type and scores are pre-filled and remain editable.

13.11 Plan with a WBS and a Gantt chart

Sign in as **pm1@harbourview.example**.

1. Open **Portfolio > WBS & Gantt** and select **New WBS**. Type Name **HAR-001 launch plan**, choose Project **HAR-001**, tick **Fill it with all tasks of this project, grouped by E2E run**, then **Create**.
2. Open the Gantt: bars show planned, in-progress, completed and overdue tasks with dependency lines.
3. Select **Export PDF** to download the chart.

13.12 Record a lesson learned

Sign in as **pm1@harbourview.example**.

1. Open **AI & knowledge > Lessons learned (REX)** and select **Add lesson**.
2. Type Title **Accessibility audit booked too late**, What went well **The audit found no blocking issue**, What did not go well **The audit slot was booked two weeks before go-live**, Root cause **No audit step in the launch plan**, Recommendation **Add the audit to UFT-05-02 Develop Detailed Launch Plan**; choose Category **Governance**; type Effectiveness rating **3**. Save.
3. The register view groups lessons by category and shows the average rating by month.

13.13 Export a report

Sign in as **exec@harbourview.example**.

1. Open **Reports & cockpits** and open **RPT-01**.
2. Select **PDF**, **Excel** or **Word**: the file is named with the report key and today's date.

13.14 Choose how you are notified

Sign in as **pm1@harbourview.example**.

1. Open **Notifications**, tab **Preferences**, and tick **E-mail** for **Gate submissions and decisions**.

2. Open the tab **Delivery log** to see each delivery with its status and attempts.

13.15 Add a user within the licence limit

Sign in as **admin@harbourview.example**.

1. Open **Administration > Users & roles** and select **Add user**.
2. Type Name **Nora Idrissi**, E-mail **nora.idrissi@harbourview.example**, choose Roles **Quality Manager**, Language **Français**, and type Password **Welcome#2026**. Save.
3. The seat counter increases by one. When all seats are used, the application refuses new users.

13.16 Place people in a project team with their roles (OBS)

Sign in as **admin@harbourview.example**.

1. Open **Administration > Organizations, OBS & teams**, tab **OBS & project teams of Harbourview City Services**.
2. In **Tree**, choose **HAR-001 Online Parking Permit Renewal**, then **Add node**. Type Name **HAR-001 project team**, Type **Project**, and Save.
3. Select **Add node** again: Name **Delivery team**, Type **Team**, Parent **HAR-001 project team**. Save, then open the new node.
4. Under **People and their role in this node**, choose Person **the Engineering Lead**, Role **R05 Engineering Lead**, type Role played here **Engineering lead**, and select **Add person**. Add the Quality Manager the same way with **Quality lead**.
5. The column **People and roles** now lists both people with the role they play. Seeded organizations already have a team tree for every project (steering committee, project management, delivery teams).

13.17 Back up the database

Sign in as **admin@cortexplm.example / Admin#2026 (platform administrator)**.

1. Open **Administration > Configuration & AI model** and scroll to **Backups**.
2. Select **Back up now**. The new file appears in the list; one automatic backup is also made every day.

13.18 Check the audit trail

Sign in as **auditor@harbourview.example**.

1. Open **Administration > Audit trail**, type **accessibility** in the search box and select **Search**.
2. Each line shows who changed what, when, the old and new values and the justification. The trail is read-only.

13.19 Create a second project in the same organization

Sign in as **pm1@harbourview.example**.

1. Tenancy: **Group: No > Harbourview City Services** (created in Run 1) > a second project.

2. Open **Portfolio > Innovation projects** and select **New project**. **Step 0** shows Organization **Harbourview City Services** and Belongs to a group? **No**.
3. Type Project name **Street Lighting Fault Reporting**, Description **Residents report broken street lights with a photo; crews receive work orders.**, Offer type **Service**, Executive Sponsor **the Executive Sponsor**.
4. Select **Decision matrix** to check the scores, then choose **2, 1, 2, 1, 1, 2, 1** (total 10) and keep **Fast Track · recommended**. Select **Create project**: the code is **HAR-002**.

13.20 Attach documents to a task

Sign in as **pm1@harbourview.example**.

1. Open **HAR-002**, card **E2E-01**, task **UFT-01-01 Capture Strategic Idea**.
2. In **Attachments**, select **Add files** and choose several files at once, for example a PDF, an Excel sheet and a photo, or drag them onto the box. Accepted: documents, spreadsheets, presentations, images, drawings and CAD (DWG, STEP, IFC), data (JSON, XML, BPMN), archives, audio and video, e-mails; up to 10 files of 25 MB.
3. Each file shows its type, size, author and date, with **Download** and **Remove**. A file of another type, such as **.exe**, is refused.

13.21 Add checklist items at a gate, from a template or by hand

Sign in as **pm1@harbourview.example**.

1. Open **Portfolio > Gate board**, filter **Open**, and open the **T-1** line of **HAR-002**.
2. In **Add to this checklist**, keep **From a template**, choose **T-1 · Fast Track · T-1 Fast Track standard checklist**: its items are already in the checklist, so **Add to checklist** adds nothing twice.
3. Choose **Manually**, type **Photo of the fault location is mandatory in the form**, tick **Mandatory**, and select **Add to checklist**. The item appears with Source **Added by ...**
4. Select **Save as template**, keep the name, tick **Link to the gate** only if every Fast Track T-1 gate should receive these items, and select **Save**.

13.22 Build a checklist template and link it to a gate

Sign in as **process@harbourview.example**.

1. Open **Process design > Checklist templates**. The grid shows, for each gate and track, how many templates exist and how many are linked.
2. Select **New template**. Type Name **Citizen service accessibility check**, choose Track **Fast**, Gate **T3**.
3. Type the items: **WCAG 2.1 AA audit report** (tick Mandatory and Evidence required), **Plain-language review of the forms** (Mandatory), **Screen-reader test on mobile**.
4. Tick **Link to the gate** and select **Save**. From now on, every Fast Track T3 gate of the organization opens with these items in addition to the standard checklist.

13.23 See where AI helps in the process design and run a use case

Sign in as **pm1@harbourview.example**.

1. Open **Process design** > **End-to-end processes**, tab **Tasks and AI**. Each task shows its active AI use cases: a grey badge is **Assistive AI**, an orange badge is **Augmented AI**.
2. Choose **Tasks with AI** in the filter. Select the badge **AIUC-01** on **UFT-01-01 Capture Strategic Idea**.
3. In the window, type **Street lighting and road safety** in **Context (optional)** and select **Get suggestion**.
4. Select **Modify**, shorten the text, and select **Save modified version**. The decision is recorded as Edited in the usage log. **Accept** and **Reject** work the same way.
5. Open **Process design** > **Macro processes**: the **Legend: Part** card explains the Part letters A to K, and the **AI** column shows the use cases of each macro process. Open **MP-01**: the badges appear next to the steps they support.

13.24 Create, change and delete an AI use case

Sign in as **data@harbourview.example**.

1. Open **AI & knowledge** > **AI use cases** and select **Add custom use case**.
2. Type Name **Fault photo classification**, choose Tier **Assistive**, type Linked to **UFT-01-01**, Human checkpoint **The service agent confirms the fault type**. Select **Create**: it starts inactive and pending approval.
3. Sign in as **process@harbourview.example**, open the use case, select **Approve**, tick **Active for the organization**: the badge now appears on UFT-01-01.
4. Open it again, change the Trigger, type **Clarified trigger** in the change note and select **Save new version**. To remove it, select **Delete** (custom use cases only; seeded ones are deactivated instead).

13.25 Choose the live AI model

Sign in as **pm1@harbourview.example**.

1. Open **Settings** (or **Administration** > **Configuration & AI model**) and find **Live AI model (optional)**.
2. Choose AI provider **Anthropic Claude**, then a Model in the list, for example **Claude Opus 5 (default)**. To use another model, choose **Custom model...** and type its name.
3. Paste your API key and select **Test connection**; the message says whether the key and model work. Select **Save connection**. The key stays in this browser; without a key the built-in engine answers.
4. For a company gateway, choose **Custom endpoint** and type its URL in **Endpoint**.

13.26 Look at a group portfolio

Sign in as **exec@ridgeway.example / Demo#2026**.

1. Open **Portfolio > Groups, organizations & projects**. The tree shows **Group: Yes > Atlas Infrastructure Holding** with its organizations; open one to list its projects (read-only outside your organization).
2. Open **Portfolio > Portfolio overview**. Choose Group **Atlas Infrastructure Holding**, then Organization **Cedarline Precast Systems**, or add several projects with **Add a project to the set**.
3. Each row is a project, each column an E2E process. Read the legend: Completed, In progress, At gate, On hold, Stopped, Not started, Not in track. Select **Export CSV** to download the grid.
4. Open **Portfolio > Innovation projects** and filter by Group, Organization and Project in the same way.

13.27 Work on a BPMN diagram in full screen

Sign in as **process@harbourview.example**.

1. Open **Process design > BPMN diagrams** and open **E2E-02**.
2. Select **Full screen**. The diagram fills the window with the **Shapes** palette on the left, grouped as Tools, Events, Activities, Gateways, Data and Participants.
3. Use the zoom slider or **Fit to screen**; slide the palette away with its button to gain space. Select **Back to the page** (or press Escape) to return.
4. Changing the diagram documents the process; it does not change the tasks of running or future projects, which come from the process reference.

CortexPLM Harbourview City Services English Salma Mansouri Process Owner / Track Administrator

PROCESS DESIGN - MP-122

Checklist templates

A library of gate checklists per gate and per track. A template linked to its gate is copied into the checklist when the gate opens; any template can also be added from the gate screen.

[+ New template](#)

Templates by gate and track
Click a cell to list its templates. The link icon marks templates copied automatically when the gate opens.

Gate	Decision question	Full Track	Light Track	Fast Track
T-1	Is the idea strategically aligned and worth a funded opportunity study?	1 templates 🔗 1 linked	1 templates 🔗 1 linked	2 templates 🔗 1 linked
T0	Should we commit investment to design and development?	1 templates 🔗 1 linked	1 templates 🔗 1 linked	1 templates 🔗 1 linked
T1	Is the design validated and ready to be built?	1 templates 🔗 1 linked	1 templates 🔗 1 linked	Not in track
T2	Is the product complete, tested and operationally ready?	1 templates 🔗 1 linked	1 templates 🔗 1 linked	Not in track
T3	Are we ready to go live?	2 templates 🔗 1 linked	2 templates 🔗 1 linked	2 templates 🔗 2 linked
T4	Is post-launch performance stable enough for steady-state review?	1 templates 🔗 1 linked	Not in track	Not in track
T5	Should the product continue, be relaunched, or be retired?	2 templates 🔗 1 linked	2 templates 🔗 1 linked	Not in track
T6	Is the product fully and compliantly retired?	1 templates 🔗 1 linked	Not in track	Not in track

Checklist templates by gate and track.

PROCESS DESIGN REFERENCE

End-to-end processes

9 E2E processes, 81 user-facing tasks, 8 exit gates. E2E-09 runs in parallel with all others.

Processes **Tasks and AI**

Tasks and where AI is used
54 of 81 tasks are supported by at least one active AI use case.

Assistive AI suggests; a person decides and does the work **Augmented AI** drafts the result; a person reviews and approves it

Only active use cases are shown. Select a badge to run it, then Accept, Modify or Reject.

Q Filter rows All tasks 81 rows CSV

E2E ID	Task ID	Task	Responsible	AI
E2E-01	UFT-01-01	Capture Strategic Idea MP-01 Portfolio, MP-03 Requirements	Product Manager	AIUC-01 - Assistive AI AIUC-02 - Assistive AI AIUC-03 - Assistive AI
E2E-01	UFT-01-02	Assess Market Opportunity MP-01 Portfolio, MP-17 CX	Marketing	AIUC-01 - Assistive AI AIUC-02 - Assistive AI
E2E-01	UFT-01-03	Build Preliminary Business Case MP-35 Cost, MP-01 Portfolio	Finance	AIUC-01 - Assistive AI AIUC-02 - Assistive AI AIUC-08 - Assistive AI
E2E-01	UFT-01-04	Assess Risks & Compliance MP-30 Regulatory, MP-32 IP/Legal	Compliance Officer	AIUC-11 - Augmented AI
E2E-01	UFT-01-05	Describe High-Level Capability MP-03 Requirements, MP-04 Design	Engineering	AIUC-03 - Assistive AI AIUC-05 - Assistive AI

Tasks and AI: where Assistive AI and Augmented AI support each task.

AIUC-01 Idea similarity and de-duplication

Assistive AI - Human checkpoint: Product Manager confirms any merge of ideas

Context (optional)
Street lighting and road safety

Get suggestion

AI-generated. A person must review it. Assistive Built-in deterministic engine Confidence 95%

Possible duplicates or related ideas (similarity score):
- HAR-002 Street Lighting Fault Reporting (0.57)
Confirm any merge before acting (human checkpoint).

Human checkpoint: Product Manager confirms any merge of ideas
Grounded on: HAR-002 HAR-002 Street Lighting Fault Reporting

Accept Modify Reject

Running AIUC-01 from its badge: Accept, Modify or Reject.

CortexPLM Harbourview City Services English Youssef Carpentier Product Manager

HOME

- Dashboard
- My tasks
- Alerts
- Notifications

PORTFOLIO

- Groups, organizations & projects
- Portfolio overview
- Innovation projects
- Gate board
- WBS & Gantt
- Benchmarking

PROCESS DESIGN

- End-to-end processes
- Macro processes**
- BPMN diagrams
- Checklist templates
- Track configuration
- Phase-gate reference

PROCESS DESIGN REFERENCE

Macro processes

69 reusable building blocks, each described as a SIPOC card with 727 tasks and steps.

Filter rows All categories

69 rows CSV

ID	Macro process	Part	Owner role	Steps	AI	Used
MP-01	Product Portfolio & Strategy Management Align product development with corporate strategy; optimize resource allocation; ensure a profitable, market-driven product portfolio.	A	Portfolio Manager	11	AIUC-01 AIUC-02	E2E-01, E2E-02, E2E-08, E2E-09
MP-02	Product Data & Document Management Provide a secure, single source of truth for all product-related data and documents.	A	Engineering Lead	11	AIUC-07	Platform enable all E2E process (proprietary classification)
MP-03	Requirements & Systems Engineering Capture, manage, and trace all product	A	Engineering Lead	10	AIUC-03	E2E-01, E2E-02, E2E-08

Legend: Part

The Part letter is the section of the Process Design Reference the macro process comes from. Parts F to H are not used.

Part	Category	What it covers	Macro processes
A	Product Lifecycle	Macro processes of the physical product lifecycle	12
B	Service Lifecycle	Macro processes of the service lifecycle	10
C	Cross-Cutting & Governance	Governance, quality, compliance and support processes used by every lifecycle	15
D	Strategic Differentiators	Processes that differentiate the offer (sustainability, digital thread, analytics)	9

Macro processes with the Part legend and the AI column.

E2E-02 Idea-to-Business Proposal Export .bpmn Import .bpmn Save diagram 41% Back to the page

Shapes

Click a shape then click the canvas, or drag it onto the canvas.

TOOLS

- Hand tool
- Lasso tool
- Create/remove space tool
- Global connect tool

EVENTS

- Start event
- Intermediate/boundary event
- End event
- Timer start event
- Message start event
- Timer event
- Terminate end event

ACTIVITIES

- Task
- Expanded sub-process
- User task
- Service task

BPMN diagram showing a flow from Start event to End event, including various intermediate events and activities.

BPMN.IO

Shapes palette on the left (slide it away with its button). Scroll or use the slider to zoom; drag the background to move around.

A BPMN diagram in full screen with the Shapes palette.

CortexPLM Harbourview City Services English Youssef Carpentier Product Manager

HOME

- Dashboard
- My tasks
- Alerts
- Notifications

PORTFOLIO

- Groups, organizations & projects
- Portfolio overview
- Innovation projects
- Gate board
- WBS & Gantt
- Benchmarking

PROCESS DESIGN

- End-to-end processes
- Macro processes
- BPMN diagrams
- Checklist templates
- Track configuration
- Phase-gate reference

Interface language

English

Navigation bar

Place the menu on any side of the screen. Unpinned, it slides away and opens when you point at its edge.

Left Right Top Bottom

☒ Keep the menu pinned open

Live AI model (optional) Built-in engine

Without a key, the application uses its built-in, rule-based suggestions. With a key, suggestions come from the model you choose. The key stays in this browser.

AI provider (LLM) Anthropic Claude **Model** Custom model...

Choose a model, or "Custom model" to type any other model name.

Custom model name * claude-...

API key *

Endpoint https://

Leave empty for the provider default.

Save connection Test connection Remove connection

Live AI model: provider, model list with a custom choice, key and connection test.

CortexPLM Harbourview City Services English Paul Blanc Platform Administrator

HOME

- Dashboard
- My tasks
- Alerts
- Notifications

PORTFOLIO

- Groups, organizations & projects
- Portfolio overview
- Innovation projects
- Gate board
- WBS & Gantt
- Benchmarking

PROCESS DESIGN

- End-to-end processes
- Macro processes
- BPMN diagrams
- Checklist templates
- Track configuration
- Phase-gate reference

ADMINISTRATION

Organizations, OBS & teams

Groups contain organizations; each organization is an isolated tenant with its own projects, users and data.

Organizations Groups **OBS & project teams of Harbourview City Services**

Organizational breakdown structure + Add node

Sites, departments and teams. Counts show linked records so ownership is visible at a glance.

Tree HAR-001 Online Parking Permit Renewal

Each organization has its own tree; a project can also have its own team tree.

Filter rows 2 rows CSV

Node ¹	Type ¹	People and roles ¹	Users ¹	Projects ¹	Rules ¹	Controls ¹	Risks ¹	RACSI ¹	BPMN ¹	REX ¹
HAR-001 project team	Project									
Delivery team	Team	Sara Benali - Engineering lead Leila Ouazzani - Quality lead								

A project team tree with the people and the role each one plays.

14. Messages You May Meet

Message	Why	What to do
Evidence is required before this item can be marked complete (BR-005).	A mandatory checklist item has no evidence.	Type an evidence reference or attach a file, then select Mark complete .
Gate submission blocked: ... mandatory checklist item(s) are open (BR-004).	The checklist is not finished.	Complete or waive the mandatory items, then complete the checklist task.
The person accountable for the project cannot record its gate decision (CTL-01).	You own the project.	Ask the Executive Sponsor or a Gate Review Board member to decide.
Go-live is blocked: final regulatory validation reports incomplete approvals (BR-030).	UFT-05-08 answered No .	Once the approvals are obtained, open Final Regulatory Validation , select Reopen task , type the reason, answer Yes , complete the task and submit the gate again.
Strategic-fit score below 50: the idea is parked (BR-001).	UFT-01-02 scored below 50.	The project goes On Hold for 90 days. Select Resume project after re-review.
This e-mail domain is already used by another organization.	Another organization already has accounts @ that domain.	Choose another e-mail domain for the starting team.
File type not accepted: ...	The file is not in the list of accepted types (for example .exe).	Convert it (for example to PDF) or zip it.
Seeded use cases cannot be deleted. Deactivate it instead.	Only custom AI use cases can be deleted.	Clear Active for the organization instead.
... belongs to ... You can see it here and in the portfolio overview; only its organization can open it.	The project belongs to another organization of your group.	Ask a person of that organization, or read it in the portfolio overview.
This E2E run has not started yet (observation period, Rule R1).	Light Track performance review is scheduled after launch.	Wait for the start date, or ask the Track Administrator to shorten the observation period.
