POWERACT
CONSULTING

CASE STUDY · HEALTHCARE · PRIVATE CLINICS

Training engineering for AI skills, end to end



Santéora Private Clinics Group: the real flow of the 35 end-to-end processes run in CortexSkills — macro processes, tasks and steps

Prepared by POWERACT Consulting · 16 Oct 2026

AGENDA

What this case study covers



The client and the project



How CortexSkills structures the work



Phase 1 — Scope & evidence



Phase 2 — Diagnosis



Phase 3 — Training Engineering Report & plan



Phase 4 — Design & delivery



Phase 5 — Evaluation, compliance & impact



Phase 6 — Talent, knowledge & continuous improvement



Phase 0 — Enablers (run across all phases)



Results and next steps

EXECUTIVE SUMMARY

35 processes run end to end, 100 % of tasks completed

18 Apr 2026 – 28 Sept 2026 · 27 people involved · every figure below is read from the application

35
end-to-end processes (33 standard + 2 healthcare)

53
macro processes involved

265
tasks completed, none overdue

463
steps executed



Scope and evidence first

40 stakeholders registered, 24 AI-generated questions validated, 187 responses collected before any decision.



A plan approved on facts

23 needs grouped into 6 themes; net budget 1,330,000 MAD approved by the Steering Committee.



Delivery measured up to impact

Test scores from 48 % to 81 %; 9 of 11 supervisors apply the routine at day 30; ROI 22 %.

THE CLIENT

Santéora Private Clinics Group

Training engineering cycle focused on AI skills for Healthcare Providers: scope, evidence, diagnosis, report, delivery, evaluation and continuous improvement.

Fact	Value
Sector	Healthcare providers — private clinics
Size	2,600 employees, large organization
Headquarters	Casablanca, Morocco
Project	AI Skills Full Run 2026 — Santéora Private Clinics Group
Focus	AI skills
Period	18 Apr 2026 – 28 Sept 2026
Languages	French, English, Arabic



Strategic objectives entered in the application

- SO-1: AI triage and clinical decision support used by 80% of Clinical Care & Nursing staff by end 2026 (owner: Operations Director, measured quarterly).
- SO-2: zero major audit findings on ISO 7101.
- Priority competency families: AI triage and clinical decision support; AI medical imaging assistance; ISO 7101 compliance. Target level 3 (Autonomous) for supervisors.

HOW CORTEXSKILLS STRUCTURES THE WORK

Four levels, from the value stream down to the step that is typed

End-to-end process

E2E-33 · Questionnaire-to-Response-Collection

35 run in this case

Macro process

MP-54 · Questionnaire Design, Distribution & Response Collection

53 involved

Task

UFT-33-04 · Allocate RACSI

265 completed

Step

MP-54.4 · Allocate RACSI per section

463 executed

What was entered at this step

Section 'Digital practices': R L&D Analyst, A Head of L&D, C Consultant PM, S IT, I CHRO (one Accountable only).

Each step is filled in one of three ways: typed or pasted, loaded from a template, or proposed by AI and validated by a person.

THE PROJECT PATH

Six phases closed by approval gates, with enablers running throughout

1 Scope & evidence

E2E-32 · E2E-33 · E2E-19 · E2E-24

4 processes · 37 tasks

G1 — Scope & evidence approved

2 Diagnosis

E2E-20 · E2E-25 · E2E-26 · E2E-27 · E2E-28 · E2E-29 · E2E-02 · E2E-21

8 processes · 62 tasks

G2 — Diagnostic validated

3 Training Engineering Report & plan

E2E-01 · E2E-03 · E2E-30 · E2E-22 · E2E-23 · E2E-16 · HCPR-E2E-02

7 processes · 50 tasks

G3 — Report & roadmap approved

4 Design & delivery

E2E-04 · E2E-05 · E2E-06 · E2E-13 · E2E-14

5 processes · 39 tasks

G4 — Delivery readiness

5 Evaluation, compliance & impact

E2E-07 · E2E-08 · E2E-09 · HCPR-E2E-01

4 processes · 26 tasks

G5 — Evaluation & impact validated

6 Talent, knowledge & continuous improvement

E2E-10 · E2E-11 · E2E-12 · E2E-31


4 processes · 30 tasks

G6 — Closure & continuous improvement

Phase 0 — Enablers, across all phases: E2E-15 Data-AI-Integration · E2E-17 Change-to-Adoption · E2E-18 Quality-Risk-Improvement

IN THE APPLICATION

The project cockpit: 265 of 265 tasks completed

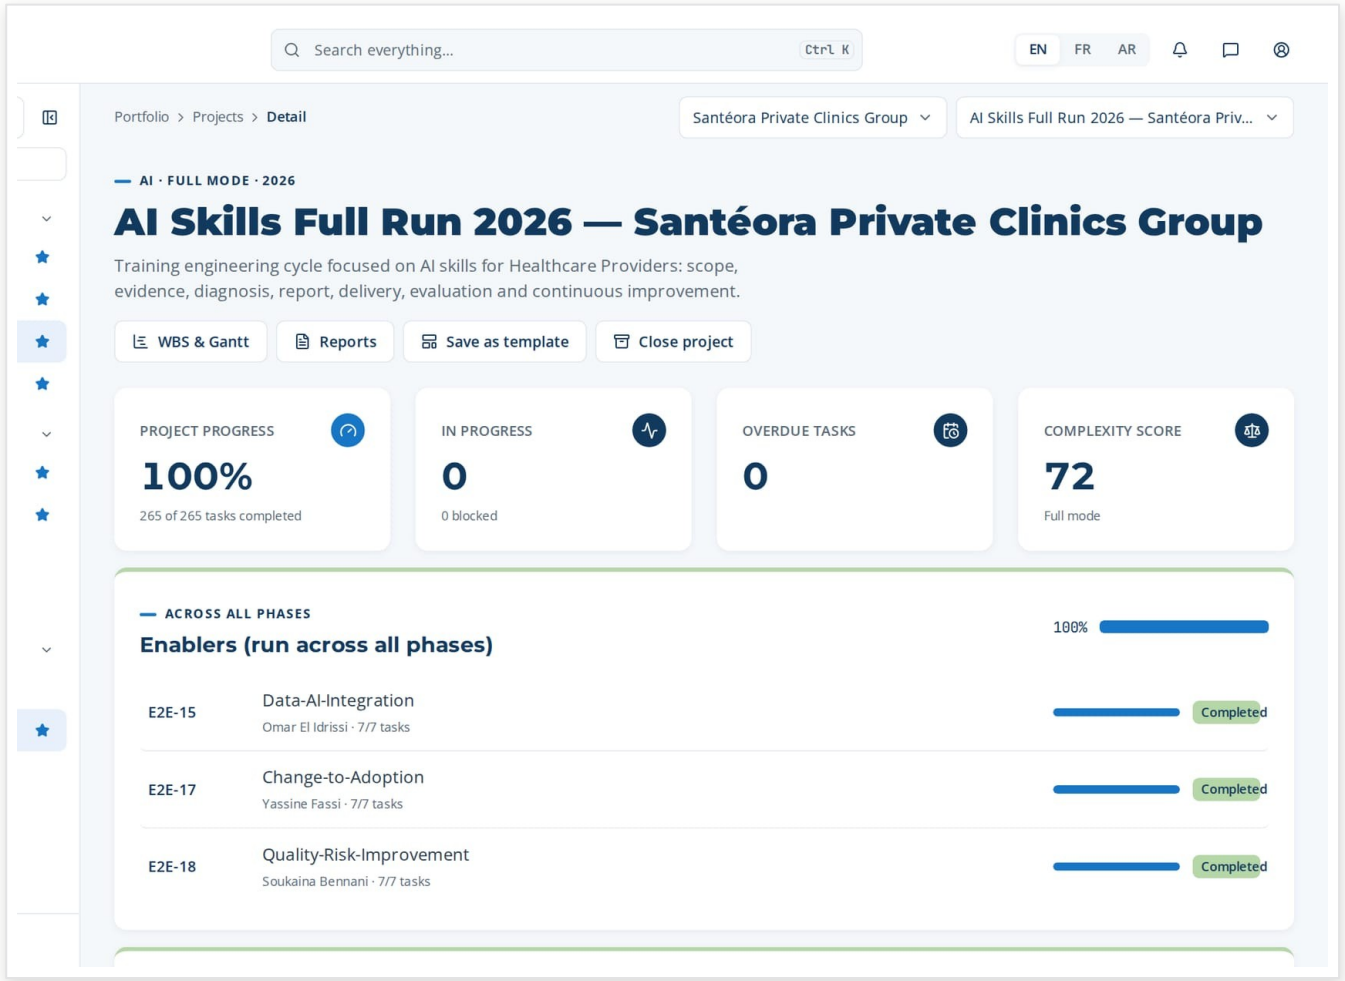

Progress per phase

Each phase lists its processes, owners and task counts.

No overdue task


Due dates, owners and evaluators are set per task.

Complexity score 72

Full mode chosen from the scoring of the project.

IN THE APPLICATION


Work breakdown and Gantt chart of the run

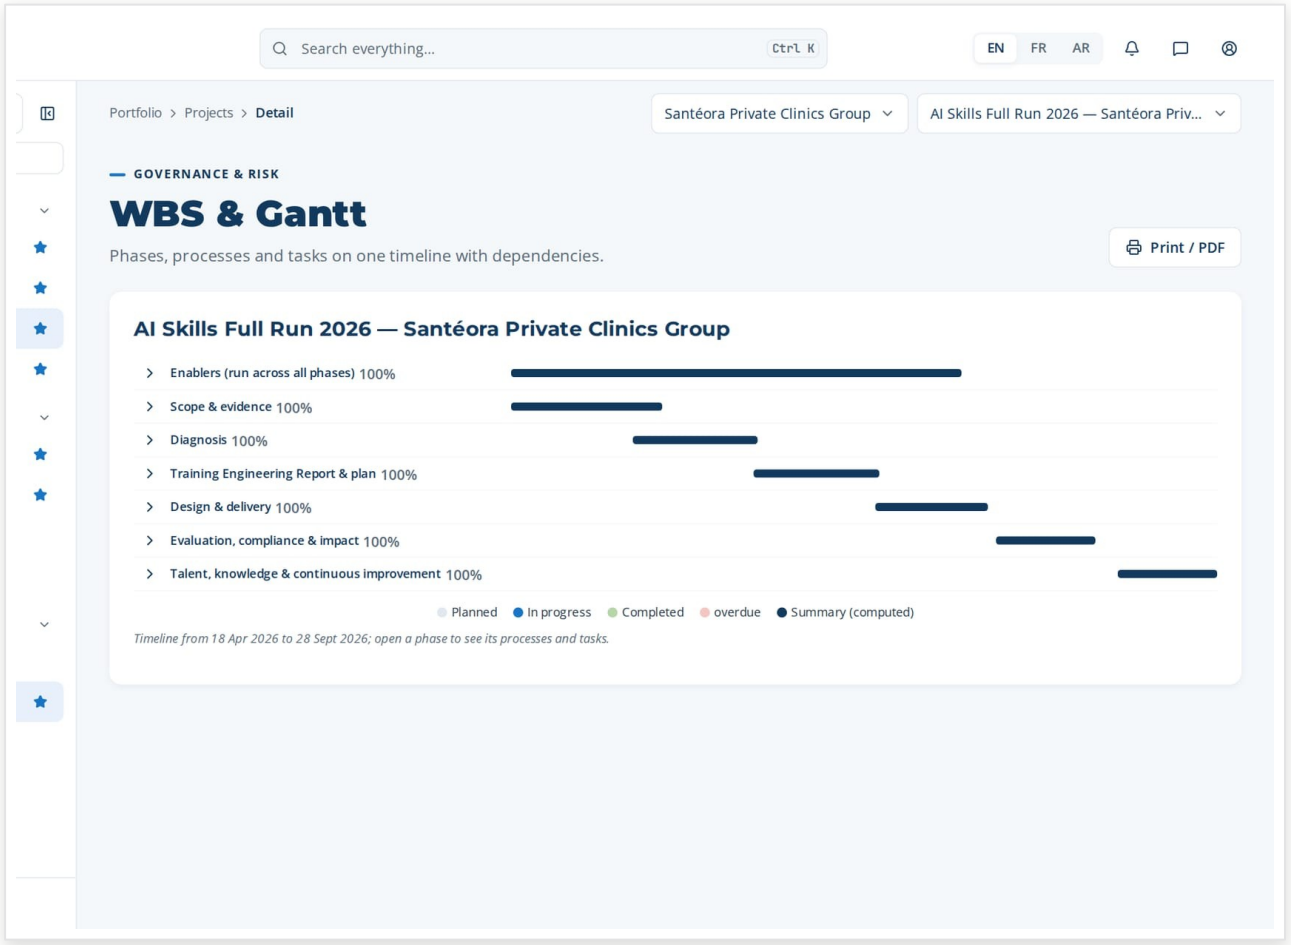

Phases, processes and tasks on one timeline, with their dependencies.

IN THE APPLICATION

How the processes feed each other

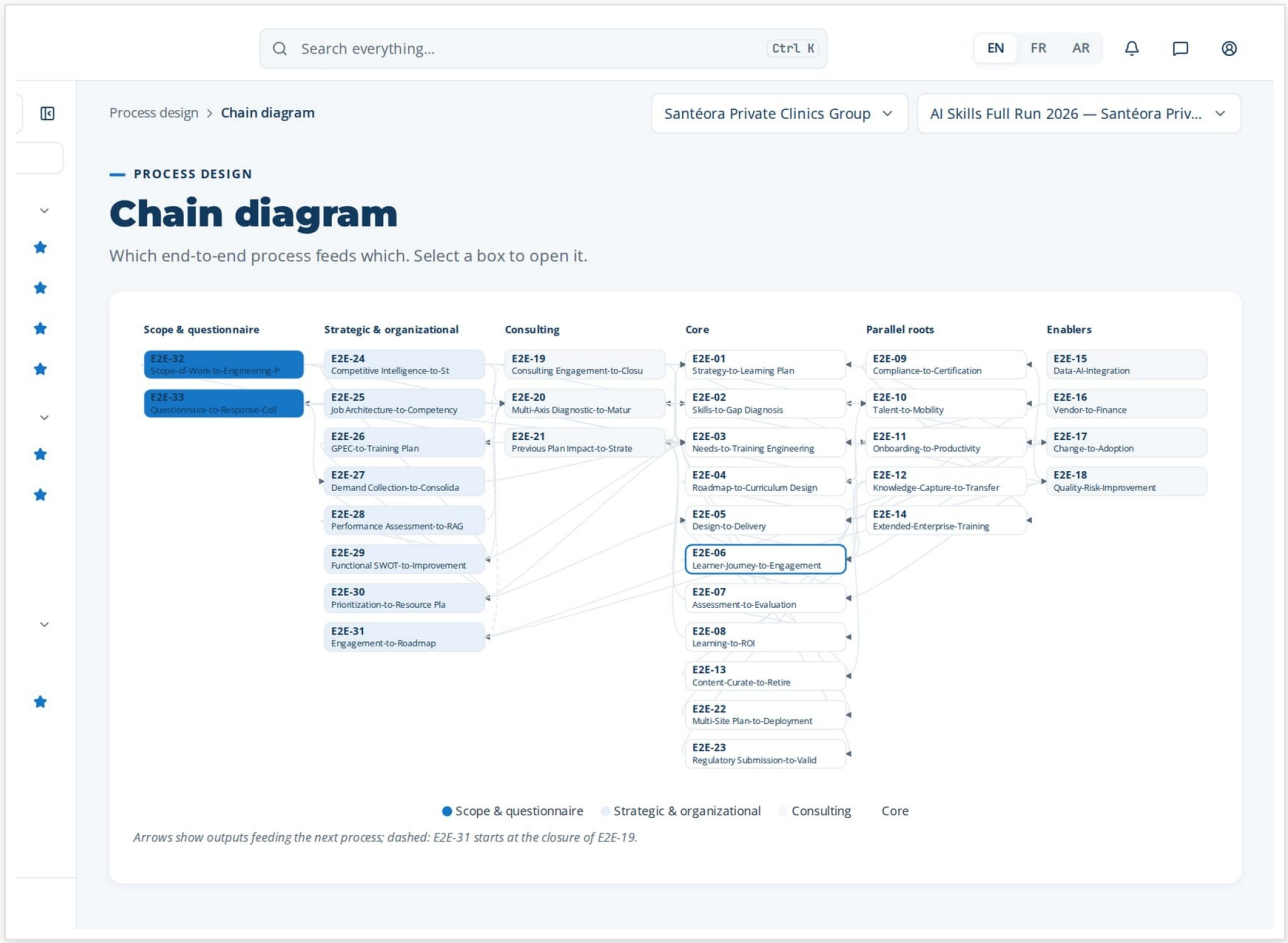

Chain diagram: the output of each process is an input of the next ones.

01

PHASE 1

Scope & evidence

4 processes · 37 tasks · 52 steps

18 Apr 2026 – 23 May 2026

Closed by G1 — Scope & evidence approved

E2E-32 Scope-of-Work-to-Engineering-Plan

E2E-33 Questionnaire-to-Response-Collection

E2E-19 Consulting Engagement-to-Closure

E2E-24 Competitive Intelligence-to-Strategy

Scope-of-Work-to-Engineering-Plan

Define and approve the structured scope of work and stakeholder register


TRIGGER
New training engineering engagement, annual plan cycle, or executive request.

END STATE
Approved Scope of Work with criteria matrix and stakeholder register released to questionnaire design (E2E-33) and needs analysis (E2E-03).

9 tasks · 12 steps
26 days · 4 owners · 100 %

Macro processes: MP-53 Scope of Work Definition & Management · MP-01 Strategy & Governance Alignment · MP-44 Job Architecture & Position Description Management · MP-45 GPEC & HR Strategic Integration (Forward Planning of Jobs and Skills) · MP-03 Needs Analysis & Diagnosis

Task	Steps executed	Owner · done	What was entered
UFT-32-01 **Define scope frame**	**MP-53.1** Define scope frame (Group Yes/No) **MP-53.2** Select Organization	Hicham Naciri 20 Apr 2026	Group scope: No. Organization: Santéora Private Clinics Group.
UFT-32-02 **Select sector**	**MP-53.3** Select sector	Yassine Berrada 23 Apr 2026	Sector: Healthcare Providers.
UFT-32-03 **Select decision levels**	**MP-53.4** Select decision level (MS/MO/OP/Custom)	Yassine Berrada 26 Apr 2026	Decision levels: MS, MO, OP (no custom level).
UFT-32-04 **Map functions × decision levels**	**MP-53.5** Map functions × decision level	Yassine Berrada 29 Apr 2026	Matrix: Clinical Care & Nursing × MS/MO/OP; Quality × MO/OP; Finance × MS/MO; HR × MS/MO.
UFT-32-05 **Select focus and add custom criteria**	**MP-53.6** Select focus (All/Digital/AI/Custom) **MP-53.7** Add custom criteria	Hicham Naciri 2 May 2026	Focus: AI. Custom criterion: 'Readiness for AI triage and clinical decision support' (weight 2.00).
UFT-32-06 **Identify stakeholders**	**MP-53.8** Identify stakeholders	Karim Chraibi 5 May 2026	Register 40 stakeholders: name, role, function, level, site, preferred channel (Email, Face-to-Face or Hybrid).

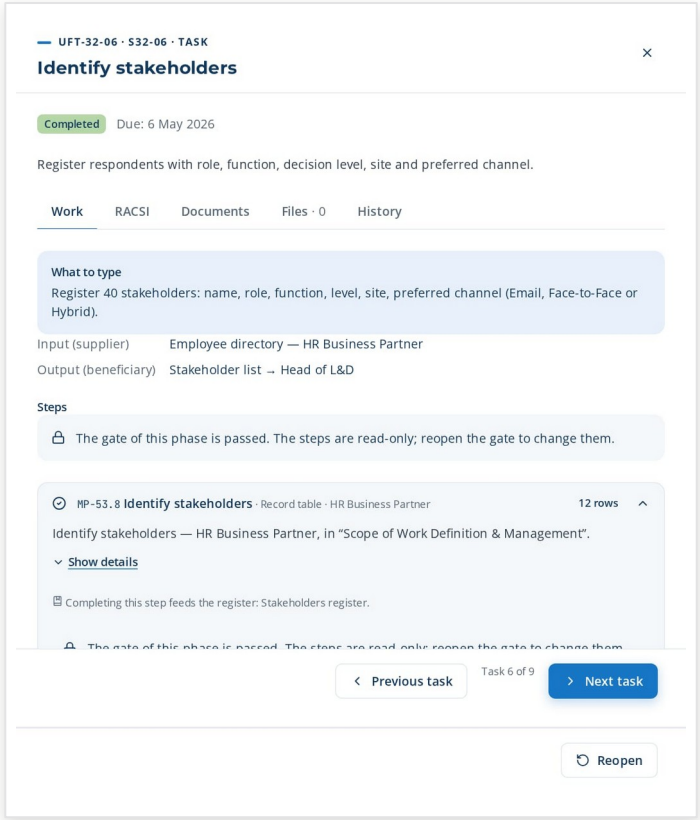


UFT-32-06 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Scope-of-Work-to-Engineering-Plan (continued)

Task	Steps executed	Owner · done	What was entered
UFT-32-07 **Validate scope**	**MP-53.9** Validate and approve scope	Hicham Naciri 8 May 2026	Validation: every function in scope has at least 3 stakeholders; completeness 100%.
UFT-32-08 **Approve scope**	**MP-53.9** Validate and approve scope **MP-53.10** Publish scope and register stakeholders	Mehdi Lahlou 11 May 2026	Approval status: Approved (version 1). Justification: scope aligned with SO-1 and SO-2.
UFT-32-09 **Publish scope and register stakeholders**	**MP-53.10** Publish scope and register stakeholders	Yassine Berrada 14 May 2026	Generate the SOW document (RPT-033) and release scope and stakeholders to the questionnaire studio.

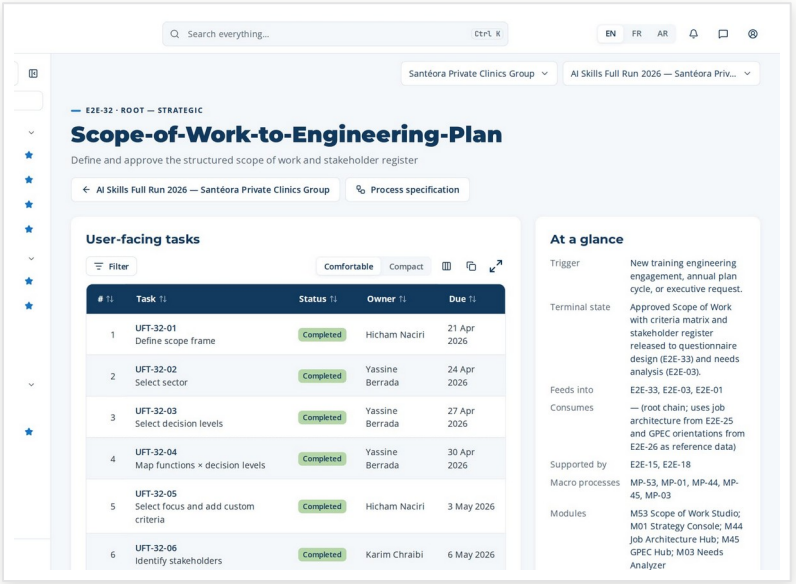

The page of E2E-32 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-53 Scope of Work Definition & Management
- MP-01 Strategy & Governance Alignment
- MP-44 Job Architecture & Position Description Management
- MP-45 GPEC & HR Strategic Integration (Forward Planning of Jobs and Skills)
- MP-03 Needs Analysis & Diagnosis

Feeds into

E2E-33, E2E-03, E2E-01

Supported by

E2E-15, E2E-18

Questionnaire-to-Response-Collection

Design, distribute and collect questionnaire responses across channels


TRIGGER
An approved Scope of Work becomes available (end of E2E-32).

END STATE
Consolidated, validated questionnaire response dataset feeding needs analysis (E2E-03), diagnostic (E2E-20) and demand collection (E2E-27).

12 tasks · 13 steps
35 days · 3 owners · 100 %

Macro processes: MP-54 Questionnaire Design, Distribution & Response Collection · MP-03 Needs Analysis & Diagnosis · MP-37 Multi-Axis Organizational Diagnostic · MP-46 Training Demand Collection & Consolidation

Task	Steps executed	Owner · done	What was entered
UFT-33-01 **Select questionnaire template**	**MP-54.1** Select questionnaire template by focus	Yassine Berrada 20 Apr 2026	Template: 'AI needs — Healthcare Providers' in the user's language, 5 sections.
UFT-33-02 **Elaborate questionnaire**	**MP-54.2** Elaborate questionnaire (Load/AI/Manual)	Yassine Berrada 23 Apr 2026	Elaboration mode: AI. 24 questions generated from the approved Scope of Work.
UFT-33-03 **Tailor and validate content**	**MP-54.3** Tailor to sector and focus	Yassine Berrada 26 Apr 2026	Validate each question; reword 5 with Clinical Care & Nursing vocabulary; delete 2 duplicates.
UFT-33-04 **Allocate RACSI**	**MP-54.4** Allocate RACSI per section	Hicham Naciri 29 Apr 2026	Section 'Digital practices': R L&D Analyst, A Head of L&D, C Consultant PM, S IT, I CHRO (one Accountable only).
UFT-33-05 **Select distribution channels**	**MP-54.5** Select distribution channels	Hicham Naciri 2 May 2026	Channels: MS and MO by Email; OP Face-to-Face with tablets; night shift Hybrid.
UFT-33-06 **Distribute questionnaire**	**MP-54.6** Distribute to stakeholders	Hicham Naciri 5 May 2026	Distribute to 40 stakeholders; 40 dispatches logged.

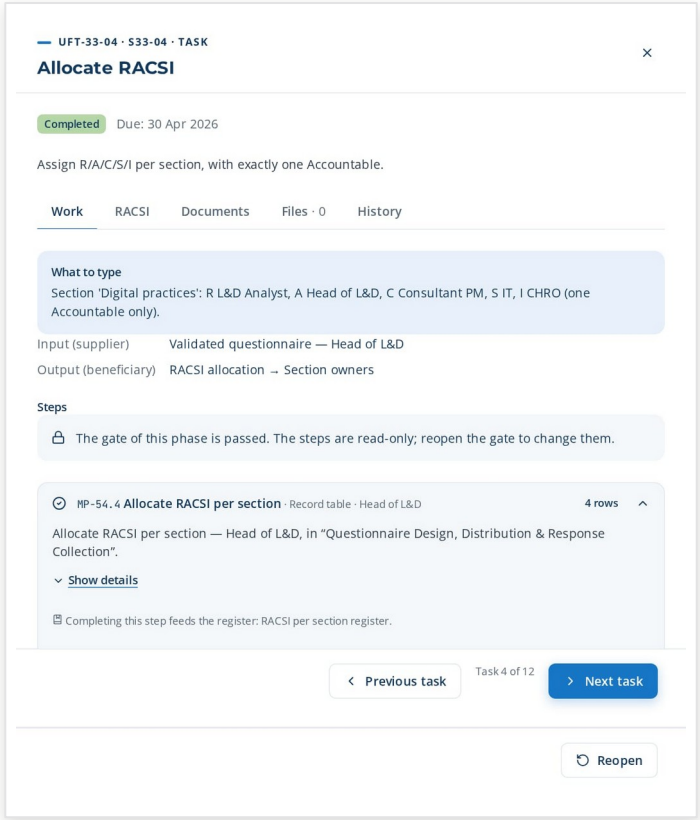


UFT-33-04 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Questionnaire-to-Response-Collection (continued)

Task	Steps executed	Owner · done	What was entered
UFT-33-07 **Send reminders**	**MP-54.7** Send reminders on cadence	Hicham Naciri 8 May 2026	Reminder 1 on day 5 to 17 non-respondents; reminder 2 on day 10 to 8.
UFT-33-08 **Collect responses**	**MP-54.8** Collect responses	Soukaina Bennani 11 May 2026	Responses: 34 collected (22 online, 12 offline synchronised).
UFT-33-09 **Validate completeness**	**MP-54.9** Validate completeness and consent	Yassine Berrada 14 May 2026	Completeness: 31 complete, 3 incomplete flagged.
UFT-33-10 **Consolidate responses**	**MP-54.10** Consolidate responses	Yassine Berrada 17 May 2026	Consolidated dataset: 31 responses, 24 questions, by function and level.
UFT-33-11 **Check consent and release dataset**	**MP-54.11** Feed responses to needs analysis and diagnostic **MP-54.12** Report on response rate and engagement	Yassine Berrada 20 May 2026	Consent given for 31 of 31 stored responses; release to needs analysis, diagnostic and demand collection.
UFT-33-12 **Report on response and engagement**	**MP-54.12** Report on response rate and engagement	Yassine Berrada 23 May 2026	Response rate 85%; engagement rate 78%; completeness 91% (RPT-034).

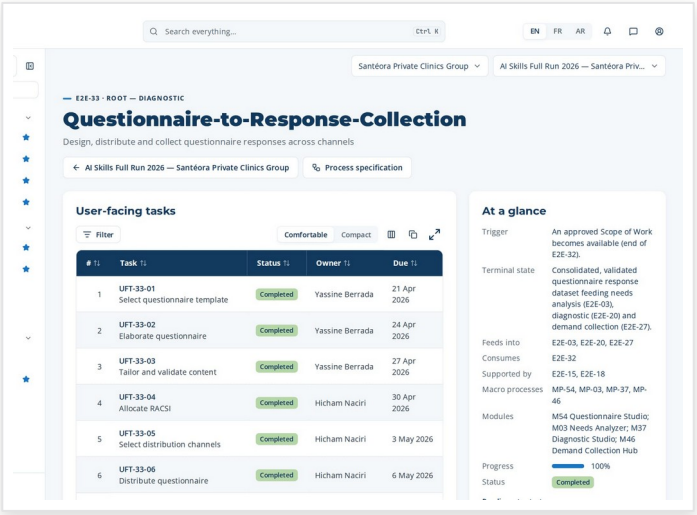

The page of E2E-33 in CortexSkills: its tasks, owners and due dates, and the process card.

Feeds into
E2E-03, E2E-20, E2E-27
Supported by
E2E-15, E2E-18

Consulting Engagement-to-Closure

Manage full consulting engagement lifecycle


TRIGGER
Client purchase order or engagement request received.

END STATE
Engagement closed with client acceptance and REX recorded.

9 tasks · 15 steps
26 days · 2 owners · 100 %

Macro processes: MP-36 Consulting Engagement Management · MP-01 Strategy & Governance Alignment · MP-19 Change Management & Adoption · MP-20 Quality, Risk & Continuous Improvement

Task	Steps executed	Owner · done	What was entered
UFT-19-01 **Register engagement and purchase order**	**MP-36.1** Register engagement and purchase order	Nadia Lahlou 20 Apr 2026	Engagement 'Training engineering 2026 — Santéora Private Clinics Group', PO-CL-221, 45 consulting days.
UFT-19-02 **Hold kickoff meeting**	**MP-36.2** Hold kickoff meeting	Nadia Lahlou 23 Apr 2026	Kickoff held on 10 February with HR Director, Head of L&D and 4 function heads.
UFT-19-03 **Draft meeting minutes**	**MP-36.3** Draft meeting minutes	Nadia Lahlou 26 Apr 2026	Review the AI minutes: 6 decisions, 9 actions, RACSI extracted; correct 1 owner name.
UFT-19-04 **Align with client strategy**	**MP-01.1** Record corporate strategic objectives **MP-01.2** Link objectives to functions and sites	Nadia Lahlou 29 Apr 2026	Client objectives recorded: AI triage and clinical decision support and ISO 7101 compliance for Clinical Care & Nursing.
UFT-19-05 **Plan engagement work breakdown**	**MP-36.4** Plan engagement work breakdown	Nadia Lahlou 2 May 2026	WBS: 6 phases, 14 deliverables, Gantt from February to November.

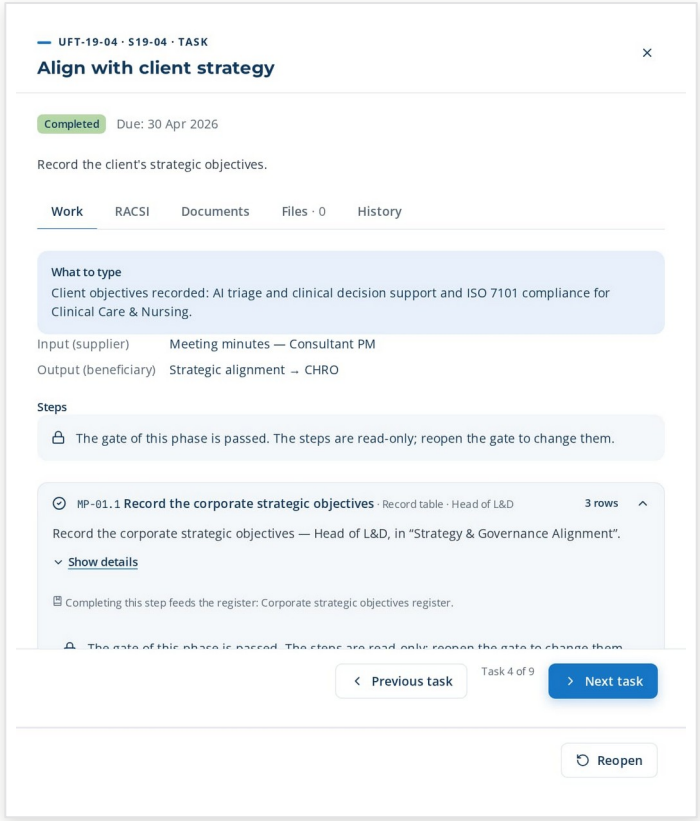


UFT-19-04 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Consulting Engagement-to-Closure (continued)

Task	Steps executed	Owner · done	What was entered
UFT-19-06 **Plan change support**	**MP-19.1** Assess change impact **MP-19.2** Build adoption plan	Yassine Fassi 5 May 2026	Change plan: 3 sponsor messages, champion network, 2 town-halls.
UFT-19-07 **Track engagement deliverables**	**MP-36.5** Track engagement deliverables **MP-20.5** Run periodic quality review	Nadia Lahlou 8 May 2026	Deliverables: 9 of 14 delivered on time, 1 late (SWOT), 4 planned.
UFT-19-08 **Deliver final report and obtain acceptance**	**MP-36.6** Deliver final report **MP-36.7** Obtain client acceptance	Nadia Lahlou 11 May 2026	Final report delivered; acceptance signed by the HR Director on 28 November.
UFT-19-09 **Record engagement REX**	**MP-36.8** Record engagement REX **MP-12.6** Record REX entry **MP-12.5** Prompt REX at closure	Nadia Lahlou 14 May 2026	REX: went well — stakeholder register; did not — late SWOT inputs; root cause — no function-head backup; rating 4/5.

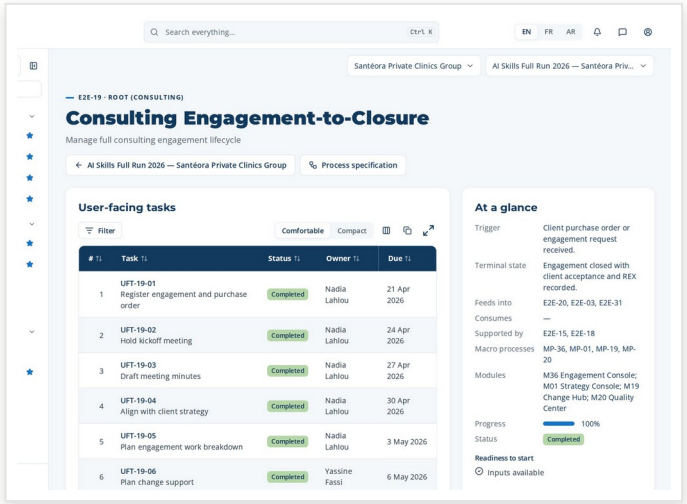

The page of E2E-19 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-36 Consulting Engagement Management
- MP-01 Strategy & Governance Alignment
- MP-19 Change Management & Adoption
- MP-20 Quality, Risk & Continuous Improvement

Feeds into

E2E-20, E2E-03, E2E-31

Supported by

E2E-15, E2E-18

Competitive Intelligence-to-Strategy

Analyze external environment and feed L&D strategy


TRIGGER
Annual strategy cycle or executive request for market positioning analysis.

END STATE
Validated competitive intelligence report feeding into L&D strategy and organizational diagnostic.

7 tasks · 12 steps
20 days · 2 owners · 100 %

Macro processes: MP-43 Strategic & Competitive Intelligence · MP-01 Strategy & Governance Alignment · MP-37 Multi-Axis Organizational Diagnostic · MP-04 Training Engineering Report & Roadmap Elaboration

Task	Steps executed	Owner · done	What was entered
UFT-24-01 **Define intelligence scope**	**MP-43.1** Define intelligence scope	Rim Ziani 20 Apr 2026	Scope: Healthcare Providers market in Morocco and export markets; horizon 3 years; focus on AI triage and clinical decision support and AI medical imaging assistance.
UFT-24-02 **Conduct Porter's Five Forces**	**MP-43.2** Conduct Porter's Five Forces analysis	Rim Ziani 23 Apr 2026	Rivalry 4/5; new entrants 3/5; substitutes 2/5; supplier power 3/5; buyer power 4/5.
UFT-24-03 **Map market segments**	**MP-43.3** Map market segments	Rim Ziani 26 Apr 2026	Segments: key accounts (55% revenue), resellers (30%), direct small customers (15%).
UFT-24-04 **Analyze competitor positioning**	**MP-43.4** Analyze competitor positioning	Rim Ziani 29 Apr 2026	Competitor A leads on AI triage and clinical decision support; competitor B cheaper but weaker on ISO 7101.
UFT-24-05 **Monitor regulatory and technology trends**	**MP-43.5** Monitor regulatory changes **MP-43.6** Track technology trends **MP-43.7** Benchmark against industry	Rim Ziani 2 May 2026	Trends: revision of ISO 7101 expected next year; fast growth of AI bed and staff capacity planning.

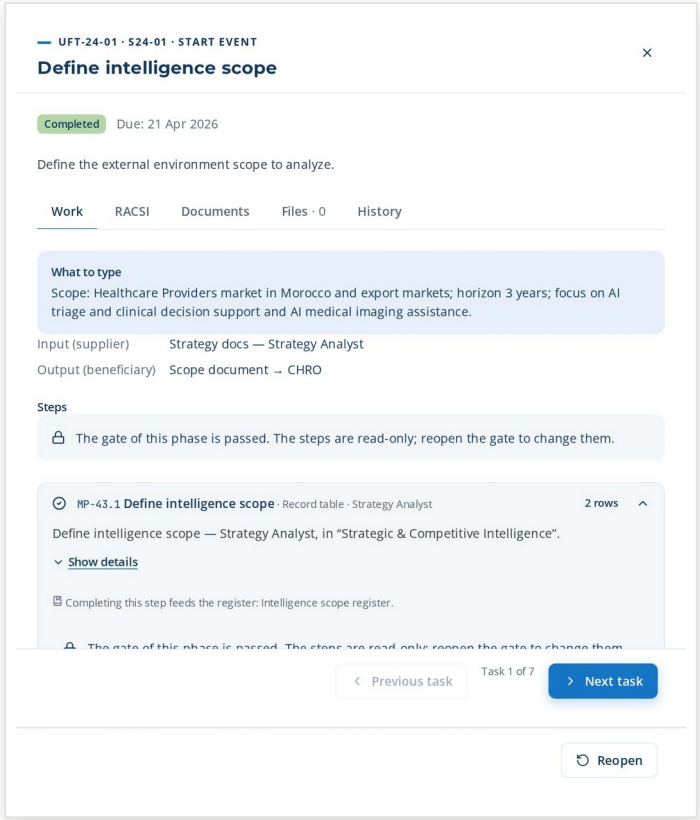


UFT-24-01 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Competitive Intelligence-to-Strategy (continued)

Task	Steps executed	Owner · done	What was entered
UFT-24-06 **Identify L&D implications**	**MP-43.8** Identify strategic implications for L&D	Amine Lahlou 5 May 2026	L&D implication: build AI triage and clinical decision support skills for key-account teams before competitor A scales.
UFT-24-07 **Publish intelligence report**	**MP-43.9** Produce intelligence report **MP-43.10** Feed intelligence into strategy and diagnostic **MP-43.11** Update intelligence continuously *+ 1 more steps*	Rim Ziani 8 May 2026	Publish RPT-007 Competitive Intelligence Report to the executive committee.

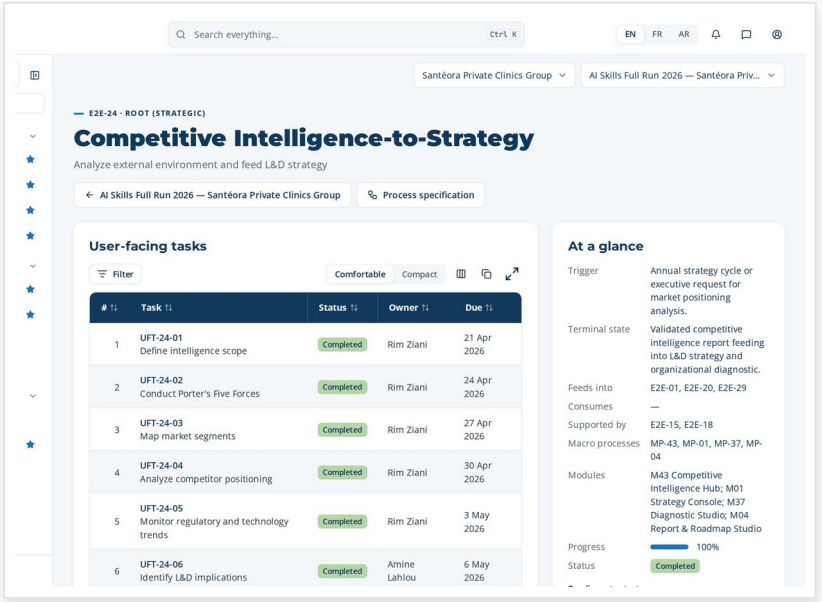

The page of E2E-24 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-43 Strategic & Competitive Intelligence
- MP-01 Strategy & Governance Alignment
- MP-37 Multi-Axis Organizational Diagnostic
- MP-04 Training Engineering Report & Roadmap Elaboration

Feeds into

E2E-01, E2E-20, E2E-29

Supported by

E2E-15, E2E-18

02

PHASE 2

Diagnosis

8 processes · 62 tasks · 100 steps
16 May 2026 – 14 Jun 2026
Closed by G2 — Diagnostic validated

E2E-20 Multi-Axis Diagnostic-to-Maturity Report
E2E-25 Job Architecture-to-Competency Map
E2E-26 GPEC-to-Training Plan
E2E-27 Demand Collection-to-Consolidation
E2E-28 Performance Assessment-to-RAG Dashboard
E2E-29 Functional SWOT-to-Improvement Axes
E2E-02 Skills-to-Gap Diagnosis
E2E-21 Previous Plan Impact-to-Strategy Update

Multi-Axis Diagnostic-to-Maturity Report

Conduct 5-axis diagnostic + CMM maturity + leadership assessment


TRIGGER
Engagement kickoff or approved Scope of Work requesting a diagnostic.

END STATE
5-axis diagnostic, CMM maturity and leadership maturity report validated with the sponsor.

10 tasks · 17 steps
29 days · 4 owners · 100 %

Macro processes: MP-37 Multi-Axis Organizational Diagnostic · MP-38 Organizational Maturity Assessment (CMM-Based) · MP-42 Leadership Maturity Assessment & Development · MP-02 Skills & Competency Management · MP-03 Needs Analysis & Diagnosis

Task	Steps executed	Owner · done	What was entered
UFT-20-01 **Define diagnostic axes and sample**	**MP-37.1** Define diagnostic axes and sample	Nadia Lahlou 18 May 2026	Axes: strategy, organization, processes, people, information systems. Sample: 40 people (MS 8, MO 16, OP 16).
UFT-20-02 **Deploy diagnostic questionnaire**	**MP-37.2** Deploy diagnostic questionnaire **MP-37.4** Collect questionnaire responses	Nadia Lahlou 21 May 2026	Diagnostic questionnaire deployed to 40 people; 34 responses (85%).
UFT-20-03 **Conduct semi-structured interviews**	**MP-37.3** Conduct semi-structured interviews	Soukaina El Idrissi 24 May 2026	Interview notes (OP, Clinical Care & Nursing): 'Procedures exist but are not updated since 2023.'
UFT-20-04 **Score diagnostic axes**	**MP-37.5** Score diagnostic axes	Soukaina El Idrissi 27 May 2026	Axis scores (1-5): strategy 3.4, organization 2.8, processes 2.6, people 3.1, IS 2.2.
UFT-20-05 **Select maturity model**	**MP-38.1** Select maturity model levels **MP-38.2** Define evidence criteria per level	Soukaina El Idrissi 30 May 2026	Maturity model: CMM 5 levels; evidence for level 3 = documented and applied process.

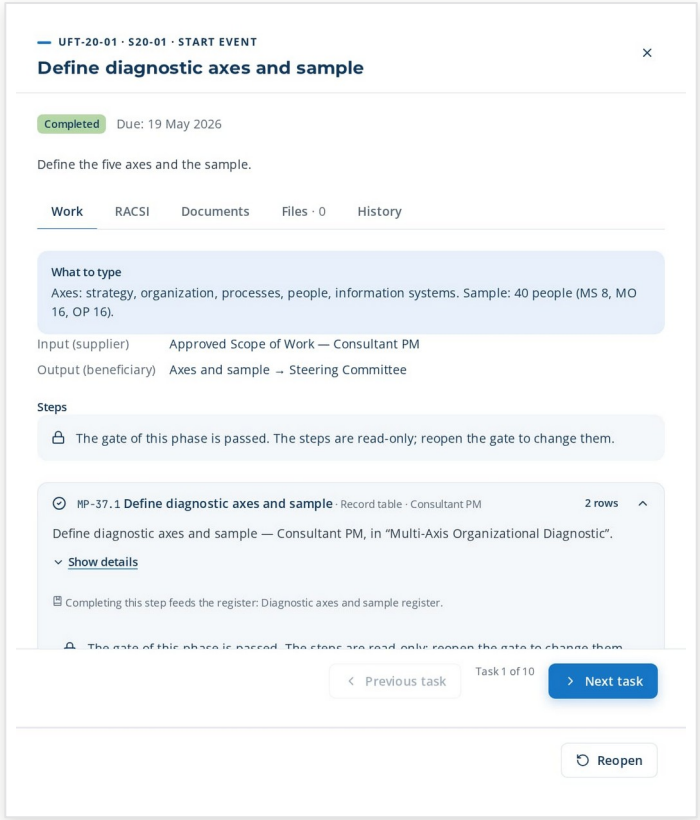


UFT-20-01 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Multi-Axis Diagnostic-to-Maturity Report (continued)

Task	Steps executed	Owner · done	What was entered
UFT-20-06 **Rate process maturity**	**MP-38.3** Rate maturity per process area **MP-38.4** Compute maturity profile	Soukaina El Idrissi 2 Jun 2026	Maturity: training management level 2; Clinical Care & Nursing processes level 3.
UFT-20-07 **Assess leadership maturity**	**MP-42.1** Launch leadership 360 assessment **MP-42.2** Compute leadership maturity level	Karim Chraibi 5 Jun 2026	Leadership 360: average level 3 (Team Leadership) across 18 managers.
UFT-20-08 **Cross-check skills and needs**	**MP-02.7** Validate skills inventory **MP-03.2** Review gap matrix by site and function	Yassine Berrada 8 Jun 2026	Cross-check: IS axis weakness confirmed by the AI triage and clinical decision support gap (-1.4).
UFT-20-09 **Draft diagnostic findings**	**MP-37.6** Draft diagnostic findings **MP-38.5** Produce maturity report	Soukaina El Idrissi 11 Jun 2026	Edit AI findings: keep 5, merge 2, add one on ISO 7101 documentation.
UFT-20-10 **Validate findings with sponsor**	**MP-37.7** Validate findings with sponsor **MP-38.6** Agree target maturity	Nadia Lahlou 14 Jun 2026	Findings validated with the sponsor; target maturity level 3 by 2026+1.

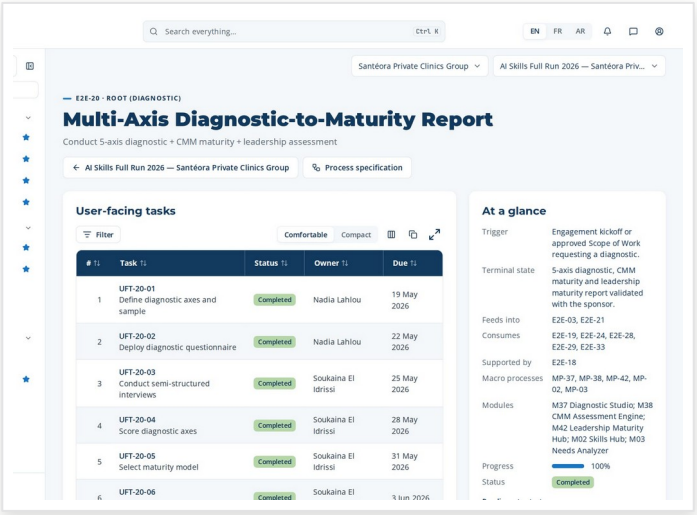

The page of E2E-20 in CortexSkills: its tasks, owners and due dates, and the process card.

Feeds into
E2E-03, E2E-21
Supported by
E2E-18

Job Architecture-to-Competency Map

Manage organizational charts, position descriptions, gap analysis


TRIGGER
Organizational change, new role creation, or annual job architecture review.

END STATE
Approved organizational charts, position descriptions, and competency maps with gap analysis.

8 tasks · 12 steps
23 days · 2 owners · 100 %

Macro processes: MP-44 Job Architecture & Position Description Management · MP-02 Skills & Competency Management · MP-13 Talent & Career Development · MP-37 Multi-Axis Organizational Diagnostic

Task	Steps executed	Owner · done	What was entered
UFT-25-01 **Map organizational structure**	**MP-44.1** Map organizational structure	Mehdi Lahlou 18 May 2026	Structure: 6 functions, 14 departments, 3 sites; 212 positions.
UFT-25-02 **Design organizational charts**	**MP-44.2** Design organizational charts	Mehdi Lahlou 21 May 2026	Org chart 'Clinical Care & Nursing': director → 3 managers → 9 supervisors → operators.
UFT-25-03 **Conduct job analysis**	**MP-44.3** Conduct job analysis	Karim Chraibi 24 May 2026	Job analysis 'Clinical Care & Nursing supervisor': 8 main activities, 2 of them now supported by AI triage and clinical decision support.
UFT-25-04 **Draft position descriptions**	**MP-44.4** Draft position descriptions	Karim Chraibi 27 May 2026	Position description drafted: mission, activities, competencies (AI triage and clinical decision support level 3, ISO 7101 level 3), KPIs.
UFT-25-05 **Validate with managers**	**MP-44.5** Validate descriptions with managers	Karim Chraibi 30 May 2026	Validated by the Clinical Care & Nursing manager with 2 changes on activities.

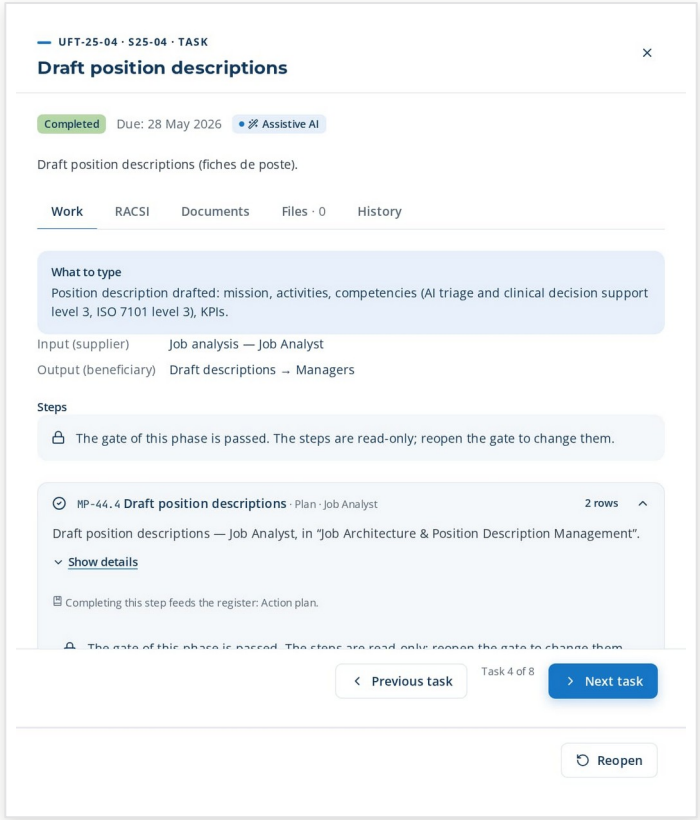


UFT-25-04 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Job Architecture-to-Competency Map (continued)

Task	Steps executed	Owner · done	What was entered
UFT-25-06 **Conduct gap analysis**	**MP-44.6** Conduct gap analysis existing versus real	Karim Chraibi 2 Jun 2026	Gap existing vs real: 11 descriptions outdated; 4 roles with new AI triage and clinical decision support tasks.
UFT-25-07 **Identify roles to develop**	**MP-44.7** Identify roles to develop **MP-44.8** Update job architecture **MP-44.9** Align with competency framework	Karim Chraibi 5 Jun 2026	Roles 'To develop': data-literate supervisor, maintenance technician 4.0.
UFT-25-08 **Publish approved architecture**	**MP-44.10** Publish approved position descriptions **MP-44.11** Track job architecture changes **MP-44.12** Report on architecture health	Mehdi Lahlou 8 Jun 2026	Publish 212 approved descriptions and the architecture map to all employees.

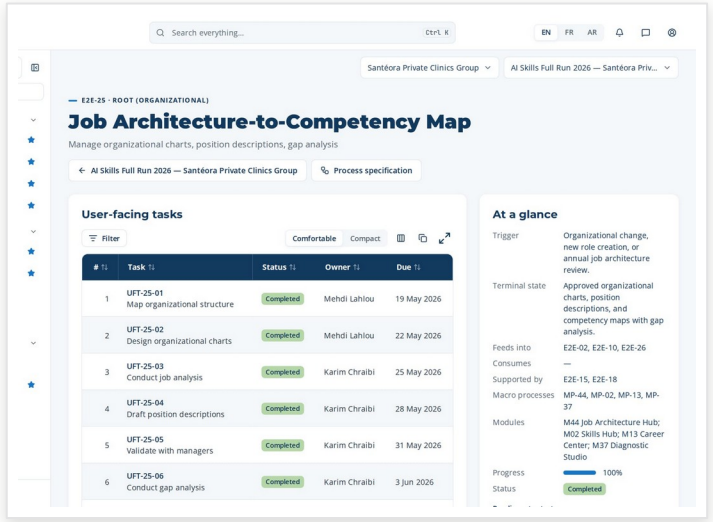

The page of E2E-25 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-44 Job Architecture & Position Description Management
- MP-02 Skills & Competency Management
- MP-13 Talent & Career Development
- MP-37 Multi-Axis Organizational Diagnostic

Feeds into

E2E-02, E2E-10, E2E-26

Supported by

E2E-15, E2E-18

GPEC-to-Training Plan

Integrate Forward Planning of Jobs and Skills into L&D


TRIGGER
Annual HR strategic planning cycle or GPEC (Forward Planning of Jobs and Skills) review.

END STATE
Training plan aligned with GPEC and HR strategic orientations.

8 tasks · 12 steps
23 days · 4 owners · 100 %

Macro processes: MP-45 GPEC & HR Strategic Integration (Forward Planning of Jobs and Skills) · MP-13 Talent & Career Development · MP-04 Training Engineering Report & Roadmap Elaboration · MP-03 Needs Analysis & Diagnosis · MP-18 Financial & Budget Management

Task	Steps executed	Owner · done	What was entered
UFT-26-01 **Define GPEC scope**	**MP-45.1** Define GPEC scope	Nadia Tazi 18 May 2026	GPEC scope: Clinical Care & Nursing and Information Systems jobs; horizon 3 years.
UFT-26-02 **Map HR strategic orientations**	**MP-45.2** Map HR strategic orientations **MP-45.3** Align training with GPEC	Mehdi Lahlou 21 May 2026	HR orientations: internal mobility first; 30% of promotions from internal talent.
UFT-26-03 **Update development foundation**	**MP-45.4** Update development foundation **MP-45.5** Support human capital development	Karim Chraibi 24 May 2026	Development foundation updated: descriptions, annual objectives, evaluation grid.
UFT-26-04 **Update Jobs and Skills Directory (REC)**	**MP-45.6** Update Jobs and Skills Directory (REC)	Nadia Tazi 27 May 2026	REC updated: 42 jobs, 3 new jobs linked to AI triage and clinical decision support.
UFT-26-05 **Redynamize periodic evaluations**	**MP-45.7** Redynamize periodic evaluations	Karim Chraibi 30 May 2026	Periodic evaluation redesigned: 2 reviews per year, competency section added.
UFT-26-06 **Design career paths**	**MP-45.8** Design career paths	Mehdi Lahlou 2 Jun 2026	Career path: operator → team leader → supervisor → Clinical Care & Nursing manager.

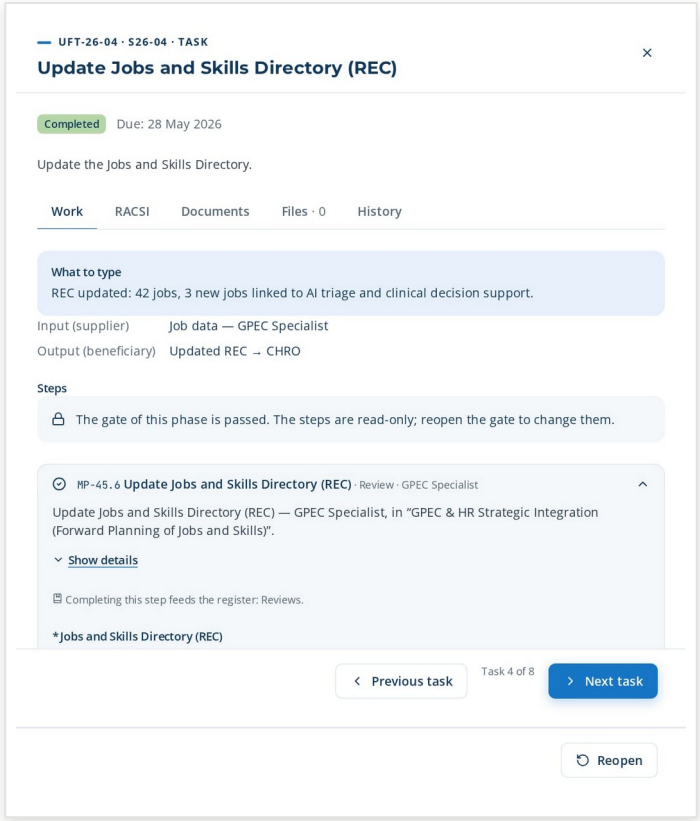


UFT-26-04 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

GPEC-to-Training Plan (continued)

Task	Steps executed	Owner · done	What was entered
UFT-26-07 **Document career management**	**MP-45.9** Document career management process **MP-45.10** Implement collective compensation	Mehdi Lahlou 5 Jun 2026	Career management procedure documented (v1): eligibility, committee, calendar.
UFT-26-08 **Align training with GPEC**	**MP-45.11** Feed GPEC into training needs **MP-45.12** Report on GPEC integration	Amine Lahlou 8 Jun 2026	Training aligned with GPEC: 4 themes cover the 3 new jobs; 2 themes removed.

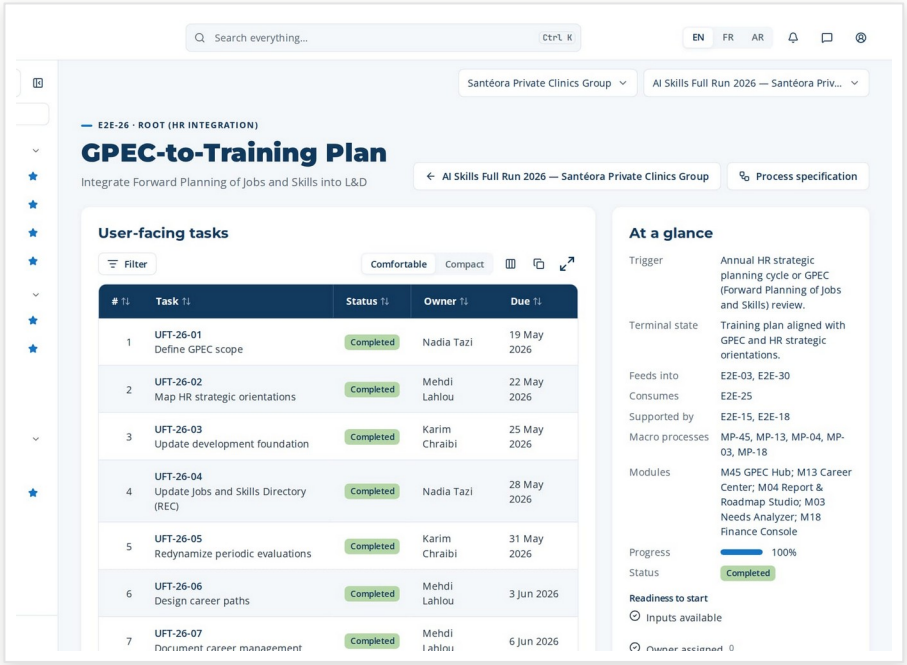

The page of E2E-26 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-45 GPEC & HR Strategic Integration (Forward Planning of Jobs and Skills)
- MP-13 Talent & Career Development
- MP-04 Training Engineering Report & Roadmap Elaboration
- MP-03 Needs Analysis & Diagnosis
- MP-18 Financial & Budget Management

Feeds into

E2E-03, E2E-30

Supported by

E2E-15, E2E-18

Demand Collection-to-Consolidation

Collect individual and collective training demands


TRIGGER
Annual training plan cycle or ad-hoc demand collection request.

END STATE
Consolidated and prioritized demand repository integrated into the training needs analysis.

7 tasks · 12 steps
20 days · 2 owners · 100 %

Macro processes: MP-46 Training Demand Collection & Consolidation · MP-03 Needs Analysis & Diagnosis · MP-04 Training Engineering Report & Roadmap Elaboration · MP-08 Learner Experience & Engagement

Task	Steps executed	Owner · done	What was entered
UFT-27-01 **Design demand collection forms**	**MP-46.1** Design demand collection forms	Yassine Berrada 18 May 2026	Forms: individual form (5 questions) and collective form per team (3 questions).
UFT-27-02 **Deploy individual demand collection**	**MP-46.2** Deploy individual demand collection	Yassine Berrada 21 May 2026	Individual collection open 1-20 March; 146 demands received.
UFT-27-03 **Deploy collective demand collection**	**MP-46.3** Deploy collective demand collection	Yassine Berrada 24 May 2026	Collective collection: 18 team demands received.
UFT-27-04 **Collect manager recommendations**	**MP-46.4** Collect manager recommendations	Nadia Lahlou 27 May 2026	Manager recommendations: 24 received, 9 flagged as priority.
UFT-27-05 **Consolidate demands by function**	**MP-46.5** Consolidate demands by function	Yassine Berrada 30 May 2026	Consolidated: Clinical Care & Nursing 64 demands, Operations 41, Quality 22, others 37.

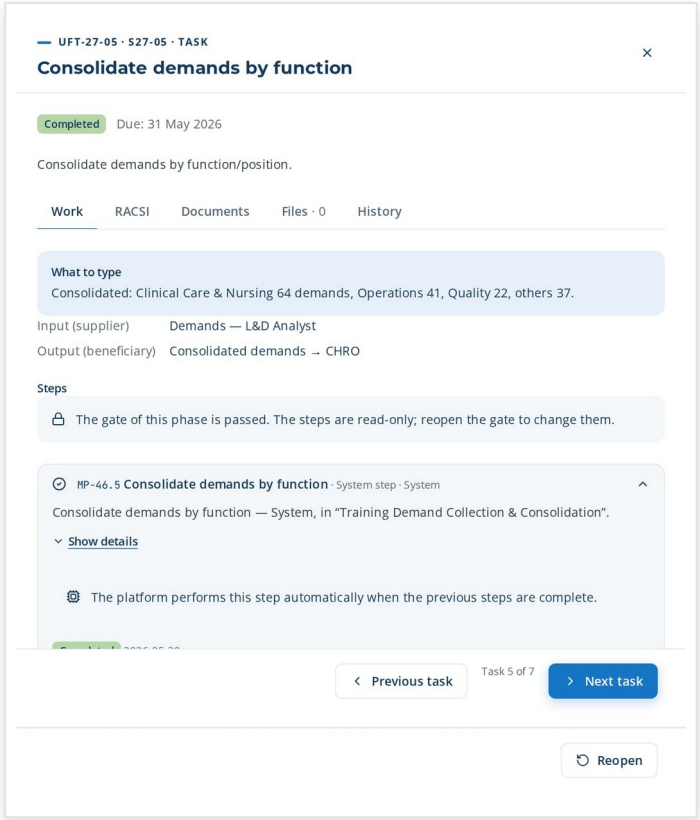


UFT-27-05 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Demand Collection-to-Consolidation (continued)

Task	Steps executed	Owner · done	What was entered
UFT-27-06 **Map demands to competencies**	**MP-46.6** Map demands to competencies **MP-46.7** Prioritize demands	Yassine Berrada 2 Jun 2026	Accept AI mapping for 139 demands; map 7 manually to 'AI medical imaging assistance'.
UFT-27-07 **Prioritize and validate demands**	**MP-46.8** Validate demands with managers **MP-46.9** Integrate demands into needs analysis **MP-46.10** Report on demand patterns *+ 2 more steps*	Nadia Lahlou 5 Jun 2026	Validated: 112 demands (High 38, Medium 51, Low 23); 34 rejected with reason.

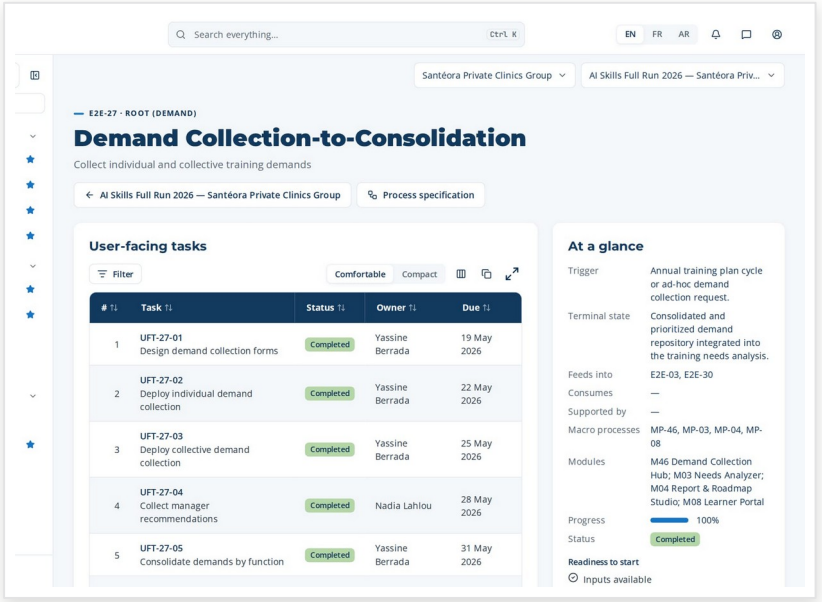

The page of E2E-27 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-46 Training Demand Collection & Consolidation
- MP-03 Needs Analysis & Diagnosis
- MP-04 Training Engineering Report & Roadmap Elaboration
- MP-08 Learner Experience & Engagement

Feeds into

E2E-03, E2E-30

Supported by

—

Performance Assessment-to-RAG Dashboard

Assess MS/MO/OP performance with RAG ratings


TRIGGER
Annual performance cycle or management request for performance visualization.

END STATE
Validated MS/MO/OP (Strategic Management / Operational Management / Operational Level) performance assessment with RAG (Green/Amber/Red) dashboards.

7 tasks · 12 steps
20 days · 1 owners · 100 %

Macro processes: MP-47 Performance Level Assessment & Visualization (MS/MO/OP) · MP-10 Reporting & Analytics · MP-37 Multi-Axis Organizational Diagnostic · MP-04 Training Engineering Report & Roadmap Elaboration

Task	Steps executed	Owner · done	What was entered
UFT-28-01 **Define MS/MO/OP framework**	**MP-47.1** Define MS/MO/OP framework	Anas Hajji 18 May 2026	MS = executive committee; MO = managers and supervisors; OP = operators and technicians.
UFT-28-02 **Define RAG criteria**	**MP-47.2** Define RAG criteria	Anas Hajji 21 May 2026	Green ≥ 90% of target; Amber 70-89%; Red < 70%.
UFT-28-03 **Collect performance data by function**	**MP-47.3** Collect performance data by function	Anas Hajji 24 May 2026	Data collected for 6 functions: 18 KPIs, last 12 months.
UFT-28-04 **Assess MS performance**	**MP-47.4** Assess MS performance	Anas Hajji 27 May 2026	MS: strategy deployment Amber (78%); governance Green (92%).
UFT-28-05 **Assess MO performance**	**MP-47.5** Assess MO performance	Anas Hajji 30 May 2026	MO: Clinical Care & Nursing team management Red (64%); planning Amber (81%).
UFT-28-06 **Assess OP performance**	**MP-47.6** Assess OP performance **MP-47.7** Apply RAG ratings	Anas Hajji 2 Jun 2026	OP: ISO 7101 compliance Amber (85%); productivity Green (93%).

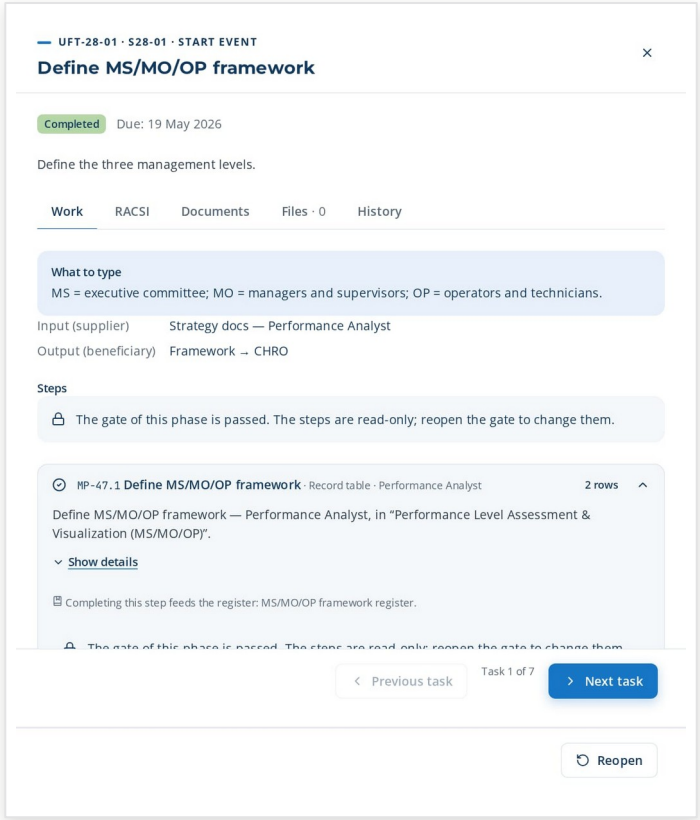


UFT-28-01 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Performance Assessment-to-RAG Dashboard (continued)

Task	Steps executed	Owner · done	What was entered
UFT-28-07 **Publish RAG dashboard**	**MP-47.8** Visualize performance dashboards **MP-47.9** Identify performance gaps **MP-47.10** Feed performance into diagnostic report *+ 2 more steps*	Anas Hajji 5 Jun 2026	Publish RPT-005 MS/MO/OP RAG dashboard to the executive committee.

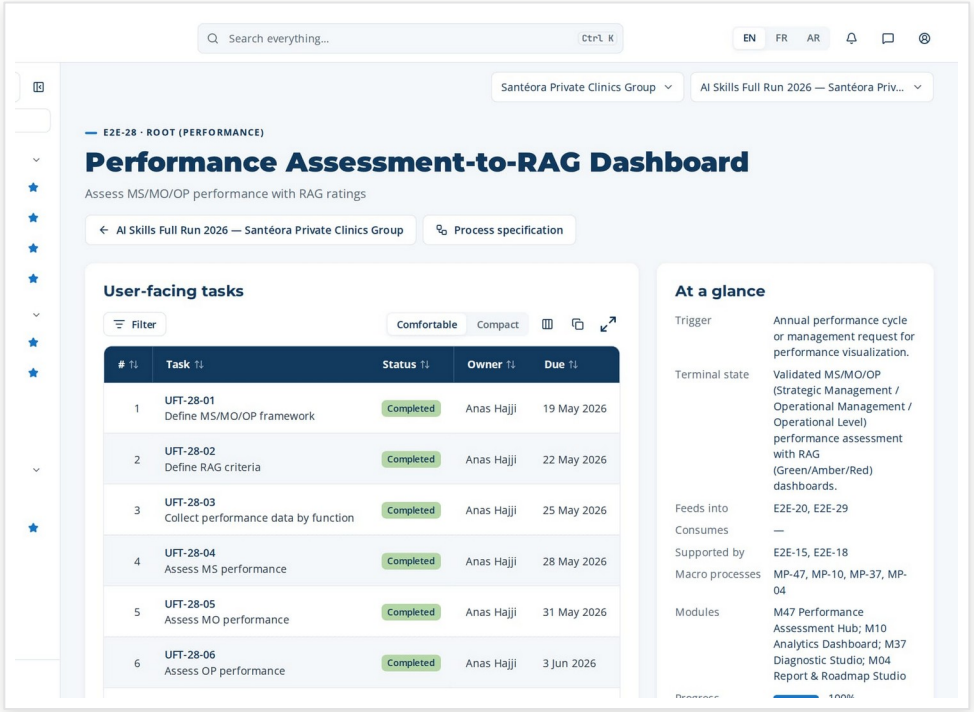

The page of E2E-28 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-47 Performance Level Assessment & Visualization (MS/MO/OP)
- MP-10 Reporting & Analytics
- MP-37 Multi-Axis Organizational Diagnostic
- MP-04 Training Engineering Report & Roadmap Elaboration

Feeds into

E2E-20, E2E-29

Supported by

E2E-15, E2E-18

Functional SWOT-to-Improvement Axes

Conduct function-level SWOT and define improvement axes


TRIGGER
Diagnostic phase of a training engineering engagement or annual functional review.

END STATE
Validated functional SWOT reports with prioritized improvement axes per function.

7 tasks · 12 steps
20 days · 3 owners · 100 %

Macro processes: MP-48 Functional SWOT & Improvement Axes Analysis · MP-37 Multi-Axis Organizational Diagnostic · MP-04 Training Engineering Report & Roadmap Elaboration · MP-20 Quality, Risk & Continuous Improvement

Task	Steps executed	Owner · done	What was entered
UFT-29-01 **Define function scope**	**MP-48.1** Define function scope	Yassine Berrada 18 May 2026	Function in scope: Clinical Care & Nursing (3 sites, 96 people).
UFT-29-02 **Conduct function SWOT**	**MP-48.2** Conduct function SWOT	Yassine Berrada 21 May 2026	SWOT workshop held with the function head and 6 supervisors.
UFT-29-03 **Identify strengths and weaknesses**	**MP-48.3** Identify strengths **MP-48.4** Identify weaknesses	Yassine Berrada 24 May 2026	Strength: experienced team. Weakness: low AI triage and clinical decision support usage, paper records.
UFT-29-04 **Identify opportunities and threats**	**MP-48.5** Identify opportunities **MP-48.6** Identify threats	Yassine Berrada 27 May 2026	Opportunity: AI bed and staff capacity planning. Threat: stricter ISO 7101 audits.
UFT-29-05 **Define improvement axes**	**MP-48.7** Define improvement axes	Nadia Lahlou 30 May 2026	Axis 1: digitalise shift records with AI triage and clinical decision support. Axis 2: certify supervisors on ISO 7101.
UFT-29-06 **Validate with function heads**	**MP-48.8** Validate axes with function heads	Nadia Lahlou 2 Jun 2026	Validated by the function head on 18 April; axis 2 deadline moved to Q3.

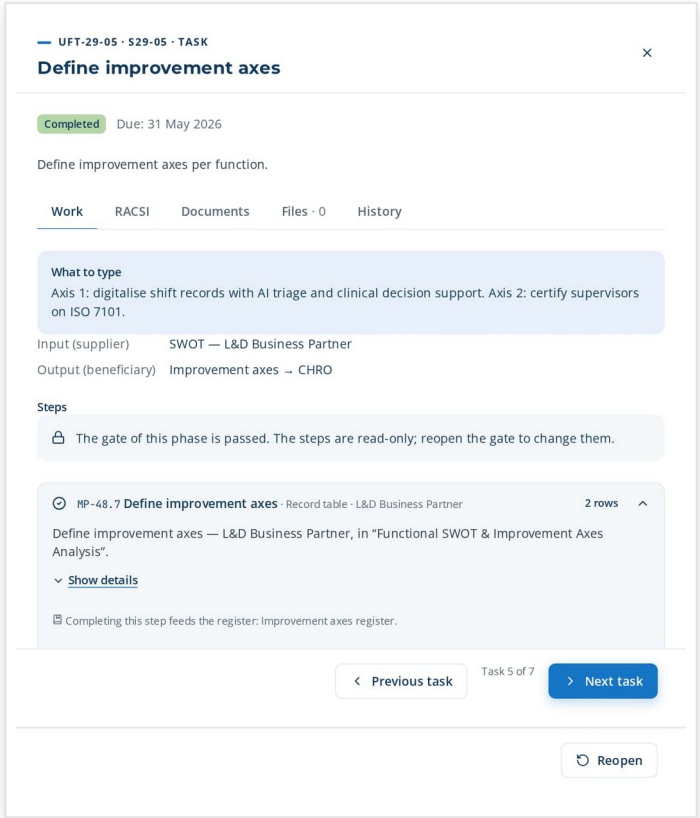


UFT-29-05 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Functional SWOT-to-Improvement Axes (continued)

Task	Steps executed	Owner · done	What was entered
UFT-29-07 **Prioritize improvement axes**	**MP-48.9** Prioritize improvement axes **MP-48.10** Feed SWOT into diagnostic report **MP-48.11** Track improvement implementation *+ 1 more steps*	Amine Lahlou 5 Jun 2026	Priority: axis 1 (impact 5), axis 2 (impact 4).

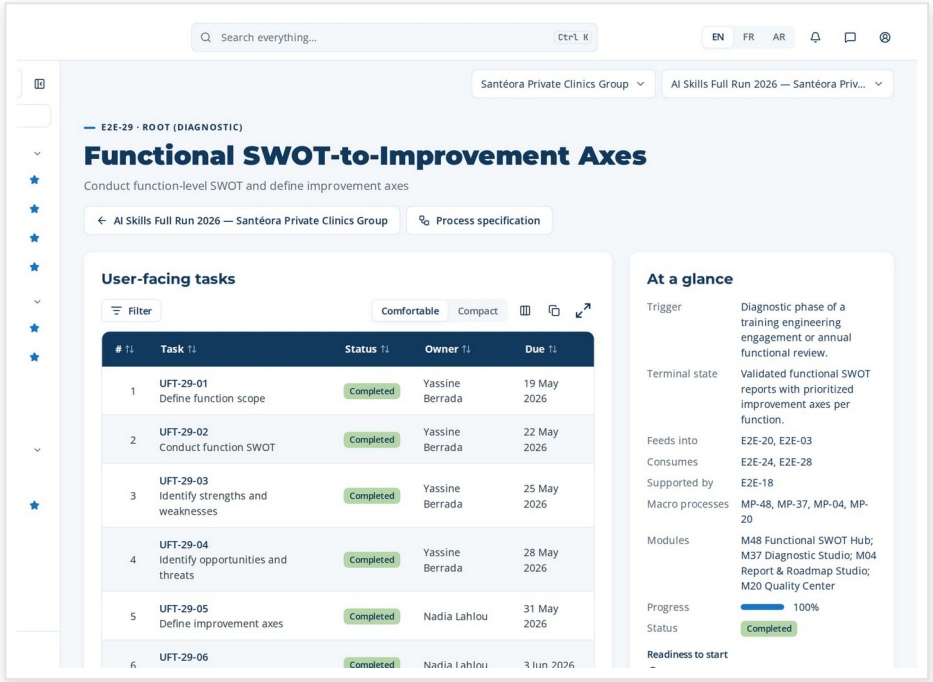

The page of E2E-29 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-48 Functional SWOT & Improvement Axes Analysis
- MP-37 Multi-Axis Organizational Diagnostic
- MP-04 Training Engineering Report & Roadmap Elaboration
- MP-20 Quality, Risk & Continuous Improvement

Feeds into

E2E-20, E2E-03

Supported by

E2E-18

Skills-to-Gap Diagnosis

Produce a validated skills gap diagnosis


TRIGGER
Approved annual L&D plan or a scheduled skills assessment campaign.

END STATE
Validated skills gap diagnosis released to needs analysis.

7 tasks · 11 steps
20 days · 4 owners · 100 %

Macro processes: MP-02 Skills & Competency Management · MP-03 Needs Analysis & Diagnosis · MP-28 Predictive Learning Analytics & Intelligence

Task	Steps executed	Owner · done	What was entered
UFT-02-01 **Maintain competency framework**	**MP-02.1** Define competency families and levels	Yassine Berrada 18 May 2026	Family 'AI triage and clinical decision support': 4 competencies on the 1-4 scale (Aware, Practitioner, Autonomous, Expert).
UFT-02-02 **Set target levels per position**	**MP-02.2** Set target levels per position	Karim Chraibi 21 May 2026	Clinical Care & Nursing supervisor: AI triage and clinical decision support = 3; ISO 7101 = 3. Clinical Care & Nursing operator: AI triage and clinical decision support = 2.
UFT-02-03 **Launch assessment campaign**	**MP-02.3** Launch assessment campaign	Yassine Berrada 24 May 2026	Campaign 'Skills 2026': population Clinical Care & Nursing and Operations (212 people), 12 competencies, close date 30 April.
UFT-02-04 **Collect self and manager assessments**	**MP-02.4** Submit self and manager assessments **MP-02.5** Consolidate assessment results	Karim El Idrissi 27 May 2026	Self-assessment AI triage and clinical decision support: 2; manager validation: 2 with comment 'needs practice on live cases'.

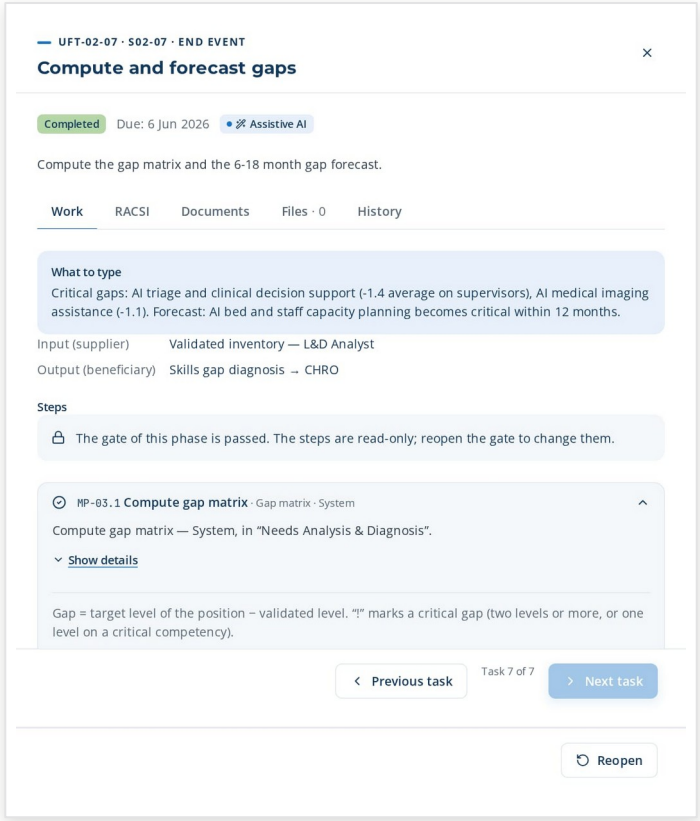


UFT-02-07 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Skills-to-Gap Diagnosis (continued)

Task	Steps executed	Owner · done	What was entered
UFT-02-05 **Suggest proficiency from evidence**	**MP-02.6** Suggest proficiency from evidence	Yassine Berrada 30 May 2026	Accept 38 suggested levels, edit 4 (evidence too old), reject 1. Every change carries a note.
UFT-02-06 **Validate skills inventory**	**MP-02.7** Validate skills inventory	Hicham Naciri 2 Jun 2026	Inventory validated: 212 employees, 96% assessments complete. Justification: sample checked by site.
UFT-02-07 **Compute and forecast gaps**	**MP-03.1** Compute gap matrix **MP-03.2** Review gap matrix by site and function **MP-28.3** Forecast skill gaps *+ 1 more steps*	Yassine Berrada 5 Jun 2026	Critical gaps: AI triage and clinical decision support (-1.4 average on supervisors), AI medical imaging assistance (-1.1). Forecast: AI bed and staff capacity planning becomes critical within 12 months.

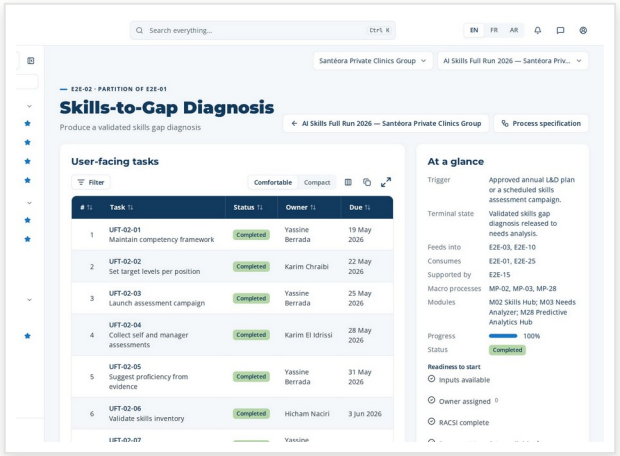

The page of E2E-02 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-02 Skills & Competency Management
- MP-03 Needs Analysis & Diagnosis
- MP-28 Predictive Learning Analytics & Intelligence

Feeds into

E2E-03, E2E-10

Supported by

E2E-15

Previous Plan Impact-to-Strategy Update

Evaluate N-1 plan impact and update strategy


TRIGGER
Start of a new plan cycle with N-1 execution data available.

END STATE
N-1 impact conclusions fed into the strategy update.

8 tasks · 12 steps
23 days · 4 owners · 100 %

Macro processes: MP-39 Training Plan Impact Study (N-1) · MP-09 Assessment & Evaluation · MP-32 Learning ROI & Business Impact Measurement · MP-01 Strategy & Governance Alignment · MP-04 Training Engineering Report & Roadmap Elaboration

Task	Steps executed	Owner · done	What was entered
UFT-21-01 **Load N-1 plan execution data**	**MP-39.1** Load N-1 plan execution data	Yassine Berrada 18 May 2026	Load N-1 plan: 28 sessions planned, 23 delivered, 1,410,000 MAD spent.
UFT-21-02 **Define impact criteria**	**MP-39.2** Define impact criteria	Yassine Berrada 21 May 2026	Impact criteria: application on the job, KPI change, satisfaction, cost per learner.
UFT-21-03 **Survey participants and managers**	**MP-39.3** Survey participants and managers **MP-09.5** Record on-the-job observation (Level 3)	Yassine Berrada 24 May 2026	Survey sent to 190 participants and 34 managers; 61% responded.
UFT-21-04 **Compare planned against realized**	**MP-39.4** Compare planned against realized **MP-32.3** Isolate training effect	Yassine Berrada 27 May 2026	Planned vs realized: 82% of sessions, 94% of budget; 2 themes not delivered.
UFT-21-05 **Review N-1 ROI**	**MP-32.4** Compute Phillips ROI **MP-32.5** Review ROI with finance	Anas Hajji 30 May 2026	N-1 ROI: AI medical imaging assistance 18%; safety theme 35%.
UFT-21-06 **Draft impact conclusions**	**MP-39.5** Draft impact study conclusions	Yassine Berrada 2 Jun 2026	Accept AI conclusions 1-3; rewrite conclusion 4 (sample too small).

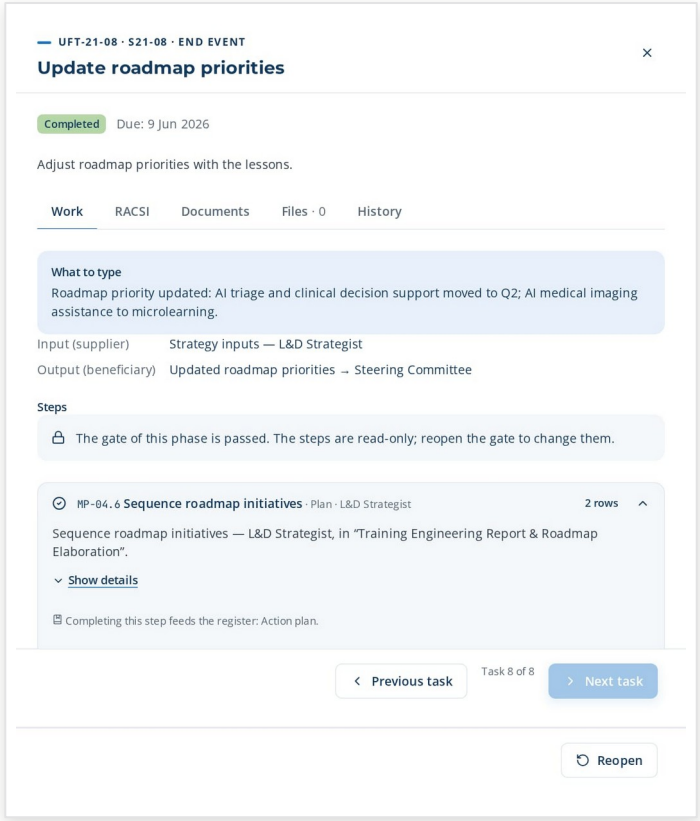


UFT-21-08 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Previous Plan Impact-to-Strategy Update (continued)

Task	Steps executed	Owner · done	What was entered
UFT-21-07 **Feed conclusions to strategy**	**MP-39.6** Feed conclusions to strategy update **MP-01.1** Record corporate strategic objectives	Hicham Naciri 5 Jun 2026	Feed to strategy: keep blended format; stop long classroom courses on AI medical imaging assistance.
UFT-21-08 **Update roadmap priorities**	**MP-04.6** Sequence roadmap initiatives	Amine Lahlou 8 Jun 2026	Roadmap priority updated: AI triage and clinical decision support moved to Q2; AI medical imaging assistance to microlearning.

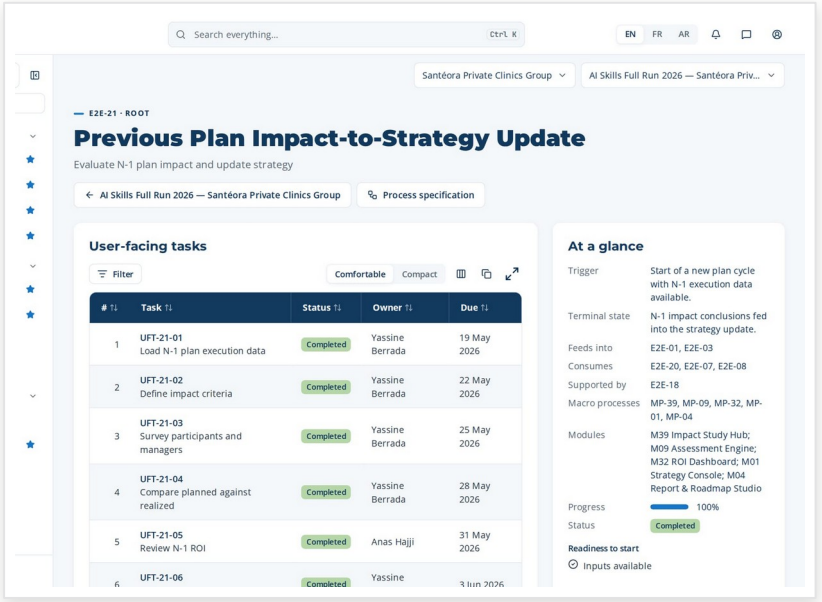

The page of E2E-21 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-39 Training Plan Impact Study (N-1)
- MP-09 Assessment & Evaluation
- MP-32 Learning ROI & Business Impact Measurement
- MP-01 Strategy & Governance Alignment
- MP-04 Training Engineering Report & Roadmap Elaboration

Feeds into

E2E-01, E2E-03

Supported by

E2E-18

03

PHASE 3

Training Engineering Report & plan

7 processes · 50 tasks · 84 steps

13 Jun 2026 – 12 Jul 2026

Closed by G3 — Report & roadmap approved

E2E-01 Strategy-to-Learning Plan

E2E-03 Needs-to-Training Engineering Report & Roadmap

E2E-30 Prioritization-to-Resource Plan

E2E-22 Multi-Site Plan-to-Deployment

E2E-23 Regulatory Submission-to-Validation

E2E-16 Vendor-to-Finance

HCPR-E2E-02 Healthcare Providers Critical-Skills-to-Transformation Plan

Strategy-to-Learning Plan

Translate corporate strategy into an approved annual L&D plan and budget


TRIGGER
Annual strategy cycle opened or revised corporate objectives published by the board.

END STATE
Annual L&D plan and budget envelope approved by the Steering Committee and locked.

8 tasks · 16 steps
23 days · 6 owners · 100 %

Macro processes: MP-01 Strategy & Governance Alignment · MP-02 Skills & Competency Management · MP-03 Needs Analysis & Diagnosis · MP-04 Training Engineering Report & Roadmap Elaboration · MP-18 Financial & Budget Management · MP-19 Change Management & Adoption

Task	Steps executed	Owner · done	What was entered
UFT-01-01 **Record strategic objectives**	**MP-01.1** Record corporate strategic objectives	Hicham Naciri 15 Jun 2026	SO-1: AI triage and clinical decision support used by 80% of Clinical Care & Nursing staff by end 2026 (owner: Operations Director, measured quarterly). SO-2: zero major audit findings on ISO 7101.
UFT-01-02 **Link objectives to functions and sites**	**MP-01.2** Link objectives to functions and sites	Amine Lahlou 18 Jun 2026	SO-1 → Clinical Care & Nursing, Operations, Information Systems (all sites). SO-2 → Quality & HSE, Clinical Care & Nursing.
UFT-01-03 **Frame skills priorities**	**MP-02.1** Define competency families and levels **MP-02.2** Set target levels per position	Yassine Berrada 21 Jun 2026	Priority competency families: AI triage and clinical decision support; AI medical imaging assistance; ISO 7101 compliance. Target level 3 (Autonomous) for supervisors.

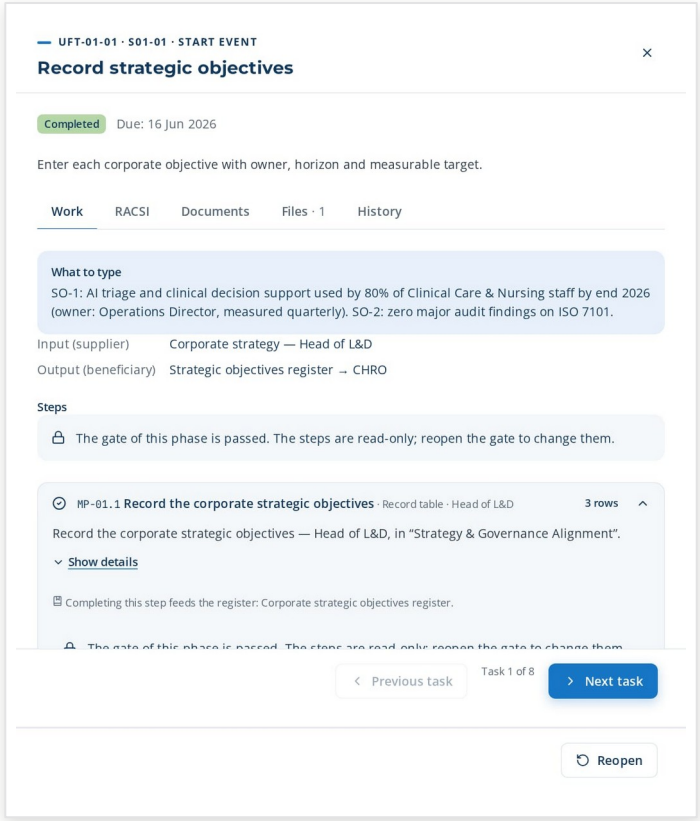


UFT-01-01 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Strategy-to-Learning Plan (continued)

Task	Steps executed	Owner · done	What was entered
UFT-01-04 **Pre-scope training needs**	**MP-03.1** Compute gap matrix **MP-03.2** Review gap matrix by site and function	Yassine Berrada 24 Jun 2026	Pre-scoped needs: 42% of Clinical Care & Nursing supervisors below target on AI triage and clinical decision support; 18 employees below target on ISO 7101.
UFT-01-05 **Define budget envelope**	**MP-01.3** Define L&D budget envelope **MP-18.1** Allocate budget by theme and site **MP-18.2** Forecast OFPPT refunds	Kawtar Chraibi 27 Jun 2026	Gross L&D budget 2026: 1,850,000 MAD; forecast refund (OFPPT/CSF): 520,000 MAD; net envelope: 1,330,000 MAD.
UFT-01-06 **Plan change and adoption**	**MP-19.1** Assess change impact **MP-19.2** Build adoption plan	Yassine Fassi 30 Jun 2026	Change impact: high for Clinical Care & Nursing supervisors (new AI triage and clinical decision support routines). Sponsors: Operations Director. Champions: one per site.
UFT-01-07 **Compile plan approval pack**	**MP-01.4** Schedule Steering Committee milestones **MP-01.5** Compile plan approval pack **MP-04.1** Consolidate feeder outputs	Hicham Naciri 3 Jul 2026	Approval pack: 2 objectives, net budget 1,330,000 MAD, 6 priority themes, committee date 15 March 2026.
UFT-01-08 **Approve and lock annual L&D plan**	**MP-01.6** Record Steering Committee decision **MP-01.7** Lock and distribute approved plan	Mehdi Lahlou 6 Jul 2026	Decision: Approve. Justification: aligned with SO-1 and SO-2; budget within envelope. Plan locked as version 1.

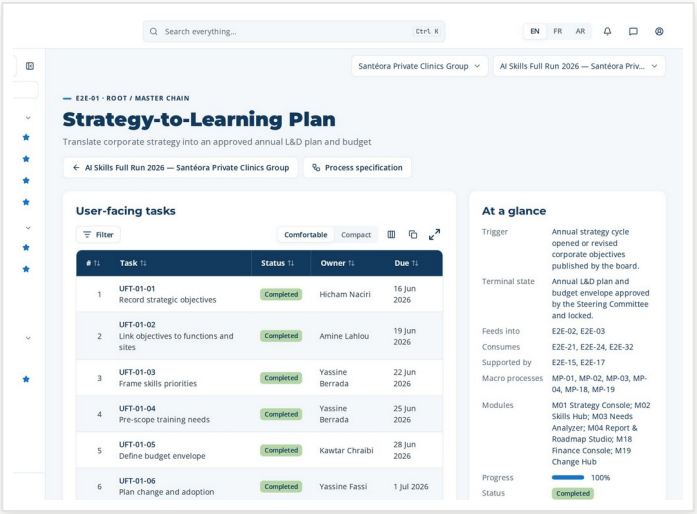

The page of E2E-01 in CortexSkills: its tasks, owners and due dates, and the process card.

Feeds into
E2E-02, E2E-03
Supported by
E2E-15, E2E-17

Needs-to-Training Engineering Report & Roadmap

Produce the Training Engineering Report and the prioritized training roadmap


TRIGGER
Validated skills gap diagnosis, consolidated demands, approved Scope of Work or diagnostic findings available.

END STATE
Training Engineering Report and prioritized roadmap approved and published.

10 tasks · 17 steps
29 days · 4 owners · 100 %

Macro processes: MP-01 Strategy & Governance Alignment · MP-03 Needs Analysis & Diagnosis · MP-04 Training Engineering Report & Roadmap Elaboration · MP-18 Financial & Budget Management · MP-20 Quality, Risk & Continuous Improvement

Task	Steps executed	Owner · done	What was entered
UFT-03-01 **Plan diagnostic interviews**	**MP-03.3** Plan diagnostic interviews	Yassine Berrada 15 Jun 2026	Interview plan: 14 semi-structured interviews (4 MS, 6 MO, 4 OP), 45 minutes each, weeks 10-11.
UFT-03-02 **Record interview findings**	**MP-03.4** Record interview findings	Yassine Berrada 18 Jun 2026	Finding (MO, Clinical Care & Nursing): 'Supervisors do not trust AI triage and clinical decision support data; they re-enter figures on paper.'
UFT-03-03 **Cluster needs into themes**	**MP-03.5** Cluster needs into training themes	Yassine Berrada 21 Jun 2026	Accept theme 'AI triage and clinical decision support for supervisors'; merge two duplicate themes on AI medical imaging assistance; split 'ISO 7101' into awareness and auditor tracks.
UFT-03-04 **Prioritize needs by impact**	**MP-03.6** Prioritize needs by business impact	Amine Lahlou 24 Jun 2026	AI triage and clinical decision support: impact 5, urgency 4. AI medical imaging assistance: impact 4, urgency 3. ISO 7101: impact 4, urgency 5.

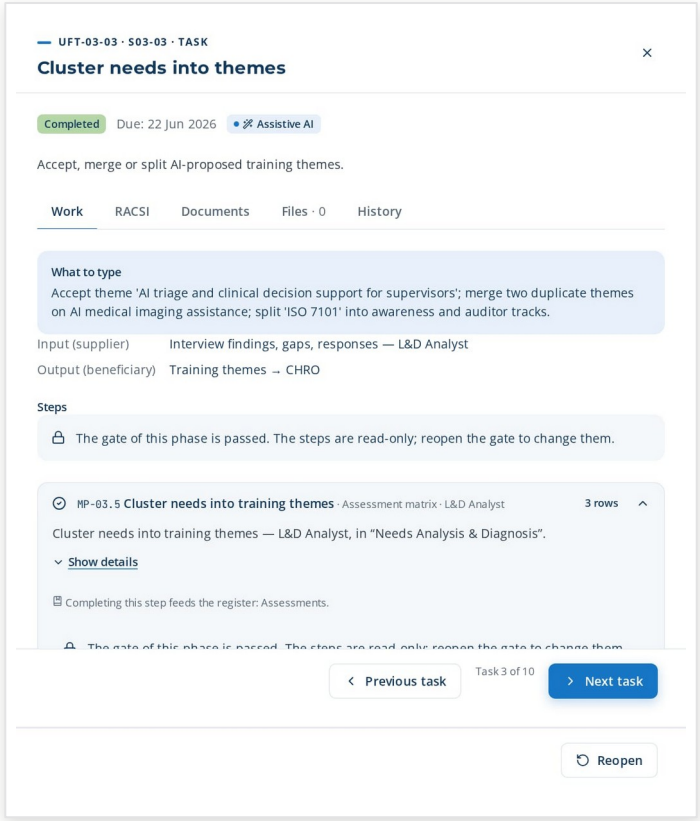


UFT-03-03 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Needs-to-Training Engineering Report & Roadmap (continued)

Task	Steps executed	Owner · done	What was entered
UFT-03-05 **Validate needs register**	**MP-03.7** Validate needs register	Hicham Naciri 27 Jun 2026	Needs register validated: 23 needs, 6 themes. Justification: covers SO-1 and SO-2; sponsor reviewed.
UFT-03-06 **Consolidate engineering inputs**	**MP-04.1** Consolidate feeder outputs **MP-04.2** Check input completeness	Yassine Berrada 30 Jun 2026	Inputs complete: Scope of Work, 187 responses, gap matrix, RAG dashboard, SWOT, demands. Missing: none.
UFT-03-07 **Draft Training Engineering Report**	**MP-04.3** Generate report draft **MP-04.4** Edit and complete report sections	Amine Lahlou 3 Jul 2026	Section 3 'Diagnostic': edit the AI draft, add the interview quote on AI triage and clinical decision support, keep the RAG table.
UFT-03-08 **Run quality review**	**MP-04.5** Run quality review of report **MP-20.5** Run periodic quality review	Soukaina Bennani 6 Jul 2026	Quality review: 11/12 checklist items met; fix item 'sources cited for every figure'. Result: pass after correction.
UFT-03-09 **Sequence and budget roadmap**	**MP-04.6** Sequence roadmap initiatives **MP-18.1** Allocate budget by theme and site	Amine Lahlou 9 Jul 2026	Roadmap: Q2 AI triage and clinical decision support (6 groups); Q3 ISO 7101 (4 groups); Q4 AI medical imaging assistance (3 groups). Total 1,240,000 MAD.
UFT-03-10 **Approve and publish report and roadmap**	**MP-04.7** Submit roadmap for approval **MP-04.8** Record roadmap approval **MP-04.9** Publish approved report and roadmap *+ 1 more steps*	Hicham Naciri 12 Jul 2026	Decision: Approve report and roadmap v1. Justification: within budget, linked to SO-1/SO-2. Publish to all stakeholders.

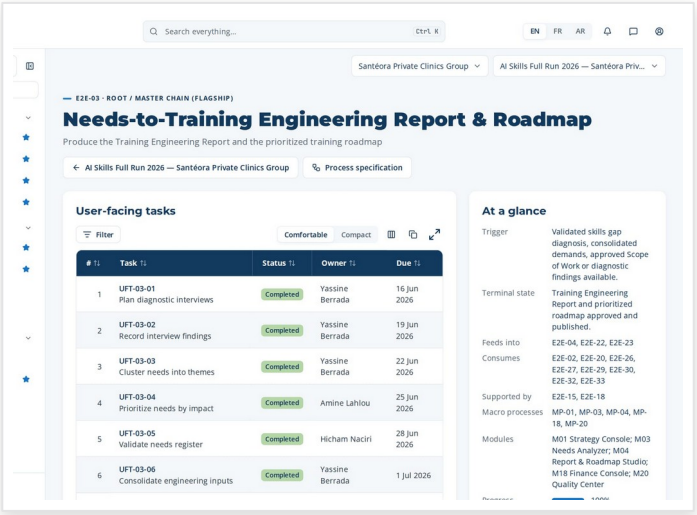

The page of E2E-03 in CortexSkills: its tasks, owners and due dates, and the process card.

Feeds into
E2E-04, E2E-22, E2E-23
Supported by
E2E-15, E2E-18

Prioritization-to-Resource Plan

Prioritize themes and plan days, groups, trainers, budget


TRIGGER
Consolidated training themes requiring prioritization and resource planning.

END STATE
Approved prioritized training plan with days per theme, group planning, trainer allocation, and budget.

7 tasks · 12 steps
20 days · 5 owners · 100 %

Macro processes: MP-49 Training Plan Prioritization & Resource Planning · MP-04 Training Engineering Report & Roadmap Elaboration · MP-18 Financial & Budget Management · MP-11 Administration & Operations · MP-07 Learning Delivery & Implementation

Task	Steps executed	Owner · done	What was entered
UFT-30-01 **Consolidate training themes**	**MP-49.1** Consolidate training themes	Yassine Berrada 15 Jun 2026	Consolidated list: 9 themes from needs, demands, GPEC and SWOT.
UFT-30-02 **Define prioritization criteria**	**MP-49.2** Define prioritization criteria	Amine Lahlou 18 Jun 2026	Criteria: strategic impact 40%, urgency 30%, number of learners 20%, cost 10%.
UFT-30-03 **Prioritize themes**	**MP-49.3** Prioritize themes	Amine Lahlou 21 Jun 2026	Rank 1 AI triage and clinical decision support (score 86); rank 2 ISO 7101 (81); rank 3 AI medical imaging assistance (74).
UFT-30-04 **Estimate days per theme**	**MP-49.4** Estimate days per theme	Hamza Sefrioui 24 Jun 2026	AI triage and clinical decision support: 3 days per group; ISO 7101: 2 days; AI medical imaging assistance: 1.5 days.
UFT-30-05 **Define groups per theme**	**MP-49.5** Define number of groups per theme **MP-49.6** Allocate trainers	Hamza Sefrioui 27 Jun 2026	AI triage and clinical decision support: 6 groups of 12; ISO 7101: 4 groups; AI medical imaging assistance: 3 groups.
UFT-30-06 **Allocate trainers and budget**	**MP-49.7** Estimate plan budget **MP-49.8** Sequence delivery **MP-49.9** Validate plan with governance	Kawtar Chraibi 30 Jun 2026	Trainers: 2 internal, vendor A; budget 1,240,000 MAD (within envelope).

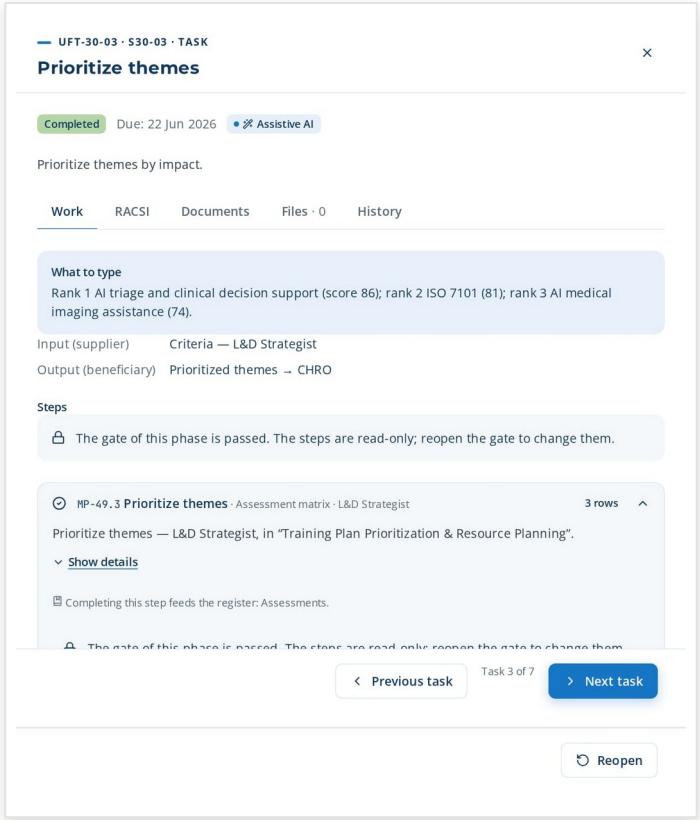


UFT-30-03 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Prioritization-to-Resource Plan (continued)

Task	Steps executed	Owner · done	What was entered
UFT-30-07 **Publish prioritized training plan**	**MP-49.10** Publish prioritized plan **MP-49.11** Track plan execution **MP-49.12** Report on resource utilization	Hicham Naciri 3 Jul 2026	Publish RPT-002 Prioritized Training Plan 2026 to all stakeholders.

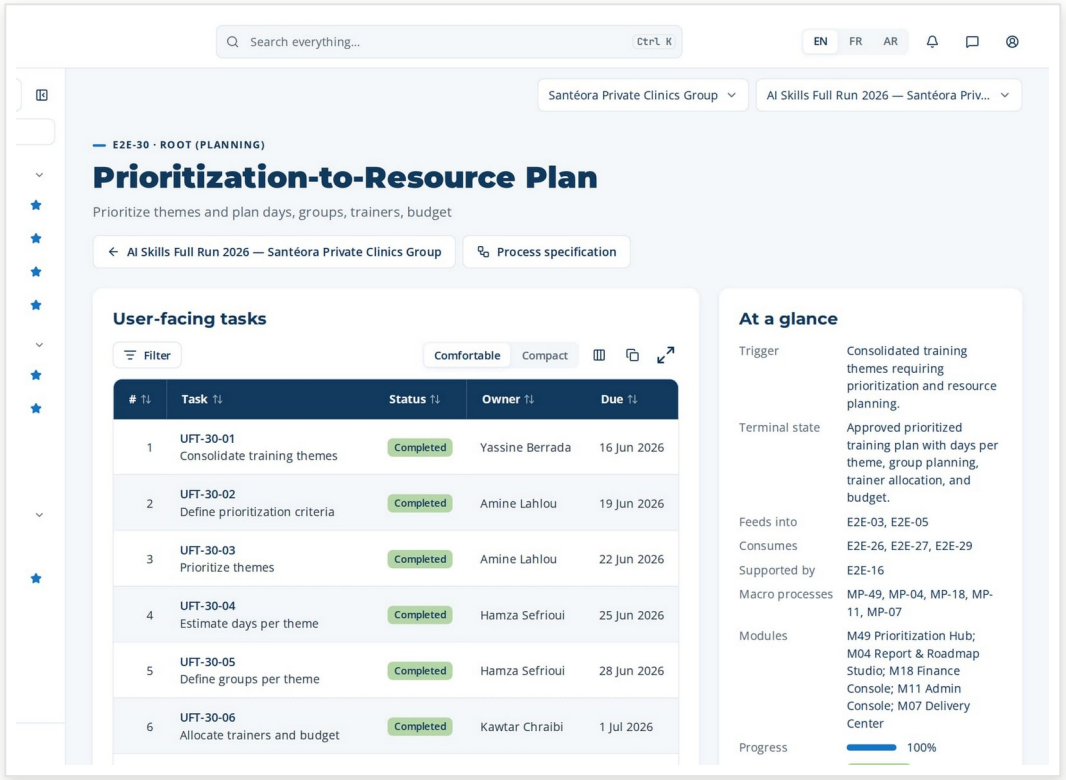

The page of E2E-30 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-49 Training Plan Prioritization & Resource Planning
- MP-04 Training Engineering Report & Roadmap Elaboration
- MP-18 Financial & Budget Management
- MP-11 Administration & Operations
- MP-07 Learning Delivery & Implementation

Feeds into

E2E-03, E2E-05

Supported by

E2E-16

Multi-Site Plan-to-Deployment

Adapt and deploy plans across sites


TRIGGER
Approved roadmap for an organization with several sites or entities.

END STATE
Site plans adapted, validated and deployed, with deviations escalated.

8 tasks · 12 steps
23 days · 4 owners · 100 %

Macro processes: MP-40 Multi-Site / Multi-Entity Training Plan Deployment · MP-04 Training Engineering Report & Roadmap Elaboration · MP-07 Learning Delivery & Implementation · MP-11 Administration & Operations · MP-23 Localization, Accessibility & Inclusion

Task	Steps executed	Owner · done	What was entered
UFT-22-01 **Split plan by site**	**MP-40.1** Split plan by site	Hicham Naciri 15 Jun 2026	Split plan into 3 sites: Casablanca 55%, Tanger 30%, Agadir 15%.
UFT-22-02 **Adapt site plan to local constraints**	**MP-40.2** Adapt site plan to local constraints	Imane Hajji 18 Jun 2026	Tanger: shift constraints → sessions of 4 hours instead of full days.
UFT-22-03 **Localize site materials**	**MP-23.1** Request translation **MP-23.3** Validate translation **MP-23.6** Review participation equity *+ 1 more steps*	Ghita Bouzidi 21 Jun 2026	Agadir materials translated to AR; validated by the site expert.
UFT-22-04 **Validate site plan**	**MP-40.3** Validate site plan	Hicham Naciri 24 Jun 2026	Site plans validated centrally; budget deviation within ±5%.
UFT-22-05 **Schedule site sessions**	**MP-07.1** Create training session **MP-11.1** Book rooms and equipment	Reda Hajji 27 Jun 2026	Tanger schedule: 8 sessions, rooms booked, 2 trainers.
UFT-22-06 **Deploy site schedule**	**MP-40.4** Deploy site schedule	Imane Hajji 30 Jun 2026	Schedules deployed and communicated to site managers.
UFT-22-07 **Consolidate site status**	**MP-40.5** Consolidate site status	Hicham Naciri 3 Jul 2026	Status: Casablanca 70%, Tanger 45%, Agadir 20% delivered.

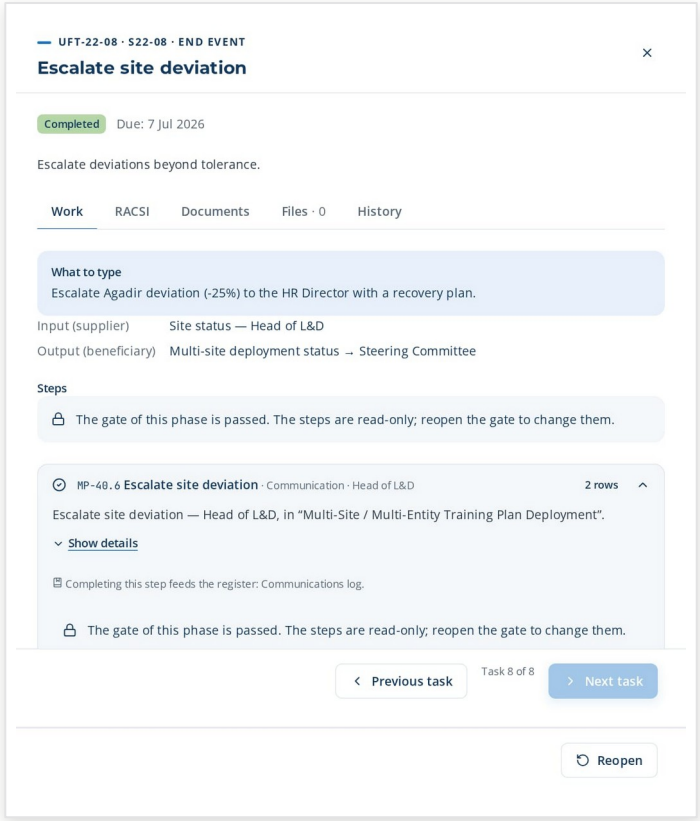


UFT-22-08 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Multi-Site Plan-to-Deployment (continued)

Task	Steps executed	Owner · done	What was entered
UFT-22-08 **Escalate site deviation**	**MP-40.6** Escalate site deviation	Hicham Naciri 6 Jul 2026	Escalate Agadir deviation (-25%) to the HR Director with a recovery plan.

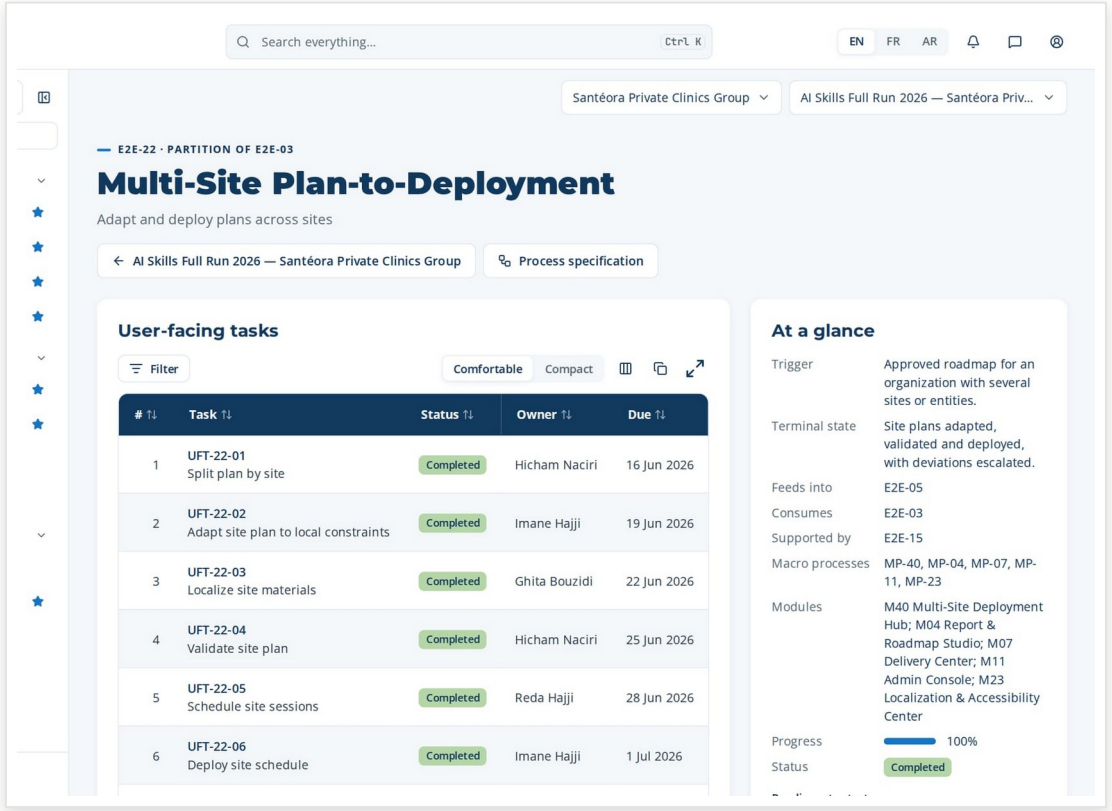

The page of E2E-22 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-40 Multi-Site / Multi-Entity Training Plan Deployment
- MP-04 Training Engineering Report & Roadmap Elaboration
- MP-07 Learning Delivery & Implementation
- MP-11 Administration & Operations
- MP-23 Localization, Accessibility & Inclusion

Feeds into

E2E-05

Supported by

E2E-15

Regulatory Submission-to-Validation

Submit and validate training plans with regulatory bodies


TRIGGER
Approved plan requiring external validation or funding (e.g. OFPPT, GIAC-Agro).

END STATE
Plan validated by the regulatory body and evidence archived.

7 tasks · 10 steps
20 days · 2 owners · 100 %

Macro processes: MP-41 External Training Plan Validation & Regulatory Compliance · MP-14 Compliance & Certification Management · MP-18 Financial & Budget Management · MP-20 Quality, Risk & Continuous Improvement

Task	Steps executed	Owner · done	What was entered
UFT-23-01 **Select regulatory template**	**MP-41.1** Select regulatory template	Rachid Kettani 15 Jun 2026	Template: OFPPT special training contracts (CSF) — plan file.
UFT-23-02 **Generate submission file**	**MP-41.2** Generate submission file **MP-20.5** Run periodic quality review	Rachid Kettani 18 Jun 2026	Submission file generated: plan, themes, providers, costs; quality check passed.
UFT-23-03 **Submit plan to regulatory body**	**MP-41.3** Submit plan to regulatory body	Rachid Kettani 21 Jun 2026	Submitted to the regional funding committee on 5 March; reference GSF-2026-118.
UFT-23-04 **Track submission status**	**MP-41.4** Track submission status	Rachid Kettani 24 Jun 2026	Status: additional document requested (provider accreditation) — sent on 12 March.
UFT-23-05 **Record regulator decision**	**MP-41.5** Record regulator decision **MP-14.1** Register regulatory requirement	Rachid Kettani 27 Jun 2026	Decision: approved with a cap of 520,000 MAD.
UFT-23-06 **Submit refund claims**	**MP-18.5** Submit refund claims	Kawtar Chraibi 30 Jun 2026	Refund claims submitted for 12 delivered actions: 318,000 MAD.
UFT-23-07 **Archive submission evidence**	**MP-41.6** Archive submission evidence **MP-18.6** Close budget period	Rachid Kettani 3 Jul 2026	Archive file, decision and claims; retention 10 years.

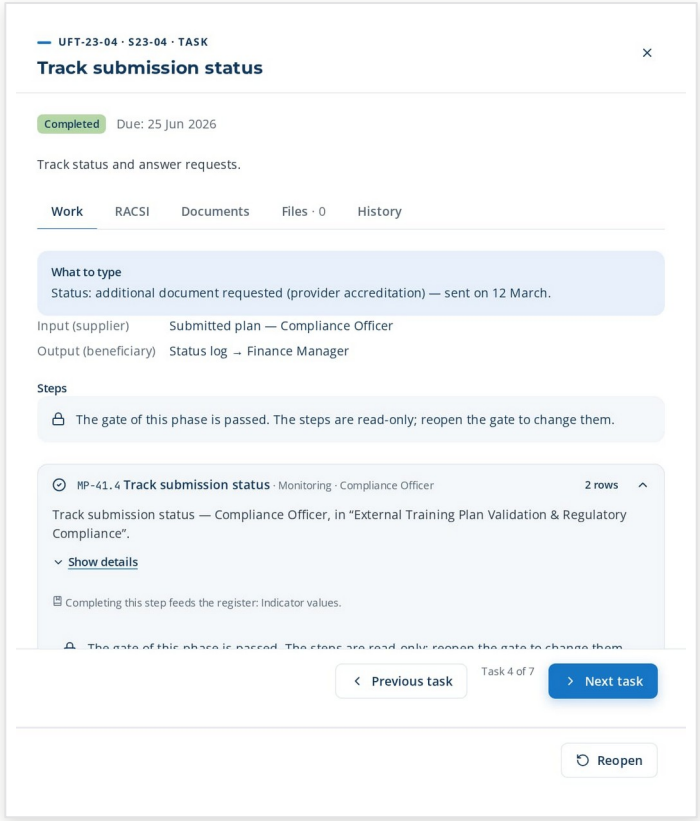

UFT-23-04 opened in CortexSkills: what to enter, its steps and its result.

Vendor-to-Finance

Manage vendors from selection to payment


TRIGGER
Training need requiring an external provider.

END STATE
Vendor selected, order issued and payment approved against attendance.

6 tasks · 10 steps
17 days · 3 owners · 100 %

Macro processes: MP-15 Vendor & Partner Ecosystem Management · MP-18 Financial & Budget Management · MP-11 Administration & Operations

Task	Steps executed	Owner · done	What was entered
UFT-16-01 **Issue request for proposal**	**MP-15.1** Issue request for proposal	Youssef Hajji 15 Jun 2026	RFP 'Training on AI triage and clinical decision support' sent to 4 vendors, answers due 15 May.
UFT-16-02 **Score vendor proposals**	**MP-15.2** Score vendor proposals	Youssef Hajji 18 Jun 2026	Scores: vendor A 82, vendor B 76, vendor C 64 (price 40%, expertise 40%, references 20%).
UFT-16-03 **Register and verify vendor**	**MP-15.3** Register vendor record **MP-15.4** Verify vendor accreditation	Youssef Hajji 21 Jun 2026	Register vendor A; accreditation OFPPT verified, valid until December.
UFT-16-04 **Issue purchase order**	**MP-15.5** Issue purchase order **MP-18.3** Record committed and actual costs	Youssef Hajji 24 Jun 2026	Purchase order PO-2026-044: 180,000 MAD on budget line 'AI triage and clinical decision support'.
UFT-16-05 **Match invoice to order and attendance**	**MP-15.6** Match invoice to order and attendance **MP-11.5** Reconcile attendance with invoices	Reda Hajji 27 Jun 2026	Invoice matched with PO and attendance (3 days × 12 learners): OK.

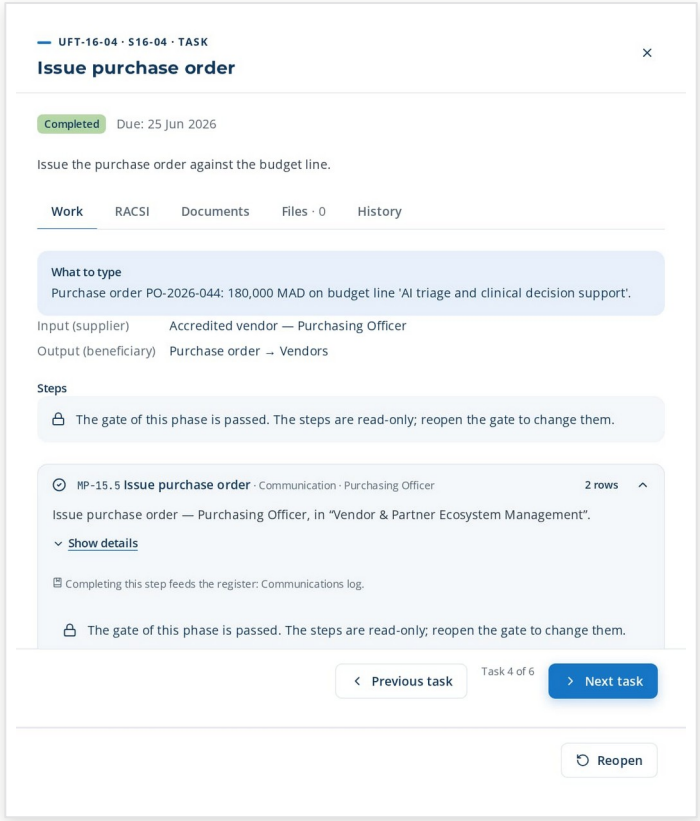


UFT-16-04 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Vendor-to-Finance (continued)

Task	Steps executed	Owner · done	What was entered
UFT-16-06 **Approve vendor payment**	**MP-15.7** Approve vendor payment **MP-18.4** Compare spend against budget	Kawtar Chraibi 30 Jun 2026	Approve payment 180,000 MAD; vendor performance rating 4/5.

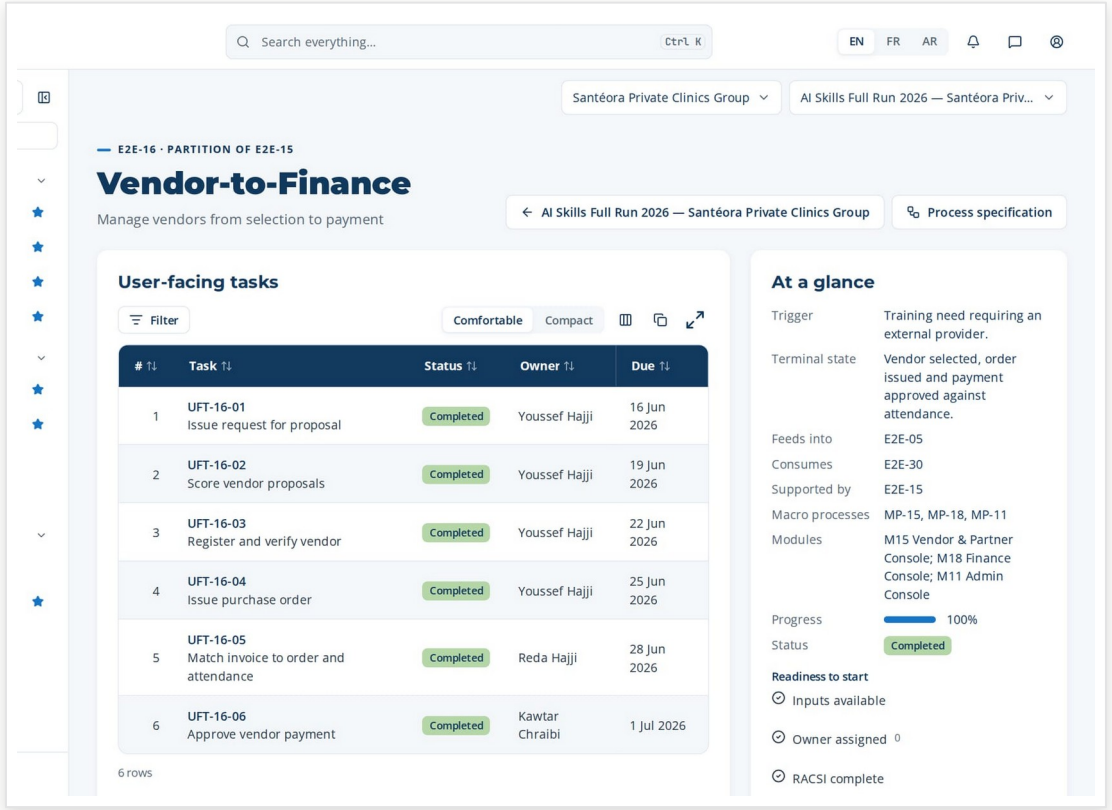

The page of E2E-16 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-15 Vendor & Partner Ecosystem Management
- MP-18 Financial & Budget Management
- MP-11 Administration & Operations

Feeds into

E2E-05

Supported by

E2E-15

Healthcare Providers Critical-Skills-to-Transformation Plan

Turn critical-skill gaps and digital and AI use cases into a transformation plan.


TRIGGER
Annual plan cycle or technology change in Healthcare Providers.

END STATE
Transformation learning paths approved.

4 tasks · 7 steps
11 days · 4 owners · 100 %

Macro processes: MP-02 Skills & Competency Management · MP-03 Needs Analysis & Diagnosis · MP-05 Learning Design & Curriculum Engineering · HCPR-MP-02 HCPR-MP-02

Task	Steps executed	Owner · done	What was entered
UFT-HCPR-E2-01 **List critical Clinical Care & Nursing skills**	**MP-02.1** Define competency families and levels **MP-03.1** Compute gap matrix	Yassine Berrada 15 Jun 2026	Critical skills: 6 for Clinical Care & Nursing, each with target level 3.
UFT-HCPR-E2-02 **List digital and AI use cases**	**MP-03.3** Plan diagnostic interviews	Amine Lahlou 18 Jun 2026	Use cases: AI triage and clinical decision support; AI medical imaging assistance; AI bed and staff capacity planning.
UFT-HCPR-E2-03 **Forecast impacted roles**	**MP-03.5** Cluster needs into training themes **MP-28.3** Forecast skill gaps	Anas Hajji 21 Jun 2026	Impacted roles: supervisors (high), operators (medium); accept the AI forecast.
UFT-HCPR-E2-04 **Approve transformation paths**	**MP-05.2** Define learning path and modules **MP-05.7** Approve design document	Ghita Bouzidi 24 Jun 2026	Approve 2 transformation paths: 'AI triage and clinical decision support for supervisors', 'AI medical imaging assistance for operators'.

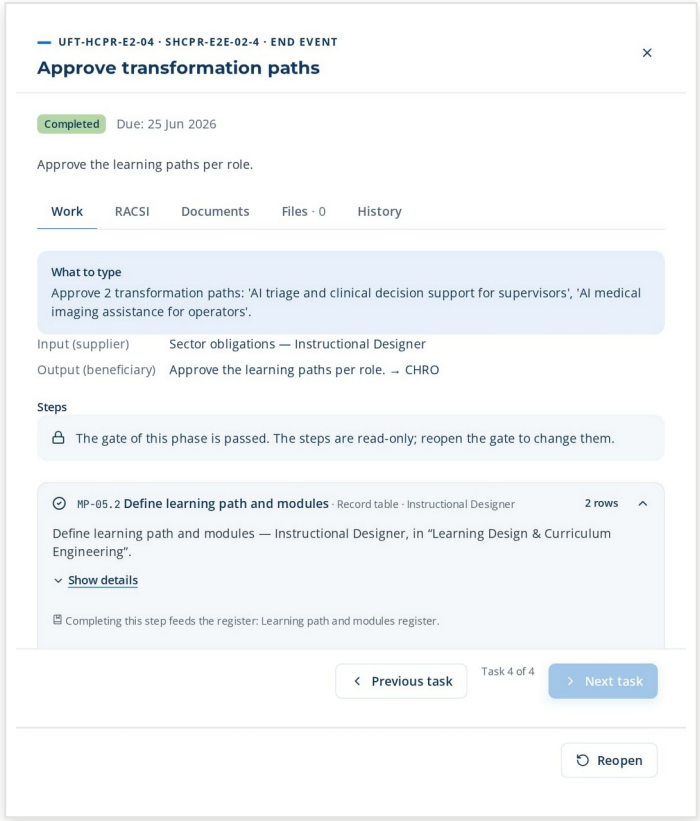

UFT-HCPR-E2-04 opened in CortexSkills: what to enter, its steps and its result.

04

PHASE 4

Design & delivery

5 processes · 39 tasks · 99 steps

11 Jul 2026 – 6 Aug 2026

Closed by G4 — Delivery readiness

E2E-04 Roadmap-to-Curriculum Design

E2E-05 Design-to-Delivery

E2E-06 Learner-Journey-to-Engagement

E2E-13 Content-Curate-to-Retire

E2E-14 Extended-Enterprise-Training

Roadmap-to-Curriculum Design

Convert roadmap into curriculum maps, learning paths, design documents


TRIGGER
Approved Training Engineering Report and roadmap published.

END STATE
Approved curriculum maps, learning paths and design documents.

8 tasks · 15 steps
23 days · 3 owners · 100 %

Macro processes: MP-04 Training Engineering Report & Roadmap Elaboration · MP-05 Learning Design & Curriculum Engineering · MP-06 Content & Resource Management · MP-23 Localization, Accessibility & Inclusion

Task	Steps executed	Owner · done	What was entered
UFT-04-01 **Create curriculum map**	**MP-05.1** Create curriculum map from roadmap	Ghita Bouzidi 13 Jul 2026	Curriculum map 'AI triage and clinical decision support': 3 learning paths (operators, supervisors, managers), 9 modules.
UFT-04-02 **Define learning paths and modules**	**MP-05.2** Define learning path and modules	Ghita Bouzidi 16 Jul 2026	Path 'Supervisors — AI triage and clinical decision support': 4 modules, 3 days blended (1 day e-learning, 2 days workshop).
UFT-04-03 **Write learning objectives**	**MP-05.3** Write learning objectives per module	Ghita Bouzidi 19 Jul 2026	Objective M1: 'By the end, the supervisor reads the AI triage and clinical decision support dashboard and decides the shift action in 5 minutes.'
UFT-04-04 **Propose module structure**	**MP-05.4** Propose module structure	Ghita Bouzidi 22 Jul 2026	Accept the proposed structure (intro, demo, practice, quiz); replace the quiz by a live case from Clinical Care & Nursing.

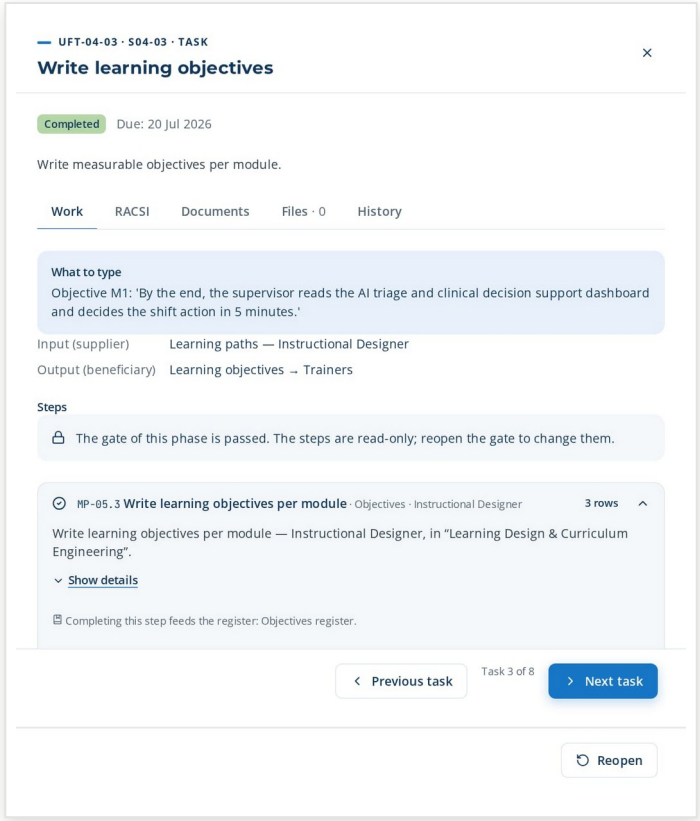


UFT-04-03 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Roadmap-to-Curriculum Design (continued)

Task	Steps executed	Owner · done	What was entered
UFT-04-05 **Set assessment strategy**	**MP-05.5** Set assessment strategy	Ghita Bouzidi 25 Jul 2026	Assessment: pre/post test (Level 2) and manager observation after 30 days (Level 3).
UFT-04-06 **Develop and tag content**	**MP-06.1** Upload content assets **MP-06.2** Validate package format **MP-06.5** Tag content with competencies	Anas Hajji 28 Jul 2026	Upload 'M1_AI triage and clinical decision support.pptx' and 'M1_video.mp4'; tag competency 'AI triage and clinical decision support' level 3.
UFT-04-07 **Localize and check accessibility**	**MP-23.1** Request translation **MP-23.2** Draft machine translation **MP-23.3** Validate translation *+ 2 more steps*	Ghita Bouzidi 31 Jul 2026	Request FR and AR versions; validate the AI draft translation; accessibility check: 0 blocking issues.
UFT-04-08 **Approve design document**	**MP-05.6** Review design with subject matter expert **MP-05.7** Approve design document	Hicham Naciri 3 Aug 2026	Decision: design approved. Comment: SME review done on 12 May; ready for delivery.



The page of E2E-04 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-04 Training Engineering Report & Roadmap Elaboration
- MP-05 Learning Design & Curriculum Engineering
- MP-06 Content & Resource Management
- MP-23 Localization, Accessibility & Inclusion

Feeds into

E2E-05, E2E-11

Supported by

E2E-18

Design-to-Delivery

Deliver training across all modalities


TRIGGER
Approved design document and prioritized training plan.

END STATE
Training delivered across all modalities with attendance and completion recorded.

9 tasks · 27 steps
26 days · 4 owners · 100 %

Macro processes: MP-05 Learning Design & Curriculum Engineering · MP-06 Content & Resource Management · MP-07 Learning Delivery & Implementation · MP-11 Administration & Operations · MP-17 Identity, Access & Security Management · MP-25 Microlearning & Learning in the Flow of Work · MP-30 Immersive Learning (VR/AR/Simulation)

Task	Steps executed	Owner · done	What was entered
UFT-05-01 **Publish content to catalog**	**MP-06.3** Route content for expert review **MP-06.4** Record review decision **MP-06.6** Publish content to catalog	Anas Hajji 13 Jul 2026	Publish module 'M1 AI triage and clinical decision support' to the catalog; audience: supervisors; languages EN/FR/AR.
UFT-05-02 **Book logistics**	**MP-11.1** Book rooms and equipment **MP-11.2** Manage trainer calendars	Reda Hajji 16 Jul 2026	Room 'Training A' (20 seats) 3-5 June; projector; trainer calendar blocked.
UFT-05-03 **Schedule sessions**	**MP-07.1** Create training session **MP-07.2** Check scheduling conflicts	Reda Hajji 19 Jul 2026	Session S-01 'AI triage and clinical decision support — supervisors', 3-5 June, 12 seats, no conflict reported.
UFT-05-04 **Enroll learners and send convocations**	**MP-07.3** Enroll learners into session **MP-07.4** Send convocations **MP-17.1** Provision users via SSO	Reda Hajji 22 Jul 2026	Enroll 12 supervisors; convocations sent by e-mail and SMS in each learner's language.
UFT-05-05 **Push microlearning capsules**	**MP-25.1** Author microlearning capsule **MP-25.2** Generate capsule draft from source **MP-25.3** Push capsule to collaboration channel *+ 2 more steps*	Ghita Bouzidi 25 Jul 2026	Capsule '5-minute AI medical imaging assistance check' pushed to the Teams channel of Clinical Care & Nursing; 48 views in week 1.

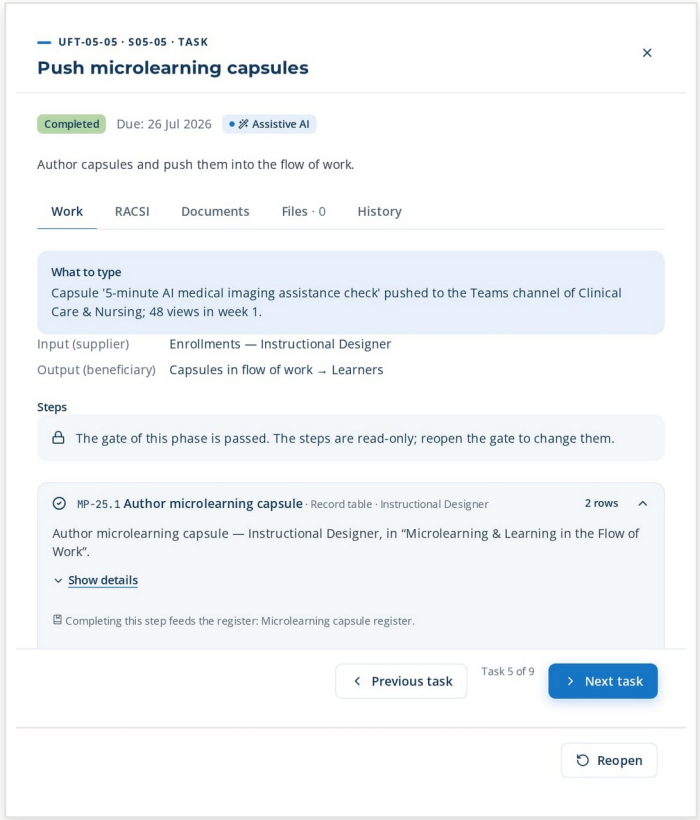


UFT-05-05 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Design-to-Delivery (continued)

Task	Steps executed	Owner · done	What was entered
UFT-05-06 **Run immersive simulations**	**MP-30.1** Define simulation scenario **MP-30.2** Configure simulation scoring **MP-30.3** Launch simulation session *+ 3 more steps*	Zineb Kettani 28 Jul 2026	Simulation 'Clinical Care & Nursing incident': score 78/100; debrief notes recorded; evidence saved.
UFT-05-07 **Record attendance**	**MP-07.5** Record attendance	Zineb Kettani 31 Jul 2026	Attendance S-01: 11 present, 1 absent (justified). Signature sheet attached.
UFT-05-08 **Close sessions**	**MP-07.6** Close session and record completion	Reda Hajji 3 Aug 2026	Close S-01: 11 completions recorded; certificate issued to each participant.
UFT-05-09 **Reconcile and archive period**	**MP-11.5** Reconcile attendance with invoices **MP-11.6** Archive period records **MP-11.3** Import external training records *+ 1 more steps*	Reda Hajji 6 Aug 2026	Reconcile invoice INV-2026-118 (3 days × 12 learners) with attendance; archive period Q2.

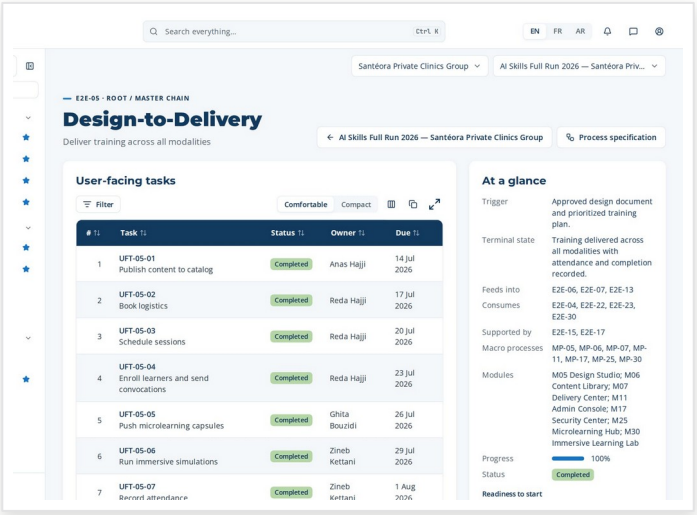

The page of E2E-05 in CortexSkills: its tasks, owners and due dates, and the process card.

Feeds into
E2E-06, E2E-07, E2E-13
Supported by
E2E-15, E2E-17

Learner-Journey-to-Engagement

Deliver personalized, engaging learning experience


TRIGGER
Learner enrolled in a learning path or session.

END STATE
Personalized learning journey completed with engagement measured.

8 tasks · 33 steps
23 days · 5 owners · 100 %

Macro processes: MP-08 Learner Experience & Engagement · MP-24 AI-Powered Personalization & Adaptive Learning · MP-25 Microlearning & Learning in the Flow of Work · MP-26 Social & Collaborative Learning Networks · MP-27 Gamification & Engagement Mechanics

Task	Steps executed	Owner · done	What was entered
UFT-06-01 **Generate personal learning plan**	**MP-08.1** Generate personal learning plan	Yassine Berrada 13 Jul 2026	Personal plan generated for each learner: 3 items on AI triage and clinical decision support, 1 capsule on AI medical imaging assistance.
UFT-06-02 **Recommend learning items**	**MP-08.2** Recommend learning items **MP-24.1** Enable personalization per scope	Reda Sefrioui 16 Jul 2026	Accept 2 recommendations, reject 1 ('already mastered'). The outcome is logged.
UFT-06-03 **Adapt path to performance**	**MP-24.2** Set adaptation rules **MP-24.3** Adapt path to learner performance **MP-24.4** Record learner response to adaptation	Ghita Bouzidi 19 Jul 2026	Rule: if the quiz score < 60%, add the remedial capsule 'AI triage and clinical decision support basics'.
UFT-06-04 **Animate social learning**	**MP-26.1** Create learning cohort group **MP-26.2** Invite group members **MP-26.3** Post question or answer *+ 3 more steps*	Asmae Ziani 22 Jul 2026	Create cohort 'AI triage and clinical decision support supervisors 2026' and invite 12 members; first question posted.

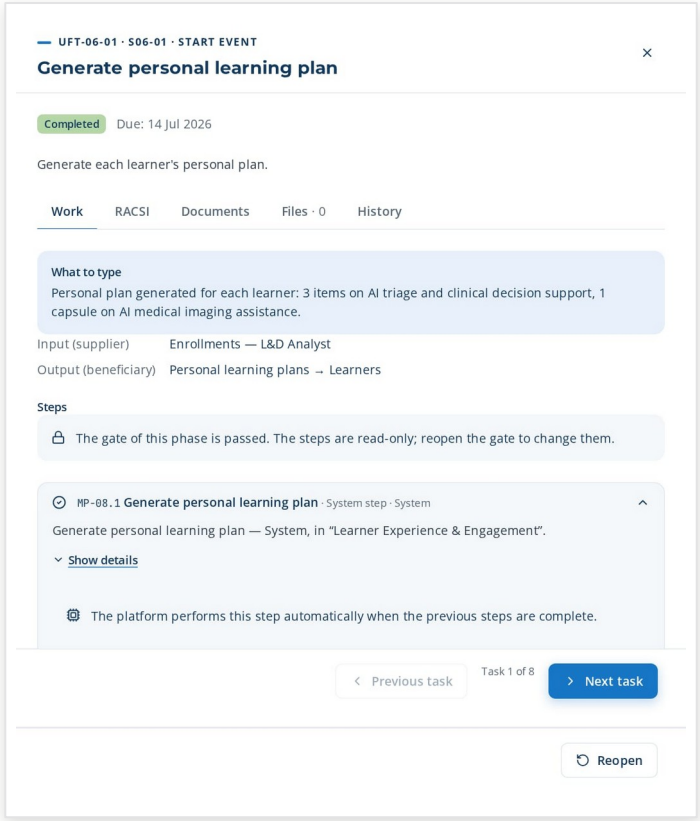


UFT-06-01 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Learner-Journey-to-Engagement (continued)

Task	Steps executed	Owner · done	What was entered
UFT-06-05 **Run gamification**	**MP-27.1** Define points and badge rules **MP-27.2** Configure leaderboard scope **MP-27.3** Award points on completion *+ 2 more steps*	Ghita Bouzidi 25 Jul 2026	Badge 'AI triage and clinical decision support Practitioner' for completing 3 modules; 10 points per capsule.
UFT-06-06 **Match and run coaching**	**MP-21.1** Request coaching **MP-21.2** Match coach to learner **MP-21.3** Schedule coaching sessions *+ 3 more steps*	Nadia Lahlou 28 Jul 2026	Match coach 'Senior Clinical Care & Nursing supervisor' to 3 learners; 4 sessions of 1 hour.
UFT-06-07 **Collect learner feedback**	**MP-08.3** Enroll in recommended item **MP-08.4** Submit learning feedback	Reda Sefrioui 31 Jul 2026	Feedback: 4.4/5; comment 'more real cases from Clinical Care & Nursing'.
UFT-06-08 **Monitor engagement and nudge**	**MP-08.5** Monitor engagement indicators **MP-08.6** Trigger re-engagement nudge **MP-24.5** Review recommendation acceptance *+ 5 more steps*	Yassine Berrada 3 Aug 2026	Engagement 81%; nudge sent to 9 inactive learners; drop-out risk high for 2 learners.

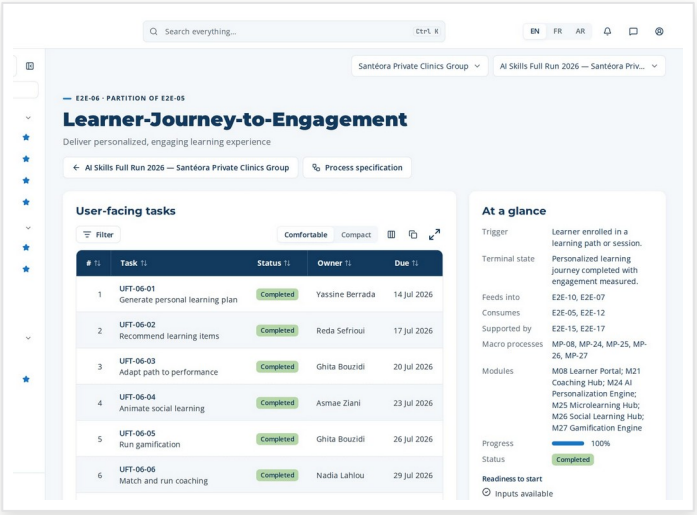

The page of E2E-06 in CortexSkills: its tasks, owners and due dates, and the process card.

Feeds into
E2E-10, E2E-07
Supported by
E2E-15, E2E-17

Content-Curate-to-Retire

Publish, maintain, retire content


TRIGGER
New content published or content past its review date.

END STATE
Catalog curated, maintained and outdated content retired.

7 tasks · 12 steps
20 days · 3 owners · 100 %

Macro processes: MP-06 Content & Resource Management · MP-29 Content Curation & Aggregation Engine · MP-33 User-Generated Content & Peer Knowledge Sharing

Task	Steps executed	Owner · done	What was entered
UFT-13-01 **Aggregate provider catalogs**	**MP-29.1** Aggregate provider catalogs	Hicham Naciri 13 Jul 2026	Aggregate 2 provider catalogs (LinkedIn Learning, Coursera): 1,240 items imported.
UFT-13-02 **Recommend curated items**	**MP-29.2** Recommend curated items	Hicham Naciri 16 Jul 2026	Keep the 15 top-ranked items on AI triage and clinical decision support; reject 3 items older than 3 years.
UFT-13-03 **Approve and organize collections**	**MP-29.3** Approve curated item **MP-29.4** Organize curated collection	Hicham Naciri 19 Jul 2026	Collection 'AI triage and clinical decision support starter kit': 8 items, audience supervisors, review date in 12 months.
UFT-13-04 **Review peer content**	**MP-33.1** Submit user-generated content **MP-33.2** Check content against policy **MP-33.3** Peer review content	Hamza Lahlou 22 Jul 2026	Peer video 'How we use AI medical imaging assistance on shift' reviewed by an expert: approved with 1 correction.
UFT-13-05 **Promote and rate content**	**MP-33.5** Send approved content to curation **MP-33.6** Rate user-generated item	Asmae Ziani 25 Jul 2026	Send approved peer content to curation; average learner rating 4.5/5.
UFT-13-06 **Flag content past review date**	**MP-29.5** Flag content past review date	Hicham Naciri 28 Jul 2026	14 items past review date flagged; owners notified.

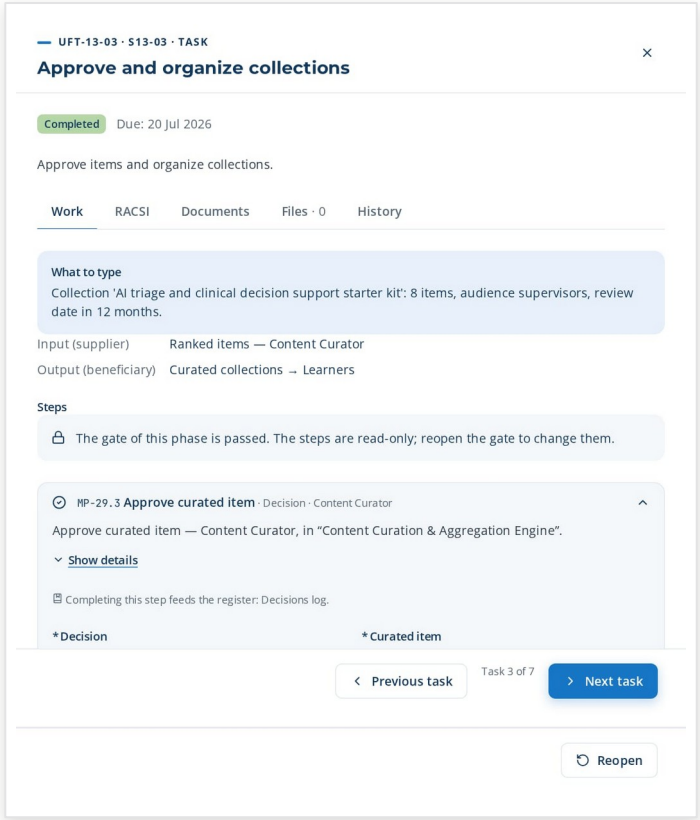


UFT-13-03 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Content-Curate-to-Retire (continued)

Task	Steps executed	Owner · done	What was entered
UFT-13-07 **Retire outdated content**	**MP-29.6** Retire outdated content **MP-25.6** Retire low-value capsule	Hicham Naciri 31 Jul 2026	Retire 6 outdated items and 2 low-value capsules; library health 92%.

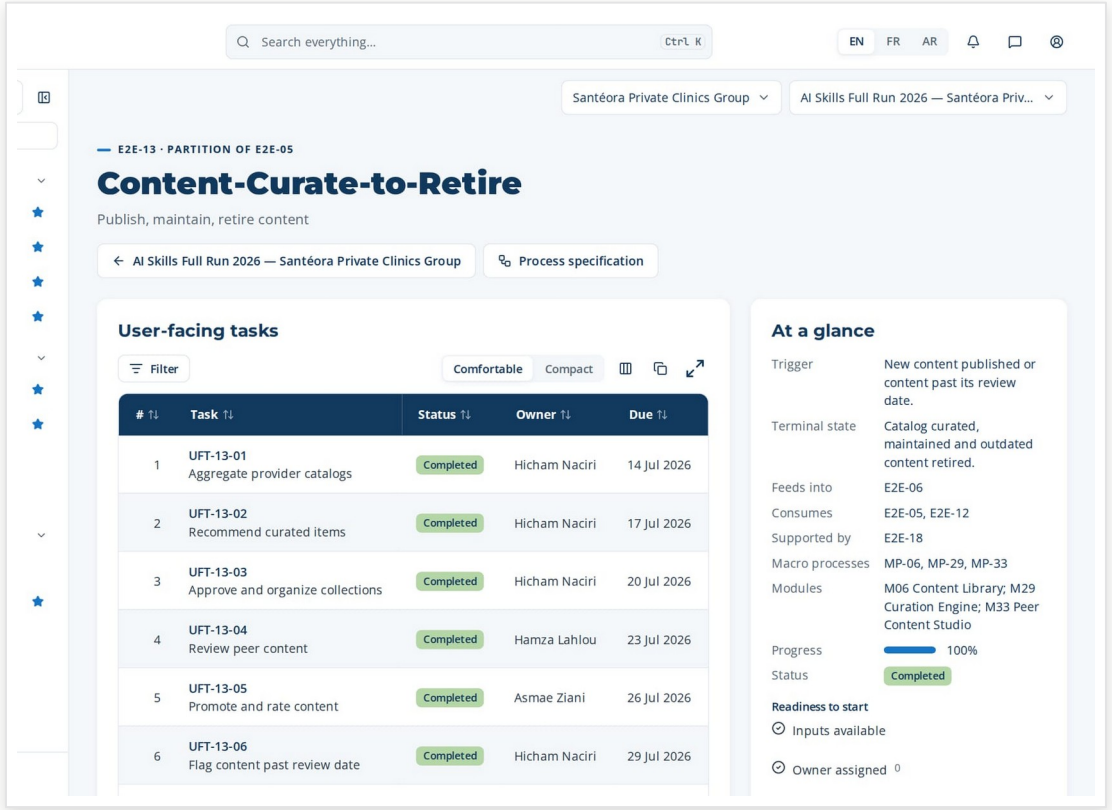

The page of E2E-13 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-06 Content & Resource Management
- MP-29 Content Curation & Aggregation Engine
- MP-33 User-Generated Content & Peer Knowledge Sharing

Feeds into

E2E-06

Supported by

E2E-18

Extended-Enterprise-Training

Certify partners and train customers


TRIGGER
Partner, reseller or customer training program launched.

END STATE
External learners trained, paid and certified.

7 tasks · 12 steps
20 days · 3 owners · 100 %

Macro processes: MP-22 Extended Enterprise & External Training · MP-07 Learning Delivery & Implementation · MP-14 Compliance & Certification Management · MP-18 Financial & Budget Management

Task	Steps executed	Owner · done	What was entered
UFT-14-01 **Create external sub-portal**	**MP-22.1** Create external sub-portal	Yassine Naciri 13 Jul 2026	Sub-portal 'Partners Academy — Santéora Private Clinics Group' created for distributors and installers.
UFT-14-02 **Configure catalog and pricing**	**MP-22.2** Configure external catalog and pricing **MP-18.1** Allocate budget by theme and site	Yassine Naciri 16 Jul 2026	Catalog: 'ISO 7101 for partners' 1,200 MAD; 'AI triage and clinical decision support certification' 2,400 MAD.
UFT-14-03 **Process payment and enroll**	**MP-22.3** Process online payment **MP-22.4** Enroll external learner	Yassine Naciri 19 Jul 2026	18 online payments processed; 18 external learners enrolled.
UFT-14-04 **Deliver external sessions**	**MP-07.1** Create training session **MP-07.5** Record attendance	Reda Hajji 22 Jul 2026	Session P-01 (virtual), 18 invited, 16 present.
UFT-14-05 **Track external completion**	**MP-22.5** Track external completion	Yassine Naciri 25 Jul 2026	Completion: 15 of 16 passed the final quiz.
UFT-14-06 **Issue partner certification**	**MP-22.6** Issue partner certification **MP-14.4** Issue certificate on completion	Yassine Naciri 28 Jul 2026	Issue 15 partner certificates valid 2 years.

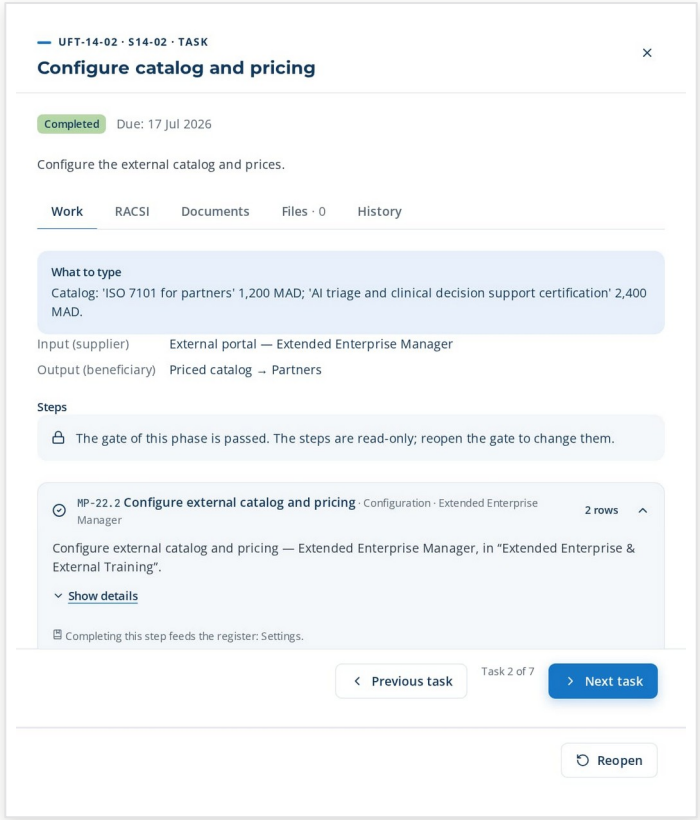


UFT-14-02 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Extended-Enterprise-Training (continued)

Task	Steps executed	Owner · done	What was entered
UFT-14-07 **Reconcile external revenue**	**MP-18.3** Record committed and actual costs **MP-18.4** Compare spend against budget	Kawtar Chraibi 31 Jul 2026	Revenue 43,200 MAD reconciled with the ERP; 0 unpaid.

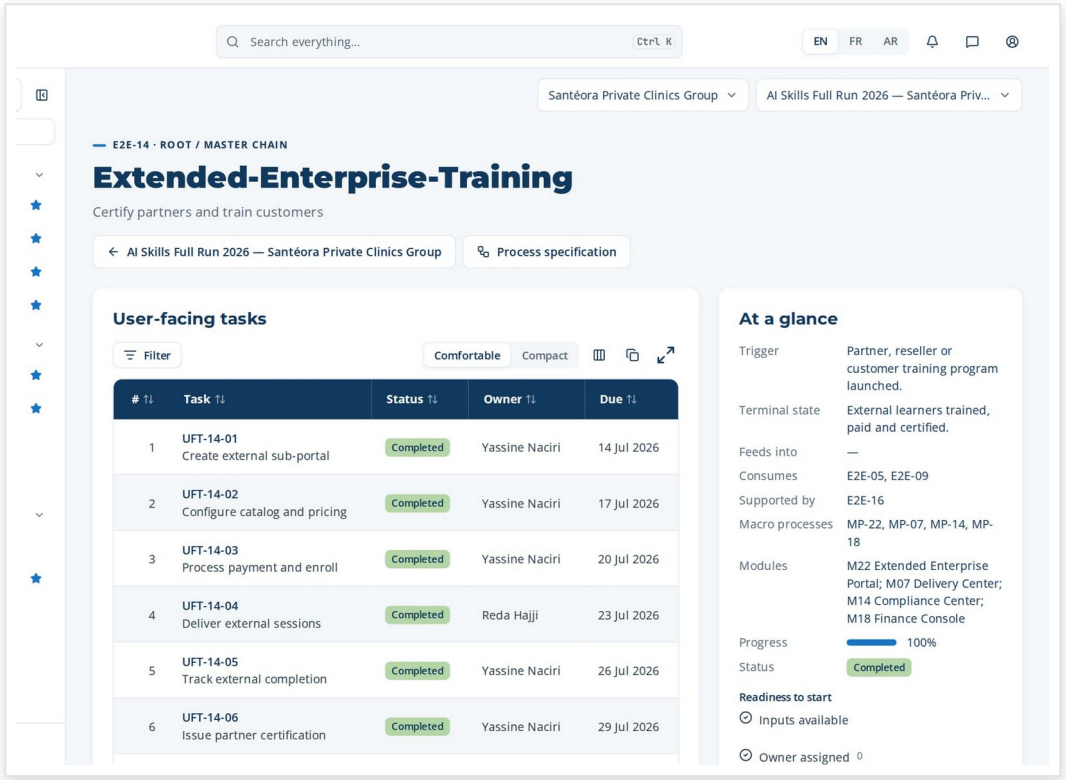

The page of E2E-14 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-22 Extended Enterprise & External Training
- MP-07 Learning Delivery & Implementation
- MP-14 Compliance & Certification Management
- MP-18 Financial & Budget Management

Feeds into

—

Supported by

E2E-16

05

PHASE 5

Evaluation, compliance & impact

4 processes · 26 tasks · 43 steps

8 Aug 2026 – 31 Aug 2026

Closed by G5 — Evaluation & impact validated

E2E-07 Assessment-to-Evaluation

E2E-08 Learning-to-ROI

E2E-09 Compliance-to-Certification

HCPR-E2E-01 Healthcare Providers Compliance-to-Certification Readiness

Assessment-to-Evaluation

Measure training effectiveness and skill progression


TRIGGER
Training session or path completed.

END STATE
Effectiveness measured on Kirkpatrick levels 1-3 and skill progression computed.

8 tasks · 12 steps
23 days · 4 owners · 100 %

Macro processes: MP-09 Assessment & Evaluation · MP-10 Reporting & Analytics · MP-20 Quality, Risk & Continuous Improvement

Task	Steps executed	Owner · done	What was entered
UFT-07-01 **Create assessment instrument**	**MP-09.1** Create assessment instrument	Ghita Bouzidi 10 Aug 2026	Instrument 'Test AI triage and clinical decision support M1': 15 questions, pass mark 70%.
UFT-07-02 **Draft question bank**	**MP-09.2** Generate question bank draft	Ghita Bouzidi 13 Aug 2026	Keep 12 AI-drafted questions, rewrite 3 with Clinical Care & Nursing vocabulary; validate each one.
UFT-07-03 **Collect reaction survey (Level 1)**	**MP-09.3** Collect reaction survey (Level 1)	Yassine Berrada 16 Aug 2026	Reaction survey S-01: 11 responses, satisfaction 4.3/5.
UFT-07-04 **Record learning results (Level 2)**	**MP-09.4** Record learning results (Level 2)	Zineb Kettani 19 Aug 2026	Level 2: average pre-test 48%, post-test 81% (+33 points).
UFT-07-05 **Record on-the-job observation (Level 3)**	**MP-09.5** Record on-the-job observation (Level 3)	Karim El Idrissi 22 Aug 2026	Level 3 (day 30): 9 of 11 supervisors apply the AI triage and clinical decision support routine daily.

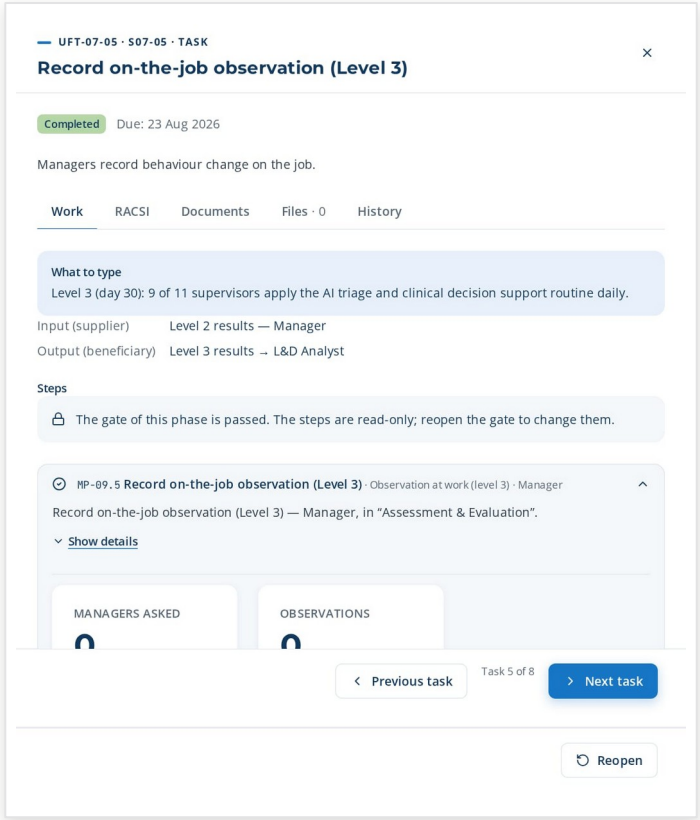


UFT-07-05 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Assessment-to-Evaluation (continued)

Task	Steps executed	Owner · done	What was entered
UFT-07-06 **Compute skill progression**	**MP-09.6** Compute skill progression **MP-10.3** Refresh KPI computation	Yassine Berrada 25 Aug 2026	Skill progression: AI triage and clinical decision support from 1.8 to 2.7 (target 3).
UFT-07-07 **Review evaluation results**	**MP-09.7** Review evaluation results **MP-20.5** Run periodic quality review	Yassine Berrada 28 Aug 2026	Review: module M3 below 70% pass rate → improvement action assigned to the designer.
UFT-07-08 **Publish evaluation report**	**MP-10.4** Export report **MP-10.6** Share insight with stakeholders **MP-10.2** Configure dashboard widgets	Yassine Berrada 31 Aug 2026	Export RPT-016 Kirkpatrick report (PDF) and share with the Steering Committee.

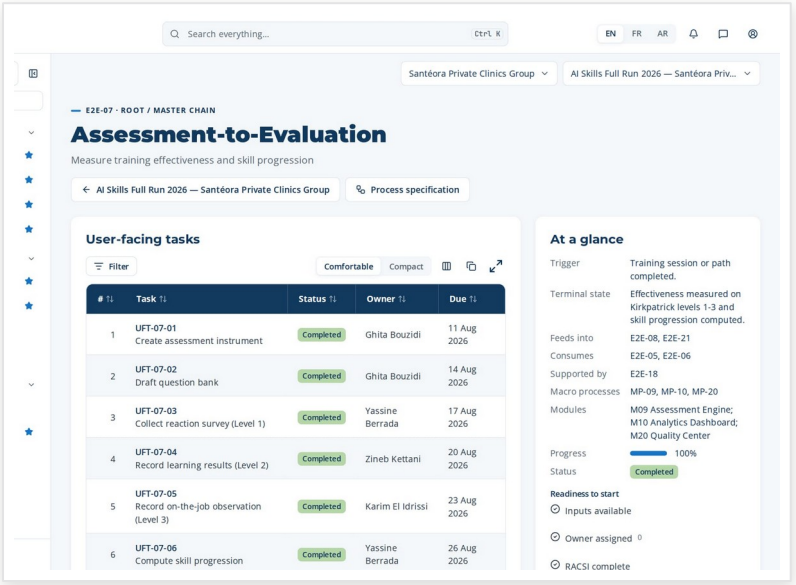

The page of E2E-07 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-09 Assessment & Evaluation
- MP-10 Reporting & Analytics
- MP-20 Quality, Risk & Continuous Improvement

Feeds into

E2E-08, E2E-21

Supported by

E2E-18

Learning-to-ROI

Validate ROI and business impact


TRIGGER
Evaluation results available for a theme selected for an ROI study.

END STATE
Phillips ROI validated with finance and business impact report published.

7 tasks · 12 steps
20 days · 3 owners · 100 %

Macro processes: MP-09 Assessment & Evaluation · MP-10 Reporting & Analytics · MP-18 Financial & Budget Management · MP-32 Learning ROI & Business Impact Measurement

Task	Steps executed	Owner · done	What was entered
UFT-08-01 **Select theme for ROI study**	**MP-32.1** Select theme for ROI study	Anas Hajji 10 Aug 2026	ROI study on theme 'AI triage and clinical decision support' — population: 36 supervisors, 3 sites.
UFT-08-02 **Define business indicators**	**MP-32.2** Define business indicators **MP-10.1** Define KPI set per audience	Anas Hajji 13 Aug 2026	Indicators: rework rate, downtime minutes per shift, data re-entry hours.
UFT-08-03 **Collect cost data**	**MP-18.3** Record committed and actual costs **MP-18.4** Compare spend against budget	Kawtar Chraibi 16 Aug 2026	Costs: design 60,000 MAD; delivery 180,000 MAD; participants' time 95,000 MAD.
UFT-08-04 **Isolate training effect**	**MP-32.3** Isolate training effect **MP-09.6** Compute skill progression	Anas Hajji 19 Aug 2026	Control group: site B (not trained). Isolated benefit: 410,000 MAD per year.
UFT-08-05 **Compute Phillips ROI**	**MP-32.4** Compute Phillips ROI	Anas Hajji 22 Aug 2026	ROI = (410,000 − 335,000) / 335,000 = 22%; benefit-cost ratio 1.22.
UFT-08-06 **Review ROI with finance**	**MP-32.5** Review ROI with finance	Kawtar Chraibi 25 Aug 2026	Finance review: assumptions accepted; downtime valued at 180 MAD per minute.

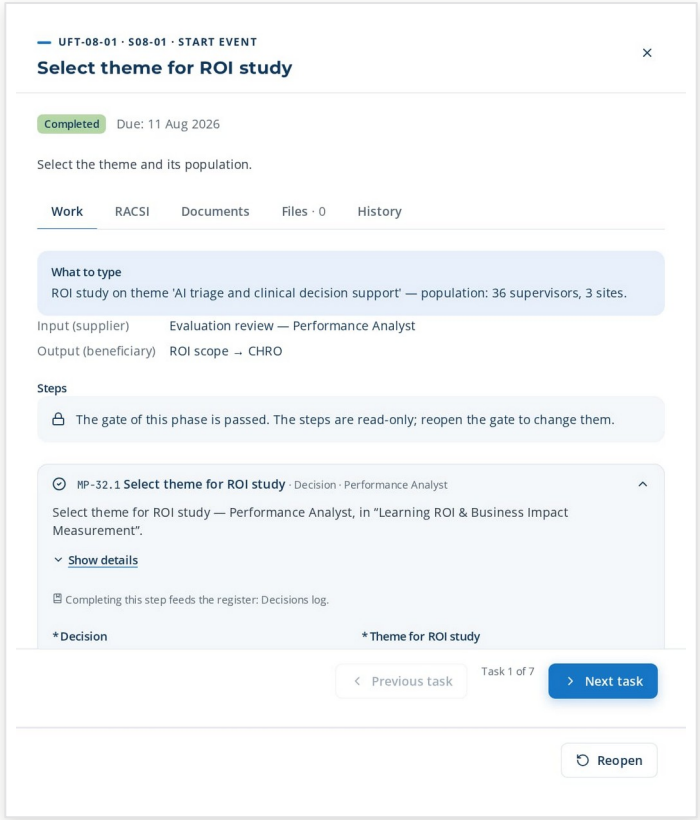


UFT-08-01 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Learning-to-ROI (continued)

Task	Steps executed	Owner · done	What was entered
UFT-08-07 **Publish business impact report**	**MP-32.6** Publish business impact report **MP-10.4** Export report **MP-10.5** Query data via AI Assistant	Hicham Naciri 28 Aug 2026	Publish RPT-012 ROI & Business Impact Report to executive leadership.

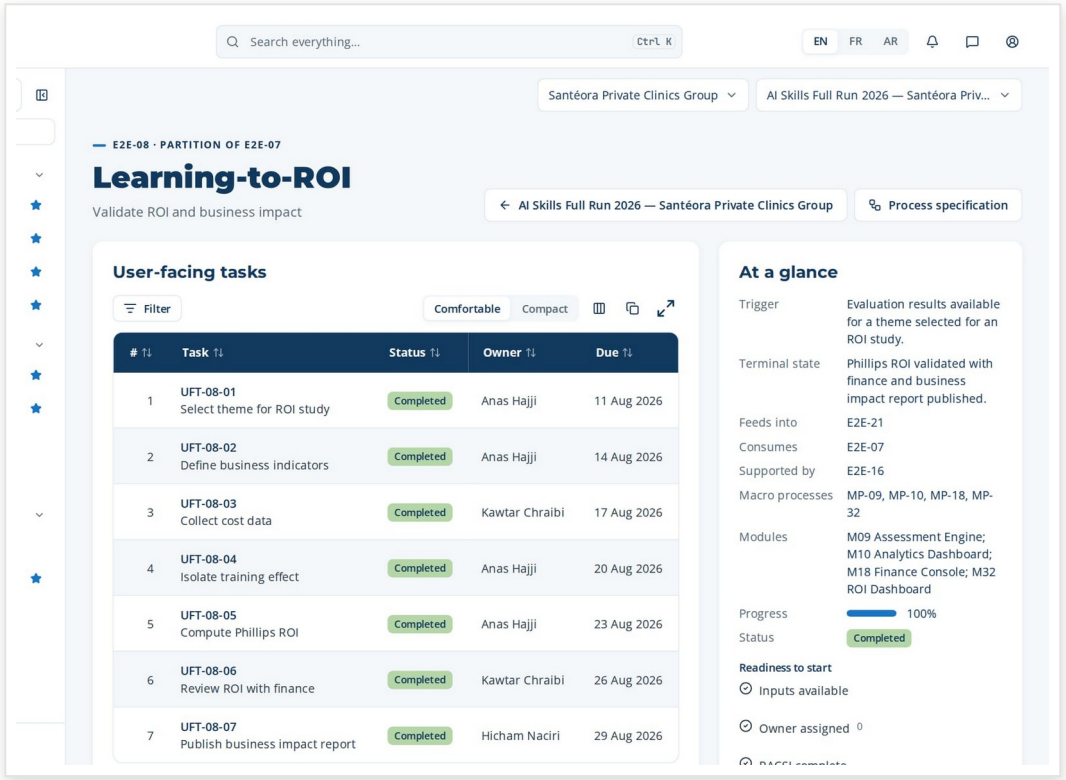

The page of E2E-08 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-09 Assessment & Evaluation
- MP-10 Reporting & Analytics
- MP-18 Financial & Budget Management
- MP-32 Learning ROI & Business Impact Measurement

Feeds into

E2E-21

Supported by

E2E-16

Compliance-to-Certification

Ensure compliant workforce with valid certifications


TRIGGER
New regulatory requirement or certification nearing expiry.

END STATE
Compliant workforce with valid certifications and an audit extract available.

7 tasks · 11 steps
20 days · 3 owners · 100 %

Macro processes: MP-14 Compliance & Certification Management · MP-07 Learning Delivery & Implementation · MP-09 Assessment & Evaluation · MP-10 Reporting & Analytics

Task	Steps executed	Owner · done	What was entered
UFT-09-01 **Register regulatory requirement**	**MP-14.1** Register regulatory requirement	Rachid Kettani 10 Aug 2026	Requirement 'ISO 7101 awareness', every 24 months, source: ISO 7101 clause on competence.
UFT-09-02 **Assign mandatory training**	**MP-14.2** Assign mandatory training by position	Rachid Kettani 13 Aug 2026	Assign to positions: Clinical Care & Nursing operator, Clinical Care & Nursing supervisor, quality inspector.
UFT-09-03 **Deliver mandatory sessions**	**MP-07.3** Enroll learners into session **MP-07.5** Record attendance	Reda Hajji 16 Aug 2026	Enroll 24 employees in session 'ISO 7101 awareness'; attendance recorded.
UFT-09-04 **Assess and certify**	**MP-09.4** Record learning results (Level 2) **MP-14.4** Issue certificate on completion	Zineb Kettani 19 Aug 2026	Result 86%; certificate 'ISO 7101 awareness' issued, valid until 2026+2.
UFT-09-05 **Compute certification validity**	**MP-14.3** Compute certification validity	Rachid Kettani 22 Aug 2026	Validity: 212 valid, 9 expire within 60 days, 3 expired.
UFT-09-06 **Manage renewals**	**MP-14.5** Launch renewal enrollment **MP-14.6** Confirm renewal completion	Rachid Kettani 25 Aug 2026	Launch renewal for the 12 employees; confirm 10 completions, 2 rescheduled.

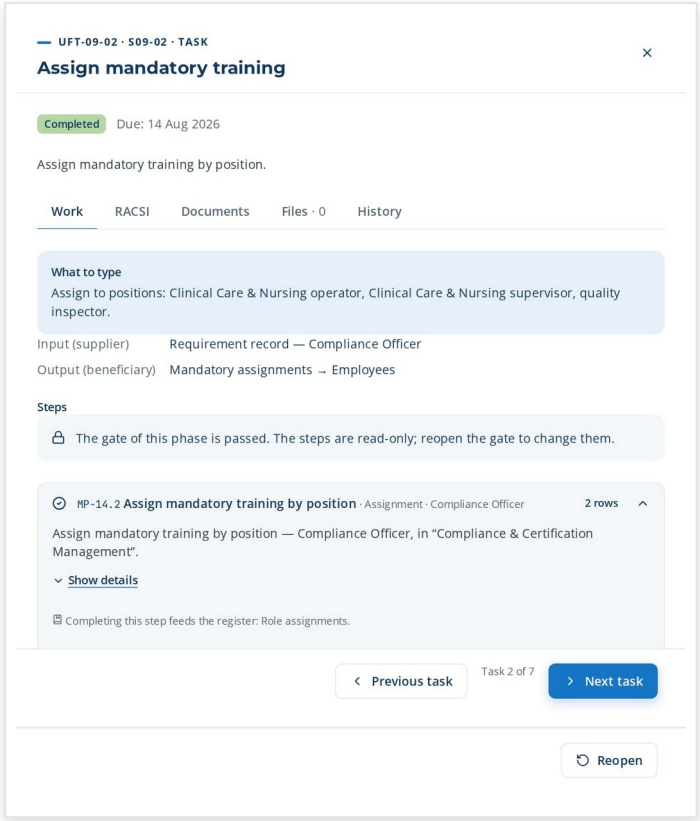


UFT-09-02 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Compliance-to-Certification (continued)

Task	Steps executed	Owner · done	What was entered
UFT-09-07 **Produce compliance audit extract**	**MP-14.7** Produce compliance audit extract **MP-10.4** Export report	Rachid Kettani 28 Aug 2026	Export compliance audit extract for ISO 7101 (XLSX) for the external auditor.

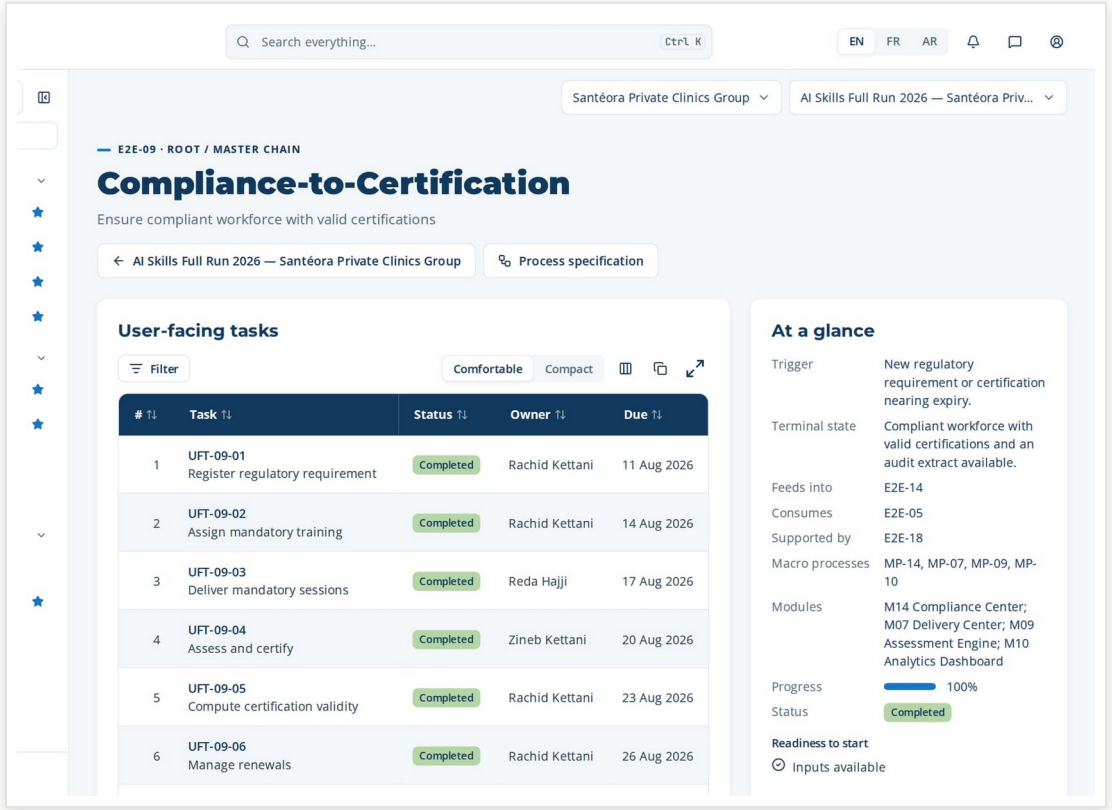

The page of E2E-09 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-14 Compliance & Certification Management
- MP-07 Learning Delivery & Implementation
- MP-09 Assessment & Evaluation
- MP-10 Reporting & Analytics

Feeds into

E2E-14

Supported by

E2E-18

Healthcare Providers Compliance-to-Certification Readiness

Keep Healthcare Providers regulated roles certified against ISO 7101.


TRIGGER
New ISO 7101 requirement or certification expiry.

END STATE
Sector compliance extract issued with every critical role certified.

4 tasks · 8 steps
11 days · 2 owners · 100 %

Macro processes: MP-01 Strategy & Governance Alignment · MP-02 Skills & Competency Management · MP-14 Compliance & Certification Management · HCPR-MP-01 HCPR-MP-01

Task	Steps executed	Owner · done	What was entered
UFT-HCPR-E1-01 **Register ISO 7101 obligations**	**MP-01.1** Record corporate strategic objectives **MP-14.1** Register regulatory requirement	Rachid Kettani 10 Aug 2026	Obligation 'ISO 7101 training', every 12 months, owner Compliance Officer.
UFT-HCPR-E1-02 **Link obligations to positions**	**MP-01.2** Link objectives to functions and sites **MP-14.2** Assign mandatory training by position	Karim Chraibi 13 Aug 2026	Linked to 5 Clinical Care & Nursing positions (38 employees).
UFT-HCPR-E1-03 **Track certification validity**	**MP-02.1** Define competency families and levels **MP-14.3** Compute certification validity	Rachid Kettani 16 Aug 2026	Validity: 33 valid, 5 expire within 60 days.
UFT-HCPR-E1-04 **Issue sector compliance extract**	**MP-02.2** Set target levels per position **MP-14.7** Produce compliance audit extract	Rachid Kettani 19 Aug 2026	Extract issued for the ISO 7101 audit on 15 October.

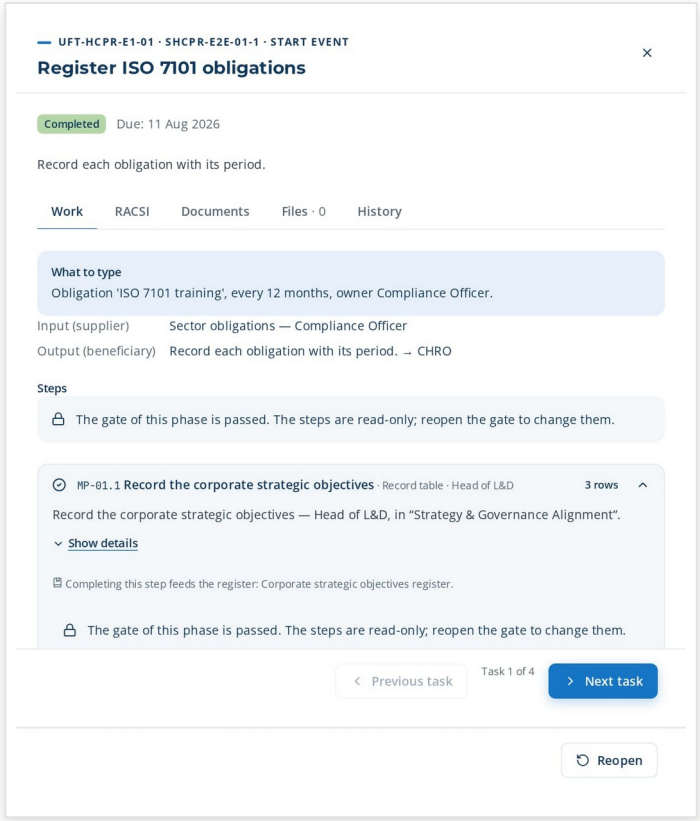

UFT-HCPR-E1-01 opened in CortexSkills: what to enter, its steps and its result.

06

PHASE 6

Talent, knowledge & continuous improvement

4 processes · 30 tasks · 51 steps

5 Sept 2026 – 28 Sept 2026

Closed by G6 — Closure & continuous improvement

E2E-10 Talent-to-Mobility

E2E-11 Onboarding-to-Productivity

E2E-12 Knowledge-Capture-to-Transfer

E2E-31 Engagement-to-Roadmap

Talent-to-Mobility

Enable internal mobility and career progression


TRIGGER
Internal opening published or annual career review.

END STATE
Internal move decided with a reskilling plan assigned.

8 tasks · 18 steps
23 days · 4 owners · 100 %

Macro processes: MP-13 Talent & Career Development · MP-31 Skills-Based Talent Marketplace & Internal Mobility · MP-02 Skills & Competency Management · MP-08 Learner Experience & Engagement

Task	Steps executed	Owner · done	What was entered
UFT-10-01 **Model career paths**	**MP-13.1** Model career path **MP-13.2** Link path steps to competency targets	Mehdi Lahlou 7 Sept 2026	Career path: Clinical Care & Nursing operator → team leader → supervisor, with competency targets per step.
UFT-10-02 **Publish internal opening**	**MP-31.1** Publish internal opening **MP-31.2** Define required skills	Karim Chraibi 10 Sept 2026	Opening 'Clinical Care & Nursing team leader', required skills: AI triage and clinical decision support level 3, leadership level 2.
UFT-10-03 **Match employees to opening**	**MP-31.3** Match employees to opening **MP-02.7** Validate skills inventory	Karim Chraibi 13 Sept 2026	Review 6 AI matches; keep 4 candidates with match score above 75%.
UFT-10-04 **Apply to internal opening**	**MP-31.4** Apply to internal opening	Reda Sefrioui 16 Sept 2026	Application with motivation note and consent of the current manager.
UFT-10-05 **Shortlist candidates**	**MP-31.5** Shortlist candidates	Karim El Idrissi 19 Sept 2026	Shortlist: 2 candidates; interviews on 20 and 21 June.

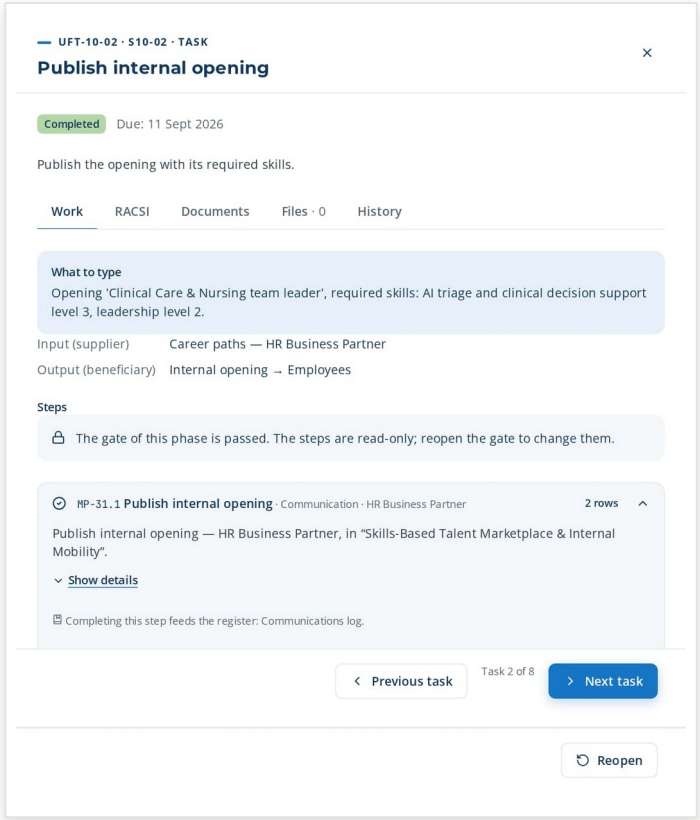


UFT-10-02 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Talent-to-Mobility (continued)

Task	Steps executed	Owner · done	What was entered
UFT-10-06 **Plan individual development**	**MP-13.3** Create individual development plan **MP-13.4** Suggest development actions **MP-42.3** Build leadership development plan *+ 1 more steps*	Karim El Idrissi 22 Sept 2026	Development plan: 2 modules AI triage and clinical decision support, 1 leadership workshop, 3 months mentoring.
UFT-10-07 **Assign reskilling plan**	**MP-31.6** Assign reskilling plan **MP-08.1** Generate personal learning plan	Karim Chraibi 25 Sept 2026	Assign reskilling path 'AI triage and clinical decision support for team leaders' to the selected candidate.
UFT-10-08 **Review career and succession**	**MP-13.5** Run career review **MP-13.6** Update succession readiness **MP-42.5** Review leadership pipeline *+ 1 more steps*	Mehdi Lahlou 28 Sept 2026	Succession readiness updated: 2 ready now, 3 ready within 12 months.

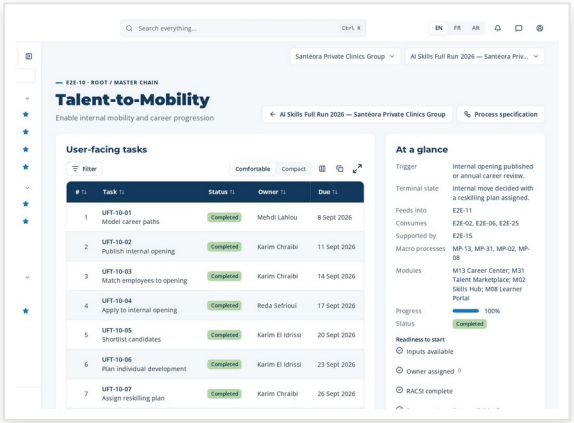

The page of E2E-10 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-13 Talent & Career Development
- MP-31 Skills-Based Talent Marketplace & Internal Mobility
- MP-02 Skills & Competency Management
- MP-08 Learner Experience & Engagement

Feeds into

E2E-11

Supported by

E2E-15

Onboarding-to-Productivity

Accelerate time-to-productivity


TRIGGER
New hire or internal mover confirmed.

END STATE
Employee productive within target time and onboarding closed.

7 tasks · 11 steps
20 days · 4 owners · 100 %

Macro processes: MP-35 Onboarding & Rapid Upskilling · MP-07 Learning Delivery & Implementation · MP-08 Learner Experience & Engagement · MP-13 Talent & Career Development

Task	Steps executed	Owner · done	What was entered
UFT-11-01 **Create onboarding record**	**MP-35.1** Create onboarding record	Karim El Idrissi 7 Sept 2026	Onboarding record for the new Clinical Care & Nursing technician, start date 1 July, buddy assigned.
UFT-11-02 **Generate 30-60-90 day path**	**MP-35.2** Generate 30-60-90 day path **MP-08.1** Generate personal learning plan	Karim Chraibi 10 Sept 2026	30-60-90 path: day 30 safety and ISO 7101; day 60 AI triage and clinical decision support; day 90 autonomy on shift.
UFT-11-03 **Enroll in onboarding sessions**	**MP-07.3** Enroll learners into session **MP-07.4** Send convocations	Reda Hajji 13 Sept 2026	Enroll in the induction session of 2 July; convocation sent.
UFT-11-04 **Complete onboarding tasks**	**MP-35.3** Complete onboarding tasks	Reda Sefrioui 16 Sept 2026	Tasks done: badge, IT account, safety tour, meeting with the team.
UFT-11-05 **Hold milestone check-ins**	**MP-35.4** Hold milestone check-in **MP-21.3** Schedule coaching sessions	Karim El Idrissi 19 Sept 2026	Day-30 check-in: on track; coaching needed on AI triage and clinical decision support data entry.
UFT-11-06 **Assess time to productivity**	**MP-35.5** Assess time to productivity	Karim El Idrissi 22 Sept 2026	Time to productivity: 74 days (target 90).

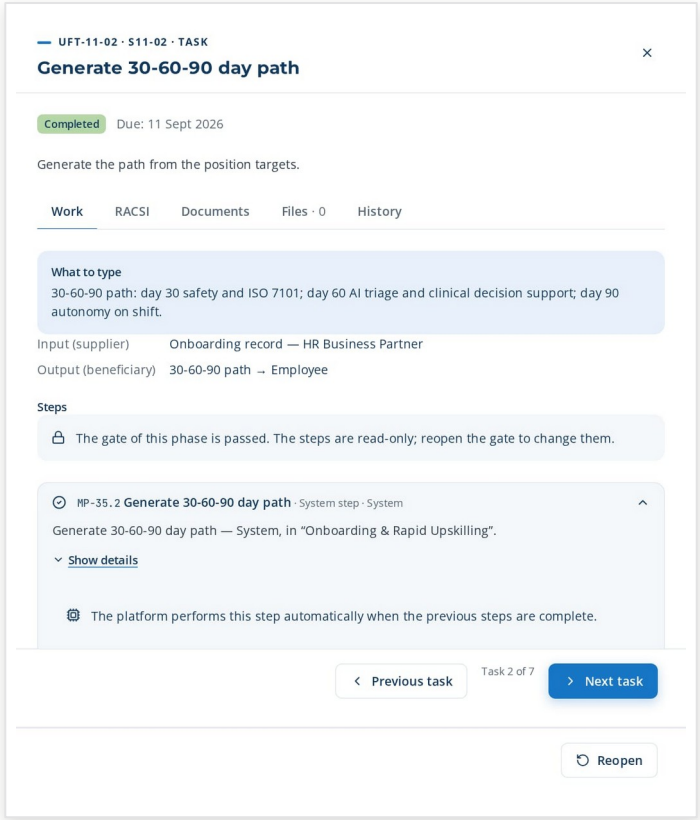


UFT-11-02 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Onboarding-to-Productivity (continued)

Task	Steps executed	Owner · done	What was entered
UFT-11-07 **Close onboarding**	**MP-35.6** Close onboarding **MP-13.3** Create individual development plan	Karim Chraibi 25 Sept 2026	Close onboarding; link the individual development plan for year 1.

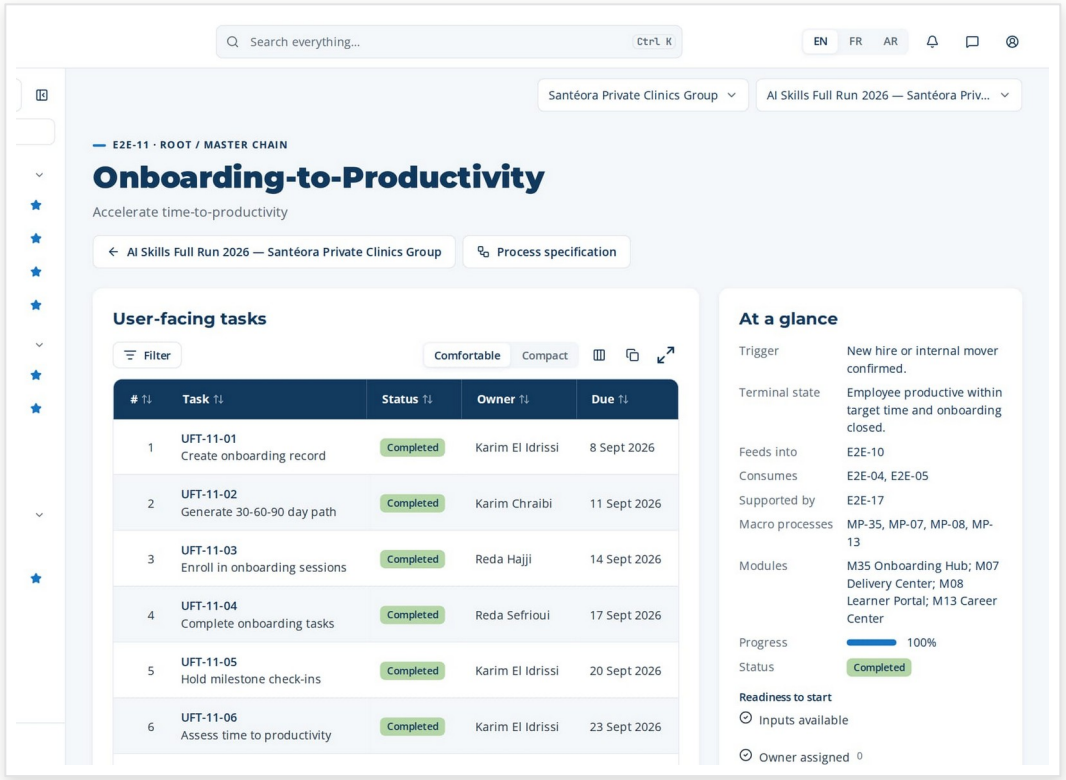

The page of E2E-11 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-35 Onboarding & Rapid Upskilling
- MP-07 Learning Delivery & Implementation
- MP-08 Learner Experience & Engagement
- MP-13 Talent & Career Development

Feeds into

E2E-10

Supported by

E2E-17

PHASE 6 · E2E-12 · ROOT / MASTER CHAIN

Knowledge-Capture-to-Transfer

Capture and transfer institutional knowledge


TRIGGER
Critical expert identified as leaving, retiring or holding at-risk knowledge.

END STATE
Knowledge captured, published and transferred to a validated successor.

7 tasks · 10 steps
20 days · 4 owners · 100 %

Macro processes: MP-34 Expert Knowledge Capture & Transfer · MP-12 Learning Culture & Knowledge Management · MP-33 User-Generated Content & Peer Knowledge Sharing · MP-06 Content & Resource Management

Task	Steps executed	Owner · done	What was entered
UFT-12-01 **Identify critical experts**	**MP-34.1** Identify critical experts	Karim Chraibi 7 Sept 2026	Critical expert: senior Clinical Care & Nursing engineer retiring in 8 months; knowledge risk: high.
UFT-12-02 **Plan capture sessions**	**MP-34.2** Plan capture sessions	Asmae Ziani 10 Sept 2026	Capture plan: 4 sessions of 90 minutes on troubleshooting and ISO 7101 practices.
UFT-12-03 **Record expert interview**	**MP-34.3** Record expert interview	Asmae Ziani 13 Sept 2026	Interview 1 recorded (82 minutes); transcript attached.
UFT-12-04 **Structure knowledge**	**MP-34.4** Structure knowledge from transcript	Asmae Ziani 16 Sept 2026	Accept the AI structure: 5 failure modes, 12 checks, 3 decision rules; correct 2 technical terms.
UFT-12-05 **Publish knowledge article**	**MP-12.1** Publish knowledge article **MP-12.2** Index article for retrieval **MP-33.4** Approve publication	Asmae Ziani 19 Sept 2026	Publish article 'Troubleshooting guide — Clinical Care & Nursing' in EN/FR/AR; indexed for search.
UFT-12-06 **Assign successor learning path**	**MP-34.5** Assign successor learning path **MP-06.6** Publish content to catalog	Karim El Idrissi 22 Sept 2026	Assign the successor path: article + 3 shadowing sessions with the expert.

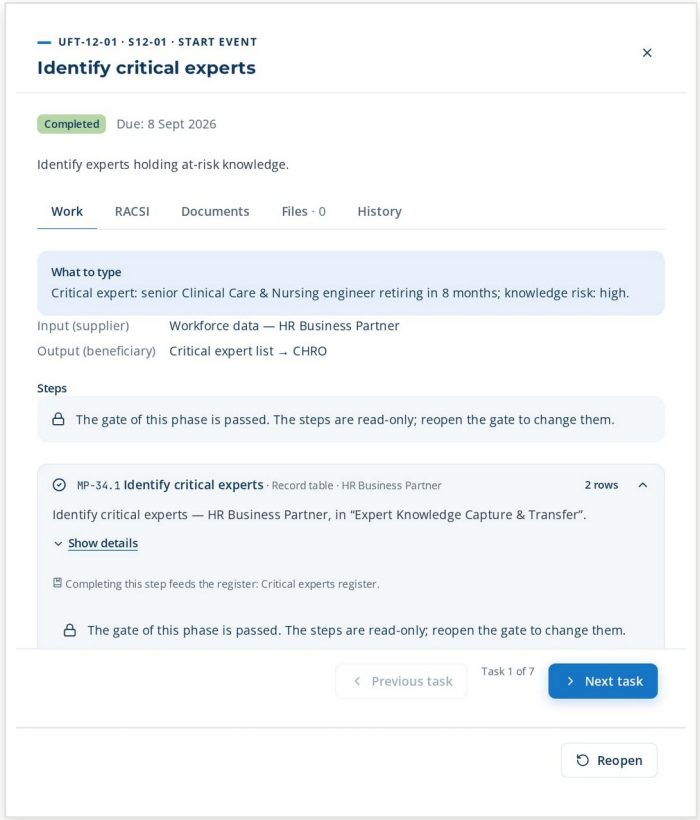


UFT-12-01 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Knowledge-Capture-to-Transfer (continued)

Task	Steps executed	Owner · done	What was entered
UFT-12-07 **Validate transfer completion**	**MP-34.6** Validate transfer completion	Hamza Lahlou 25 Sept 2026	Transfer validated: successor solved 4 of 5 test cases alone.

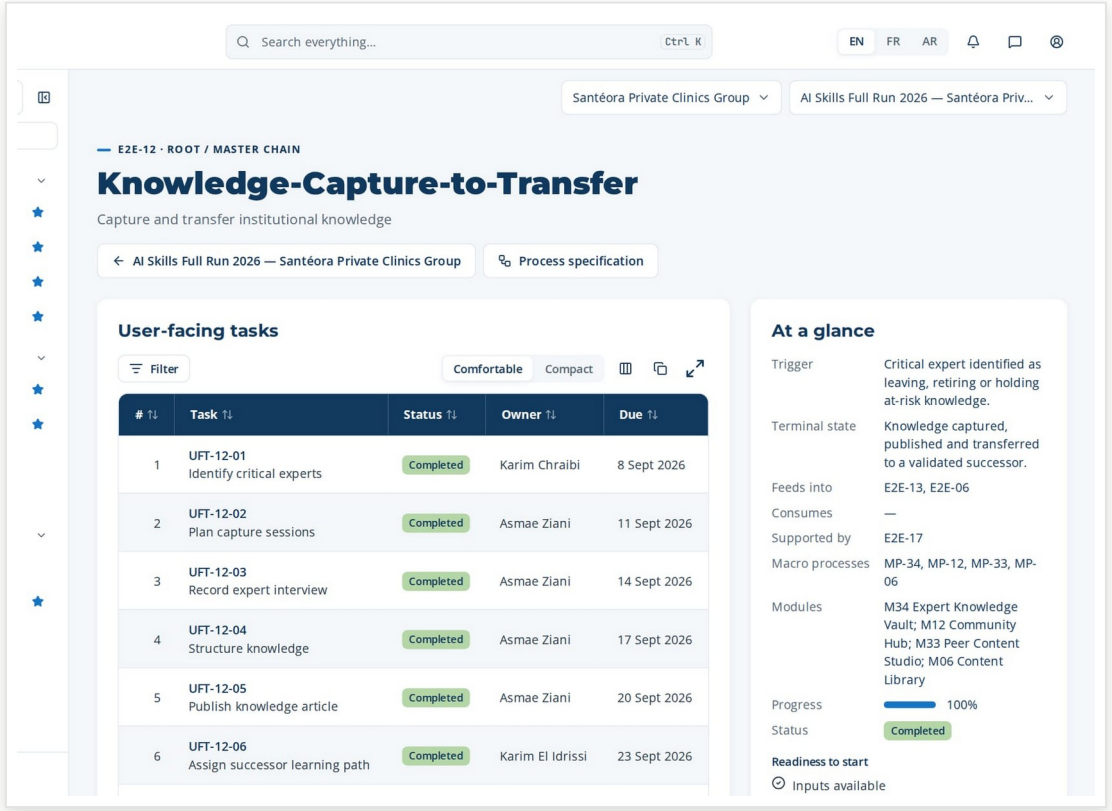

The page of E2E-12 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-34 Expert Knowledge Capture & Transfer
- MP-12 Learning Culture & Knowledge Management
- MP-33 User-Generated Content & Peer Knowledge Sharing
- MP-06 Content & Resource Management

Feeds into

E2E-13, E2E-06

Supported by

E2E-17

Engagement-to-Roadmap

Define post-engagement roadmap and continuous improvement


TRIGGER
Closure of the current training engineering engagement (E2E-19).

END STATE
Approved post-engagement roadmap with future missions and continuous improvement plan.

8 tasks · 12 steps
23 days · 5 owners · 100 %

Macro processes: MP-50 Post-Engagement Roadmap & Continuous Improvement · MP-36 Consulting Engagement Management · MP-19 Change Management & Adoption · MP-12 Learning Culture & Knowledge Management · MP-16 Data, AI & Integration Governance

Task	Steps executed	Owner · done	What was entered
UFT-31-01 **Consolidate engagement findings**	**MP-50.1** Consolidate engagement findings	Nadia Lahlou 7 Sept 2026	Findings: 6 deliverables, 3 lessons learned, 2 open topics (IS, org design).
UFT-31-02 **Define future perspectives**	**MP-50.2** Define future perspectives	Nadia Lahlou 10 Sept 2026	Perspectives: AI bed and staff capacity planning programme, second wave for OP level.
UFT-31-03 **Plan One-to-One coaching**	**MP-50.3** Plan One-to-One coaching	Amine Lahlou 13 Sept 2026	One-to-One coaching: 6 managers, 6 sessions each over 6 months.
UFT-31-04 **Plan organizational optimization**	**MP-50.4** Plan organizational optimization	Mehdi Lahlou 16 Sept 2026	Organizational optimization: merge 2 planning cells; update 11 descriptions.
UFT-31-05 **Plan IS rehabilitation**	**MP-50.5** Plan IS rehabilitation	Omar El Idrissi 19 Sept 2026	IS rehabilitation: connect HRIS and training platform; retire 2 spreadsheets.
UFT-31-06 **Define KPIs and dashboards**	**MP-50.6** Define KPIs and dashboards	Anas Hajji 22 Sept 2026	KPIs: training coverage, time to competency, ROI per theme; monthly dashboard.

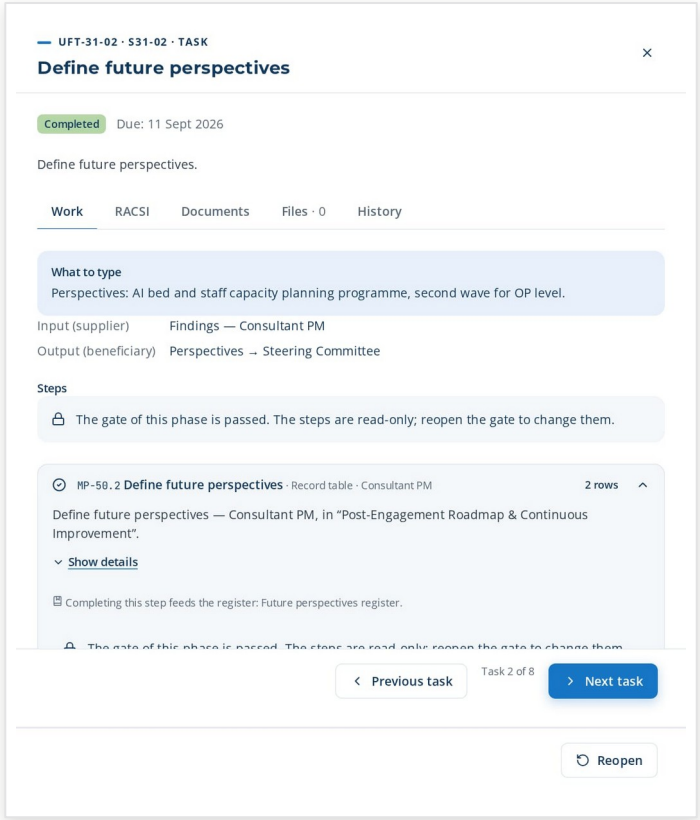


UFT-31-02 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Engagement-to-Roadmap (continued)

Task	Steps executed	Owner · done	What was entered
UFT-31-07 **Prioritize future missions**	**MP-50.7** Prioritize future missions **MP-50.8** Validate roadmap with leadership	Nadia Lahlou 25 Sept 2026	Priority missions: 1 IS rehabilitation, 2 coaching, 3 org optimization.
UFT-31-08 **Publish roadmap**	**MP-50.9** Publish post-engagement roadmap **MP-50.10** Track roadmap execution **MP-50.11** Improve roadmap continuously *+ 1 more steps*	Nadia Lahlou 28 Sept 2026	Publish RPT-010 Post-Engagement Roadmap to the executive committee.

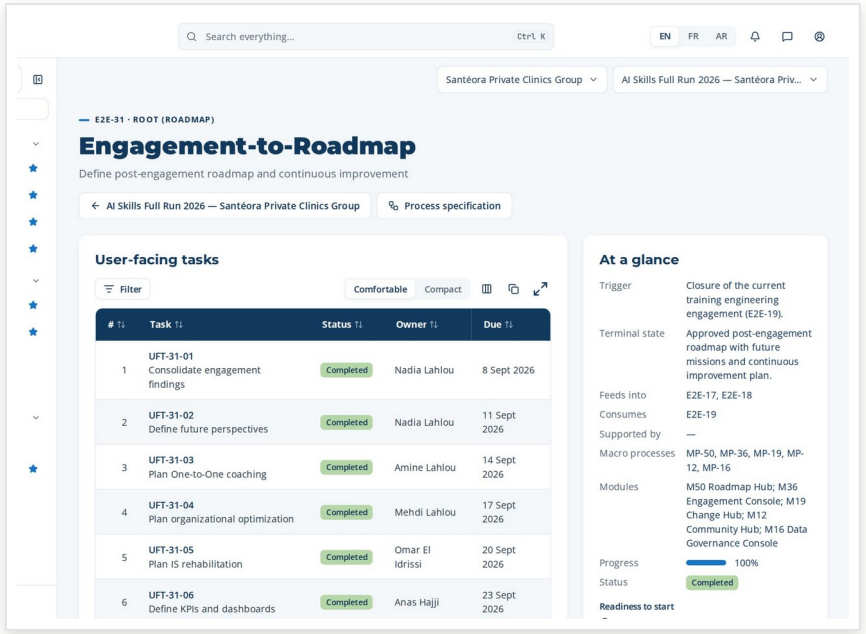

The page of E2E-31 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-50 Post-Engagement Roadmap & Continuous Improvement
- MP-36 Consulting Engagement Management
- MP-19 Change Management & Adoption
- MP-12 Learning Culture & Knowledge Management
- MP-16 Data, AI & Integration Governance

Feeds into

E2E-17, E2E-18

Supported by

—

00

PHASE 0

Enablers (run across all phases)

3 processes · 21 tasks · 34 steps

18 Apr 2026 – 31 Jul 2026

Runs across all phases

E2E-15 Data-AI-Integration

E2E-17 Change-to-Adoption

E2E-18 Quality-Risk-Improvement

PHASE 0 · E2E-15 · ROOT / ENABLER

Data-AI-Integration

Govern data, AI, integrations


TRIGGER
New integration, data source or AI use case to govern.

END STATE
Integrations, data and AI governed with health, retention and usage reviewed.

7 tasks · 11 steps
20 days · 3 owners · 100 %

Macro processes: MP-16 Data, AI & Integration Governance · MP-17 Identity, Access & Security Management · MP-10 Reporting & Analytics · MP-24 AI-Powered Personalization & Adaptive Learning · MP-28 Predictive Learning Analytics & Intelligence

Task	Steps executed	Owner · done	What was entered
UFT-15-01 **Register external integration**	**MP-16.1** Register external integration	Loubna Mansouri 20 Apr 2026	Register integration 'HRIS — Workday' (INT-HR-01); credential reference stored encrypted.
UFT-15-02 **Map fields and check health**	**MP-16.2** Map integration fields **MP-16.3** Check integration health	Omar El Idrissi 23 Apr 2026	Map fields: employee_id → matricule; position → poste. Health check: success.
UFT-15-03 **Run HRIS synchronisation**	**MP-16.4** Run HRIS synchronisation **MP-16.5** Review synchronisation rejections	Omar El Idrissi 26 Apr 2026	Sync run: 1,204 records updated, 3 rejected (missing position) — corrected.
UFT-15-04 **Set data retention rule**	**MP-16.6** Set data retention rule	Yassine Berrada 29 Apr 2026	Retention: questionnaire responses 3 years; training records 10 years.
UFT-15-05 **Maintain AI use case register**	**MP-16.7** Maintain AI use case register	Loubna Mansouri 2 May 2026	Add custom use case 'Shift-report summarizer' (Assistive), version 1.
UFT-15-06 **Set AI activation per scope**	**MP-16.8** Set AI activation per scope **MP-24.1** Enable personalization per scope	Loubna Mansouri 5 May 2026	Activate AIUC-35 and AIUC-36 for the organization; override Off for pilot project B.

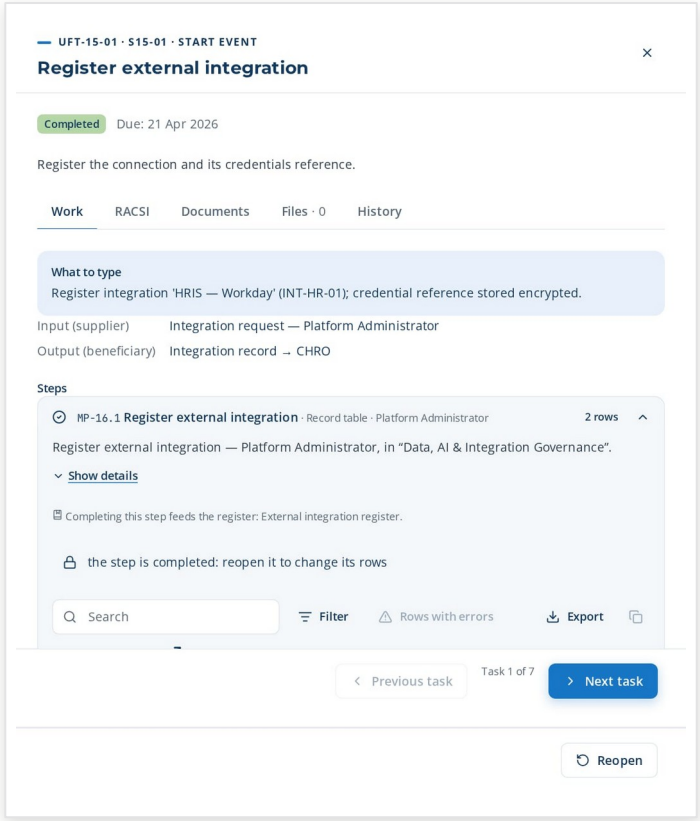


UFT-15-01 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Data-AI-Integration (continued)

Task	Steps executed	Owner · done	What was entered
UFT-15-07 **Review AI usage log**	**MP-16.9** Review AI usage log **MP-28.2** Validate dataset quality	Omar El Idrissi 8 May 2026	Usage review: 412 suggestions — 71% accepted, 20% edited, 9% rejected.

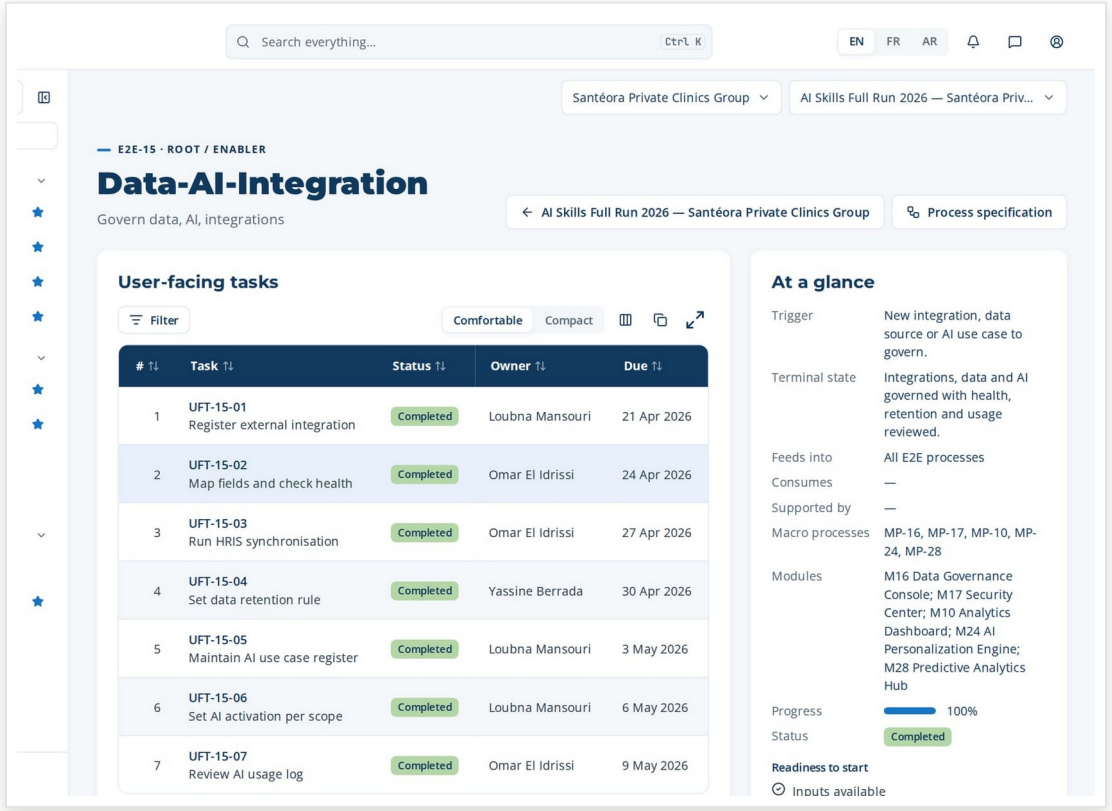

The page of E2E-15 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-16 Data, AI & Integration Governance
- MP-17 Identity, Access & Security Management
- MP-10 Reporting & Analytics
- MP-24 AI-Powered Personalization & Adaptive Learning
- MP-28 Predictive Learning Analytics & Intelligence

Feeds into

All E2E processes

Supported by

—

Change-to-Adoption

Drive sustained adoption and culture change


TRIGGER
Approved plan or new platform capability requiring adoption.

END STATE
Sustained adoption reached with low-adoption groups reinforced.

7 tasks · 11 steps
20 days · 3 owners · 100 %

Macro processes: MP-19 Change Management & Adoption · MP-12 Learning Culture & Knowledge Management · MP-08 Learner Experience & Engagement · MP-26 Social & Collaborative Learning Networks

Task	Steps executed	Owner · done	What was entered
UFT-17-01 **Assess change impact**	**MP-19.1** Assess change impact	Yassine Fassi 13 Jul 2026	Impact: Clinical Care & Nursing supervisors high, operators medium, support functions low.
UFT-17-02 **Build adoption plan**	**MP-19.2** Build adoption plan	Yassine Fassi 16 Jul 2026	Adoption plan: sponsor message, 6 champions, weekly 15-minute huddles for 8 weeks.
UFT-17-03 **Launch communication campaign**	**MP-19.3** Launch communication campaign	Yassine Fassi 19 Jul 2026	Campaign 'AI triage and clinical decision support — why it matters' on e-mail, intranet and screens.
UFT-17-04 **Open community space**	**MP-12.3** Create community space **MP-12.4** Moderate community posts **MP-26.1** Create learning cohort group	Asmae Ziani 22 Jul 2026	Community space 'AI triage and clinical decision support Q&A' opened; moderation rules published.
UFT-17-05 **Track adoption usage**	**MP-19.4** Track adoption usage **MP-08.5** Monitor engagement indicators	Yassine Berrada 25 Jul 2026	Weekly active users: 64% of the target population.
UFT-17-06 **Identify low-adoption groups**	**MP-19.5** Identify low-adoption groups	Yassine Fassi 28 Jul 2026	Low adoption confirmed for night shift (31%); one group rejected as false positive.

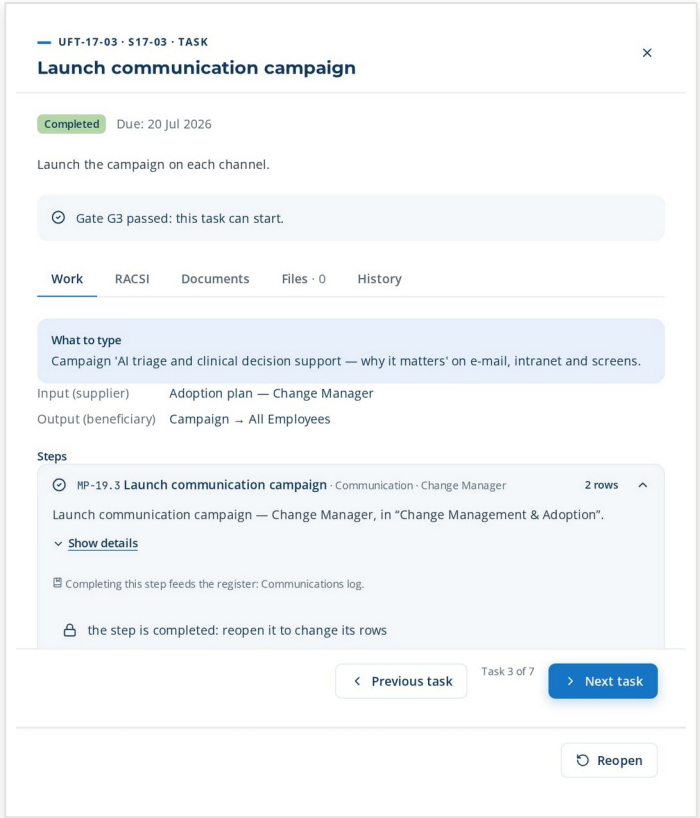


UFT-17-03 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Change-to-Adoption (continued)

Task	Steps executed	Owner · done	What was entered
UFT-17-07 **Run reinforcement actions**	**MP-19.6** Run reinforcement actions **MP-08.6** Trigger re-engagement nudge	Yassine Fassi 31 Jul 2026	Reinforcement: night-shift coaching sessions; adoption reached 58% after 4 weeks.

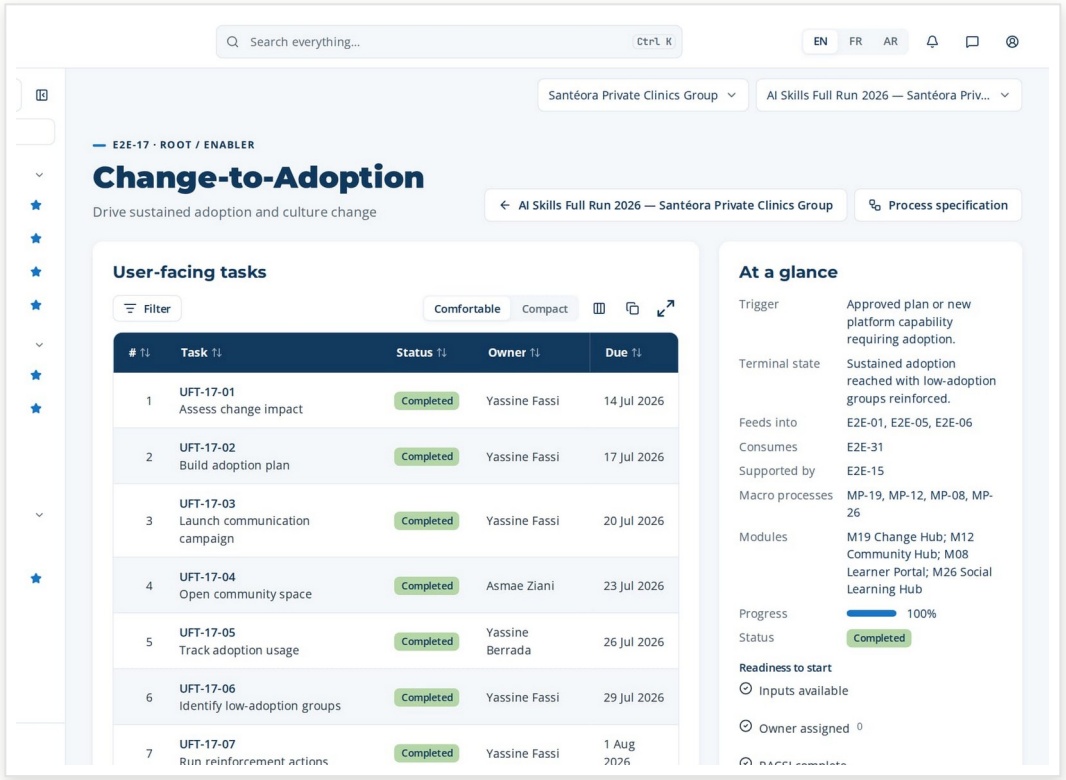

The page of E2E-17 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-19 Change Management & Adoption
- MP-12 Learning Culture & Knowledge Management
- MP-08 Learner Experience & Engagement
- MP-26 Social & Collaborative Learning Networks

Feeds into

E2E-01, E2E-05, E2E-06

Supported by

E2E-15

PHASE 0 · E2E-18 · ROOT / ENABLER

Quality-Risk-Improvement

Improve processes and mitigate risk


TRIGGER
Risk logged, periodic quality review due or control test scheduled.

END STATE
Risks mitigated, actions evaluated by a different person, controls rated.

7 tasks · 12 steps
20 days · 2 owners · 100 %

Macro processes: MP-20 Quality, Risk & Continuous Improvement · MP-16 Data, AI & Integration Governance · MP-17 Identity, Access & Security Management · MP-09 Assessment & Evaluation

Task	Steps executed	Owner · done	What was entered
UFT-18-01 **Log risk or opportunity**	**MP-20.1** Log risk or opportunity	Soukaina Bennani 20 Apr 2026	Risk 'Trainers unavailable in Q3': likelihood 3, impact 4, score 12.
UFT-18-02 **Assign mitigation action**	**MP-20.2** Assign mitigation action	Soukaina Bennani 23 Apr 2026	Action: contract a second vendor; owner Purchasing Officer; evaluator Quality Manager.
UFT-18-03 **Execute improvement action**	**MP-20.3** Execute improvement action	Soukaina Bennani 26 Apr 2026	Action done: framework contract signed with vendor B; evidence attached.
UFT-18-04 **Evaluate action effectiveness**	**MP-20.4** Evaluate action effectiveness	Soukaina Bennani 29 Apr 2026	Verdict: effective. The evaluator is a different user from the owner.
UFT-18-05 **Review access and security**	**MP-17.4** Review access violation log **MP-17.6** Enforce login rate limit **MP-17.2** Assign roles to user *+ 2 more steps*	Omar El Idrissi 2 May 2026	Access review: 2 dormant accounts disabled; 0 cross-tenant attempts.
UFT-18-06 **Run periodic quality review**	**MP-20.5** Run periodic quality review **MP-09.7** Review evaluation results	Soukaina Bennani 5 May 2026	Quality review minutes: 3 KPIs red, 2 actions opened, next review in 30 days.

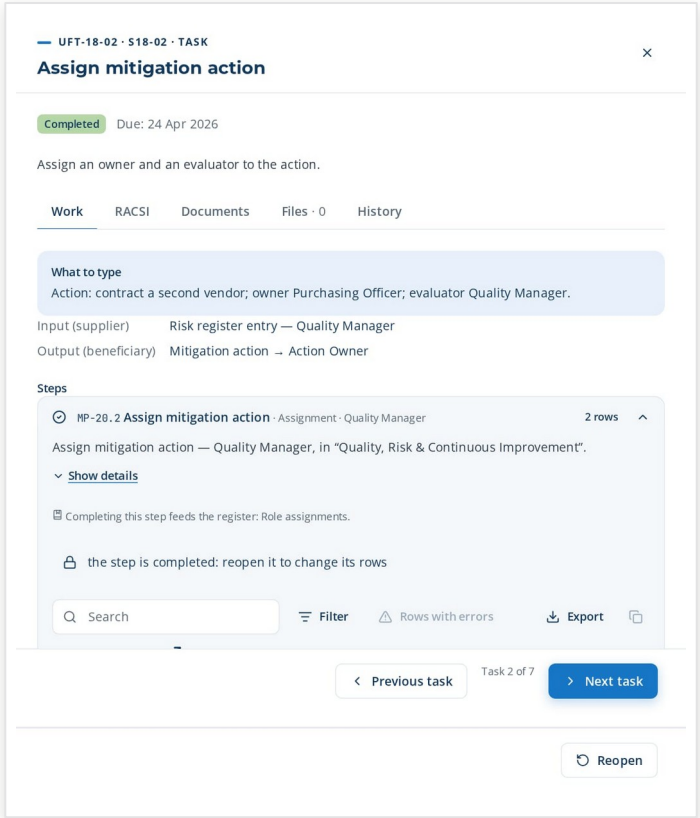


UFT-18-02 opened in CortexSkills: what to enter, its steps and its result.

Continued on the next slide

Quality-Risk-Improvement (continued)

Task	Steps executed	Owner · done	What was entered
UFT-18-07 **Update control effectiveness**	**MP-20.6** Update control effectiveness rating	Soukaina Bennani 8 May 2026	Control CTRL-002 effectiveness: Effective; CTRL-031: Partially effective.

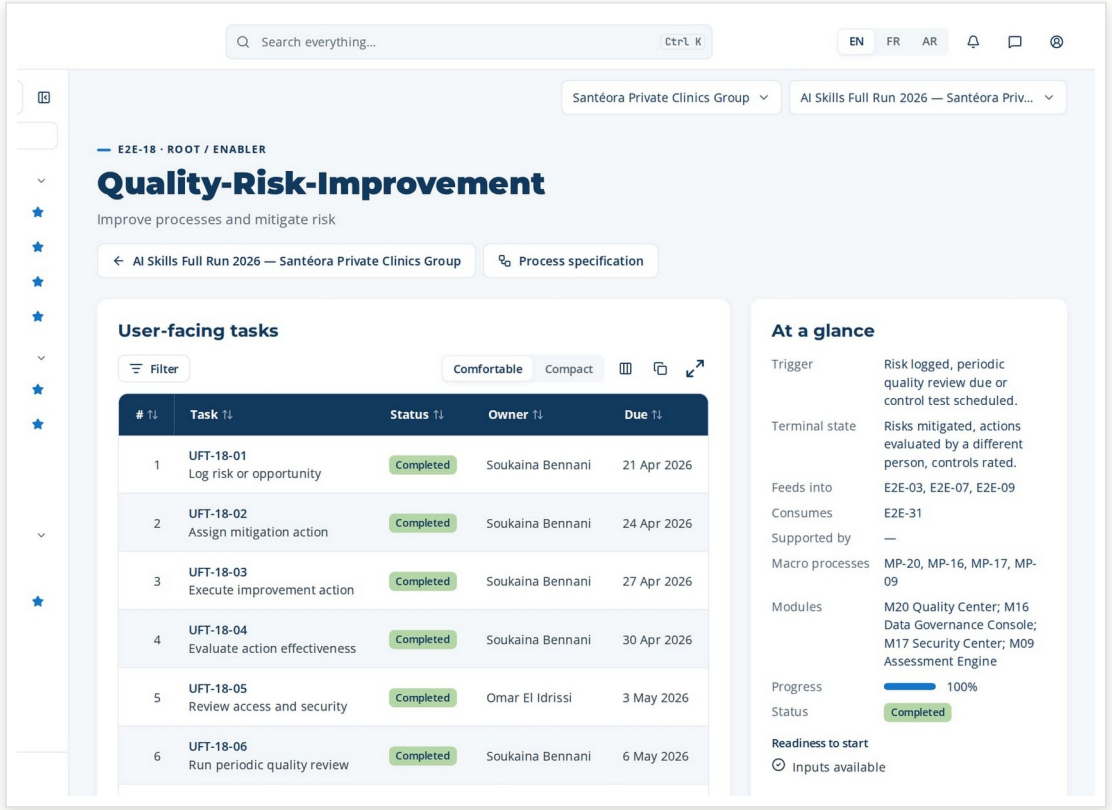

The page of E2E-18 in CortexSkills: its tasks, owners and due dates, and the process card.

Macro processes

- MP-20 Quality, Risk & Continuous Improvement
- MP-16 Data, AI & Integration Governance
- MP-17 Identity, Access & Security Management
- MP-09 Assessment & Evaluation

Feeds into

E2E-03, E2E-07, E2E-09

Supported by

—

RESULTS

What the run produced, in figures

Each figure is the value entered or computed at the step shown under it

187

questionnaire responses consolidated

UFT-03-06

6

themes built from 23 validated needs

UFT-03-05

1.33 M

MAD net L&D budget approved

UFT-01-05

+33 pts

test score, 48 % to 81 % (level 2)

UFT-07-04

9 / 11

supervisors apply the routine at day 30

UFT-07-05


22 %

ROI, benefit-cost ratio 1.22

UFT-08-05

Training measured at every Kirkpatrick level

Session S-01, AI triage and clinical decision support for supervisors

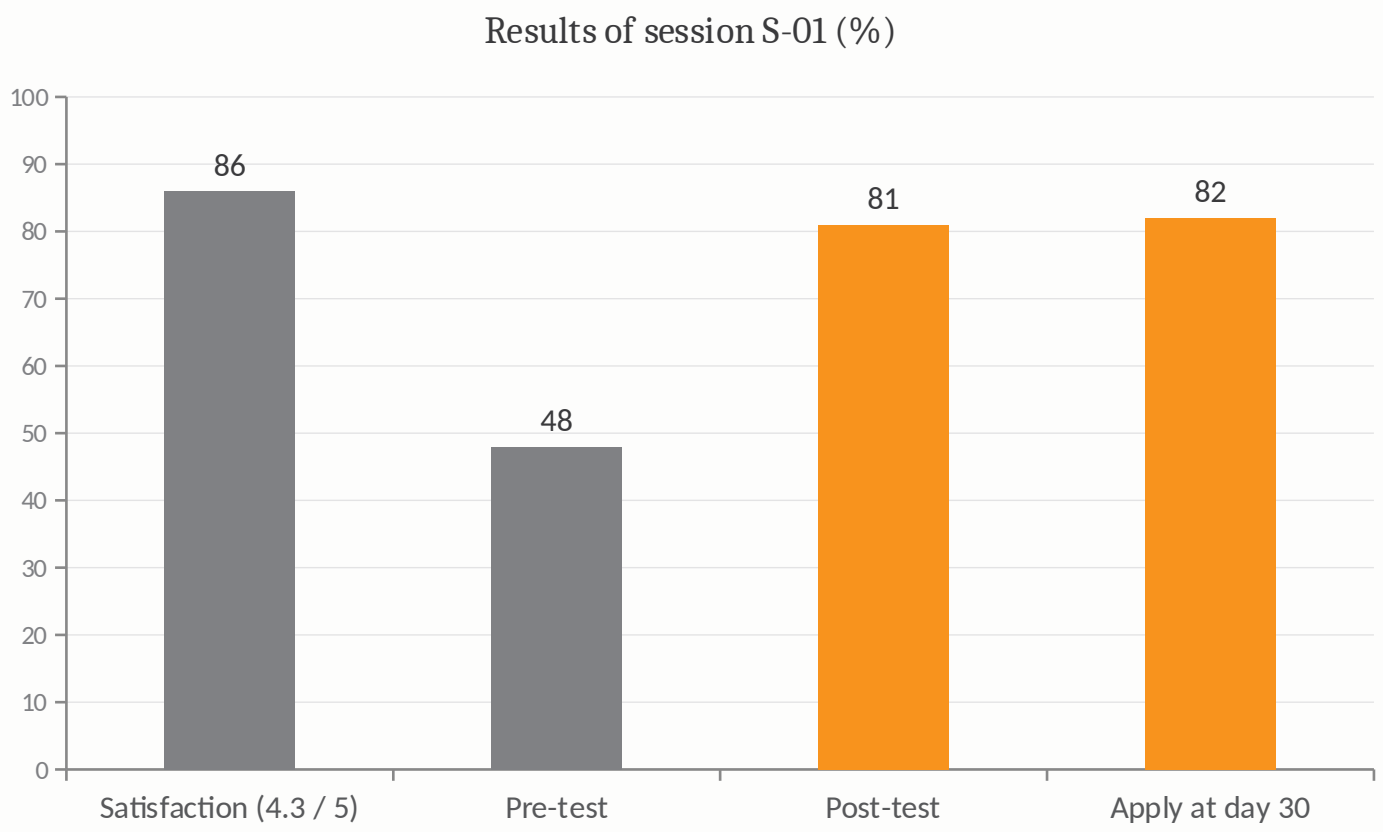

Satisfaction 4.3/5 shown as 86 %; 9 of 11 participants shown as 82 %. Source: tasks UFT-07-03 to UFT-07-05.

Level 1 — Reaction
Reaction survey S-01: 11 responses, satisfaction 4.3/5.

Level 2 — Learning
Level 2: average pre-test 48%, post-test 81% (+33 points).

Level 3 — Behaviour
Level 3 (day 30): 9 of 11 supervisors apply the AI triage and clinical decision support routine daily.


Level 4 — ROI
ROI = (410,000 − 335,000) / 335,000 = 22%; benefit-cost ratio 1.22.

RESULTS

Every KPI of the project on target


61 of 61 KPIs green — the first ten

ID	KPI	Value	Target	Status
KPI-001	Strategic objective coverage	108	100	**On target**
KPI-002	Skills inventory validation rate	102.6	95	**On target**
KPI-003	Critical gap rate	8.2	10	**On target**
KPI-004	Training Engineering Report cycle time	24.6	30	**On target**
KPI-005	Design approval lead time	16.4	20	**On target**
KPI-006	License Compliance %	108	100	**On target**
KPI-007	Content publication lead time	12.3	15	**On target**
KPI-008	Session fill rate	91.8	85	**On target**
KPI-009	Plan realization rate	97.2	90	**On target**
KPI-010	Learner completion rate	86.4	80	**On target**

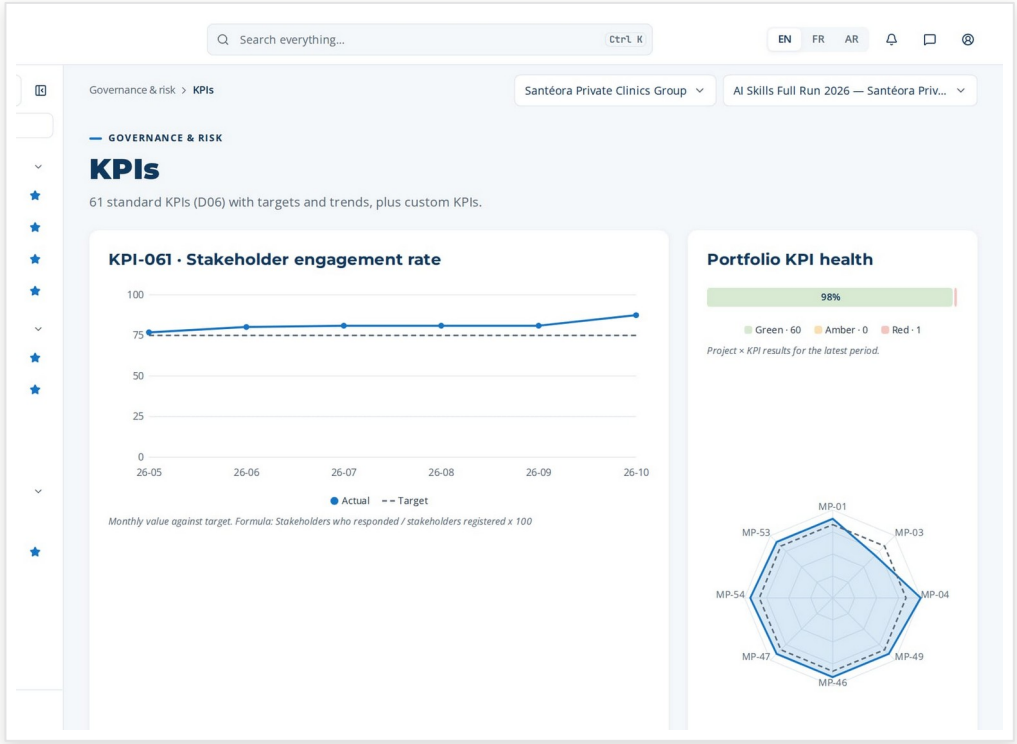

KPI page of the project in CortexSkills.


The questionnaire campaign

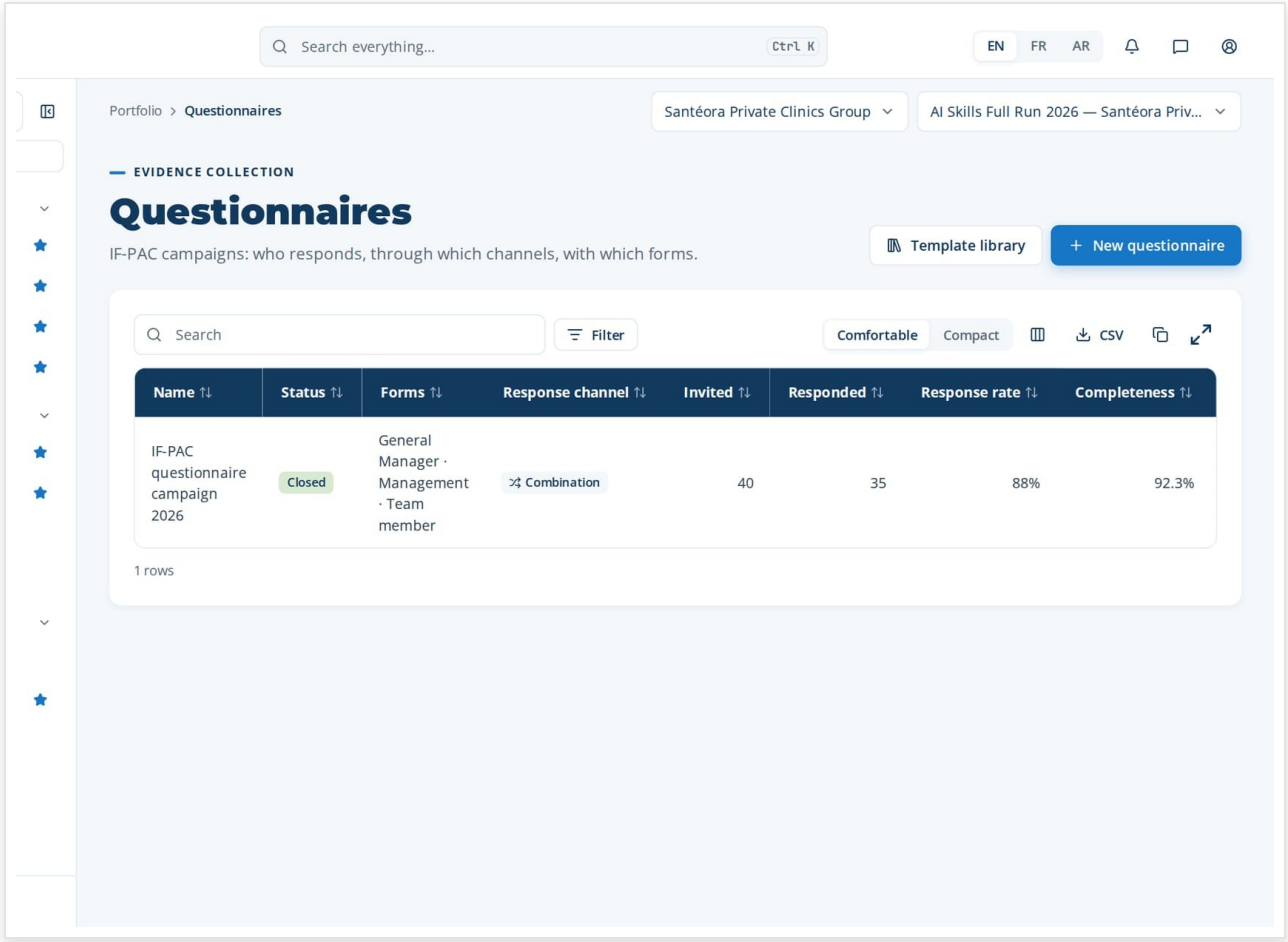

Campaign with three forms (top management, management, staff), channels, response rate and completeness.

DELIVERABLES


The 2026 training plan

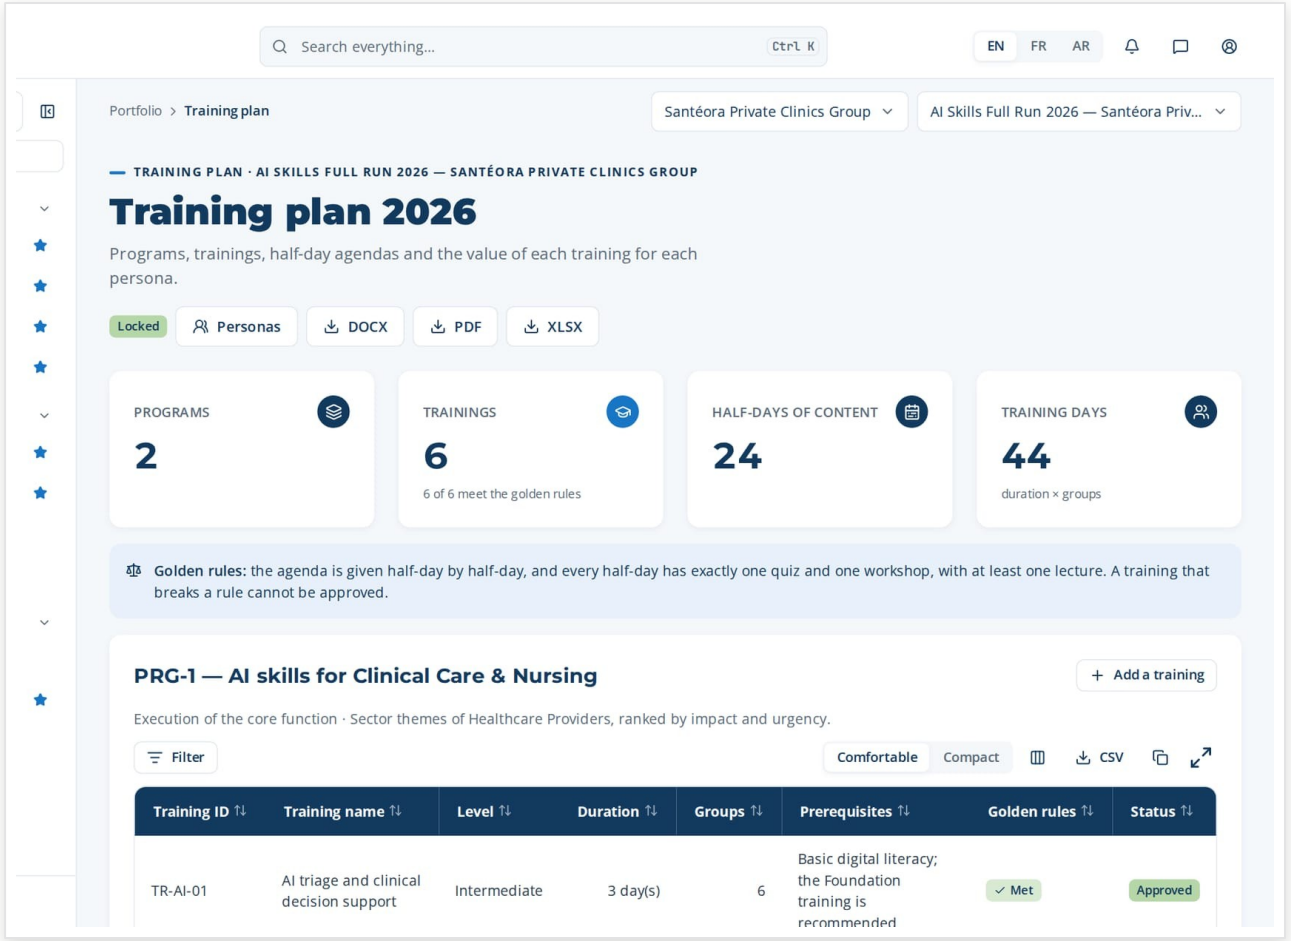

Programmes, trainings, half-day agendas and the golden rules checked on every training.


DELIVERABLES

37 documents published, versioned and approved

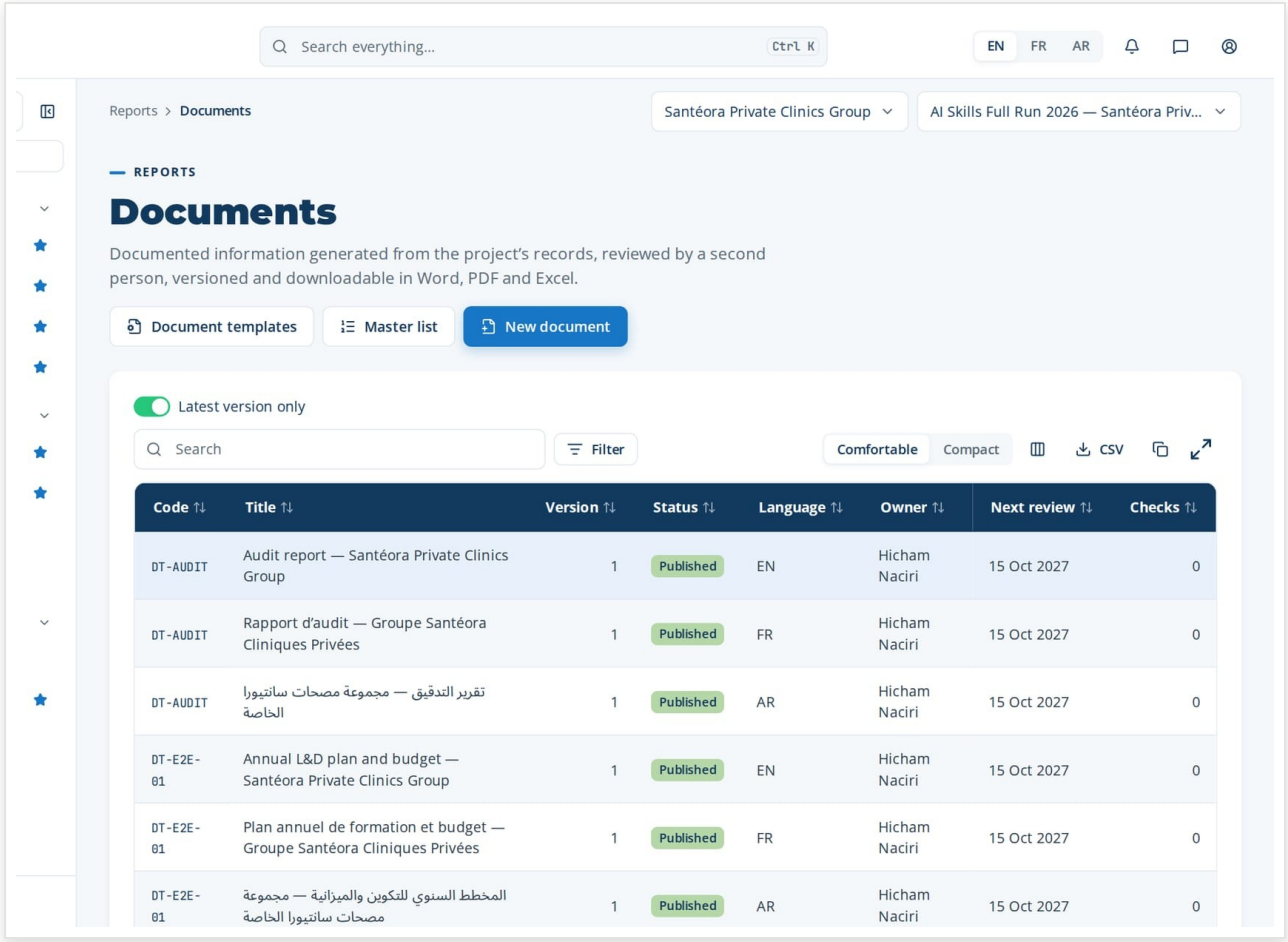

Training Engineering Report, training plan, audit, ROI report and the other documents, each with an author, an approver and a review date.

Standard reports, ready to export

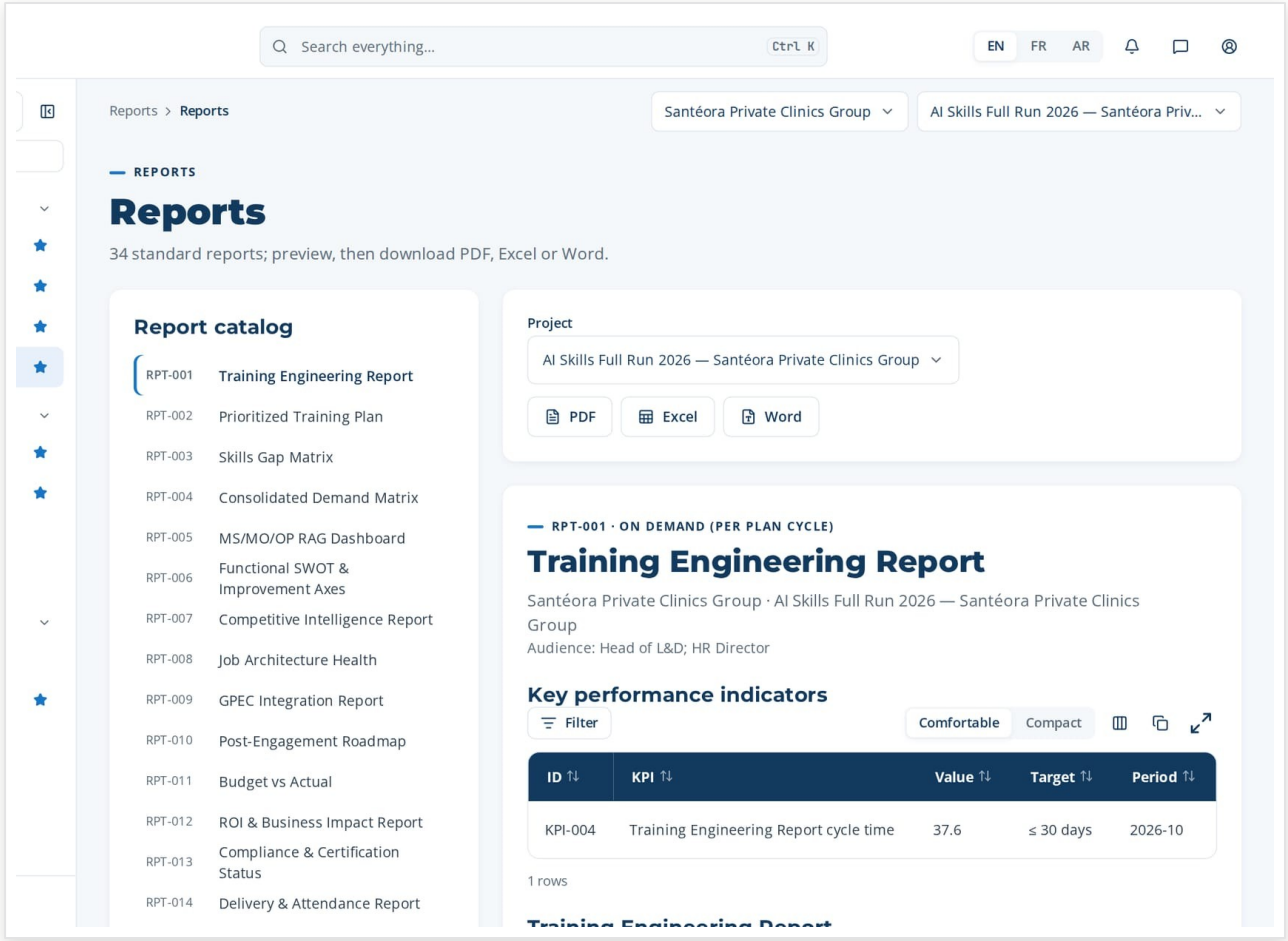

34 standard reports, previewed and downloaded as PDF, Excel or Word.

NEXT STEPS

Proposed path for your clinics

Durations are indicative and set with you during the scoping workshop

1

Scoping workshop

Half a day: sites, functions, decision levels, focus and stakeholders — Phase 1 in the application.

2

Pilot on one clinic

Questionnaires, diagnosis and Training Engineering Report on your data — Phases 1 to 3.

3

Deployment to all clinics

Delivery, evaluation up to ROI and continuous improvement — Phases 4 to 6.

Deployment on your private cloud or on site, under a licence; interface and documents in French, English and Arabic.

Thank you

POWERACT Consulting · CortexSkills, training engineering for healthcare

Questions and discussion
